



भारत सरकार / Government of India
विद्युत मंत्रालय / Ministry of Power
पूर्वी क्षेत्रीय विद्युत समिति / Eastern Regional Power Committee

सं /NO. ERPC/EE/OPERATION/2026/ 1258

DATE:25.09.2026

सेवा में /To
संलग्न सूची के अनुसार /As per list enclosed.

विषय : 16.09.2026 (बुधवार) को ईआरपीसी सचिवालय, कोलकाता में भौतिक रूप से आयोजित 243वीं ओसीसी बैठक के कार्यवृत्त – के संबंध में

Sub: Minutes of 243rd OCC Meeting held on 16.09.2026 (Wednesday) physically at ERPC Secretariat, Kolkata – reg

महोदय/महोदया,
Sir(s)/Madam,

कृपया अपनी जानकारी और आवश्यक कार्रवाई के लिए **16 सितम्बर 2026 (बुधवार)** को आयोजित **243वीं ओसीसी बैठक** के **कार्यवृत्त** संलग्न देखें। यह ईआरपीसी वेबसाइट (www.erpcc.gov.in) पर भी उपलब्ध है।

Please find enclosed **Minutes of 243rd OCC Meeting** held on **16.09.2026 (Wednesday)** physically at **ERPC Secretariat, Kolkata** at **10:30 hrs.** This is for your **kind information** and **necessary action**. The same is also available at ERPC website (www.erpcc.gov.in).

टिप्पणियाँ, यदि कोई हों, कृपया यथाशीघ्र इस कार्यालय को अग्रेषित करें।

Observations, if any, may please be forwarded to this office at the earliest.

इसे सदस्य सचिव के अनुमोदन से जारी किया जाता है।

This issues with the approval of Member Secretary.

भवदीय /Yours faithfully


आर.के.मीना / (R.K.Meena)
एसई (ऑपरेशन)/SE(Operation)

Sl. No	Organization	Category	E-mail
1	CEA	GM division	gmcea@nic.in
2	ERPC	RPC	mserpc-power@nic.in
3	ERPC		secomml.erpc@gov.in
4	ERPC		seop-erpc@gov.in
5	ERPC		erpc-protection@gov.in
6	ERPC		hoo-erpc@gov.in
7	CEA	RPSO	hoorpso.kol-power@gov.in
8	DVC	Central GENCO	sanjay.sharma@dvc.gov.in
9	DVC		santosh.panda@dvc.gov.in
10	NTPC		prasannasahoo@ntpc.co.in
11	NTPC		jaiprakashverma@ntpc.co.in
12	NTPC Farakka		sumeetnarang@ntpc.co.in
13	NTPC		sraybarman@ntpc.co.in
14	NTPC		ksureshababu@ntpc.co.in
15	NTPC		arshadjilani@ntpc.co.in
16	NTPC Nabi Nagar		skupadhyay@ntpc.co.in
17	NTPC-Barh		aksrivastava16@ntpc.co.in
18	NTPC-Barh		abhishekmurari@ntpc.co.in
19	NTPC-TSTPS		suranjandas@ntpc.co.in
20	BRBCL/NTPC		bnvadav01@ntpc.co.in
21	POWERGRID ER-II	Central TRANSCO	partha.ghosh@powergrid.in
22	POWERGRID ER-II		mithun.gaven@powergrid.in
23	POWERGRID ER-II		snayek@powergrid.in
24	POWERGRID ER-II		pmaity@powergrid.in
25	POWERGRID ER-I		sudeepkumar@powergrid.in
26	Powergrid, Odisha Project		eswar@powergrid.in
27	Powergrid, Odisha Project		ajayasahu@powergrid.in
28	WBSEDCL	DISCOM	preeban72@gmail.com
29	ERLDC	RLDC	surajit.banerjee@grid-india.in
30	ERLDC		dbiswas@grid-india.in
31	ERLDC		bilash.achari@grid-india.in
32	ERLDC		manasdas@grid-india.in
33	ERLDC		chandan.mallick@grid-india.in
34	ERLDC		rkpradhan@grid-india.in
35	ERLDC		apsingh@grid-india.in
36	GRIDCO	Others	ele.plsahoo@gridco.co.in
37	GRIDCO		ele.bpmohapatra@gridco.co.in
38	CESC	Private GENCO	koushik.banerjee@rpsg.in
39	CESC		anupam.biswas@rpsg.in
40	CESC		debarshi.de@rpsg.in
41	MPL		rautpv@tatapower.com
42	GMR, Odisha		swapnajiit.panigrahi@gmrgroup.in
43	GMR, Odisha		diptikanta.panda@gmrgroup.in
44	JSW		biswanath.patel@jsw.in
45	JSW		mahendra.malik@jsw.in
46	APNRL		ashishghosh@adhunikpower.co.in
47	APNRL		rajukumarsharma@gmail.com
48	APNRL		rahul.kumar@adhunikpower.co.in
49	MPL		jetir@tatapower.com
50	HEL		archita.dutta@rpsg.in
51	SJVN		emd.stpl@sjvn.nic.in
52	JIPL		jiplscheduling@jindalgroup.com
53	INDIGRID	Pvt.TRANSCO	abhishek.kukreja@indigrid.com
54	INDIGRID		dinesh.laha@indigrid.com
55	INDIGRID		somnath.mukherjee@indigrid.com

Sl. No	Organization	Category	E-mail
56	SIKKIM POWER TRANSMISSION		avyappa.v@greenkogroup.com
57	WBSLDC	SLDC/STU	ce.wbsldc@gmail.com
58	WBSLDC		arnab.basu@wbsetcl.in
59	WBSLDC		utsab.aditya@gmail.com
60	WBSLDC		svkbanerjee@yahoo.com
61	WBSLDC		sanjiibroy12235@gmail.com
62	WBSETCL		cecpwbsetcl@gmail.com
63	WBSETCL		cpd.wbsetcl@gmail.com
64	BSPTCL		sldc.bseb@gmail.com
65	BSPTCL		gagankmishra@gmail.com
66	SLDC, Ranchi, JUSNL		tuneshwarkumar@gmail.com
67	SLDC, Ranchi, JUSNL		rimiltopno@gmail.com
68	SLDC, Ranchi, JUSNL		rajmailme82@gmail.com
69	WBSETCL		sajalkbag74@gmail.com
70	WBSETCL		ce.wbsldc@gmail.com
71	WBSETCL		cpd.wbsetcl@gmail.com
72	OPTCL		ele.smsahoo@optcl.co.in
73	OPTCL		ele.scdash@optcl.co.in
74	SLDC, Odisha		cld_sldc@sldcorissa.org.in
75	SLDC, Odisha		sanjayasldc@gmail.com
76	WBPDC	State GENCO	mpodder@wbpdcl.co.in
77	WBPDC		rk.koley@wbpdcl.co.in
78	TVNL		bk20tvnl@gmail.com
79	OHPC		chandan.panda143@gmail.com
80	OHPC		dasakshaya26@gmail.com



Eastern Regional Power Committee

MINUTES OF 243rd OCC MEETING

Venue: ERPC Secretariat, Kolkata

Date: 16.09.2026

Contents

1. PART-A: CONFIRMATION OF MINUTES	4
1.1. Confirmation of Minutes of 242 nd OCC Meeting held physically at ERPC Secretariat on 20 th August 2026	4
2. PART-B: ITEMS FOR DISCUSSION.....	4
2.1 Update on follow up agenda: ERPC	4
2.2 Issues for follow-up: ERLDC	15
2.3 Augmentation of Transformation Capacity at Critically Loaded Substations Feeding Major Urban & Industrial Clusters: ERLDC.....	20
2.4 Performance of Automatic Demand Management Scheme (ADMS) –ER: ERLDC	24
2.5 Shutdown of GIS Bays at POWERGRID’s 220 kV Rangpo Substation for Teesta-VI HE Project: NHPC.....	25
2.6 Agenda from WBSEDCL	26
2.6.1 Accessibility of Generation Outage Information	26
2.6.2 Real-Time Pan-India Generation Outage Information.....	27
2.6.3. Transparency in Ancillary Charges and Inclusion of SCUC Details in WBES .	27
2.6.4. Prevention of Forced Backdown During Total Full Requisition Blocks	28
2.7 Agenda from NTPC Barauni.....	30
2.8 Agenda from NTPC Kahalgaon	30
2.9 Shutdown proposal of Thermal generating units: ERPC	32
2.10 Reconsideration of the month of October under the High Inflow Period for FY 2026-27 in respect of Jorethang Loop HEP (JLHEP) and Tashiding HEP (THEP): DANS Energy	33
2.11 Replacement of 400 KV Isolators & Bus Bar protection commissioning at Malda Substation: ERPC	33
2.12 Formal Procedure for sharing IMD Wind Sensors’ Data with Power Utilities: ERPC	34
2.13 Submission of Year-Ahead Resource Adequacy Data for FY 2027-28: ERLDC	34
2.14 Miscellaneous agenda by PVUNL	35
2.15 Procurement of Reactors under ADD-CAP Block 2024-29 in Odisha based on RLA submitted by M/s CPRI: POWERGRID ODISHA	39
2.16 Establishment of Inter-State Tie-Line Connectivity between DVC–BSPTCL and DVC–JUSNL: DVC	40
2.17 Review of DSM Charges due to system issue in WBES Scheduling Portal for HVDC Pusauli from NTPC Kahalgaon Stage-1.: POWERGRID ER-I	41
2.18 Installation of Transmission Line Arrestor in 220kV & 400kV Lines in High Lightning prone areas of North-Bengal & South-Bengal: POWERGRID ER-II.....	44
2.19 Way leave charge payment for crossing of Railway Lines by various overhead transmission lines of POWERGRID after expiry of initial construction period agreement of 10 years: POWERGRID ER-II	49
2.20 Proposal for AMC support against sustained operations and maintenance of AMR application Web Client Access extended to SLDC/ER-Constituents & DVC: POWERGRID ER-II	50
2.21 DCU replacement plan in the AMR circuit of Eastern Region, towards cyber security enforcement and ensure future proof solutions: POWERGRID ER-II.....	52

2.22	Conducting VAPT assessment for AMR Asset in ERLDC (in Compliance with Cyber security guidelines): POWERGRID ER-II.....	54
2.23	Lower DC declaration during peak hours as compared to off-peak hours of the same day by ER ISGS under Partial Outage: ERLDC	55
2.24	Establishment of Disaster Recovery (DR) Facility for SAMAST Project of SLDC, WBSETCL: WB SLDC.....	56
3.	PART-C: ITEMS FOR INFORMATION.....	58
3.1.	ER Grid performance during August 2026	58
3.2.	Regarding Non-Submission of Forecasting and Resource Adequacy Data from States: ERLDC	58
4.	PART-D: OPERATIONAL PLANNING.....	60
4.1.	Major Thermal Generating Units/Transmission Element outages/shutdown in ER Grid (as on 08.09.2026)	60
4.2.	Long outage report of transmission Element (MORE THAN 01 WEEK) (As on 08.09.2026):	61
4.3.	Commissioning of new units and transmission elements in Eastern Grid in the month of August-2026.....	64
4.4.	UFR operation during the month of August 2026.....	66

EASTERN REGIONAL POWER COMMITTEE

MINUTES OF 243rd OCC MEETING HELD ON 16.09.2026 (THURSDAY) AT 10:30 HRS

Member Secretary, ERPC welcomed all OCC members and other participants to the **243rd OCC Meeting**.

Thereafter he requested all the participants to give brief introduction.

□ He outlined the performance of ER grid during **August-2026** highlighting the following points:

- In **August-2026**, energy consumption of ER was **21087 MU** which is **9.2 % more** than **August - 2025**.
- In **August-2026**, Peak demand met of ER was **33824 MW** which is **9.3 % more** than **August -2025**.
- ❖ Thermal **PLF** of **ER** during **August-2026** was **75%** whereas National average is **66.8%**.
- ❖ Generating stations whose **PLF** was **90%** or more during **August-2026**:

Utility	Generating station	PLF (%)
WBPDC	BAKRESWAR TPS	92
	SANTALDIH TPS	92
IPP	HALDIA TPP (HEL)	98

- ❖ During **August-2026**, **77.15%** of the time, the ER grid frequency was within IEGC Band (49.90Hz-50.05Hz).

Coal stock position (As on 12.09.2026) is as follows:

SL.	Name of States/Power Stns.	% of Actual Stock vis-à-vis Normative Stock
1.	Jharkhand (TVNL)	50%
2.	Odisha (IB TPS)	86%
3.	West Bengal (WBPDC)	63%
4.	D.P.L. TPS	26%
5.	DVC	59%
6.	NTPC	46%

Concerns were expressed regarding the fuel-stock position reported by generating stations; NTPC, DPL and TVNL stations in particular were reporting very low coal-stock positions where stock levels were flagged as depleted.

He informed that it has already been communicated to Member (Thermal), CEA, requesting that the generating companies may be directed to ensure coal availability, and that a communication has been forwarded for allocation of additional power for West Bengal.

All generating utilities were advised to keep thermal generating units at technical minimum during solar hours and be available for despatch during non-solar peak hours. Beneficiaries were asked to reduce market dependence and they should pursue firm medium or long-term power-purchase arrangements in place of ad-hoc short-term or RTM procurement, especially ahead of high-demand festival periods.

MS, ERPC also stressed the need to strengthen inter-State/inter-regional transmission capability (ATC/TTC) so that States have adequate ability to draw power when required, and underlined that resource adequacy planning must factor in nuclear, thermal, hydro and battery/pumped-storage options rather than depending solely on the power market.

ED, ERLDC touched upon the following key facets:

- Sustained overdrawl by West Bengal and Bihar between 5th and 15th September 2026. Detailed presentation enclosed at **Annex A**.
- On 15.09.2026, between 17:30 hrs and 19:15 hrs, when the grid frequency was below 49.5 Hz, it was observed that, despite several messages issued by the ERLDC Control Room, certain ER constituents continued to overdraw from the grid, with the maximum overdrawal reaching 1251 MW on certain instances. Such overdrawal, particularly when the grid frequency was already close to or below 49.4 Hz, is extremely unhealthy for grid security and forced ERLDC to resort to the extreme measure of physical regulation by opening ISTS-connected tie lines with West Bengal as the last resort to safeguard grid security, after Alert, Emergency & Extreme Emergency messages had failed to secure compliance.
West Bengal was issued 17 messages on 9th September (maximum overdrawal 1,251 MW) and 10 messages on 14th September (maximum overdrawal about 1,600 MW); Bihar was issued 5 messages on 12th September (maximum overdrawal about 594 MW) and 7 messages on 14th September (maximum overdrawal about 756 MW).
- He emphasised that each State must ensure proper portfolio planning, timely procurement of power and maintenance of adequate operating reserves to effectively manage unforeseen contingencies, ensure grid security, and maintain grid discipline in accordance with the provisions of the IEGC. It was reiterated that constituents must schedule and draw strictly within entitlement, failing which the grid would be exposed to unacceptable risk of UFR operation and cascading tripping.

In response, **WBSEDCL** explained that the overdrawal was driven by a combination of rising demand and shortfall in market-purchased power (RTM/DAM clearance was reported to be negligible — about 0.01% — due to extremely high exchange prices of around Rs 35/unit against the market cap of Rs 20/unit), compounded by internal generation constraints. It was submitted that the State had already cut about 250–300 MW of load and initiated tie-ups (including with NTPC's gas-based capacity) from the previous day to improve compliance, and apologised for the recent incident.

West Bengal SLDC further flagged that approximately 1,440 MW of installed capacity within the State was under forced/planned outage (units at Bandel, Bandel-2, Sagardighi-2, IPCHL, KTPP-3, KTPP-4 and DPL-7), several of which had exceeded their scheduled shutdown/time-overrun period; it was suggested that a standardised, region-wide norm for permissible unit-shutdown duration be evolved, since this internal generation shortfall was contributing materially to the overdrawal.

CESC (West Bengal) informed that it had also resorted to manual load-shedding of about 250 MW during evening peak hours on the previous day, in addition to automatic operation of ADMS/UFLS stage-1 (about 92 MW), due to non-availability of power in the RTM, it was also requested that resource adequacy be treated as a regional or national issue rather being attributed solely to the distribution licensee.

OCC advised all state utilities not to overdraw from the grid and to adhere to grid discipline and that any shortfall must be met through short term resource adequacy measures such as bilateral agreements and utilising own resources while minimising outages. Further, all states were urged to plan long term resource adequacy and optimal balancing of demand portfolio to avert recurrence of persistent overdrawl from grid.

*List of participants attached at **Annex-B**.*

Member Secretary, ERPC requested S.E (Operation) to take up the agenda for discussion.

1. PART-A: CONFIRMATION OF MINUTES

1.1. Confirmation of Minutes of 242nd OCC Meeting held physically at ERPC Secretariat on 20th August 2026

The Minutes of 242nd Operation Coordination Sub-Committee meeting held on 20.08.2026 was circulated vide letter dated 28.08.2026.

Deliberations in the meeting

- In the MOM of 242nd OCC meeting held on 20.08.2026, certain portions of **Item No: B.2.4** were requested to modify from WBSETCL as detailed below:

“Powergrid stated that diversion of the spare ICT will require approval from the Corporate HQ as well as highlighting availability of only one spare ICT (315 MVA) in ER-II at present,i.e at Durgapur(PG).This ICT, though old (1991), has been refurbished with new bushings and sound healthiness is assessed. Another spare 315 MVA ICT is available at Jamshedpur(PG) posing constraints in inter-state transportation.”

by

“Powergrid stated that diversion of the spare ICT will require approval from the Corporate HQ. One spare ICT (315 MVA) in ER-II is available at present at Durgapur(PG).”

- Also, in **Item No: B.2.4** : The planned overhauling of **NTPC Kahalgaon Unit-6** is approved from **25.09.2026 to 28.10.2026 (35 days)**

Forum agreed with the modifications and confirmed the Minutes of 242nd OCC with above mentioned modifications.

2. PART-B: ITEMS FOR DISCUSSION

2.1 Update on follow up agenda: ERPC

a) Intrastate Transmission Network Assessment & Mitigation-Odisha

Reference:

- ☐ Following the near-miss event in Odisha on 12.08.2025, the matter has been under continuous review since the 231st OCC meeting. OCC had advised OPTCL and SLDC Odisha to implement a UVLS scheme for safeguarding the capital city and nearby areas from cascading failures. Subsequently, 300 MW load was identified for UVLS implementation before Summer-2026 as deliberated in the 55th TCC meeting.
- ☐ Implementation of the Under Voltage Load Shedding (UVLS) scheme in the Odisha system has been under review since the 231st, 232nd, 233rd, and 234th OCC Meetings held on 22.09.2025, 24.10.2025, 22.11.2025, and 23.12.2025 respectively.

- The matter was also discussed in the recently concluded 55th TCC/ERPC meeting held on 16.12.2025 and 17.12.2025 at Kalimpong, West Bengal. As per deliberation in 55th TCC Meeting, **300MW load** has been identified and it will be operationalized before **Summer '26**.

The continued delay in implementation is posing increasing risks not only to the Odisha system but also to the Eastern Region as a whole during the forthcoming Summer-2026 period.

- During a review meeting held on 30.04.2026, OPTCL and SLDC Odisha informed that the quotation from the existing ADMS vendor had been received and was under examination. Further, 31 feeders of TPCODL and 23 feeders of TPNODL have been identified under the scheme. The target date for completion was indicated as June-2026.

As per 56th ERPC meeting:

Odisha officials were not present in the preceding (ERPC) discussion.

ERLDC highlighted the urgency of early completion of this scheme for voltage stability of Bhubaneswar region.

56th ERPC Decision:

ERPC forum advised OPTCL to implement the UVLS scheme by June-2026 without any further delay. Detailed work plan for reconductoring of intrastate transmission line shall be shared with ERPC & ERLDC within two weeks.

Deliberations in the meeting

OPTCL informed:

- ✓ *ADMS software logic development and testing is nearly complete, testing at ADMS server in SLDC is planned by the current week.*
- ✓ *Balance work will be completed within the current month with testing.*

*Details of feeders integrated under UVLS enclosed at **Annex B.2.1.(a)**.*

OCC Decision

- *OPTCL was advised to complete UVLS implementation by 10th October 2026. Weekly progress reports to be submitted to ERPC/ERLDC.*

b) Urgent Review of Phase I Compliance for CEA Flexible Operation Regulations, 2023

- CEA has issued a gazette notification dated January 30, 2023, regarding flexible operation of coal-fired generating units.
- As per CEA gazette notification extraordinary, part III, section 4, no. 61 (CG-DL-E-31012023-243299), the coal-based power generating units shall have flexible operation capability with minimum power level of 55%. This capability includes a ramp rate of 2% between 55%-70% and a ramp rate of 3 above 70%. This capability was mandated within one year of the notification, i.e., by Jan 2024. Further, the regulation mandates that generating units not capable of achieving a minimum power level of 40% shall achieve the same as per the CEA phasing plan.
- It may be noted that CEA's flexible operation regulations were notified after successful pilot test/study conducted across the country in association with international partners and BHEL.

- ❑ In this regard, it is pertinent to mention that 91 Units of total installed Capacity 51,080 MW in aggregate of various thermal power plants have been notified under Phase I (July 2024 – June 2026) for operation at 40% MTL (Minimum Technical Load). These units are required to carry out the necessary retrofitting/modifications as recommended by the respective OEMs so as to be fully prepared for sustained operation at 40% MTL by June 2026, as mandated under the provisions of the aforesaid Regulations.
- ❑ It may also be noted that successful and sustained operation at 40% MTL with Indian coal has been demonstrated by other generating utilities (Under Pilot Phase) such as West Bengal Power Development Corporation Limited (WBPDC) at Sagardighi Unit-8 and Damodar Valley Corporation (DVC) at Mejia Unit-8, following suitable retrofits as advised by the OEMs.
- ❑ Further, in order to compensate the losses on account of flexible operation, CERC has already incorporated most of the recommendations of CEA's compensation methodology such as for additional Capex, oil consumption, additional auxiliary power consumption, and heat rate degradation.
- ❑ Therefore, all generating utilities are requested to complete the retrofit, control system tuning, trial runs etc. of all units under Phase I by June 2026 in consultation with the OEM positively.
- ❑ It is also requested to furnish the progress and updates (as per attached format) of First Phase units by the end of November 2025 and thereafter every month.

As per 56th TCC meeting

DVC informed that 40% MTL can be achieved only with higher grade of coal. As coal is arranged from various sources having different grades, the sustained operation of boilers at 40% MTL with different grades of coal has not yet been demonstrated.

DVC representative further highlighted that many of the state generators has not yet implemented 55% technical minimum norm.

56th TCC Decision:

TCC advised DVC & JSWEUL to send their inputs & difficulties faced by them in achieving 40% MTL on sustained basis to ERPC.

As per 56th ERPC meeting

- ✓ MS, ERPC stated that considering the projected increase in penetration of RE power (rooftop solar, Solar parks, wind power), there is a need of operating all thermal generators at their technical minimum (including intra-state TPPs).
- ✓ Representatives of Thermal generators (identified under Phase I) expressed the technical constraints due to non-availability of quality coal for operating at 40% technical minimum.
- ✓ Member (GO&D), CEA inquired about whether there is any compensation mechanism at state level for operation of intra-state thermal generators at technical minimum in ER.
- ✓ WB informed that they have prepared a draft regulation regarding compensation for intra-state TPPs for operating at technical minimum which is yet to be approved by WBERC.

56th ERPC Decision:

- ✓ ERPC advised all thermal generating stations to intimate their preparedness as well as technical difficulties, if any, in achieving 40% MTL to ERPC Secretariat. ERPC Secretariat would subsequently forward the issues to CEA.

- ✓ The forum also advised to ER states to operate intra-state TPPs at MTL (55%) to assist in grid stability in view of increasing RE penetration and to introduce compensation mechanism for operation of intra-state thermal generators at technical minimum through respective SERCs.

Deliberations in the meeting

DVC and JIPL shared the operational constraints for generating upto Tehnical minimum including coal quality, boiler flame stability and others. (Annex B.2.1.(b))

OCC Decision

- *OCC forum was apprised that most inter-state generating stations are presently operating at around 55% technical minimum, and are now required to move towards 40% MTL for flexible operation. It is also advised to state generating stations to operate at 55% Tehnical minimum level adopting the best practices of inter-state generating stations.*
- *All thermal generators were advised to furnish specific operational difficulties, if any, in operating at 40% technical minimum to ERPC secretariat.*
- *OCC opined that the technical constraints for operating at technical minimum as received from concerned generators of ER may be forwarded to CEA.*

c) Restoration of ICTs at Koderma

The ICT#1 at Koderma (DVC) had been taken out of service since 10th Feb'26 due to a rising trend of acetylene (C₂H₂) concentration in the transformer oil. The ICT was proposed to be sent to the factory for necessary rectification. Meanwhile, one ICT from DSTPS was diverted and installed at Koderma. After commissioning, the diverted ICT was idle charged from the 400 kV side on 02.08.2026. Subsequently, Dissolved Gas Analysis (DGA) of the transformer oil sample indicated a rising trend of acetylene (C₂H₂) concentration. Accordingly, the ICT was taken under shutdown on 04.08.2026 for carrying out further investigation and necessary corrective action.

As per 242nd OCC meeting:

DVC submitted:

ICT 1 was taken under shutdown on 04.08.2026 and ICT 2 was taken under shutdown on 19.08.2026 due to DGA violation. Bushing problem is suspected in both the ICTs and order for detailed internal inspection is placed with M/S Hitachi.

242nd OCC Decision

- DVC was advised to expedite restoration of the both ICT#1 and ICT#2 at Koderma.
- OCC noted that shutdown of 220 kV Maithon(PG) bus will not be availed by Powergrid in September 2026.

Deliberations in the meeting

DVC submitted:

As per inspection carried out by M/S Hitachi, core earthing cable fault was detected and has been repaired. ICT#2 is still facing DGA violation when impressed with voltage. ICT#2 is expected to be restored by 25th September 2026 while ICT#1 can be tentatively restored by the next month.

OCC Decision

DVC was advised to strictly adhere to the submitted timeline for restoration of the both ICTs at Koderma.

d) Requisition for one no. 400/220 kV, 315 MVA Transformer from the Regional Spare Pool available at Durgapur 400 KV substation of PGCIL on loan basis for 400 kV Arambag (WB) Substation: WBSETCL

- ☐ 400 kV Sub Station at Arambag had 04 (four) Nos. 315 MVA, 400/220 kV Power Transformers (PTRs) with total installed capacity of 1260 MVA. The maximum peak demand recorded at Arambag 400 kV Sub-station reached around 800 MVA in June 2026 and further increase in load is anticipated.
- ☐ Due to sudden breakdown of one no. 400/220 KV, 315 MVA Power Transformers (Make: TELK | Sl. No.: 140164-2 | YOM: 2011) at Arambag 400 kV Sub Station on 01.05.2026, the existing functional capacity of the substation was reduced to 945 MVA (3 x 315 MVA) only.
- ☐ The loss of the faulted transformer has resulted in severe non-compliance with the standard N-1 Contingency Philosophy. Any further tripping or breakdown of an operational 315 MVA PTR may trigger cascaded system tripping, load shedding, or grid instability across the region.
- ☐ Though the procurement of 315 MVA, 400/220 KV Transformer is under process but it is apprehended that supply of above rated Transformer may take around 1.5 years to 02 years.
- ☐ Considering the situation, this agenda is placed for allotment of one no. 400/220 kV 315 MVA Transformer from the Regional Spare Pool available at Durgapur 400 KV substation of PGCIL on temporary basis for Arambag 400 kV Substation. The same would be returned after supply and commissioning of transformer which is presently under procurement.

242nd OCC Decision

- After detailed deliberation and to meet demand during upcoming Durga Festival, OCC forum granted in-principle consent to the diversion of a spare 400/220 kV transformer from Durgapur(PG).to Arambagh on loan basis and referred to TCC/ERPC for concurrence.
- WBSETCL was advised to expedite its ongoing procurement of the replacement transformer and to pursue repair of the faulty unit in parallel, so that the diverted spare can be returned at the earliest.
- **All ER states were also advised to maintain spare pool of 400/220 kV transformers to deal with intra-state network contingencies. They were advised to submit details of their in-service ICTs, spare ICTs and ICTs under procurement (along with tentative delivery schedule) at present in next OCC meeting.**

Deliberations in the meeting

OCC Decision

- West Bengal STU to provide an update on procurement of the replacement transformer and repair of the faulty Transformer unit in the next OCC meeting. The matter was referred to TCC/ERPC.
- All constituent utilities to furnish their operational and spare ICT status as per format (**Annex B.2.1.d**), and to initiate as well as expedite procurement wherever shortfalls exist, given the long lead time for supply.

e) HTLS upgradation of OPTCL lines

As per 242nd OCC:

OPTCL informed

- The root cause of recurring overloading/manual tripping on certain lines (e.g., in the Bolangir area) was attributed to loading imbalance pending completion of a parallel system-strengthening (S2S) line, expected to relieve the situation once commissioned.
- Proposal for an additional double-circuit line between Bolangir(PG) and Bolangir (OPTCL sub-station) is recently placed and is expected to be progressed soon.
- Along with 220 kV lines, reconductoring of 132 kV lines from Bargarh & Katapalli is also taken up.
- Price bids for reconductoring of the lines: Budhipadar-Lapanga and Lapanga-katapalli has been opened on 10th August 2026 and order placement is expected within next 30 days after bid evaluation. Reconductoring of 400 kV Meramandali-mendhasal line is also taken up in this project.
- HTLS reconductoring of all relevant lines is expected to be completed within next 10 months.

Detailed status of HTLS reconductoring enclosed at **Annex B.2.1.e**

242nd OCC Decision

OCC forum urged OPTCL to place orders for reconductoring works promptly on evaluation of price bids and to furnish periodic progress reports to ERPC. OPTCL has to ensure HTLS upgradation of all the associated transmission lines before the onset of next Summer. This is essential for both ISTS network and intra-state network of Odisha.

Deliberations in the meeting

OPTCL update was provided on multiple 400 kV lines identified for HTLS conductor up-gradation on account of high loading in the Odisha system as follows:

- ✓ *Orders have been placed for the Lapanga– Katapalli line (9th September; completion in about 10 months) and Lapanga– Budhipadar line (31st August; completion in about 6 months);*
- ✓ *Two further packages have been awarded to contractors, one line's award was reported as being with a vendor, and the tender for the 400 kV Mendhasal–Meramundali line was reported cancelled and had been re-floated.*
- ✓ *The 400 kV Bolangir line (Bolangir(PG) to Bolangir (OPTCL))reconductoring was reported as approved for tendering that shall commence shortly.*

*Detailed status of HTLS reconductoring as submitted by OPTCL is enclosed at **Annex B.2.1.e***

OCC Decision

- *OCC forum urged OPTCL to place orders for reconductoring works in the remaining lines, to expedite the execution process and to furnish periodic progress reports to ERPC*
- *OPTCL has to ensure HTLS upgradation of all the associated transmission lines before the onset of next Summer. This is essential for both ISTS network and intra-state network of Odisha.*

f) Update on islanding schemes in ER.

The list of existing Islanding schemes in ER is as under:

Eastern Region (ER)		
1	Kolkata (CESC) IS	City/Major Town/ Strategic Load

2	Howrah (Bandel) IS	City/Major Town/ Strategic Load
3	Bakreswar TPS IS	Industrial and Railway load
4	Haldia (Tata Power) IS	Industrial areas of Haldia and Port
5	Chandrapura (CTPS DVC) IS	Industrial areas

As per 238th OCC:

OCC suggested for formation of a sub group committee under chairmanship of S.E. (Operation), ERPC comprising members from ERPC, ERLDC, concern SLDC and Generating company for regular monitoring of islanding scheme formation and implementation in the ER States. **The committee shall coordinate with stakeholders and submit progress report in OCC.**

A special sub-group has been constituted for the identification and implementation of islanding schemes in the capital cities of ER states.

56th ERPC Decision:

The forum advised that the matter may be regularly followed up in OCC meetings.

1. Ranchi Islanding Scheme

- ☐ Nomination for ER sub-group of islanding scheme implementation was received from JUSNL.
- ☐ The kick-off meeting for the implementation of the Ranchi City Islanding Scheme was held on **23rd April 2026** under chairmanship of ERPC.
- ☐ To accurately define the electrical boundaries and load behaviour of the island, SLDC Jharkhand was requested to share:

- **Island Boundary & Feeder Logic:** Clearly define the islanded area and provide a comprehensive list of feeders that must be disconnected to ensure successful island formation.
- **Load Profiles:** Node-wise load data (Maximum, Minimum, and Average) for the identified area to ensure generation-load balancing.
- **Defense Mechanism Data:** Current node-wise loads of Jharkhand that are already covered under **AUFLS** (Automatic Under Frequency Load Shedding) and **ADMS** (Automatic Demand Management System).
- **Infrastructure Timeline:** Confirmation of the expected commissioning date for the **400kV Latehar New – Patratu New D/C** line, as this must be integrated into the islanding model.

As per 56th TCC meeting

JUSNL informed that they have already provided data regarding Ranchi islanding scheme.

As per 242nd OCC:

ERLDC submitted

- ✓ A detailed dynamic feasibility study has been completed jointly with the State Load Despatch Centre (SLDC), Jharkhand and the report has been shared with SLDC. Patratu generating station has been considered in the islanding scheme.
- ✓ A load-shedding/stabilization scheme was also proposed as part of the study to keep the island stable under contingency conditions

- ✓ The next step is preparation of the Detailed Project Report (DPR) by the state, followed by ERPC approval and PSDF Committee approval and, before implementation can proceed.
- ✓ The 400 kV Patratu-Latehar line was highlighted as critical to island stability, since the Ranchi island currently relies only on 220 kV lines, which get overloaded; the 400 kV line will relieve loading and improve voltage stability, and thus, needs to be commissioned before the islanding scheme itself. It was emphasized that commissioning of 400 kV Latehar–Patratu (New) D/C is a pre-requisite for implementation of the islanding scheme, considering its importance for voltage stability of the island. JUSNL informed that construction of the line has been awarded to PGCIL as a deposit work.

Powergrid ER-I updated that ownership of the line has been settled and completion of the 400 kV Patratu-Latehar line is expected within a year, tentatively by March 2027.

242nd OCC Decision

- SLDC Jharkhand was advised to finalize the DPR of Ranchi islanding scheme in consultation with ERLDC and place it for approval of ERPC so that sanction of funds from PSDF can be obtained at the earliest. Commissioning of 400 kV Latehar–Patratu (New) D/C shall be appropriately considered while finalizing the implementation sequence of the Ranchi Islanding Scheme.
- Powergrid ER-I was urged for expedited commissioning of the 400 kV Patratu-Latehar line, given its criticality for the Ranchi islanding scheme.

Deliberations in the meeting

ERLDC updated that in Online meeting held on 11th September with SLDC Jharkhand, the scheme details were deliberated along with discussion on DPR preparation.

OCC Decision

SLDC Jharkhand was advised to expedite preparation of DPR for Ranchi Islanding Scheme so that the same may get approved in the ERPC forum.

2.Patna Islanding Scheme under PSDF

- In 54th TCC meeting held on 23.06.2025, BSPTCL had proposed to implement Patna Islanding Scheme through Internal Resource Fund.
- However, a meeting was held on 24th June 2025 under the chairmanship of the Hon'ble Minister of Power and Housing & Urban Affairs, wherein the matter of Islanding Patna city was discussed. In the meeting, it was decided that the State of Bihar would submit a proposal for funding the Islanding scheme by the Ministry of Power).
- In compliance to minutes of the meeting held on dt. 24.06.2025, Board of Directors, BSPTCL has approved for implementation of Patna Islanding Scheme through PSDF in 131st BOD meeting held on dt. 17.07.2025 vide its resolution no. 131-06.
- In line with the above, a proposal has been submitted for Implementation of Patna Islanding Scheme under PSDF to NLDC vide this office letter no. 549 dt. 18.07.2025 along with all the required documents in compliance to minutes of meeting held on dt. 24.06.2025.
- Further, Chief Engineer (Generation), CEA has requested the recommendation of ERPC for implementation of Patna Islanding Scheme through PSDF.

As per 56th TCC meeting

SLDC Bihar informed that the PSDF Appraisal committee approved the PSDF grant proposal of Patna islanding scheme and the approval from the PSDF monitoring committee is awaited.

As per 242nd OCC:

SLDC Bihar informed:

- ✓ In-principle funding approval has been received from PSDF. Also, it has been clarified by NLDC on 28th July that the Letter of Award (LOA) can be issued without waiting for final PSDF sanction.
- ✓ Accordingly, internal approvals have been obtained and the LOA is to be placed by 25th August 2026.
- ✓ Implementation is estimated to take about **15 months** thereafter.

242nd OCC Decision

OCC noted the progress. Bihar was advised to adhere to the timeline of placing the LOA (by **25th August'26**) as well as ensure timely implementation of Patna Islanding Scheme.

Deliberations in the meeting

SLDC Bihar informed:

- ✓ *Final sanction of funds from PSDF is still awaited.*
- ✓ *Meanwhile, LOA for implementing Patna islanding has been issued on 21st August 2026 with tentative timeline of 15 months for completion.*

OCC Decision

SLDC Bihar was advised to ensure early implementation of Patna Islanding Scheme.

3.Bhubaneswar Islanding Scheme (Odisha)

As per 242nd OCC:

OPTCL updated:

- ✓ The earlier proposal to island using a small 65 MW generator was assessed as inadequate.
- ✓ A larger generating station in the vicinity— GMR Kamalanga (2×350 MW) was identified. The sole STU-connected unit of GMR KEL has been proposed as the generating station, with around 300 MW load of Bhubaneswar, Cuttack and Puri proposed for inclusion in the island.
- ✓ PRDC has been assigned to carry out the detailed studies (load flow, short-circuit, dynamic stability, frequency response) and prepare the DPR.
- ✓ Meeting with DISCOMs is under progress for identification of essential loads and associated schematic single-line diagrams (SLDs).
- ✓ Sambalpur islanding is also proposed (with 2×24 MW units of Chipilima + units of Burla, if available) hydro station as support.

ERLDC requested SLDC ODISHA to share the study results with ERPC & ERLDC considering GMR-STU unit of 350MW as the source supplying the island, for further validation.

242nd OCC Decision

OPTCL was advised to complete the technical studies (load flow, short-circuit, dynamic stability, frequency response) for the Bhubaneswar and Sambalpur schemes and share the study results with ERPC & ERLDC.

Deliberations in the meeting

OPTCL updated:

In respect of Bhubaneswar islanding scheme, network modelling for the identified generators and the suburban network has largely been completed, with a small portion of primary-substation modelling still in progress. Network modelling for Sambalpur islanding has also been completed.

A meeting with the GMR authorities is scheduled in third week of September'26 in presence of ERPC/ERLDC to finalise bus-segregation arrangements. The concerned generating station has agreed in principle to connect its bus for the scheme, with detailed continuity arrangements to be worked out.

OCC Decision

OCC advised OPTCL to proceed for DPR preparation of the proposed islanding schemes (Bhubaneswar and Sambalpur).

4.IB Valley TPS Islanding Scheme (Odisha)

IB valley TPS Islanding scheme has also been put on hold for long time. The status regarding the same has been sought on urgent basis by Ministry of Power (Govt of India).

As per 56th TCC meeting

OPGC informed that those necessary lines have been identified for Ib valley islanding scheme but base data is required from SLDC Odisha for further action.

As per 242nd OCC:

It was apprised that OPGC will take up this islanding proposal for study and implementation, the same is not under priority now.

Deliberations in the meeting

OCC Decision

OCC opined that the IB Valley TPS Islanding Scheme shall be temporarily put on hold and may be pursued when OPGC is prepared for its implementation.

5. Farakka islanding scheme

This is presently not in service due to long outage of 220 kV Farakka-Lalmatia line.

Deliberation:

JUSNL updated that the bay upgradation work at Farakka end will be completed in 3 months.

OCC Decision

- *Implementation of Farakka islanding scheme shall be taken up after restoration of 220KV FSTPP LALMATIA Line.*
- *JUSNL was advised to expedite bay upgradation at Farakka end in coordination with NTPC. The upgradation should comprise all necessary aspects including CT/PT, isolators and breakers.*

- ♦ Based on the recommendation and decisions in 14th NPC meeting held on 05.02.24, 214th OCC meeting and special meeting on 10.07.2024, a load relief quantum of 6916 MW was finalized for Eastern Region. UFR Feeders real time monitoring has been discussed in NPC as well as various fora of ERPC.
- ♦ Further, with new IEGC 2023 the same has been mandated as quoted below: IEGC 2023, Clause 13.d: "SLDC shall ensure that telemetered data of feeders (MW power flow in real time and circuit breaker status) on which UFR and df/dt relays are installed is available at its control centre. SLDC shall monitor the combined load in MW of these feeders at all times.
- ♦ SLDC shall share the above data with the respective RLDC in real time and submit a monthly exception report to the respective RPC. RLDC shall inform SLDCs as well as the concerned RPC on a quarterly basis, durations during the quarter when the combined load in MW of these feeders was below the level considered while designing the UFR scheme by the RPC. SLDC shall take corrective measures within a reasonable period and inform the respective RLDC and RPC, failing which suitable action may be initiated by the respective RPC."

As per 56th TCC meeting

Both Bihar & Jharkhand updated that they will Complete AUFLS implementation as well as SCADA integration by end of June 2026.

56th TCC Decision:

TCC urged early completion of AUFLS implementation as well as SCADA integration.

56th ERPC Decision:

ERPC advised concerned ER states for early completion of AUFLS as well as SCADA integration.

Update:

The load relief quantum to be implemented at each stage of AUFLS for FY 2026-27 is computed by NPC based on the regional peak demand met in FY 2025-26.

Stage-wise Load relief= Stage-wise relief (%)*RPRegion*AP/RP

AP: All India Peak Demand Met in MW

RP: Regional Peak Demand Met

As per this methodology, total load relief quantum for ER comes out as 7195 MW against 6916 MW in preceding year.

This 7195 MW of load relief has to be distributed among all ER states as per methodology to be finalized in OCC forum.

As per 242nd OCC meeting:

- ✓ SLDC Bihar apprised that additional load quantum is communicated to DISCOMs but receipt of feeder list is awaited. Once feeder list is received, revised load relief quantum will be implemented within 1 week.
- ✓ SLDC Jharkhand intimated around 1 month time for completion.
- ✓ DVC and Odisha informed that the implemented load relief quantum exceeds the requirement in almost all stages.

- ✓ Citing an approximate 3.6% load-growth, WB SLDC informed implemented quantum is already more than the requirement.

242nd OCC Decision

- ✓ All SLDCs were advised to ensure implementation of adequate stage-wise load relief quantum as detailed below by 10th September 2026. Entire number of feeders should also be integrated in SCADA within the stipulated timeline.

Latest status as follows:

Control Area	Required Load Relief					Implemented Load Relief				
	Stage –I (49.4 Hz)	Stage –II (49.2 Hz)	Stage– III (49.0Hz)	Stage– IV (48.8Hz)	Total Relief by Control Area	Stage –I (49.4 Hz)	Stage –II (49.2 Hz)	Stage– III (49.0Hz)	Stage– IV (48.8Hz)	Total Relief by Control Area
	(MW)	(MW)	(MW)	(MW)		(MW)	(MW)	(MW)	(MW)	
BSEB	345	399	466	466	1676	316	373	409	424	1522
JSEB	103	130	151	151	535	90	103	157	129	479
DVC	159	208	243	243	853	171	214	203	239	827
Odisha	304	372	434	434	1544	374.5	377.5	370	452	1574
WB & CESC	523	613	715	715	2567	560	574	712	715	2561
Sikkim	5	5	5	5	20	0	0	0	0	0
TOTAL	1439	1727	2015	2015	7194	1508.5	1642.5	1848	1927	6963

Deliberations in the meeting

SLDC Bihar apprised that as per latest peak load data of the DISCOMs, load relief quantum across all four stages of AUFLS already exceeds required quantum as detailed below:

Stages	Proposed by NPC	Completed as per latest peak load of 33 kV feeders under AUFLS
Stage1	345	478.3
Stage2	399	615.12
Stage3	466	624.17
Stage4	466	613
Total	1676	2330.59

Jharkhand updated that 520 MW load relief already implemented, only two feeders under AUFLS remaining that shall be completed by end September'26.

OCC Decision

- OCC advised that entire number of AUFLS feeders should also be integrated in SCADA within the stipulated timeline to ensure visibility in control rooms of respective SLDCs.
- OCC also opined that feeders with ADMS and AUFLS should be properly segregated in order to avoid any possible overlap in load relief quantum.

2.2 Issues for follow-up: ERLDC

a) Replacement of CLR insulators of PMJTL lines

- Replacement of faulty Decan make CLR insulators in the 765 kV New Ranchi–Medinipur–New Jeerat corridor and associated 400 kV PMJTL lines has been under discussion in various OCC/TCC meetings owing to the strategic importance of these transmission corridors for reliable power supply to Kolkata and adjoining areas of South Bengal.
- In 239th OCC, POWERGRID informed that around 5,000 faulty Decan make CLR insulators in the 400 kV system have been replaced, significantly reducing trippings compared to the previous year. However, procurement of replacement insulators for the identified 765 kV corridors has been delayed, with completion targeted by October 2026. OCC directed POWERGRID to expedite replacement of defective insulators, undertake comprehensive condition assessment of vulnerable locations, improve shutdown planning through consolidated weekly outages, and minimize emergency shutdowns, particularly during the summer.
- In 240th OCC, POWERGRID informed that approximately 28,000 insulators (400 & 765 kV combined) are planned for replacement. Total 10273 Nos (400KV) and 17785 Nos (765KV) CLR insulators are under procurement. As of 30th June 2026, 700 (at 400 kV level) and 850 (at 765 kV level) insulators have been supplied at site and progressive supply will continue. Replacement work will be prioritized on critical lines (e.g. 765 kV D/C Ranchi- Medinipur) and shall be carried out progressively, aiming to complete both supply and replacement by October- November 2026.
- In 241st OCC, Powergrid updated the detailed Plan as well as status for replacement of defective CLR insulator in PMJTL elements. As on 08th Jul'26, 2680 nos. of 400kV insulators and 1295 nos. of 765kV insulators were replaced as reported by POWERGRID. The Insulator replacements in 400kV and 765kV were scheduled to be completed by Oct'26 and Dec'26 as per tentative timelines submitted by POWERGRID.
- In 242nd OCC, POWERGRID intimated that 6900 nos. 400kV Insulators and 7520 nos. 765kV insulators have been supplied. POWERGRID also shared that 2900 nos. of 400kV insulators and 4152 nos. 765kV insulators have been replaced as on 19th Aug'26 with replacement completion targeted by Dec'26.

Deliberations in the meeting

Powergrid updated that out of 28000 insulators being planned, 10000 insulators have already been replaced cumulatively. Heavy rain and inundation have hindered the progress in work. Replacement on 400kV New Jeerat-Subhasgram line is planned in the next week with consent from WB SLDC.

*Detailed plan for replacement of insulators attached at **Annex B.2.2.a***

OCC Decision

Powergrid shall continue replacement of the defective insulators on priority as per submitted plan cum schedule and furnish weekly progress/status updates to ERPC/ ERLDC.

b) Shifting of 400kV Barh-Motihari D/C to pile foundation

- Outage of the 400 kV Barh–Motihari D/C transmission line was sought by POWERGRID vide email dtd. 11th Jul'26 in view of the precarious condition of Tower Location No. 27, situated on the bank of the Ganga River, necessitating urgent destringing and dismantling of the affected tower. An online meeting was convened on 14th Jul'26 to deliberate the shutdown requirement where POWERGRID requested shutdown of the line for destringing and dismantling of the affected tower and proposed restoration of the line by 20th August 2026. Thereafter, based on site visit report of the committee comprising of POWERGRID, BSPTCL and NTPC Barh, outage of the line was allowed from 21st Jul'26 to 20th Aug'26. POWERGRID was also requested to submit weekly progress reports to ERPC and ERLDC for effective monitoring.

- ❑ Subsequently, POWERGRID updated that the restoration of the line is delayed and expected to be revived by 10th Sep'26 during the online coordination meeting held on 11th Aug'26 for facilitating outage of 400kV KHSTPP-Banka D/C.

As per 242nd OCC meeting:

Powergrid ER-I presented the details of pile foundation works started on bank of Ganga river (from 12.08.26) for restoration of the 400kV Barh-Motihari D/C line.

- ✓ Continuing river erosion and associated site risks were also highlighted.
- ✓ The earlier completion target could not be achieved due to water-logged site and overflowing river conditions after heavy rainfall.
- ✓ At present, owing to unfavorable conditions on the river bank, work is stalled temporarily.

242nd OCC Decision

- Powergrid was advised for adhering to the timeline (by 10.09.2026) for restoration of 400kV Barh-Motihari D/C line.
- Once the barge arrives at the site, Powergrid was advised to intimate to ERPC/ERLDC on the commencement of tower erection works.
- Powergrid shall share progress photographs, detailed activity schedule and regular progress updates with ERPC/ERLDC.

Deliberations in the meeting

PGCIL informed:

- ✓ *The area near Motihari has remained flooded since around 20th August 2026, and that the Ganga river has crossed its maximum flood level on 7th September 2026.*
- ✓ *Tower-erection activity at the affected locations has been suspended as the site is unsafe amidst high river current; the affected tower location is reported to be within about 150 metres of the river, with a risk of cascading impact on an adjacent tower as well, necessitating a proposed extension in outage/shutdown.*
- ✓ *Based on last year's pattern, full flood recession and resumption of full-scale erection/stringing activity is expected around 15th October 2026; assuming works commence by that date, completion of the balance activity (erection and stringing) is targeted by around 10th November 2026, i.e. about one month from resumption.*
- ✓ *MS, ERPC informed that he will assess the severity of the situation after site visit.*

OCC Decision

- *Powergrid to continue monitoring the flood/water-level situation and resume erection/stringing activity as soon as it is safe to do so, targeting completion of the balance work at the earliest. Weekly progress reports to be shared with NTPC and ERPC/ERLDC.*

c) Reconductoring of 400kV TSTPP-Meramundali D/C lines

- ❑ Reconductoring works of 400kV TSTPP-Meramundali D/c lines were approved under ERES-43 with completion schedule of 02.03.2026. The reconductoring works were started from 20.11.25 in the Ckt#2 LILO part. Owing to the very slow progress, reconductoring in LILO part was paused and reconductoring in Ckt#1 was started from 06.01.2026. Subsequently, the progress of the work and network scenarios were reviewed in a special meeting held on 06.03.2026 and reconductoring works were discontinued in view of prevailing network conditions. It was also decided that reconductoring work will be continued after reduction of peak Demand period of Bhubaneswar i.e. after July 2026.

- ❑ Post summer, online meetings were held on dtd. 06.07.2026 and 13.07.2026 and it was decided to resume the reconductoring work in the LILO portion of Ckt#2 by 3rd / 4th week of July 2026 depending on manpower mobilization.
- ❑ In the 241st OCC meeting held on 17.07.26, POWERGRID informed that deployment of agency for the reconductoring/ bypassing work has been delayed and is expected by end of July'26. It was decided to isolate the LILO portion and start reconductoring work by end of Jul'26 without any further delay. Subsequently, the LILO part of 400kV TSTPP-Meramundali #2 was made available for reconductoring on 07.08.2026 after isolating the LILO part.
- ❑ In the 242nd OCC meeting held on 20.08.26, POWERGRID informed that only about 1.2 ckm of reconductoring could be completed in LILO part due to repeated rainfall. POWERGRID agreed to avail shutdown of 400 kV Talcher–Meramundali Ckt-1 from 01.09.2026 for carrying out the remaining 9 ckm. reconductoring work by Oct'26 end to allow HVDC Talcher-Kolar line diversion work in Nov'26 for 15 days. After restoration of HVDC Talcher-Kolar line, reconductoring in Ckt#2 will be started.

Deliberations in the meeting

Powergrid Odisha informed:

- ✓ *A total reconductoring of about 22.3 km of the LILO portion and about 42.2 km of Circuit-1 (out of 51.6 km) has been completed.*
- ✓ *Balance works are held up on account of rain and other site hindrances.*
- ✓ *Three gangs have been deployed to expedite progress of work.*
- ✓ *Shutdown of Circuit-1 is expected to be availed within about a week.*
- ✓ *Jack-bus reconductoring works at the Meramundali switchyard requires a double-bus shutdown, which SLDC Odisha has not agreed to on account of system-security concerns. It was informed that bay upgradation requires at least 60 days. In this regard, proposed hot line method is under assessment at Meramundali end while it is not feasible at NTPC Talcher end.*
- ✓ *Support structure for bay upgradation works has not reached site yet while other materials (except CTs required for the bay upgradation have been received at site. Supply of CTs is expected to be completed by the end of September 2026; however, there has been considerable delay in supply of the support structures. Bay upgradation work can be commenced only after receipt of the support structures.*

ERLDC intimated gist of online meeting held on 08.09.2026 to review the progress of reconductoring works.

- ✓ *Reconductoring of 5.6Ckm had been completed as on 08.09.2026 in LILO portion since availing shutdown on 07.08.2026. POWERGRID informed that it plans to complete the reconductoring work in the LILO portion by the second week of October 2026.*
- ✓ *It was agreed that the reconductoring work in Ckt-I would commence by 20.09.2026 in parallel with the LILO portion so that the works are completed before HVDC Talcher-Kolar line diversion work scheduled from 01.11.26.*
- ✓ *It was agreed that the bay upgradation associated with 400 kV TSTPP–Meramundali Ckt-I at Meramundali end would be taken up at a later stage, as the work requires approximately 60 days of outage, which is longer than the time required for completing the balance 9 Ckm of reconductoring.*

ERLDC further updated that reconductoring of jack bus at TSTPP and Meramundali are important even for utilizing existing bay equipment capacity of 2000A. The quantum of generation backdown from TSTPP will be higher in case reconductoring of jack buses at both TSTPP and Meramundali are not completed before the HVDC Talcher-Kolar line diversion works.

OPTCL informed that shutdown of both 400 kV buses at Meramundali S/s for three days for carrying out jack-bus reconductoring work cannot be allowed and that the work needs to be carried out through hotline method.

TSTPP proposed outage of Unit#1 (500 MW) for three days during the planned overhauling period of Unit#2 (500 MW) for carrying out the jack-bus reconductoring work.

OCC Decision

- OCC opined that while Unit-2 of NTPC Talcher remains under a pre-planned 45-day outage, Unit-1 could be taken out for an additional 3 days to facilitate the Jack-bus reconductoring within that window, since giving simultaneous outage of two units at a later date would be far more difficult to accommodate.
- Powergrid Odisha was advised to complete the balance reconductoring by 31st October 2026 so as to facilitate the planned HVDC Talcher-Kolar Bipole shutdown scheduled from 1st November 2026.
- OCC emphasised the significance of this transmission corridor for both the Eastern and Southern regions, thus must be completed within the committed timeline.
- Considering significant time of 60 days in bay upgradation works i.r.o each circuit, OCC opined that bay upgradation at both ends may be taken up in the lean season of next year.

d) Higher loading in 400/132 kV 200MVA ICTs at NTPC Kahalgaon

- ❑ Higher loading of 400/132kV ICTs at KHSTPP were flagged by NTPC post shutdown of 400kV KHSTPP-Banka D/C. As the 132kV buses downstream of ICT#1,2 (2x200MVA) (Stage-I) and ICT#3,4 (2x200MVA) (Stage-II) are not coupled, there is uneven loading of the ICTs of stage-I and stage-II. While ICT#1&2 remain loaded up to 100MW each, loading in ICT#3&4 remain below 50MW combinedly. Besides, 132kV KHSTPP-Sabour line has been upgraded to HTLS and charged on 08-Aug-2026. However, O/C protection settings i.r.o. 132kV KHSTPP-Sabour(BH) line are kept at 550A (~125MW) at KHSTPP end to limit loading of the 400/132kV ICT#1,2, whereas the line can operate at 900A (~205MW) post reconductoring. For enhanced utilization of the 400/132kV ICTs, NTPC was requested to explore feasibility of coupling 132kV buses.
- ❑ In 242nd OCC meeting NTPC submitted that the two 132 kV systems (old bay associated with ICT-1 &2 and new bay associated with ICT-3 &4) are physically separated by approximately 1 km; a scheme for inter-connection using the existing 132 kV cable/feeder was discussed, including provision to keep the link normally open and close it only as a fault-restoration or backup arrangement, subject to cable rating and protection coordination. NTPC was advised to explore possibility of the replacement of old inter-connecting 132 kV cable and accordingly intimate ERPC/ERLDC at the earliest.

Deliberations in the meeting

NTPC updated:

Old and new 132 kV systems are at different locations. Thus, shifting of feeders ,envisaged for dead bus charging, from old to new location or vice versa is not feasible. Also, no synchronising scheme between 132 kV systems had been considered since the time of commissioning.

OCC Decision

NTPC to pursue the alternate ICT arrangement and also evaluate replacement of the ageing 132 kV interconnecting cable at Kahalgaon TPS. A site visit to be undertaken by ERPC/ERLDC for proper assessment of the situation.

e) Monthly Reporting of Commissioned/De-commissioned Generation Capacity in State Control Area

- ☐ The matter regarding establishment of a structured and uniform mechanism for collection of information on generation capacity commissioned/de-commissioned in the State control areas was deliberated in the 242nd OCC meeting. Accordingly, ERLDC mailed Google Sheet to all ER SLDCs for furnishing the requisite details of FTC, COD and de-commissioning of generation/transmission capacity, as applicable.
- ☐ As of date, the requisite information has been furnished by WB, Sikkim, Odisha and Bihar SLDCs. The remaining SLDCs are requested to furnish the required information at the earliest.
- ☐ It is proposed that the above reporting mechanism may be continued on a monthly basis, with the data pertaining to the previous month being furnished by the 7th day of the succeeding month. In case no FTC/COD has taken place during the relevant month, the same may also be indicated in the Google Sheet for record purposes.

Deliberations in the meeting

OCC Decision

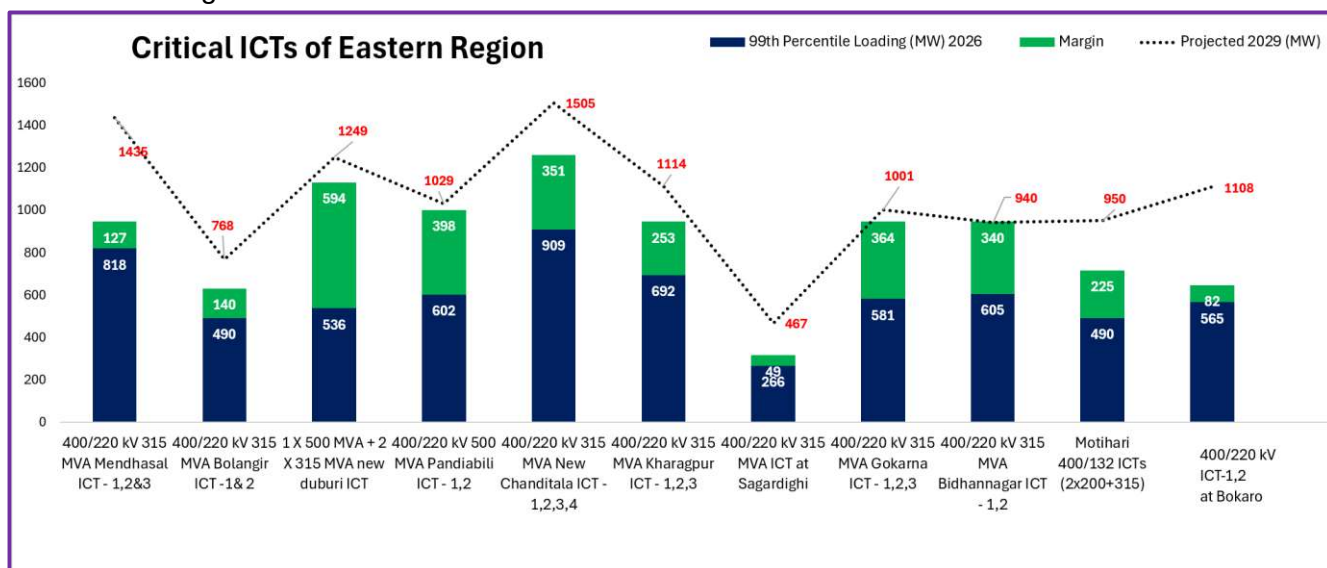
All SLDCs were advised to update the shared Google Sheet with commissioning/decommissioning (FTC/COD) details by the 7th of every month for the preceding month, including nil-reports where applicable.

2.3 Augmentation of Transformation Capacity at Critically Loaded Substations Feeding Major Urban & Industrial Clusters: ERLDC

- ☐ Demand in the Eastern Region has grown at a CAGR of around 8% during the last five years, broadly in line with the growth in All-India Maximum Demand. In the Eastern Region, the increase in demand has been particularly significant in major urban and industrial clusters, including Bhubaneswar, Kolkata, Western Odisha, and Northern and Southern Bihar. Consequently, ICT loading at several substations feeding these load centres has increased significantly.
- ☐ A study has been carried out covering all 400/220 kV ISTS substations in the Eastern Region, including POWERGRID ER-I, ER-II, POWERGRID Odisha Project, etc., as well as 400/220 kV substations under State jurisdiction feeding important urban centres. The study analysed the historical growth in ICT loading and projected the loading up to 2029 based on the prevailing growth trend. It has been observed that several substations are already operating at critical loading levels and considering the prevailing growth, the projected loading at some substations are likely to exceed the installed ICT capacity by 2029 unless adequate augmentation is undertaken.
- ☐ Based on the above study, a reconciliation has been carried out for the transformation capacity of the Eastern Region, considering the load growth and probable future loading of the identified ICTs

vis-à-vis the planning/procurement actions taken so far by the Region and the States, as per the available information, along with the regional spare ICTs available in the ISTS pool.

A) ICT Loading Pattern Analysis: Based on the maximum loading of ICTs during the last three years, the available transformation margin under the present condition vis-à-vis the projected loading in 2029 has been assessed. For the identified critical substations, the same growth rate has been considered for projection, keeping in view that no new substation are expected to come up in the vicinity during the timeframe of 2028–29. The assessment is depicted in the following chart.



- The study indicates that a few ICTs at substations under POWERGRID Odisha Project, the States of Odisha and West Bengal, and DVC have some margin at present; however, the available capacity is expected to be exceeded during 2028–29 considering the same growth rate. The summary of such ICTs is given below:

Sr. No.	Name of Substation	Capacity (MVA)	Qnty. (Nos) required	Ownership
1	Pandiabili	500	1	PG Odisha Project
2	Mendhasal	500	1	Odisha State
3	New Duburi	500	1	Odisha State
4	Bokaro	500	1	DVC
Sub Total		2000	4	
5	Bolangir(PG)	315	1	PG Odisha Project
6	Kharagpur	315	1	West Bengal
7	Bidhannagar	315	1	West Bengal
8	New Chanditala	315	1	West Bengal
9	Gokarna	315	1	West Bengal
10	Sagardighi	315	1	West Bengal
Sub Total		1890	6	

Table :1

Accordingly, the total requirement identified is 4 Nos. of 500 MVA and 6 Nos. of 315 MVA ICTs in the Eastern Region.

A) Transformer Augmentation plan/ Procurement Status

As for the information available from various meetings/discussions, some of the above requirements have already been taken up for augmentation. The details of the planned/ongoing works (WIP) are as follows:

Sr. No.	Name of Substation	Capacity (MVA)	Qnty. (Nos) required	Already planned/WIP	Balance ICT required to be planned	Ownership
1	Pandiabili	500	1	1		PG Odisha Project
2	Mendhasal	500	1	1		Odisha State
3	New Duburi	500	1	---	1	Odisha State
4	Bokaro	500	1	1		DVC
Sub Total			4	3	1	
5	Bolangir(PG)	315	1	---	1	PG Odisha Project
6	Kharagpur	315	1	1 (WIP)		West Bengal
7	Bidhannagar	315	1	1		West Bengal
8	New Chanditala	315	1	1 (WIP)		West Bengal
9	Gokarna	315	1	1		West Bengal
10	Sagardighi	315	1	--	1	West Bengal
Sub Total			6	4	2	

Table :2

From the above Tables 1 and 2, it is observed that out of the total identified requirement of 4 Nos. of 500 MVA and 6 Nos. of 315 MVA ICTs in the Eastern Region, 1 No. of 500 MVA and 2 Nos. of 315 MVA ICTs require immediate attention for planning/procurement.

C) Regional Pool of Spare for ICT in Eastern Region:

With reference to the 56th TCC Meeting held on 25th and 26th May at Gangtok and the subsequent discussion held in the 242nd OCC Meeting on 20.08.2026, the consolidated availability of spare transformers under the Regional Pool of the Eastern Region ISTS system is Two **(2)** only one spare of each 500 & 315 MVA is currently available in ER Regional Pool, compared to a population of 56 & 115 nos of Transformer of 500MVA and 315 MVA Capacity respectively in the Eastern Region.

Accelerated renewable energy integration, rural electrification and substation expansions have overwhelmed existing lead time for new ICTs which is around 30–36 months. Therefore, augmentation planning needs to be initiated well in advance to meet the growing demand and ensure reliability of the System.

Deliberations in the meeting

- ✓ ERLDC presented a comprehensive study on loading of some ICTs exceeding threshold limits in ER ISTS network as well as in intra-state network of various ER states. (Details at **Annex B.2.3**). Loading pattern of past three years as well as future load growth has been factored in. As per the study carried out, the number of ICTs in N-1 or N condition follows an increasing trend year-on-year basis.

- ✓ OPTCL updated that 500 MVA ICT at New Duburi has already reached site and to be installed shortly while ICT installation is under progress at Mendhasal.
- ✓ WBPDCCL updated that 315 MVA ICT at Sagardighi is expected to be commissioned by November 2026.
- ✓ WBSETCL apprised that orders have been placed for ICTs at Bidhannagar & Gokarna.
- ✓ DVC stated that 500 MVA ICT at Bokaro is under procurement.
- ✓ PG ER-I updated on the proposal of 500 MVA ICT at Maithon(PG).

Sr. No.	Name of Substation	Capacity (MVA)	Qnty. (Nos) required	Planned (as submitted in meeting)	Make	Target date	Balance ICT required to be planned	Ownership
1	Pandiabili	500	1	1				PG Odisha Project
2	Mendhasal	500	1	1				Odisha State
3	New Duburi	500	1	---			1	Odisha State
4	Bokaro	500	1	1				DVC
Sub Total			4	3			1	
5	Bolangir(PG)	315	1	---			1	PG Odisha Project
6	Kharagpur	315	1	1				West Bengal
7	Bidhannagar	315	1	--			1	West Bengal
8	New Chanditala	315	1	1				West Bengal
9	Gokarna	315	1	--			1	West Bengal
10	Sagardighi	315	1	2			1	West Bengal
Sub Total			6	3			3	

OCC Decision

- All SLDCs & STUs were requested to implement all planned ICTs as per the shared target date of commissioning along with augmentation of those S/S as soon as possible, so that it can be installed within 2029 and thereby the transformation adequacy of those S/S can be ensured.
- All States and Transmission licences are also advised to update their respective ICT augmentation plans vis-à-vis the current procurement status, as on date, to arrive at a consolidated assessment of the ICT requirement for the Eastern Region.

2.4 Performance of Automatic Demand Management Scheme (ADMS) –ER: ERLDC

- ERPC/ERLDC took one initiative to streamline the logic of ADMS across the constituent of ER and harness the maximum relief during the low frequency event. In this regard, a meeting was conducted on 07.07.2026 to implement a standardised ADMS logic (49.7 Hz for at least 3 minutes) for Eastern Region which has been implemented by all constituents of Eastern Region barring Odisha and Jharkhand. Further, healthiness of ADMS scheme was also stressed upon.
- In last few weeks, there were several instances low frequency events when ADMS criteria were satisfied for one or more constituents, however actual ADMS relief obtained was in very few of the instances and the quantum of ADMS relief was miniscule in comparison to total load under ADMS, suggesting non-healthiness of ADMS scheme. A summary of ADMS operation is attached as below (10.08.2026-06.09.2026):

State	Criteria	Events	Cumulative Duration (Min)	Min Freq. (Hz)	Quantum Installed	ADMS Operated (No. of Times/ MW)
Bihar	F < 49.7 Hz for >= 3 min	5	33	49.47	400 MW approx.	Nil
Jharkhand (Old logic)	F < 49.9 Hz for >= 3 min	120	1380	49.47	150 MW	Nil
DVC	F < 49.7 Hz for >= 3 min	4	24	49.47	280 MW	Nil
Odisha (Old logic)	F < 49.9 Hz for >= 3 min	40	268.00	49.47	400 MW	1 (Once) (119 MW)
West Bengal	F < 49.7 Hz for >= 3 min	4	20.00	49.47	225 MW	4 (Four times) (66,14, 7.5, 6 MW)
Sikkim	Not established	0	0.00	49.47	Not established	-

A sample report for one day (06.09.2026) is attached as **Annexure-B.2.4**

Jharkhand and Odisha are requested to update the status of new logic implementation.

All constituents are requested to clarify the reason of non-operation of ADMS in maximum instances and very low ADMS relief obtained when operated.

Deliberations in the meeting

ERLDC highlighted that despite SCADA command is being set, it is not reaching the end load point and consequently no load relief is obtained on several instances. This is attributed to deficiency in communication links, thus healthiness of communication system needs to be ensured for successful ADMS operation.

Odisha SLDC confirmed removal of the DISCOM-level blocking logic in ADMS.

OCC Decision

- A separate meeting to be convened, with communication and protection representatives of all SLDCs, to review ADMS non-operation cases station-wise and identify whether the root cause is related to relay-logic, SCADA, communication, or field-breaker. OCC referred the matter to the TeST sub-committee.
- All ER constituents were advised to remove any local blocking logic or admin restriction on ADMS operation within 15 days and confirm compliance to ERPC/ERLDC.

2.5 Shutdown of GIS Bays at POWERGRID's 220 kV Rangpo Substation for Teesta-VI HE Project: NHPC

- ❑ Construction of **02 Nos. 220 kV GIS Bays for Teesta-VI HE Project** at the 220 kV GIS Substation of POWERGRID at Rangpo has been completed. The bays are required to undergo **Extra High Voltage (EHV) testing** prior to their commissioning.
- ❑ For carrying out the EHV testing, shutdown of the concerned 220 kV GIS bays is required. Accordingly, shutdowns were planned/approved on earlier occasions for conducting the requisite testing.
- ❑ Despite obtaining approval for the shutdown, **three attempts have already been made** to conduct the EHV testing within the approved shutdown period. However, on all three occasions, the shutdown was cancelled by **SLDC, Sikkim at the eleventh hour**, citing system constraints, including **high tidal time and VIP movement**.
- ❑ As a result, the EHV testing could not be completed and the commissioning of the newly constructed 220 kV line bays is consequently getting delayed.
- ❑ It is pertinent to mention that the **EHV testing kit is a specialized equipment and is not readily available locally**. Its mobilization and demobilization involves considerable logistical planning, time and expenditure. Further, deployment of the testing team and associated equipment is required to be coordinated well in advance.
- ❑ Therefore, cancellation of the approved shutdown at the last moment results in substantial avoidable expenditure and logistical difficulties, besides adversely affecting the planned commissioning schedule of the Teesta-VI transmission system.
- ❑ In view of the above, it is proposed that following shutdown may kindly be **approved/confirmed well in advance** for conducting the EHV testing of the 02 Nos. 220 kV GIS line bays at POWERGRID's 220 kV Rangpo Substation.

SL. No.	Name of Element	From	To	Name of Work to be done	Remarks
		Date & Time	Date & Time		
01.	Shut down of 220 KV Bus -I & Bus-II at POWERGRID Rangpo	07.11.26 (09:00 Hrs)	11.11.26 (17:00 Hrs)	HV Test of 220 kV GIS bays for Teesta-VI Line	On Daily Basis

It is also requested that, once the shutdown is approved, **SLDC, Sikkim may kindly ensure implementation of the approved shutdown during the specified period**, barring any unforeseen emergency/system exigency, so that the EHV testing can be completed without further cancellation.

Deliberations in the meeting

- ✓ NHPC (Teesta-VI HEP) requested a shutdown of the relevant bay, submitting that the preferred window would be October–November on account of hydrological/water-level considerations for the run-of-the-river station, and that units run-of-the-river cannot readily be taken out of service outside this window.
- ✓ It was submitted that, based on prior experience, a total outage window of the order of 60–70 days may be required for reconductoring/bypass-related works at the Gangtok circuits (Circuit-1 and Circuit-2).
- ✓ Shutdown planning has been under discussion in previous OCC meetings as well without resolution due to absence of Sikkim.

Sikkim representative was absent in the meeting.

OCC Decision

OCC opined to convene a special meeting in this regard involving all stakeholders (Powergrid, Sikkim SLDC along with all hydro generating stations in Sikkim, ERPC, ERLDC).

2.6 Agenda from WBSEDCL

2.6.1 Accessibility of Generation Outage Information

Accurate and up-to-date information on national generation outages is of critical importance for assessing the demand-supply scenario and accordingly strategizing portfolio management, including procurement through the Collective and Term-Ahead Markets.

Until recently, Generation Outage Reports were publicly accessible through the websites of all RLDCs, from which the requisite data was being scrapped. However, NRLDC has recently introduced IP-whitelisting-based access to the Generation Outage Report, while access has been completely restricted by WRLDC and NERLDC. In contrast, the information continues to remain publicly accessible through SRLDC and ERLDC.

In view of the above, a **uniform policy across all RLDCs for sharing Generation Outage Information** is proposed, with at least every licensed DISCOM/ Stake holders being provided access to the Generation Outage Reports of the respective RLDCs.

Deliberations in the meeting

- ✓ WBSEDCL raised the issue of non-availability of real-time/day-ahead generation outage information, which is critical for DISCOMs to strategize their market bidding, since generation outages directly influence exchange price and volume.
- ✓ It was pointed out that such data, earlier available in the public domain through RLDC websites, is currently not accessible for the Eastern Region (ERLDC), whereas it remains accessible on most other RLDC websites; the Western Region (WRLDC) website was reported to be temporarily inaccessible on account of cyber-security related restrictions.
- ✓ NLDC's daily report publishes only the aggregate all-India capacity under outage, without plant-wise segregation, which limits its usefulness for market strategy.
- ✓ It was proposed that a single, dynamic, all-India outage-information portal (a National Real-Time Outage Programme) be developed and hosted at NLDC, to be raised at the forthcoming National Power Committee meeting.

ERLDC clarified that the earlier reporting software of NLDC has become outdated and could not be continued in its present form; migration to a new reporting platform is already under way, which will enable publication of more comprehensive outage information once operational.

ERLDC informed of development of the 'India Energy Stack', a Pan-India real-time data-sharing platform under Ministry of Power guidelines, is under way; once operational, it is expected to provide real-time visibility of outage-status changes to all eligible stakeholders. In the interim, constituents wishing to access the existing ERLDC outage report were advised to apply for IP whitelisting.

OCC Decision

- ERLDC to expedite migration to the new reporting software/platform to restore plant-wise outage-report accessibility for the Eastern Region, and to apply for restoration of public access once cyber-security clearance is obtained (in respect of WRLDC's portal, applicable at the all-India level).
- Interested constituents to apply to ERLDC for IP whitelisting to access the existing outage reports till development of the India Energy Stack platform.
- All SLDCs were also advised to update Generation Outage data on their respective websites for convenience of the beneficiaries.

2.6.2 Real-Time Pan-India Generation Outage Information

Although Generation Outage Information is available through platforms such as GRID-INDIA and NPP, the information is generally published only after the Day-Ahead Market hours and therefore has limited utility for real-time portfolio management. Further, real-time updation of Generation Outage Information is presently not being undertaken uniformly across RLDCs, with NRLDC being an exception where generation outage information is updated on a real-time basis.

Accordingly, a **uniform mechanism for dissemination of Pan-India Generation Outage Information on a real-time basis** is proposed to ensure timely and comprehensive visibility of the generation availability scenario.

Deliberations in the meeting

OCC Decision

- OCC suggested for development of a pan-India Generation outage portal with provision for updating the details on real time basis to facilitate DISCOMs in portfolio management.
- The matter was referred to TCC/ERPC forum for further deliberation.

2.6.3. Transparency in Ancillary Charges and Inclusion of SCUC Details in WBES

DISCOMs and SLDCs are required to bear DSM Charges, of which Ancillary Charges constitute a significant component. While the block-wise breakup of Ancillary Charges is published on the GRID-INDIA website, the underlying plant-wise derivation remains largely non-transparent.

Since DISCOMs are the actual payers of the Ancillary Charges, it is proposed that the **calculation methodology and plant-wise derivation of Ancillary Charges be made transparent and published at regular, time-bound intervals.**

Further, plant-wise breakup of Ancillary Charges is presently being updated in WBES on a real-time basis, except for AGC. However, **SCUC details are not presently included** in the relevant section. Since SCUC constitutes an important input in the determination of payable Ancillary Charges, it is

proposed that the **requisite SCUC details also be incorporated in the corresponding section of WBES.**

Deliberations in the meeting

WBSEDCL raised concerns that ancillary-service charges appear to be levied on a round-the-clock basis irrespective of frequency, and that the underlying rate/quantum computation (including distinction between open-cycle and closed-cycle gas pricing, wherever relevant) is not visible in the WBES/ancillary-services portal, resulting in a lack of transparency for the paying constituents. Thus, background calculation details were sought, including the basis on which particular generators/units are dispatched under the Ancillary Services Mechanism and the applicable price category.

It was clarified by ERLDC as:

- ✓ *This issue had been discussed in earlier ERPC forums (54th TCC/RPC Meeting), following which additional data had been made available to West Bengal through WBES, enabling the State to independently verify or calculate ancillary-service charges. Various data required for analysis and calculation of Ancillary Charges, including AS data, SCUC data, etc., are already available with SLDCs through user credential-based access.*
- ✓ *West Bengal is utilizing the available data for independent calculation of Ancillary Charges and the corresponding block-wise DSM Normal Rate. West Bengal had requested ERLDC to cross-check its calculation, as a mismatch was observed between the Ancillary Charges calculated by West Bengal and those published by NLDC. Upon cross-checking the calculations, it was observed that certain components, such as the incentive received by generating stations based on their performance under AGC, had not been considered in the calculation.*

OCC Decision

- *ERLDC was advised to continue providing West Bengal (and other requesting constituents) with the requisite block-wise computation basis for ancillary-services charges through the WBES portal or equivalent means, to enable independent verification.*
- *The matter was referred to Commercial sub-committee for further deliberation on the methodology for sharing of the requisite data for calculation of Ancillary Charges and the corresponding DSM Normal Rate.*

2.6.4. Prevention of Forced Backdown During Total Full Requisition Blocks

It has been observed that ISGS NTPC generating stations are selling power in the Real Time Market (RTM) during blocks wherein the beneficiary has “Total Full Requisition”. Consequently, unwanted backdown is being forcefully imposed on the beneficiary at WBES, even during blocks witnessing an acute power crisis in the All India Power Market.

In view of the above, it is requested that the matter be accorded the highest possible priority and necessary action be taken to ensure that such situations are strictly avoided in future.

Deliberations in the meeting

WBSEDCL raised concern and showcased instances where generating stations appear to have 'backed down' scheduled generation (of the order of 4–5 MW per instance in the cited examples) during the first ramping block despite full requisition having been placed by beneficiaries, with the corresponding capacity apparently sold in the real-time market (RTM) at high prices — effectively depriving beneficiaries of contracted capacity.

- ✓ ERLDC clarified the technical basis: while beneficiaries may vary their requisition from zero to full at any point without a ramp-rate check on the requisition itself, the schedule actually issued to a generator must be operationally achievable. Since it is not practically possible for a thermal unit (even ramping at about 1% per minute) to move from a low base to full output within the very first scheduling block, a ramp restriction of 50% is applied while converting the requisition (beneficiary entitlement) into an actual despatch schedule for the first ramping block — a principle already discussed and accepted in other regional forums (including NRPC and SRPC).
- ✓ In certain time blocks, the schedule of a beneficiary may be lower than its requisition, even when the requisition is equal to the beneficiary's entitlement, due to the ramping capability of the concerned ISGS being considered while finalizing the schedule.
- ✓ During ramp-up/ramp-down operation, the scheduled injection of a generating station for a time block represents the average generation/injection over the duration of that time block, whereas the actual generation changes progressively in accordance with the ramping capability of the generating station. Accordingly, during the first and last time blocks of a ramping period, the scheduled injection reflects the average impact of the ramp over the respective time block, while during the intermediate time blocks, the scheduled injection reflects the applicable ramping capability of the generating station.
- ✓ It was explained that the capacity 'held back' on account of this ramp restriction is technically classified as merchant capacity for that block, since the generator is otherwise able but the schedule cannot lawfully be issued at full value; the deviation-settlement (DSM/RTM) formula currently applied for such blocks was flagged as not correctly distinguishing this ramp-restricted capacity from an actual generation shortfall, unlike the Day-Ahead Market (DAM) formula.
- ✓ Communications had been received from WBSEDCL regarding instances wherein, during certain time blocks, power was not scheduled to WBSEDCL against its entitlement from NTPC generating stations, despite the requisition being equal to the entitlement. Examining such instances, it was observed that in the concerned time blocks, the schedule of WBSEDCL had been reduced below its entitlement to accommodate the schedule of the generating station within its ramping capability as described above. However, the generating stations had subsequently considered the difference between DC and schedule as URS and offered/sold the same in RTM.
- ✓ The quantum considered as URS for RTM sale, i.e. the difference between DC and schedule, was not available for scheduling to the beneficiary in the concerned time blocks, as the beneficiary schedule had already been reduced below its entitlement on account of the ramping constraint of the generating station. Therefore, irrespective of whether such quantum was subsequently sold in RTM, the said quantum would not have been scheduled to the beneficiary during the concerned time block.

NTPC assured that the methodology being followed for determination of URS quantum for bidding in RTM would be examined and, wherever required, suitably rectified to ensure that the quantum considered for RTM bidding is appropriately determined.

OCC Decision

- OCC forum advised ERLDC to take up the matter with NLDC for examining the alignment of the RTM settlement formula with the DAM formula so that ramp-restricted first-block capacity is not treated as saleable merchant capacity.

- ERLDC and NTPC were advised to jointly verify and confirm to West Bengal, on a sample basis, that capacity held back on account of the 50% first-block ramp restriction is not being scheduled/sold in the real-time market to the detriment of beneficiaries.
- The matter was referred to the Commercial sub-committee for detailed deliberation.

2.7 Agenda from NTPC Barauni

Sl. No.	Issue	Brief Details
1	Non-availability of PLCC system	PLCC/tele-protection system is not available/commissioned for 220 kV BTPS-Begusarai Ckt-01 & 02 and 220 kV BTPS-Hajipur Ckt-01 & 02 affecting protection coordination and reliability. The issue was earlier highlighted in NTPC letters dated 03.07.2025 and 25.09.2025. (Details enclosed at Annex B.2.7)
2	Implementation of Auto-Reclosure scheme in 220 kV BTPS-Begusarai Ckt-01 & 02	Auto-Reclosure scheme for 220 kV BTPS-Begusarai Ckt-01 & 02 is required for system reliability and continuity of power evacuation. BSPTCL has also requested necessary action for resolving the issue. (Details enclosed at Annex B.2.7)
3	Tripping of Both lines, 220 kV BTPS-Hajipur Ckt-01 & 02 on 08.08.2026 and sharing of the exact cause of such Tripping.	The matter has already been taken up with Hajipur; however, their reply is still awaited. (Details enclosed at Annex B.2.7)

Deliberations in the meeting

NTPC submitted:

Owing to absence of teleprotection scheme in 220 kV lines to Begusarai and Hajipur from NTPC Barauni, these are frequently subjected to spurious trippings. The lines are owned by BSPTCL.

BSPTCL updated installation of DTPC in Begusarai circuit by September 2026. While for Hajipur circuit, the space required for DTPC installation has been provided recently in BTPS. Site visit will be carried out by communication team of BSPTCL within next two days.

OCC Decision

- BSPTCL was advised to expedite pending DTPC installation to ensure healthy teleprotection in lines meant for reliable power evacuation from NTPC Barauni.
- The matter was referred to the protection sub-committee for detailed deliberation.

2.8 Agenda from NTPC Kahalgaon

Old Agenda Points

- 132 kV Kahalgaon–Lalmatia Line outages are being approved without obtaining the consent of NTPC Kahalgaon**, despite the line being of critical importance from the power generation perspective. During the recent outages of the **132 kV Kahalgaon–Lalmatia Line**, coal supply from the **Lalmatia Mines** to NTPC Kahalgaon was severely affected. The outages resulted in **low voltage conditions at the Lalmatia end**, adversely impacting mining operations and significantly reducing coal production and dispatch to the station. Since the uninterrupted availability of this line is vital for maintaining reliable power supply to the mining operations and ensuring continuous coal

availability to NTPC Kahalgaon, it is requested that **no outage of the 132 kV Kahalgaon–Lalmatia Line be approved without prior consultation of NTPC Kahalgaon**, except under emergency conditions. **(NTPC shall be informed regarding Lalmatia shutdown).**

2. Implementation of PLCC/OPGW-based communication and protection for the three 132 kV transmission lines from NTPC Kahalgaon: Kahalgaon–Sabour, Kahalgaon–Lalmatia, and Kahalgaon - Kahalgaon. As per CEA Grid standard fault in 132kV system should be cleared in 160 msecs, most of the times Kahalgaon substation end breaker fails to OPEN during line faults and the fault gets cleared only by opening of breaker at NTPC Kahalgaon. **(To be taken up with BSPTCL by ERLDC Protection team)**
3. A three-day shutdown of 200 MVA ICT#1 (400/132 kV) has been proposed for the replacement of the 132 kV (LV side) circuit breaker. Despite repeated follow-ups, the outage approval has not yet been issued by the **ERLDC Outage Team**, as the shutdown has not been **concurred** by the **Bihar SLDC and Jharkhand SLDC**. The continued deferment of this critical maintenance activity may adversely affect the reliability and operational security of the 132 kV system at NTPC Kahalgaon. Early approval of the proposed shutdown is, therefore, requested to facilitate timely replacement of the old breaker and ensure reliable system operation. **(Shutdown given for three days from 09.09.2026)**
4. As communicated earlier during the OCC meeting, the 400 kV Sectionaliser-1 and Sectionaliser - 2 breakers at NTPC Kahalgaon are presently being kept in the **CLOSED** condition, considering the high power flow requirement during the summer months. In view of the prevailing system conditions, clarity may kindly be provided regarding the continued operation of the 400 kV Sectionaliser-1 and Sectionaliser-2 breakers in the CLOSED condition or whether any change in the present operating philosophy is envisaged. **(This will be implemented during LILO of Goddda - Adani Power Limited).**

New Agenda Point

5. On 31.08.2026, 07:51 Hrs. 132kV Kahalgaon - Lalmatia Line tripped on **Zone-1 R-PH to Ground fault** and breaker at KHSTPP end tripped. Fault current registered in the numerical relay was **10.85 KA** at a calculated distance of **1.1 KM**. The breaker at remote end (Lalmatia) did not trip and the same was manually opened. **Non-opening** of remote end breaker on **Z-1 Fault** is a serious violation of **ERLDC protection guidelines**. This issue may please be taken up by **ERLDC** with Lalmatia Sub-Station to avoid it's recurrence.

Deliberations in the meeting

NTPC Kahalgaon summarized all the issues as mentioned above.

OCC Decision

- *All Generating Stations including NTPC to participate in OCC outage meetings regularly for cognizance of any shutdown/outage approvals affecting their respective stations network.*

- The bus-sectionalizer to be kept open at NTPC Kahalgaon based on prevailing system conditions and loading pattern of 400 kV Farakka-Kahalgaon line. ERLDC was advised to issue instructions to close if loading or import conditions on the transmission corridor change.
- NTPC to pursue completion of teleprotection communication arrangements for the identified 220 kV lines and PLCC availability for the three 132 kV lines, in coordination with the communication teams of Bihar and Jharkhand. The matter was referred to the TeST sub-committee for detailed deliberation.

2.9 Shutdown proposal of Thermal generating units: ERPC

✓ Rescheduling of Start of Overhauling of Unit-5 of NTPC Barh: NTPC

- As per the approved LGBR 2026-27, the annual overhauling/shutdown schedule for the generating units of NTPC Barh was approved as follows:
 - **Unit-1: 01.11.2026 to 15.12.2026**
 - **Unit-4: 27.06.2026 to 31.07.2026**
- Subsequently, during the **240th OCC** Meeting, the shutdown programme was reviewed, and it was approved that the shutdown originally earmarked for Unit-4 during 27.06.2026 to 31.07.2026 be reassigned to Unit-2. Accordingly, Unit-2 shutdown was approved from 01.07.2026 to 14.08.2026 in place of Unit-4. It was agreed that in place of shutdown of Unit-1, NTPC Barh will undertake shutdown of Unit-4.
- In line with the above decision of the OCC forum and considering the operational and maintenance requirements of the Unit-4 whose last overhauling was done in Nov-23, NTPC Barh proposes to undertake the planned shutdown/overhauling of **Unit-4** from **01.11.2026 to 15.12.2026**.

✓ Postponement of Overhauling commencement date of MTPS Kanti: NTPC

Overhauling commencement date of MTPS Kanti U#4 (195MW) w.e.f. 01.02.2027 instead of 01.10.2026. Supporting documents enclosed as annexures. (**Annex B.2.9**)

✓ Re-scheduling of planned Annual Overhauling (AOH) of Unit #2: JIPL

- This is with reference to the 238th OCC Meeting of ERPC held on 17.04.2026, wherein based on the request of BSPHCL and the deliberations held during the meeting, Jindal India Power Limited (JIPL) had agreed to reschedule the planned Annual Overhauling (AOH) of Unit #2 from 30.07.2026-29.08.2026 to November 2026. According the same was communicated to ERPC vide our letter dated 20.04.2026.
- Subsequently, JIPL had planned to undertake the Annual Overhauling of **Unit #2** from 1st November 2026 (00:00 Hrs).
- However, considering the upcoming Deepawali festival on 08th November 2026 and Chhath Puja during **13th-16th November 2026**, during which higher electricity demand is generally experienced across the Eastern Region and other beneficiary states, JIPL has decided to further reschedule the Annual Overhauling in the larger interest of ensuring reliable power supply during the festive period.
- Accordingly, the shutdown of **Unit #2** shall now be taken from **18th November 2026** (00:00 Hrs), and the Annual Overhauling activities will commence thereafter.

- ❑ The shutdown is planned for the period of **31 days**, i.e. from **18th November 2026** (00:00 Hrs) to **18th December 2026** (24:00 Hrs).

Deliberations in the meeting

- ✓ *NTPC proposed a 45-day shutdown for Unit 4 (Barh STPP) from 25th November 2026.*
- ✓ *The beneficiary utility (Bihar) raised concerns on overlap of shutdown of several generating units that may result in power deficit for Bihar, thus it was requested to defer upto 20.01.2027.*

OCC Decision

OCC forum agreed with the following planned overhauling shutdowns:

- *NTPC Kahalgaon U#5 from 20.11.2026 to 31.12.2026.*
- *NTPC Barh U#4 from 20.01.2027 for 45 days.*
- *MTPS Kanti U#4 from 01.02.2027 for 25 days.*
- *JIPL Unit #2 from 18th November 2026 for 31 days.*

2.10 Reconsideration of the month of October under the High Inflow Period for FY 2026-27 in respect of Jorethang Loop HEP (JLHEP) and Tashiding HEP (THEP): DANS Energy

The High Inflow Period for these run-of-river stations was declared in the 238th OCC on the basis of barrage spillage alone. During October, the excess inflows were absorbed through overload generation above installed capacity and hence did not appear as barrage spillage. It is therefore requested that October be reconsidered and declared as a high-inflow month for JLHEP and THEP for FY 2026-27, to be reckoned in the RTDA accounts.

Deliberations in the meeting

OCC Decision

- *OCC opined that any additional generation utilised by the grid (rather than spilled) during this high-inflow period, including Sundays/off-peak days where generation is still absorbed by the system, may be considered under the existing dispensation, so that the station is not penalised under RTDA for such high-inflow generation.*
- *OCC agreed to consider October as high inflow period in addition to the months accepted (June to September) in 238th OCC meeting for JLHEP and THEP.*

2.11 Replacement of 400 KV Isolators & Bus Bar protection commissioning at Malda Substation: ERPC

In 242nd OCC Outage co-ordination meeting held on 18th August 2026, POWERGRID submitted the proposal for replacement of 400 KV Pantograph and HCB/Line Isolators at Malda Substation under ADDCAP. It was informed that the Malda 400 KV system is presently operating in split-bus mode, with the Bus Coupler kept open, and commissioning of the new bus bar is pending & the proposed replacement works involve isolators associated with the following 400 kV elements:

- Malda–Purnea-I.
- Malda–Purnea-II.
- 400 kV Bus Coupler.

- ❑ It was further highlighted that replacement of Pantograph Isolators (Bus isolators) requires shutdown of the corresponding bus as well as feeder, whereas replacement of HCB/Line Isolators requires only the corresponding feeder shutdown.
- ❑ Detailed plan and options for carrying out the proposed replacement works enclosed at **Annex B.2.11.**

Deliberations in the meeting

*Powergrid presented Isolator replacement plan at 400 kV Malda S/S (enclosed at **Annex B.2.11**)*

OCC Decision

OCC advised ERLDC and WB SLDC to carry out detailed study and to apprise the forum of the feasible shutdown window for the proposed 400 kV elements.

2.12 Formal Procedure for sharing IMD Wind Sensors' Data with Power Utilities: ERPC

CEA on Formal Procedure for sharing IMD Wind Sensors' Data with Power Utilities. IMD has informed that Power Transmission Utilities may enter into MoUs with IMD for sharing meteorological data/services, including wind speed data. IMD has further informed that Power-sector utilities desirous of obtaining meteorological data/services may forward a formal proposal/ request to the Director General of Meteorology, IMD (directorgeneral.imd@imd.gov.in), clearly indicating their specific requirements and the proposed scope of collaboration. The proposal/request may also be forwarded with a copy to the Organization Section and PHT Cell of IMD at organisationsection@gmail.com , imd.pht@gmail.com.

Deliberations in the meeting

*ERPC representative apprised the forum on the procedure delineated by CEA regarding collaboration between IMD and Power utilities Letter in this regard from CEA dated 08.09.2026 attached at **Annex B.2.12**.*

OCC Decision

- *ERLDC to finalise the formal data-sharing procedure/agreement with IMD for wind-sensor data, ensuring cyber-security clearance, and circulate the same to constituent utilities once operational.*
- *With regard to the cyber-security implications of establishing this data connection (firewall/IT-system compatibility) with IMD's systems on a different IT framework, all ER constituents were advised coordinated with their concerned cyber-security nodal officers.*

2.13 Submission of Year-Ahead Resource Adequacy Data for FY 2027-28: ERLDC

- ☐ As per Clause 3.2 of Section-3 of the CEA Guidelines for Resource Adequacy Planning Framework for India, NLDC is required to annually publish a one-year look-ahead Short-Term National Resource Adequacy Plan (ST-NRAP).
- ☐ Further, as per Regulation 5.3(d) of the Indian Electricity Grid Code (IEGC), 2023, the concerned agencies are required to furnish the requisite technical data to NLDC through the respective RLDCs every year for carrying out the national-level generation resource adequacy assessment.
- ☐ Accordingly, the requisite Year-Ahead Resource Adequacy data for FY 2027-28 (April 2027 to March 2028) is required to be furnished by the concerned SLDCs for undertaking the resource adequacy assessment.
- ☐ The following data is required to be submitted in the prescribed formats:
 - ✓ Electricity Demand Data – Format RA-1
 - ✓ Reserve Requirement – Format RA-2
 - ✓ Tie-Line Details – Format RA-3

- ✓ Transfer Capability – Format RA-4
- ✓ Generation Data of State Control Area – Format RA-5
- ❑ The prescribed Excel formats and online submission link has already been provided via mail dated **31.08.2026**.
- ❑ The concerned constituents are requested to furnish the above data to ERLDC by 15.09.26 to facilitate timely compilation and further submission/assessment at the national level.

Deliberations in the meeting

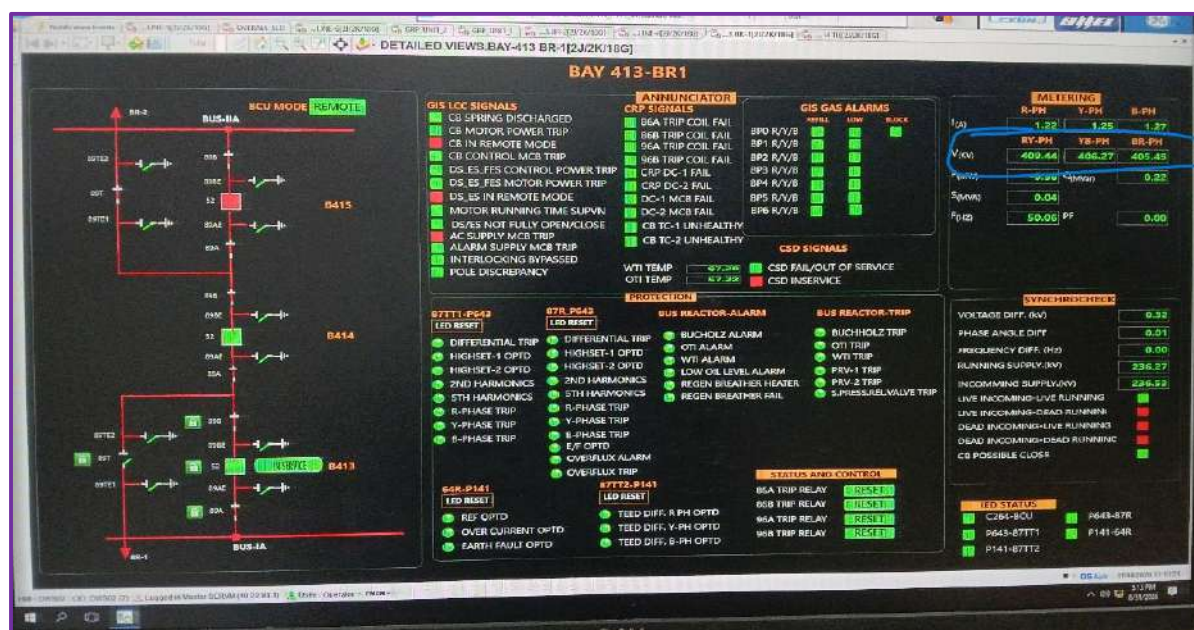
OCC Decision

It was advised that resource-adequacy planning data pertaining to the 2027–28 horizon should be routed through the respective SLDCs in coordination with the concerned STUs before forwarding the consolidated submission to ERLDC.

2.14 Miscellaneous agenda by PVUNL

a) Tenughat line side Voltage is maintaining at high side due TAP position of GT

- ❑ During charging of the Tenughat-PVUNL 400 kV transmission line after completion of insulator replacement works on 31.08.2026, both 400 kV Bus Reactor-1 and Bus Reactor-2 at PVUNL were taken out of service to raise the PVUNL bus voltage from 406.5 kV to 410 kV for facilitating line charging from the Tenughat end. Upon charging of the line, the voltage received at the PVUNL end was observed to be 428.5 kV due to the line charging effect under lightly loaded conditions. To facilitate synchronization of the line at the PVUNL end, both bus reactors remained out of service during the synchronization process. After successful synchronization, Bus Reactor-1 and Bus Reactor-2 were brought back into service.
- ❑ BR-1 taken out of service to improve voltage from 407 to 409KV





- ☐ Line Charged from Tenughat end and voltage difference is marginal of 18.15 KV .

Deliberations in the meeting

PVUNL expressed the issue of higher voltage upon charging from Tenughat .

ERLDC apprised that the matter had been examined in the special meeting held on GT synchronisation. It was informed that the concerned generating utility had consulted its OEM regarding the change required on the GT, and that the same would be carried out at the time of the next unit shutdown of TVNL.

OCC Decision

OCC opined to convene a special meeting by ERLDC in this regard involving all stakeholders.

b) Frequent Disconnection of AGC communication

- ☐ In the Month of Aug 2026, frequent communication failure is observed due to which the AGC has been kept OFF. NLDC has informed that Link frequent failing which needs to be addressed.
- ☐ Need to resolve the AGC issue so that commercial loss to PVUNL can be avoided.

Deliberations in the meeting

ERLDC informed that frequent disconnection of AGC links had been deliberated in earlier CCM and OCC meetings and that the NLDC–SLDC interconnection needs to be properly sorted out. SLDC- NMS status of link healthiness from PVUNL to Bero is reported as working fine.

It was informed that a high-level group has already been constituted in this regard, and that the regulatory obligations and the commercial aspects were being dealt with separately. Grid-India stated that link availability had been reviewed, that the target is 100% availability, and that the availability report, including the UNMS-based report, would be furnished.

Jharkhand apprised that communication link has been established upto Maithon (PG) while the rest(Maithon(PG) to NLDC) is under the scope of Powergrid.

OCC Decision

OCC advised Powergrid to look into equipment level, i.e FOTE configuration & check for issue in NMS upto NLDC. This was referred to TeST sub-committee.

c) Redundant Communication Channel link from PVUNL to NLDC is required

- ❑ Presently, the PVUNL-NLDC AGC communication link is extended through the Patratu-PVUNL transmission line, with two independent communication channels available at PVUNL. While this arrangement provides redundancy within the same communication route, both channels are dependent on a common transmission corridor.
- ❑ In addition to the Patratu-PVUNL line, PVUNL is also connected through the Tenughat line, which offers an opportunity to establish an alternate communication path for AGC connectivity with NLDC. Such an arrangement will minimize the risk of simultaneous communication failure arising from outages, maintenance activities, or faults associated with a single transmission corridor and will support uninterrupted AGC operation as per grid requirements.
- ❑ In view of the above, feasibility assessment and implementation of a redundant AGC communication channel through the Tenughat line to strengthen the overall reliability of AGC communication infrastructure at PVUNL.



Deliberations in the meeting

PVUNL informed that the unit has already been placed in AGC service. PVUNL explained that it is connected to the grid through two lines, of which only the line on the Patratu side carries the communication channel, and that the entire communication to NLDC/Grid-India is presently routed through this single path. It was further informed that an alternate path for the AGC link through POWERGRID's communication channel has already been configured. It was noted that the AGC link had suffered disconnections on multiple occasions.

OCC Decision

OCC advised PVUNL and POWERGRID to ensure a redundant, independently routed communication path for the AGC link to Grid-India. The alternate path needs to be commissioned and tested through POWERGRID's communication channel, which has already been configured. This was referred to TeST sub-committee.

d) PVUNL - Patratu Line PLCC to be provided by JUSNL

- ☐ During commissioning of **PVUNL Unit-1**, power evacuation was established through the **Patratu-PVUNL 400 kV Double Circuit transmission line** having a route length of approximately **6.6 km**. At present, the transmission line is equipped with a **single FOTE-based communication link** for protection carrier channel operation.
- ☐ To ensure redundancy and improve the availability of protection carrier communication, it is requested that **Channel-2 communication through PLCC** may be provided by **JUSNL**.
- ☐ Provision of the redundant PLCC channel will enhance the reliability of teleprotection, ensure continuity of protection signaling during failure of the primary communication path and strengthen the overall security of power evacuation from PVUNL.

Deliberations in the meeting

PVUNL informed that the carrier signal through PLCC Channel-2 on the concerned line has been realised and that communication has been established. A stretch of about 6.6 km within the Jharkhand network was also referred to, for which the estimate was stated to be under process.

OCC Decision

JUSNL was advised to expedite contract for PLCC material. This was referred to TeST sub-committee.

e) Black Start power source for PVUNL Switchyard

- ☐ To make procedure for Black start during any emergency , details of Startup power source needs to be confirmed.
- ☐ To ensure preparedness for emergency restoration and development of a comprehensive Black Start Procedure, the details and availability of the startup power source for station auxiliaries need to be confirmed. In this regard, it is requested that the RLDC for confirmation of the designated startup power source, switching arrangements, restoration sequence and associated operational requirements during black start conditions.

Deliberations in the meeting

PVUNL sought clarity on the blackout start-up procedure applicable to it, being a generating station only, and on the procedure to be followed in handling of emergency.

OCC Decision

OCC advised PVUNL to collect the Black Start procedure from SLDC Jharkhand or may take up directly with ERLDC for the same.

2.15 Procurement of Reactors under ADD-CAP Block 2024-29 in Odisha based on RLA submitted by M/s CPRI: **POWERGRID ODISHA**

- Residual Life assessment was carried out by M/s CPRI for various old Transformers and Reactors in Odisha, which have completed useful life of 25-years. M/s CPRI recommended the replacement of the following reactors due to various issues as detailed below: -

Sl. no.	Name of the equipment	Violations of technical parameters and issues observed by M/s CPRI	CPRI Recommendations
01.	420kV,50MVAR, 3-Ph Line Reactor of 400 kV Rourkela-Chaibasa-II line at Rourkela Substation (Non-switchable). Sr.no.: 6005038 Make: BHEL, Yr. of Mfg:1989, Date of commng:31.08.1993 Project: Jamshedpur Rourkela Transmission system project. Age: 37 years old. Service:33 years.	DGA results show increasing trend in hydrocarbon gases, From the diagnostic test data, it can be inferred that the condition of the Reactor is critical. The values of Co and Co2 are high and are showing increasing trend, which indicates deterioration of solid insulation". (ii)Furan analysis also shows increasing trend in total furan content from 2.056 mg/kg in 2023 to 2.27 mg/kg in 2024 indicating active deterioration of solid insulation. The calculated Degree of Polymerization shows lower DP values indicating substantial aging of solid insulation.	"From the diagnostic test data, it can be inferred that the condition of the Reactor is critical. Considering the requirement for high system reliability, replacement of the Reactor is recommended to prevent potential failures and ensure continued safe operation".
02.	420kV,63MVAR, Bus Reactor-I at Jeypore S/S. Sr.no.: 6005650 Make: BHEL, Yr. of Mfg:1997, Date of commng:26.05.1998 Project: Gazuwaka HVDC Back-to-Back Project Age: 29 years old. Service:28 years.	Furan analysis shows increasing trend in total furan content from 0.346 mg/kg in 2020 to 1.163 mg/kg in 2024 indicating rapidly deteriorating condition of the solid insulation.	A long-term replacement plan needs to be made to address progressive solid insulation deterioration.
03.	420kV,50MVAR, 3-Ph Line Reactor of 400 kV Indravati-Rengali Line at Indravati S/S. (Non-switchable) Sr.no.: 6004880 Make: BHEL,	Furan analysis shows increasing trend in total furan content from 0.311 mg/kg in 2020, through 0.561 mg/kg in 2023 to 0.778 mg/kg in 2024 indicating rapidly deteriorating condition of the solid insulation.	Furans levels should be monitored closely and if there a further rise in furan concentration, replacement of the reactor should be considered to ensure reliability and prevent potential failure. <i>(Latest furan value found to be 1.344 mg/kg tested</i>

	Yr. of Mfg:1987, Date of commng:16.03.1990 Project: Jeypore Talcher Transmission System project. Age: 39 years old. Service:36 years.		on 28.06.2026. Huge Increasing trend observed. Oil test Report enclosed for reference).
--	---	--	--

- ☐ CPRI RLA report enclosed for kind reference.
- ☐ As the lead time for procurement of Reactors is around 3 years, it is proposed to procure new reactors in this ADD-CAP block 2024-29.
- ☐ Also, it is pertinent to mention that the above 02 nos. Line reactors are Non-Switchable type. As per the latest guidelines, for better control and reliable operations, it is proposed to convert these Non-switchable line reactors to Switchable type with the provisioning of suitable switchgears.
- ☐ Request for consideration in ADDCAP Block :2024-29:
- ☐ Hence, in line with the facts stated above and as the above reactors are eligible **for replacement under ADD-CAP** as per prevailing guidelines (**completed service of more than useful life of 25 years**), it is proposed to consider for **Procurement of New Bus Reactor for Jeypore Substation & New Line Reactors for Rourkela and Indravati Substation along with the associated switchgear for further use as Switchable Line reactors under ADD-CAP Block 2024-29.**

Deliberations in the meeting

POWERGRID (Odisha) informed:

- ✓ *Residual Life Assessment (RLA) of its ageing transformers and reactors had been carried out through CPRI. Where assets had completed their useful life, or had shown DGA violations or an increasing trend of dissolved gases, CPRI has recommended replacement.*
- ✓ *Procurement of a reactor takes almost three years, and requested that the replacement be considered under the 2024–29 block so that timely action could be taken. The CPRI test reports enclosed at **Annex B.2.15**.*

OCC Decision

OCC referred the proposal to CMETS-ER for further study by CTU in ascertaining the requirement of the line & Bus reactors (at Jeypore, Rourkela and Indravati Substations) in view of sustaining optimal voltage profile in ER ISTS network.

2.16 Establishment of Inter-State Tie-Line Connectivity between DVC–BSPTCL and DVC–JUSNL: DVC

- ☐ The **132 kV Barhi–Rajgir/Nalanda tie line has been dismantled**, resulting in the loss of direct 132 kV tie-line connectivity between the **DVC and BSPTCL systems** through this corridor. Consequently, during a system crisis or contingency condition in the **Koderma–**

Barhi region of DVC, power assistance from the Bihar system through this route is no longer available, thereby reducing the flexibility and reliability of the interconnected system.

- It is gathered that **BSPTCL's Barachati substation is located relatively close to DVC's Barhi substation**. In view of the above, it is proposed to examine the feasibility of **extending the DVC portion of the erstwhile Barhi–Rajgir/Nalanda tie-line up to BSPTCL's Barachati substation**. Establishment of such connectivity would provide an additional source/path for power support during contingency conditions and is expected to **enhance system reliability, operational flexibility and emergency power assistance capability** in the Koderma–Barhi area.
- Similarly, the **132 kV Patratu–Patratu tie-line connection at the JUSNL end is presently disconnected**. It is proposed to examine the feasibility of **connecting the available DVC Patratu tie-line with JUSNL's Katia substation**, thereby establishing an additional direct tie-line connectivity between the **DVC and Jharkhand systems**.
- The proposed interconnections may be examined through appropriate **load-flow, short-circuit and contingency (N-1) studies**, subject to technical feasibility and concurrence of the concerned utilities, these interconnections may be considered as **system-reliability improvement measures and additional avenues for emergency power assistance** to DVC during critical system conditions.

Deliberations in the meeting

DVC submitted :

- ✓ *132 kV Barhi–Rajgir line for connectivity between Bihar and DVC has been dismantled.*
- ✓ *The importance of tie-line connectivity was emphasized against the backdrop of both the ICTs being presently out of service at Koderma.*
- ✓ *The connectivity was proposed to be restored with Bihar via BSPTCL's Barachati substation located in proximity to DVC's Barhi substation.*
- ✓ *Similarly, as vthe 132 kV Patratu–Patratu tie-line connection at the JUSNL end has been disconnected, It was proposed to examine the feasibility of connecting the available DVC Patratu tie-line with JUSNL's Katia substation*

OCC Decision

- *DVC, BSPTCL and JUSNL shall coordinate with ERLDC for finalisation of the tie-line connectivity details.*
- *OCC opined in favor of joint study by DVC, SLDC Jharkhand, SLDC bihar, ERPC and ERLDC to assess operational feasibility of ISTS connectivity of DVC with Bihar and Jharkhand respectively. A special meeting may be convened in this regard with all stakeholders.*

2.17 Review of DSM Charges due to system issue in WBES Scheduling Portal for HVDC Pusauli from NTPC Kahalgaon Stage-1.: POWERGRID ER-I

- Energy scheduling for HVDC Pusauli is being carried out on a daily **D-1 basis** through the WBES portal (<https://newwb.es.gridindia.in/>).
- Earlier, the portal operated in the "**Full Requisition**" mode by default, wherein it was sufficient to enter **zero (0)** in the **OnBar(n)** column (Manual Input mode) for the time blocks from **08:00 hrs to 16:00 hrs**, as the energy requirement during this period was met through renewable sources.

- However, following the recent change in the portal's default mode to "**Full Surrender**", users are required to enter the required quantum of power (limited to the allotted GNA capacity) in the **OnBar(n)** column. It has been observed that whenever the value entered in the **OnBar(n)** column exceeds the value displayed in the "**OnBar Ent**" column, the system automatically changes the entered value to **zero (0)** upon saving, without generating any warning, validation message, or error notification.
- As a result, on the following dates:
- **03.07.2026, 04.07.2026, 07.07.2026, 08.07.2026, 09.07.2026, 11.07.2026, 23.07.2026, 25.07.2026, 27.07.2026, 31.07.2026, 01.08.2026, 02.08.2026, 03.08.2026, 07.08.2026, 09.08.2026, 10.08.2026, 11.08.2026, 15.08.2026, 16.08.2026, 17.08.2026, 18.08.2026 and 19.08.2026**, the value displayed in the **OnBar Ent** column was lower than the allotted GNA capacity of **0.80 MW**. Consequently, while entering the scheduling requirement in Manual Input mode, the entered values were automatically reset to zero by the system during the save operation, without any notification to the user. This led to inadvertent scheduling mismatches and the subsequent levy of substantial DSM charges in the bills for the concerned period.

Value more than "OnBar Ent" is reduced to "0", without giving any error while saving.

Time Block	Time Desc	OnBar Ent	OffBar Ent	Latest Restrict Req	OnBar (I/P)	RestrictReq(n)	OnBar(n)	OffBar (I/P)	OffBar (n)	Operation
1	00:00-00:15	0.68	0	0	0	0	0	0	0	Manual input
2	00:15-00:30	0.68	0	0	0	0	0	0	0	Manual input
3	00:30-00:45	0.68	0	0	0	0	0	0	0	Manual input
4	00:45-01:00	0.68	0	0	0	0	0	0	0	Manual input
5	01:00-01:15	0.68	0	0	0	0	0	0	0	Manual input
6	01:15-01:30	0.68	0	0	0	0	0	0	0	Manual input
7	01:30-01:45	0.68	0	0	0	0	0	0	0	Manual input
8	01:45-02:00	0.68	0	0	0	0	0	0	0	Manual input
9	02:00-02:15	0.68	0	0	0	0	0	0	0	Manual input
10	02:15-02:30	0.68	0	0	0	0	0	0	0	Manual input
11	02:30-02:45	0.68	0	0	0	0	0	0	0	Manual input
12	02:45-03:00	0.68	0	0	0	0	0	0	0	Manual input
13	03:00-03:15	0.68	0	0	0	0	0	0	0	Manual input

In view of the facts stated above and issue mentioned (which is solely due to a system-related issue in the scheduling portal), it is requested that the **schedule equivalent to the entitlement (for blocks 1 to 32 and 65 to 96) from 03.07.2026 to 19.08.2026 may kindly be provided and DSM charges may be revised accordingly.**

It is further submitted that, effective **20.08.2026**, all personnel responsible for energy scheduling of HVDC Pusauli have been instructed not to enter values in the **OnBar(n)** column

exceeding the corresponding value displayed in the **On Bar Ent** column, in order to avoid recurrence of the issue.

Deliberations in the meeting

POWERGRID ER-I summarised the issue and stated the following:

- ✓ *In respect of the utility's GNA allocation through HVDC Pusauli and its share from NTPC Kahalgaon, one unit of NTPC Kahalgaon had remained under outage for the last two months, as a result of which the scheduled generation capacity and the utility's entitlement had come down.*
- ✓ *It was explained that when a requisition higher than the reduced entitlement is entered on the WBES portal, the system treats it as an invalid requisition.*
- ✓ *On clicking "Save and Publish", the portal by default saves the previously saved requisition, which in this case resulted in a zero requisition, without any error message being generated. As the position continued unnoticed for multiple days, the requisition against the concerned source remained zero and the utility's requirement had to be met through additional/market purchase. It was submitted that no error had been flagged by the portal at the time of entry.*
- ✓ *It was also apprised that the portal has been modified later so that an entry above the limit is now restricted with an error message. The beneficiary requested a one-time settlement, stating that full attention has been paid since August 2026 and no such error would recur, and sought that some discount be offered on the amount involved.*

ERLDC submitted that retrospective revision of the scheduled quantum of power is not feasible and clarified as:

- ✓ *Requisition submission by HVDC Pusauli that, as per the logic implemented in WBES on a pan-India basis, in case a beneficiary attempts to submit a requisition exceeding its available entitlement in any time block, the system retains the previously saved requisition value for that time block.*
- ✓ *In the case of HVDC Pusauli, for several dates referred to in the Agenda, POWERGRID attempted to enter a requisition of 0.8 MW against an available entitlement of 0.68 MW. Since the entered requisition exceeded the available entitlement, the system retained the previously saved requisition values for the respective time blocks, which were zero. Accordingly, the zero requisition values were subsequently submitted by HVDC Pusauli through the "Save & Publish" button in ISGS requisition page of WBES.*
- ✓ *HVDC Pusauli had correctly submitted manual requisition against its entitlement on several other days when the entitlement was less than 0.8 MW, including 30 July 2026, 4 August 2026, 5 August 2026, 6 August 2026, 7 August 2026, 8 August 2026, 12 August 2026, 13 August 2026 and 14 August 2026. This indicated that manual requisition could be submitted correctly in such cases.*
- ✓ *The requisition was ultimately submitted from the beneficiary end through the said "Save & Publish" button in ISGS requisition page of WBES and, therefore, the requisitioned values were required to be verified by the concerned operator prior to submission. It was also observed that zero requisitions had been submitted continuously for several days, without the same being identified and corrected at the HVDC Pusauli end. Thus, the issue was not attributable to any system-related fault in the WBES but was due to submission of incorrect/zero requisition values from the beneficiary end.*

*Detailed presentation on the alleged discrepancy in WBES Scheduling Portal enclosed at **Annex B.2.17***

OCC Decision

- OCC Forum opined that post-facto revision of the schedule for the concerned dates was not feasible and advised POWERGRID to ensure proper verification of the requisitioned values by all the operator before submission in WBES to avoid recurrence of such instances.
- OCC observed that the portal logic should take the lower of the requisition entered and the entitlement where the requisition exceeds the entitlement, instead of defaulting to zero without an alert.
- The matter was referred to the Commercial sub-committee for further deliberation.

2.18 Installation of Transmission Line Arrestor in 220kV & 400kV Lines in High Lightning prone areas of North-Bengal & South-Bengal: POWERGRID ER-II

220kV D/C Siliguri-Kishanganj TL II) 220kV D/C Birpara-Binaguri TL III) 400kV D/C Binaguri-Purnea TL located in North-Bengal: -

The details of the lines are tabulated below: -

SI No.	Name of TL	Year of Commissioning	Line Length	No. of Towers
1	220kV D/C Siliguri-Kishanganj TL (A)	1986 (Original line) 2014 (KSNJ LILO)	108	335
2	220kV D/C Birpara-Binaguri TL (B)	1986 (Original line) 2007 (BNG LILO)	80	235
3	400kV D/C Binaguri-Purnea TL(C)	2006	173	467

- ☐ All the above mentioned 3(Three) lines are located in the in the Himalayan Foothills and encounter severe lightning incidents during the monsoon period starting from April-Oct. As stated by NASA, The Himalayan Foreland is declared as Principal Lightening Hotspot zone.
- ☐ As per IMD Lightening vulnerability data (1998 to 2013) which provides the Annual Avg Lightening Flashed per Sq km per day, the lines fall in the following category: -

SI No.	Name of TL	Lightning Intensity
1	220kV D/C Siliguri-Kishanganj TL(A)	0.07 to 0.10 per Sq. KM per day
2	220kV D/C Birpara-Binaguri TL(B)	0.11 to 0.13 per Sq. KM per day
3	400kV D/C Binaguri-Purnea TL(C)	0.07 to 0.10 per Sq. KM per day

*Line route imposed on IMD lightning map for above lines enclosed for reference.

- Year-wise AR & lightning related tripping incidents in the line since 2021 are tabulated below:-

SI No.	Name of TL	FY 2021-22		FY 2022-23		FY 2023-24		FY 2024-25		FY 2025-26		FY 2026-27	
		AR	Trip	AR	Trip	AR	Trip	AR	Trip	AR	Trip	AR	Trip
1	SLG-KSNJ TL	8	1	15	3	4	1	5	0	3	0	4	3
2	BRP-BNG TL(B)	3	0	8	1	3	0	1	2	3	0	3	3
3	BNG-PRN TL(C)	4	1	5	0	0	2	5	1	6	1	8	1

- The earlier preventive measures taken in the line to reduce AR & trippings are tabulated below:-

SI No.	Name of TL	Actions taken		
1	220 KV D/C SLG-KSNJ TL	-Porcelain insulators replaced with CLR in YR 2018	Additional earthing provided all Towers having High TFRs	TL LA (660 nos.) installed in 165 Towers in the YR Jan-2023
2	220 KV D/C BRP-BNG TL(B)	-Do	-Do	No TL LA installed in line
3	400 KV D/C BNG-PRN TL(C)	-Do	-Do	No TL LA installed in line

- Upon installing TL LA there was marked reduction in the lightning related AR & tripping in 220kV D/C Siliguri-Kishanganj TL as tabulated below:

Si No	Name of Line	Before fixing TL LA			After fixing TL LA		
		2022-23			2023-24		
		A/R	Trip	Total	A/R	Trip	Total
1	220kV D/C Siliguri-Kishanganj line	15	3	18	4	1	5

- Even after carrying out various earthing improvement measures, TFI values in few sections of the lines where AR & Trippings are mostly occurring are having High TFR as tabulated below: -

SI No.	Name of TL	No. of Towers having high TFR
1	220kV D/C Siliguri-Kishanganj TL(A)	59
2	220kV D/C Birpara-Binaguri TL(B)	59
3	400kV D/C Binaguri-Purnea TL(C)	87

- ☐ Last monsoon season and this season during the period April to Oct, it has been observed that lightning related AR & tripping incidents are occurring in the above mentioned 3(Three) lines in spite of various preventive measures as taken as mentioned above.
- ☐ A considerable no. of towers of the above mentioned lines are in River bed having sandy soil having wide fluctuations in TFR values with high TFRs encountered during summer period /start of monsoon resulting in multiple AR/Tripping at the starting of monsoon. Gradually the area gets submerged and TFR value improves but till then the said lines faces a considerable nos. of Tripping & AR.

II) 400kV D/C Andal-Jamshedpur TL II) 400kV D/C Maithon-Jamshedpur TL III) 400kV D/C Maithon-Mejia TL located in South-Bengal:-

- The details of the above-mentioned lines are tabulated below: -

SI No.	Name of TL	Year of Commissioning	Line Length	No. of Towers
1	400kV D/C Andal-Jamshedpur TL(C)	2010	156	428
2	400kV D/C Maithon-Jamshedpur TL(D)	1984	152	411
3	400kV D/C Maithon-Mejia TL(E)	2010	59	179

- All the above mentioned 3(Three) lines passes through the Chota Nagpur Plateau and encounter severe lightning related AR and trippings. As per India's Annual Lightning Report 2019-2020, the Chota Nagpur Plateau were identified as lightning hot-spots zones in the country.
- As per IMD Lightening vulnerability data (1998 to 2013) which provides the Avg Lightening Flashed per Sq km per day, the lines fall in the following category: -

SI No.	Name of TL	Lightning Intensity
1	400kV D/C Andar-Jamshedpur TL(C)	0.07 to 0.10 per Sq. KM per day
2	400kV D/C Maithon-Jamshedpur TL(D)	0.07 to 0.10 per Sq. KM per day
3	400kV D/C Maithon-Mejia TL(E)	0.07 to 0.10 per Sq. KM per day

*Line route imposed on IMD lightning map for above lines enclosed for reference.

☐ Year-wise AR & lightning related tripping incidents in the line since 2021 are tabulated below: -

SI No.	Name of TL	FY 2021-22		FY 2022-23		FY 2023-24		FY 2024-25		FY 2025-26	
		AR	Trip	AR	Trip	AR	Trip	AR	Trip	AR	Trip
1	ADL-JSR(C)	4	0	6	0	2	0	8	1	4	1
2	MTN-JSR(D)	4	1	4	3	3	3	1	0	8	0
3	MTN-Mja(E)	4	0	2	1	1	0	2	1	5	0

☐ The earlier preventive measures taken in the line to reduce AR & trippings are tabulated below: -

SI No.	Name of TL	Actions taken	
1	AJ-JSR(C)	-Porcelain insulators replaced with CLR in YR 2018	Additional earthing provided all Towers having High TFRs
2	MTN-JSR(D)	-Do	-Do
3	MTN-Mja(E)	-Do	-Do

☐ Even after carrying out various earthing improvement measures, TFI values in few sections of the lines where AR & Trippings are mostly occurring are having High TFR as tabulated below: -

SI No.	Name of TL	No. of Towers having high TFR
--------	------------	-------------------------------

1	400kV D/C Andal-Jamshedpur TL(C)	25
2	400kV D/C Maithon-Jamshedpur TL(D)	46
3	400kV D/C Maithon-Mejia TL(E)	32

- ☐ Last monsoon season, it has been observed that lightning related AR & tripping incidents have increased in the said 3 (Three) lines in spite of various preventive measures taken earlier as taken as mentioned above. Few towers of the above mentioned lines are located in hills having rocky soil with consistent high TFRs in spite of various earthing improvement measures taken.
- ☐ Now, so far earthing is concerned, additional earthing has been carried out in 100% of the line and porcelain insulator has been replaced with CLR insulator in almost 100% of the lines. By carrying out above activities, tripping due to lightning have reduced from earlier years in the said lines but still the tripping rate is quite high. It has been observed from the weather conditions over the years that lightning phenomenon have now increased drastically in West Bengal. Several newspaper publications also justify severity of lightning in West-Bengal. It seems that the prevailing earthing design used in the towers are not sufficient to arrest the frequent tripping/auto-reclosures.
- ☐ It has been felt necessary to adopt installation of Transmission Line Arresters as per latest practices adopt worldwide in certain stretches of lines where instances of auto-reclosures and tripping are high.

Sl No.	Name of Line	Original Package	Total Tower considered for TL LA	Total No of TLAs proposed
1	220kV D/C Birpara-Binaguri T/L	CTS	59	236
2	220kV D/C Silguri-Kishanganj T/L		59	236
3	400kV D/C Binaguri-New Purnea T/L	Kathalguri Transmission	87	348
4	400kV D/C Maithon-Jamshedpur T/L	Kahalgaon Transmission System	46	184
5	400kV D/C Andal-Jamshedpur T/L	ERSS-I	25	100
6	400kV D/C Maithon-Mejia T/L	DVC Supplementary	32	128
	Total		308	1232

The tentative cost estimate for installation of 1232 Nos. of Transmission Line Arrestors in 308 Nos. of Towers of said lines shall be around 18 Crores.

Considering the increase in lightning phenomenon, it seems that existing Tower Earthing system are not sufficient and as such as a system improvement measure it is requested to consider the TL LA installation as per above estimated cost in the ongoing ADDCAP 2024-2029 tariff block of Chukha Transmission System, Kathalguri Transmission, Kahalgaon Transmission System, ERSS-I, DVC Supplementary.

On getting technical approval, further cost analysis and recovery mechanism shall be placed in forthcoming Commercial Sub Committee meeting.

Deliberations in the meeting

POWERGRID ER-II submitted:

- ✓ *Passage through high lightning-strike zones and recent increase in frequency of lightning related auto-reclose were put forth as justification for installation of Transmission Line Arrestors in 220kV & 400kV Lines. Transmission Line Arrestors are planned to be procured along with reconductoring of the lines in Chukha transmission system.*
- ✓ *The technical evaluation i.r.o Chukha transmission system reconductoring is targeted for completion by the end of September 2026.*

OCC Decision

- *All OCC members were advised for perusal of the proposal and submit their views/comments(if any) by the next OCC.*
- *The matter shall thereafter be referred to the Commercial sub-committee for financial concurrence.*

2.19 Way leave charge payment for crossing of Railway Lines by various overhead transmission lines of POWERGRID after expiry of initial construction period agreement of 10 years: POWERGRID ER-II

- ☐ Powergrid ER-II maintaining various overvoltage transmission lines across the West Bengal, Sikkim, Bihar & Jharkhand. The overhead transmission lines normally crosses various railway tracks under various railway zone. At the time of construction of the overhead transmission lines way leave charges along with agreement is being paid/executed with Railways for initial period of 10 years in accordance with Ministry of Railways circular on "Policy for Management of Railway Land" (Leasing/Licensing/Way-Leave Facilities on Railway Land) dated 04.10.2022.
- ☐ Upon expiry of initial agreement period, Railway Divisions are submitting revised Demand Letter for renewal of Way-Leave agreement/Charges for 25 years [@ 1.5% of market value of land per annum with annual escalation of 6%.] This type of Demand Letters are being received from various Railway Divisions for different line crossings of POWERGRID.
- ☐ Copy of sample way leave demand letter from Northeast Frontier Railway, Alipurduar JN Division enclosed. As per NFR Railway, POWERGRID have to deposit again way leave charges for overhead railway crossing of 132 KV Earth Electrode Line amounting **Rs. 5,72,576.06 including GST.**

- ❑ As per Regulation 25(1)(a) of the CERC Tariff Regulations, 2024 -25. Additional Capitalisation within the original scope and after the cut-off date:
 - The additional capital expenditure incurred or projected to be incurred in respect of an existing project or a new project on the following counts within the original scope of work and after the cut-off date may be admitted by the Commission, subject to prudence check:
 - Payment made against award of arbitration or for compliance with the directions or order of any statutory authority, or order or decree of any court of law;
- ❑ Considering the demand letters being received from various Railway Division for Overhead Transmission Line crossing & renewal of agreement, it is proposed that the expenditure on account of renewal of way-leave charges may be booked under ongoing ADDCAP tariff block of concerned Project.
- ❑ On getting technical approval, further cost analysis and recovery mechanism shall be placed in forthcoming Commercial Sub Committee meeting.

Deliberations in the meeting

POWERGRID ER-II submitted:

- ✓ *The issue of charges levied by Indian Railways in respect of transmission lines was discussed and the zones concerned were Eastern Railway, South Eastern Railway and North Frontier Railway.*
- ✓ *It was requested that the matter needs direct communication between the Ministry of Power and the Ministry of Railways, and that a change in the statutory or regulatory provisions may be required.*

OCC Decision

- *POWERGRID ER-I, ER-II & POWERGRID (Odisha/Bhubaneswar) and other concerned transmission licensees shall furnish the cumulative, project-wise, line-wise and railway-zone-wise break-up of the charges levied or payable.*
- *The matter shall be placed before the Commercial Sub-Committee.*

2.20 Proposal for AMC support against sustained operations and maintenance of AMR application Web Client Access extended to SLDC/ER-Constituents & DVC: POWERGRID ER-II

- ❑ In the initial solution design phase of the AMR system in ER, the primary requirement was providing SEM data access to ERLDC for the weekly accounting process. However, there have been multiple discussions on sharing the application access of AMR to SLDC.
- ❑ After multiple meetings with the SLDC & other constituents, it was decided to develop a new application setup to provide SEM data access to the utilities and host the application in separate Servers. This approach was taken to physically isolate this new solution from the existing ongoing system of AMR. In 54th TCC & ERPC meeting, it was principally approved to roll-out this new project and share the SEM data access for 05 SLDC (WB, Bihar, Jharkhand, Odisha & Sikkim) and DVC. Timeline was decided for 09 months from LOA.
- ❑ The Layer3/Layer4 network upgrade of AMR was completed in Jun25 month and subsequently, for SLDC environment customization LOA placed for this new project in Sep25. The first pilot application development started for WBSETCL Meters, and the project was developed and deployed in WBSLDC live environment in the month of Dec25.

Gradually, development activities started for 05 new applications for the remaining 05 utilities. The key features which have been integrated into these new applications are as follows:

- ✓ Instant data (MW) of SEM in 01-minute interval.
 - ✓ Displaying MWH data Meter/Feeder wise.
 - ✓ System Dashboard for SEM communication status.
 - ✓ SEM data view block-wise for Load Survey and Midnight.
 - ✓ Meter information.
 - ✓ Reports: NPC report (15 min) & SEM block-wise data Report
- Application development, internal testing, end user's testing & the deployment was completed in the live environment of respective constituents in phased manner and got successfully completed in the month of Mar26. All the utilities have also arranged a separate system at their offices, and this new AMR application access was also configured and made accessible in that system. At present, the new AMR application is available in the live environment of all the 05 SLDC & DVC.
- As members may appreciate, this is a first-of-its-kind project in Pan India basis which was made live in the Eastern Region. PGCIL would like to express thanks for the co-operation of ERPC, ERLDC, DISCOMS and all the stakeholders associated with this project to make this possible and set a new benchmark in the Metering system of Eastern Region, and definitely surely will be followed by other regions shortly.
- Utilities have shared some additional requirements which are primarily in line with the following areas: (details in **Annexure-A**)
- ✓ New Substation/Feeder/Meter addition, primarily the POWERGRID end Meters.
 - ✓ Additional meter/parameters inclusion.
 - ✓ Customized notification/alert mechanism.
 - ✓ Design changes for representation of various data.
 - ✓ Additional graphical representation of data.
 - ✓ 01 min MVAR data availability.
- Some of these requirements are meter-dependent, meaning installation of 01 min compatible meters at stations. And the other set of requirements are primarily related to the upgradation of application and DCU firmware. This will require a significant effort and time. Additional cost may also be incurred since these requirements are not part of the original proposal envisaged in pilot project.
- As part of the original requirements & the agreed timelines, the development has been completed by incorporating the set of requirements and currently the system is under stabilization support. Stabilization support is active till 16-Dec-2026.
- Considering the new requirements which have been requested by utilities and also the stabilization support is ending in Dec26 month, it is proposed to have comprehensive AMC support of the system. The primary scope of AMC support will be as follows:
- All the new requirements which have been received so far will be developed and integrated into the scope of the AMC (list of detailed requirements are in Annexure-A). This will be done as a part of the AMC support of the system.

- ❑ In the future, if any requirements are received which are related to modifications in the look & feel in the User Interface of the application, will be developed and deployed under the scope of AMC.
- ❑ New reports will be developed if requirement received, based on the existing data that is already available in the system as per the scope. (max 15 reports per year).
- ❑ As part of comprehensive system, system monitoring and maintenance activities will be carried out to ensure data availability and to comply with the cyber security aspects. (detailed activity list are mentioned in **Annexure-B**, which will be performed in the AMC phase).
- ❑ The required cyber security patch upgradation will be adopted in the solution, which are as per the guidelines of standard security practices for sharing any critical data beyond its boundary points.
- ❑ To perform all these activities, ensure the SEM data availability to the respective utilities, a dedicated support team shall be deployed during the entire contract period. The team shall function from the existing AMR Central Data Center premises, as remote support via VPN is not permissible in accordance with the prevailing cybersecurity guidelines.
- ❑ Considering this, it is proposed to plan for 04 years of AMC support after completion of the stabilization period. AMC duration will be 17-Dec-2026 to 16-Dec-2030. Total cost of ownership will be tentatively **2,59,45,895 INR (without taxes)**.
- ❑ On getting technical approval, further cost analysis and recovery mechanism shall be placed in forthcoming Commercial Sub Committee meeting.

Deliberations in the meeting

POWERGRID ER-II submitted:

- ✓ *One-minute resolution data of the Eastern Region is available at ERPC and that the SLDCs are deriving considerable benefit from it. The data also serves as a backup where SCADA data of some important lines is doubtful or unavailable, and has helped considerably on such occasions.*
- ✓ *Financial implications for the proposed Annual Maintenance Contract (AMC) of the system were detailed to the forum.*

OCC Decision

- *All OCC members were advised for perusal of the proposal and submit their views/comments (if any) in the next OCC.*
- *The matter shall thereafter be referred to the Commercial sub-committee.*

2.21 DCU replacement plan in the AMR circuit of Eastern Region, towards cyber security enforcement and ensure future proof solutions: POWERGRID ER-II

- ❑ The AMR project has been in operation since 2013. In the initial phase, the Meters were Non DLMS types and for that customized DCUs (VIOLA Make, based out of Finland) were procured and installed. The total number of DCUs which were procured at that time was 106 (in 2013-2014). The primary function of these DCUs were to collect data from the non-DLMS Meters and transmit the data to ERLDC data center using SIM card based public internet.
- ❑ Gradually, after the DLMS standard introduced in the Metering protocol (in 2018), the data collection process was generalized. To incorporate those new set of Meters along with the

already existing meters of non-DLMS types, indigenous vendors for DCU solution was developed (OEM: Verticross). A total of 85 no of DCUs were procured for AMR project in 2020-2021, as part of project expansion since the number of energy meters had been increased in scope.

- The DCU which were initially designed and procured, the primary design features were in-line with the GPRS modem devices with public IP based data communication. Afterwards, as there have been multiple cyber security vulnerability incidents occurred due to public IP based data communications, it was a clear guideline from CSK to permanently dismantle the SIM cards and upgrade the solution to use the OPGW fiber for data communication. In Sep2022, SIM card-based communication was completely dismantled, and the data communication was fully migrated to LAN.
- In the design features of those DCUs procured in earlier periods, the SIM card modem module was present in the model. Though the SIM slots are not operating, having active SIM provision in a critical device like DCU may create cyber security issues in the network if any unwilling mistake happens. Considering the “Zero Trust” cybersecurity framework, it is strongly recommended to eliminate any hardware or module that could pose a potential cybersecurity threat to critical systems such as the AMR platform, thereby ensuring enhanced security and operational resilience.
- In accordance with that, earlier it was planned to completely remove all 106 number of VIOLA make DCUs with the new model of DCUs. This new DCU does not have any SIM card modem slots and has additional features of 01 min data availability etc. The DCU replacement project was approved in 53rd TCC/ERPC meeting, subsequently LOA placed in Aug25, and the replacement of VIOLA DCU got completed in Apr26 month.
- The Verticross make DCUs of 85 qty are currently active and operating in the AMR system (list of Substations are mentioned in **Annexure-C**). However, those DCUs have the feature of SIM card modules within it and also most of the DCU are operating in the 7th year of life, facing few technical limitations in the hardware/firmware level to cater the newly introduced requirements in AMR like 01 min MW data, 01 min MVAR data etc.
- As such, to make the system uniform and be future proof on the reliability and security perspective, it is proposed to plan for replacement of the 85 DCUs. Timeline required for this DCU replacement will be 06 months. **Total cost of ownership will be 97,02,750 INR without taxes. (INR 79,17,750 for HW supply & INR 17,85,000 for installation services).**
- On getting technical approval, further cost analysis and recovery mechanism shall be placed in forthcoming Commercial Sub Committee meeting.

Deliberations in the meeting

POWERGRID ER-II briefed the proposal along with cost implications.

OCC Decision

- *All OCC members were advised for perusal of the proposal and submit their views/comments (if any) by the next OCC.*
- *The matter shall thereafter be referred to the Commercial sub-committee.*

2.22 Conducting VAPT assessment for AMR Asset in ERLDC (in Compliance with Cyber security guidelines): POWERGRID ER-II

- ☐ The 222nd OCC accorded with principal approval to the proposal of conducting VAPT for AMR assets present at ERLDC. In the 52nd Commercial Committee it was agreed with the proposed cost estimate.
- ☐ A total of 04 cycles of VAPT (Vulnerability Assessment and Penetration Testing) and WAPT (Web Application Penetration Testing) were conducted, the last being in March 2026. The results helped identify and reinforce potential threats and vulnerabilities in AMR system. There was no critical vulnerability detected as the AMR system was already compliant with all cyber security guidelines since inception and had undergone through periodic path updates. However, few moderates were detected because of continuous technology advancements in Software domain. Those recommendations have been successfully implemented in the AMR system.
- ☐ As per CEA cyber security guidelines 2021, VAPT needs to be conducted every 6 months. Therefore, the next eligible cycle begins after September 2026.

Below is the scope of VAPT and WAPT:

S.no	Item	Category	Quantity
1	Server	Hardware	07
2	Router	Hardware	09
3	Firewall	Hardware	01
4	Switch	Hardware	02
5	HMI	Hardware	05
6	Application	Software	07

- ☐ Conducting regular VAPT assessments not only identify cyber security threats but also helps in smooth running of existing operations as multiple regions are interconnected in same network.
- ☐ VAPT will be conducted on both the Hardware and the Application. Cost estimation has been received from a CERT-IN certified vendor to conduct one round of VAPT. VAPT will be needed for upcoming 06 cycles in 03 years starting from Sep-26 month. Cost involvement for each year will be around Rs. 10 Lacs excluding GST and total implications will be around 30 Lacs excluding GST for 03 Years.
- ☐ Above activities shall be finalized on Limited Tendering basis among certified bidders.
- ☐ On getting technical approval, further cost analysis and recovery mechanism shall be placed in forthcoming Commercial Sub Committee meeting.

Deliberations in the meeting

Powergrid briefed the forum on the necessity and scope of VAPT assessment of AMR Asset in ERLDC in compliance with Cybersecurity guidelines.

Financial implications along with modus operandi have been detailed above.

OCC Decision

- *All OCC members were advised to go through the proposal and submit their views/comments (if any) by the next OCC.*

➤ The matter shall then be referred to the Commercial sub-committee.

2.23 Lower DC declaration during peak hours as compared to off-peak hours of the same day by ER ISGS under Partial Outage: ERLDC

- ☐ The instances of declaration of lower DC during peak hours as compared to off-peak hours of the same day have been observed in respect of certain ER ISGS, wherein “Partial Outage” has been cited as the reason for such revision.
- ☐ In this regard, Clause 63(j)(iv) of Hon’ble CERC order in Petition No. 9/SM/2024 dated 05.10.2025 stipulates as follows:
- ☐ “The generating stations shall not be permitted to declare Peak hours DC less than off-peak hours DC, other than in cases of forced outage or partial outage. Grid India shall strictly monitor the same. In case a generating station provides less DC during peak hours of the day than off-peak hours, the DC for such generating station for the purpose of fixed charges shall be taken as the lower of the two.”
- ☐ During the last six months, several instances of reduced DC declarations during peak hours as compared to off-peak hours have been observed, as detailed in Annexure-I.
- ☐ ERLDC has sought clarification from Patratu STPP Stage- I for the period 13.04.2026 to 15.04.2026 and Talcher Stage-I for the period 27.07.2026 to 30.07.2026, vide letters dated 15.04.2026 and 31.07.2026 respectively, regarding the reduction of DC during peak hours and the corresponding higher DC declaration during off-peak hours, wherein “Partial Outage” has been cited as the reason for revision. However, the requisite clarifications, including the specific reason/cause of the partial outage and supporting details/digital records, are yet to be furnished by the generating stations.
- ☐ In the absence of reasonable justification for such lower DC declaration during peak hours by the generating stations mentioned in Annexure-I, the reduced DC may be considered for determination of fixed charges for the concerned generating stations for the days on which such instances has been observed, in accordance with the provisions of the aforesaid Hon’ble CERC Order.
- ☐ Further the modalities for calculation and furnishing of such reduced DC by ERLDC in the data being furnished for preparation of REA, and the corresponding utilization of such reduced DC by ERPC in publication of REA, may be finalized.

Deliberations in the meeting

ERLDC submitted:

- ✓ *In many cases the DC declared by ISGS during peak hours is less than the DC declared during off-peak hours, contrary to the CERC order in Petition No. 9/SM/2024. As per operative provisions of the order, generating stations shall not be permitted to declare a peak-hour DC lower than the off-peak DC, except in cases of forced and partial outages and Grid-India shall strictly monitor the same. In case a generating station declares a lower DC during peak hours than off-peak hours, its DC for the purpose of fixed charges shall be taken as the lower of the two.*
- ✓ *Although generators indicate partial outage while declaring the reduced DC, ERLDC does not have the intra-plant and auxiliary details, and the generators themselves must state, with proof, why the reduced DC has been declared. Where proof is furnished for a partial outage, the same can be accepted; without any proof from the generating station, ERLDC has to act as per the order and reduce the DC for that day for that generator.*

- ✓ Letters have been issued to NTPC stations -Farakka, Kahalgaon and BTPS, but no reply has been received so far.
- ✓ The date-wise and plant-wise details, showing the average peak-hour and average off-peak-hour DC, are given in the **Annex B.2.23**. In every listed case the difference was negative, and cases where it exceeded 10% were specifically marked. Repeated instances were noticed at Farakka and, in some cases, at Talcher, North Karanpura and a few other stations.
- ✓ It was pointed out that supporting evidence would in any case be required for DSM purposes as well, including for claiming any rebate, and that the modality for applying the provision had to be finalised.
- ✓ Generators were requested to reply to the letters, failing which the DC may have to be reduced for the purpose of fixed-charge calculation.

OCC Decision

- All ISGS generating stations concerned, in particular Farakka, Kahalgaon, BTPS, Talcher and North Karanpura, shall reply to the letters of ERLDC with supporting evidence of forced/partial outage or plant constraints for the instances flagged, at the earliest and before the next OCC Meeting.
- Generating stations shall ensure that peak-hour DC is not less than off-peak-hour DC, except in cases of forced and partial outage.
- In the absence of evidence, ERLDC shall take the DC for the purpose of fixed charges as the lower of the peak-hour and off-peak-hour DC, in line with the CERC order, and shall strictly monitor compliance.
- ERLDC shall finalize the modalities for implementation, share it with the generating stations and report the status in the next Commercial sub-committee Meeting.

2.24 Establishment of Disaster Recovery (DR) Facility for SAMAST Project of SLDC, WBSETCL: WB SLDC

Background & Current Status

- The **SAMAST** (Scheduling, Accounting, Metering, and Settlement of Transactions) project of SLDC, WBSETCL went live on **05.12.2024** and has been operating successfully.
- To ensure seamless business continuity and safeguard against unforeseen disruptions at the main SAMAST Data Centre (located at the SLDC building, Howrah), a geographically separated **Disaster Recovery (DR) Facility** is planned.
- The proposed DR facility will be established at the **Durgapur 220 kV AB-Zone Substation, WBSETCL** to take over operations during critical system failures.

Approvals & Financial Outlay

- **Board Approval:** The project was formally approved in the **106th meeting of the Board of Directors of WBSETCL** held on **20.02.2026**.
- **Estimated Cost:** **INR 13.4114 Crores** (inclusive of a 4-year Annual Maintenance Contract / AMC).
- **Funding Mechanism:** The entire scheme is proposed to be funded **100% through the Power System Development Fund (PSDF)**.

Submission to the Forum

- The Forum is appraised of the above developments and is kindly requested to **accord its consent** for the establishment of the DR facility and its subsequent PSDF funding proposal.

Deliberations in the meeting

WB SLDC apprised the forum that in compliance with the decisions of the disaster-management meeting, the work for a disaster recovery system of SAMAST Project has been taken up. Internal Board approval has been obtained and the project is envisaged for implementation on 100% funding from PSDF.

OCC Decision

- *OCC noted and appreciated the progress as submitted by WB SLDC, also technically agreed for availing PSDF funding i.r.o Disaster Recovery (DR) Facility of SAMAST Project at WB SLDC.*
- *Other ER states, except WB, having SAMAST Project implemented were advised to implement Disaster Recovery (DR) Facility and update the same to OCC forum at the earliest.*
- *The proposal was referred to TCC/ERPC forum for concurrence.*

3.1. ER Grid performance during August 2026

AVERAGE CONSUMPTION (MU)	MAXIMUM CONSUMPTION(MU)/ DATE	MAXIMUM DEMAND (MW)	MINIMUM DEMAND (MW)	SCHEDULE IR EXPORT	ACTUAL IR EXPORT
		DATE / TIME	DATE / TIME	(MU)	(MU)
680 MU	734 MU, 22.08.2026	33824 MW, 21.08.2026 at 22:56 Hrs.	23078 MW, 06.07.2026 at 06:08 Hrs.	3157	3342

The grid performance of ER for the month of August 2026 was highlighted.

- Clause 2 of Regulation 31 of IEGC 2023 has mandated all SLDCs to timely submit the demand estimate data to the respective RLDC and RPC.
- Current data submission status is given in the table below: Hence, it is again requested to all the concerned for timely submission of demand estimation data to ERLDC. This collaboration is essential for effective planning and preparedness to meet the region's electricity demands efficiently and reliably.
- Latest Forecast and Resource Adequacy Data receipt status at ERLDC is shown below:

[illegible]

4. PART-D: OPERATIONAL PLANNING

4.1. Major Thermal Generating Units/Transmission Element outages/shutdown in ER Grid (as on 08.09.2026)

SL No	STATION	STATE	AGENCY	UNIT NO	CAPACITY (MW)	REASON(S)	OUTAGE DATE
1	ADHUNIK	JHARKHAND	APNRL	2	270	Annual Overhauling	15-Aug-2026
2	DARLIPALI	ODISHA	NTPC	1	800	Tripped on boiler tube leakage but later taken into comprehensive overhaul	03-Aug-2026
3	KHSTPP	BIHAR	NTPC	3	210	Overhauling	28-Jul-2026
4	SAGARDIGHI	WEST BENGAL	WBPDC	2	300	Boiler Turbine Overhauling	04-Sep-2026
5	DPL	WEST BENGAL	DPL	7	300	Capital overhauling	12-Jul-2026
6	JSWEUL	ODISHA	JSWEUL	2	350	Lube oil leakage	06-Sep-2026
7	NORTH KARANPURA	JHARKHAND	NTPC	3	660	Eco flow low	28-Aug-2026
8	KODERMA	DVC	DVC	1	500	Tripped on boiler tube leakage	06-Sep-2026
9	RTPS	DVC	DVC	2	600	Bearing temperature high	21-Aug-2026
10	MEJIA TPS	DVC	DVC	5	250	Gen differential protection fault	12-Aug-2026
11	KOLAGHAT	WEST BENGAL	WBPDC	3	210	Due to Fire hazard in boiler	18-Jun-2026

Major Generating stations Out on Reserve Shutdown due to low system demand:

SL No	STATION	STATE	AGENCY	UNIT NO	CAPACITY (MW)	REASON(S)	OUTAGE DATE
NA							

Hydro Unit Outage Report: -

S. NO	STATION	STATE	AGENCY	UNIT NO	CAPACITY (MW)	REASON(S)	OUTAGE DATE
1	U. KOLAB	ODISHA	OHPC	3	80	Stator Earth Fault	19-Jul-2026

2	U. KOLAB	ODISHA	OHPC	2	80	Heavy Leakage in guide vane	22-Jan-2026
3	BALIMELA HPS	ODISHA	OHPC	5	60	Renovation and modernization work	16-Jan-2025
4	BALIMELA HPS	ODISHA	OHPC	6	60	Initially unit was out due to Severe water leakage from turbine, later unit was taken under Renovation and modernisation work from 00:00 hrs of 16.01.25	06-Jan-2025
5	BURLA HPS/HIRAKUD I	ODISHA	OHPC	7	37.5	Spark observed at PMG rotor	08-Jul-2026
6	TEESTA STG III Hep	SIKKIM	TUL	1	200	Sudden cloudburst at glacier fed LOHNAK Lake followed by huge inrush of water in Teesta River and damage of Teesta III Dam & downstream Powerhouses	04-Oct-2023
7	TEESTA STG III Hep	SIKKIM	TUL	2	200		04-Oct-2023
8	TEESTA STG III Hep	SIKKIM	TUL	3	200		04-Oct-2023
9	TEESTA STG III Hep	SIKKIM	TUL	4	200		04-Oct-2023
10	TEESTA STG III Hep	SIKKIM	TUL	5	200		04-Oct-2023
11	TEESTA STG III Hep	SIKKIM	TUL	6	200		04-Oct-2023

4.2. Long outage report of transmission Element (MORE THAN 01 WEEK) (As on 08.09.2026):

Transmission Element / ICT	Outage Date	Reasons for Outage
220KV-FSTPP-LALMATIA-1	21-04-2021	Two nos. of tower collapsed on 29.05.2024 near to Lalmatia GSS in the Loc. No. 246 & 247. 220KV S/C Farakka-Lalmatia Transmission Line is in anti-theft charging condition from Loc no 248 (Lalmatia end) to Loc no 24. Foundation ,erection and stringing in progress from loc 1 to 24.
132KV-BARHI-RAJGIR-1	25-03-2023	Dismantling of tower no. 227, 228, and 229 crossing the premises of Mahabodhi Cultural centre along with Destringing of conductor of both circuits and Earthwire between tension tower no. 218-237 in same line.The lines from Barhi(DVC) will be terminated at Barachatti(BH) and new line to be constructed from Barachatti to Rajgir(BH)

132KV-NALANDA-BARHI(DVC)-1	25-03-2023	Dismantling of tower no. 227, 228, and 229 crossing the premises of Mahabodhi Cultural centre along with Destringing of conductor of both circuits and Earthwire between tension tower no. 218-237 in same line. The lines from Barhi(DVC) will be terminated at Barachatti(BH) and new line to be constructed from Barachatti to Nalanda(BH)
132KV-CHANDIL-MANIQUEI-1	05-06-2024	Line is closed when power assistance required by either party. Presently, line is opened as power assistance not required by any party.
400KV/220KV 315 MVA ICT 1 AT NORTH KARANPURA	12-09-2024	Tripped on Differential protection.
400KV/220KV 315 MVA ICT 1 AT TSTPP	01-11-2024	Tripped on PRD protection. The failed transformer has reached the vendor; the repair scope has been finalized
400KV/220KV 315 MVA ICT 2 AT MEJIA-B	20-01-2025	315 MVA ICT-2 at MTPS-B got damaged while charging from 220kV GIS bay. New procurement of ICT has been taken up & installation of the same may complete by end of Mar'28.
400KV-DIKCHU-RANGPO-2	05-08-2025	Shutdown taken for damaged insulator replacement work. While charging the line, bus bar protection operated at Dikchu. Issue in GIS chamber of Y ph Isolator between line CB and bus 2. Powder formation inside isolator chamber has occurred. Restoration work delayed. Current Status: Line is anti-theft charged from Rangpo end to Dikhchu extended via Teesta-III, Unable to take in service due to issue in tie bay at Dikchu.
400KV MAIN BUS - 2 AT DIKCHU	05-08-2025	Bus bar protection operated while charging 400kV Dikchu-Rangpo 2. Issue in GIS chamber of Y ph Isolator between rangpo ckt 2 line CB and bus 2. Powder formation inside isolator chamber has occurred. Restoration work delayed. Current Status: Negotiation with GE for procurement is under process, Further 6 to 8 months required by GE for order delivery.
220KV-PATNA-KHAGAUL-1	02-08-2025	LBB relay operated during rectification of DC grounding defect by M/S KRR at GSS khagaul. Earlier w.e.f 02-08-2025 12:06 Hrs, Tower No. 63 has bent significantly on one side. As on 18.06.2026, Tower No. 63 has bent significantly on one side, tender has been awarded. Foundation work for tower has been completed. Expected Revival - 12/08/2026
220KV-BIDHANNAGAR-WARIA-1	29-10-2025	Line kept open to control loading of 220 kV Waria-Mejia D/C (Anti-theft charged from Waria end.)
220KV-BIDHANNAGAR-WARIA-2	29-10-2025	Initially line was opened to control line loading. In between B-phase CT Blasted at Bidhannagar end. Now Line is charged as anti-theft from Waria end to control loading of 220 kV Waria-Mejia D/C.
220KV-BALIMELA-UPPER SILERU-1	21-11-2025	Idle charged from U. Sileru end. Power drawl by Odisha halted due to non-concurrence by Andhra Pradesh.

400KV/220KV 315 MVA ICT 1 AT KODERMA	10-02-2026	The ICT had been taken out of service due to a rising trend of acetylene (C₂H₂) concentration in the transformer oil. The ICT was proposed to be sent to the factory for necessary rectification. Meanwhile, one ICT from DSTPS was diverted and installed at Koderma. After commissioning, the diverted ICT was idle-charged from the 400 kV side at 17:09 Hrs on 02.08.2026. Subsequently, Dissolved Gas Analysis (DGA) of the transformer oil sample indicated a rising trend of acetylene (C₂H₂) concentration. Accordingly, the ICT was taken under shutdown at 18:11 Hrs on 04.08.2026 for carrying out further investigation and necessary corrective action.
132KV-RANGIT-SAGBARI-1	28-02-2026	Line was taken out to carry out necessary jumpering modification at Sagbari station to connect directly to Legship 220/132/66kV. The FTC of the line is pending in absence of necessary statutory clearance.
400KV-TEESTA-III-RANGPO-1	15-03-2026	Line is anti-theft charged from Rangpo end to Dikhchu extended via Teesta-III
400KV/220KV 315 MVA ICT 2 AT DSTPS(ANDAL)	03-05-2026	ICT has been shifted to KTPS.
400KV/220KV 315 MVA ICT 4 AT ARAMBAGH	29-05-2026	Tripped on buchholz protection.
220KV-KATAPALLI- BOLANGIR(PG)-1	17-06-2026	For system requirement
220KV-Rongnichu-RANGPO-1	18-06-2026	Dead end Tower No. 30 (at the boundary of Rangpo s/s) from the Rongnichu end has collapsed
220KV-SAHARSA(PMTL)- KHAGARIA(NEW)-2	14-07-2026	Distance protection operated Bihar: R phase, zone 1 , dist-52.77km IR-1.798kA IY-30.61A IB-27.60A. During tower-top patrolling, multiple polymer insulators found punctured.
400KV-BARH-MOTIHARI-2	21-07-2026	For tower dismantling and erection of tower at pile foundation at Location No. 27 (Athmal Gola, Barh, Patna).
400KV-BARH-MOTIHARI-1	21-07-2026	For tower dismantling and erection of tower at pile foundation at Location No. 27 (Athmal Gola, Barh, Patna).
220KV-SAHARSA(PMTL)- BEGUSARAI-2	14-08-2026	Emergency shutdown as one no pile leg with Raised chimney at Tower location no-99 was washed again by River flow
220KV-SAHARSA(PMTL)- BEGUSARAI-1	14-08-2026	Emergency shutdown as one no pile leg with Raised chimney at Tower location no-99 was washed again by River flow
132KV-MADHEPURA (BH)- SAHARSA-1	16-08-2026	To control the line loading. Line kept idle charged from Saharsa.
400KV-MALDA(PG)-NEW PURNEA-1	18-08-2026	Replacement of 405 89L(DBR) & 405 89T(Pantograph) Isolators of 400KV Malda-Purnea Ckt-I under ADDCAP at Malda Substation
400KV/220KV 315 MVA ICT 2 AT KODERMA	19-08-2026	DGA Violation
132KV-PATRATU-PATRATU- 2	21-08-2026	For permanently switching off / disconnection from PTPS S/Y. Currently idle charged from DVC end.
220KV-KISHANGANJ(PG)- KISHANGANJ(BSPTCL)-2	22-08-2026	Kishanganj(BH): R-N, Ir- 1.872kA, 9.804 km,

132KV-SAHARSA(PMTL)-Saharsa-1B(BH)-1	28-08-2026	Saharsa(PG) End:Y-B, Z-2, FCy: 3.5 kA, FCb:3.3 kA. Line is under patrolling.
765KV-DHARAMJAIGARH-JHARSUGUDA-1	30-08-2026	H/T ON VOLTAGE REGULATION
400KV/220KV 250 MVA ICT 1 AT TENUGHAT	31-08-2026	Differential Protection Operated

Deliberations in the meeting

Members noted.

4.3. Commissioning of new units and transmission elements in Eastern Grid in the month of August-2026

The details of new units/transmission elements commissioned in the month of August-2026 based on the inputs received from beneficiaries:

NEW ELEMENTS COMMISSIONED DURING July, 2026							
उत्पादन इकाइयाँ / GENERATING UNITS							
क्र. सं. Sl. No.	स्थान Location / Pooling Station	मालिक/यूनिट का नाम OWNER/UNIT NAME	यूनिट संख्या/स्रोत Unit No/Source	संकलित क्षमता (मेगावाट) Capacity added (MW)	कुल/स्थापित क्षमता (मेगावाट) Total/Installed Capacity (MW)	दिनांक DATE	टिप्पणी Remarks
1	TEESTA HPS	TEESTA HPS - UNIT 1	Hydro	170	510	12-07-2026 18:38	These units have been restored and recommissioned following the Glacial Lake Outburst Flood (GLOF) that occurred in October 2023.
2		TEESTA HPS - UNIT 2	Hydro	170	510	12-07-2026 21:02	
3		TEESTA HPS - UNIT 3	Hydro	170	510	15-07-2026 17:00	
आई.सी.टी./जी.टी./एस.टी. / ICTs/ GTs / STs							
क्र. सं. Sl. No.	एजेंसी/मालिक Agency/ Owner	उप-केन्द्र SUB-STATION	आईसीटी संख्या ICT NO	वोल्टेज (केवी) Voltage Level (kV)	क्षमता (एमवीए) CAPACITY (MVA)	दिनांक DATE	टिप्पणी Remarks
1	NIL						
प्रेषण लाइन / TRANSMISSION LINES							
क्र. सं. Sl. No.	एजेंसी/मालिक Agency/ Owner	लाइन का नाम LINE NAME	लंबाई (किमी) Length (KM)	कंडक्टर प्रकार Conductor Type	दिनांक DATE	टिप्पणी Remarks	
NIL							
लिलो / प्रेषण लाइन की पुनर्व्यवस्था / LILO/RE-ARRANGEMENT OF TRANSMISSION LINES							
क्र. सं. Sl.	एजेंसी/मालिक	लाइन का नाम / लिलो पर Line Name/LILO at	लंबाई (किमी) Length (KM)	कंडक्टर प्रकार Conductor Type	दिनांक DATE	टिप्पणी Remarks	

No .	Agency/ Owner					
1	PGCIL	400 kV New Purnea–Farakka S/C	171.62	ACSR Triple Snowbird	29-07-2026 12:05	The above transmission lines were charged as the 400 kV Farakka–Gokarna S/C line under an interim bypass arrangement to facilitate the execution of transmission strengthening works by POWERGRID.
2	PGCIL	400 kV New Purnea–Gokarna S/C	248.71	ACSR QUAD MOOSE	29-07-2026 13:19	
3	PGCIL	400KV-GAYA-KODERMA-1	125.966	ACSR QUAD MOOSE	27-07-2026 00:02	These D/C transmission lines were temporarily charged as the 400 kV Koderma–Maithon D/C transmission line for carrying out transmission strengthening works by PGCIL.
4	PGCIL	400KV-GAYA-KODERMA-2	125.966	ACSR QUAD MOOSE	27-07-2026 00:05	
5	PGCIL	400KV GAYA-MAITHON-1	275.665	ACSR QUAD MOOSE	27-07-2026 00:20	
6	PGCIL	400KV GAYA-MAITHON-2	01-10-1900	ACSR QUAD MOOSE	27-07-2026 00:21	
7	BSPTCL	132KV-SAHARSA(PMTL)-Saharsa-1B(BH)-1	30	Single Panther	24-07-2026	LILO of Saharsa-1B and Banmankhi(BH) at 132 kV Saharsa(PG)
बस/लाइन रिएक्टर / BUS/LINE REACTOR						
क्र . सं. Sl. No .	एजेंसी/ मालिक Agency/ Owner	एलेमेंट का नाम Element Name	उप-केन्द्र SUB-STATION	रेटिंग (एमवीएआर) Rating (MVA _r)	दिनांक DATE	टिप्पणी Remarks
1	NIL					
एच.वी.डी.सी/ए.सी फिल्टर बैंक/फैक्ट्स डिवाइस संबद्ध प्रणाली / HVDC /AC Filter bank / FACTS DEVICE associated System						
क्र . सं. Sl. No .	एजेंसी/ मालिक Agency/ Owner	एलेमेंट का नाम Element Name	उप-केन्द्र SUB-STATION	वोल्टेज (केवी) Voltage Level (kV)	दिनांक DATE	टिप्पणी Remarks
NIL						
बस - बे / BUS - BAYS						
क्र . सं. Sl. No .	एजेंसी/ मालिक Agency/ Owner	एलेमेंट का नाम Element Name	उप-केन्द्र SUB-STATION	वोल्टेज (केवी) Voltage Level (kV)	दिनांक DATE	टिप्पणी Remarks

I.N o.						
1	NHPC	400 kV GIS Bay: 405 (Bus Coupler Bay) at Teesta V	TEESTA V	4006V	29-07-2026	
2	NHPC	400 kV GIS Bay: 404 (Rangpo-II Bay) at Teesta V	TEESTA V	4006V	10-07-2026 01:15	
3	NHPC	400 kV GIS Bay: 406 (Rangpo-I Bay) at Teesta V	TEESTA V	4006V	29-07-2026	
NIL						

Deliberations in the meeting

Members noted.

4.4. UFR operation during the month of August 2026

Frequency profile for the month as follows:

MONTH	MAX	MIN	% LESS IEGC BAND	% WITHIN IEGC BAND	% MORE IEGC BAND
	(DATE/TIME)	(DATE/TIME)			
August 2026	50.30 (on 23-August-26 at 13:04 Hrs.)	49.53 (on 11-August-26 at 19:18 Hrs.)	7.59	77.15	15.26

Hence, no report of operation of UFR has been received from any of the constituents.

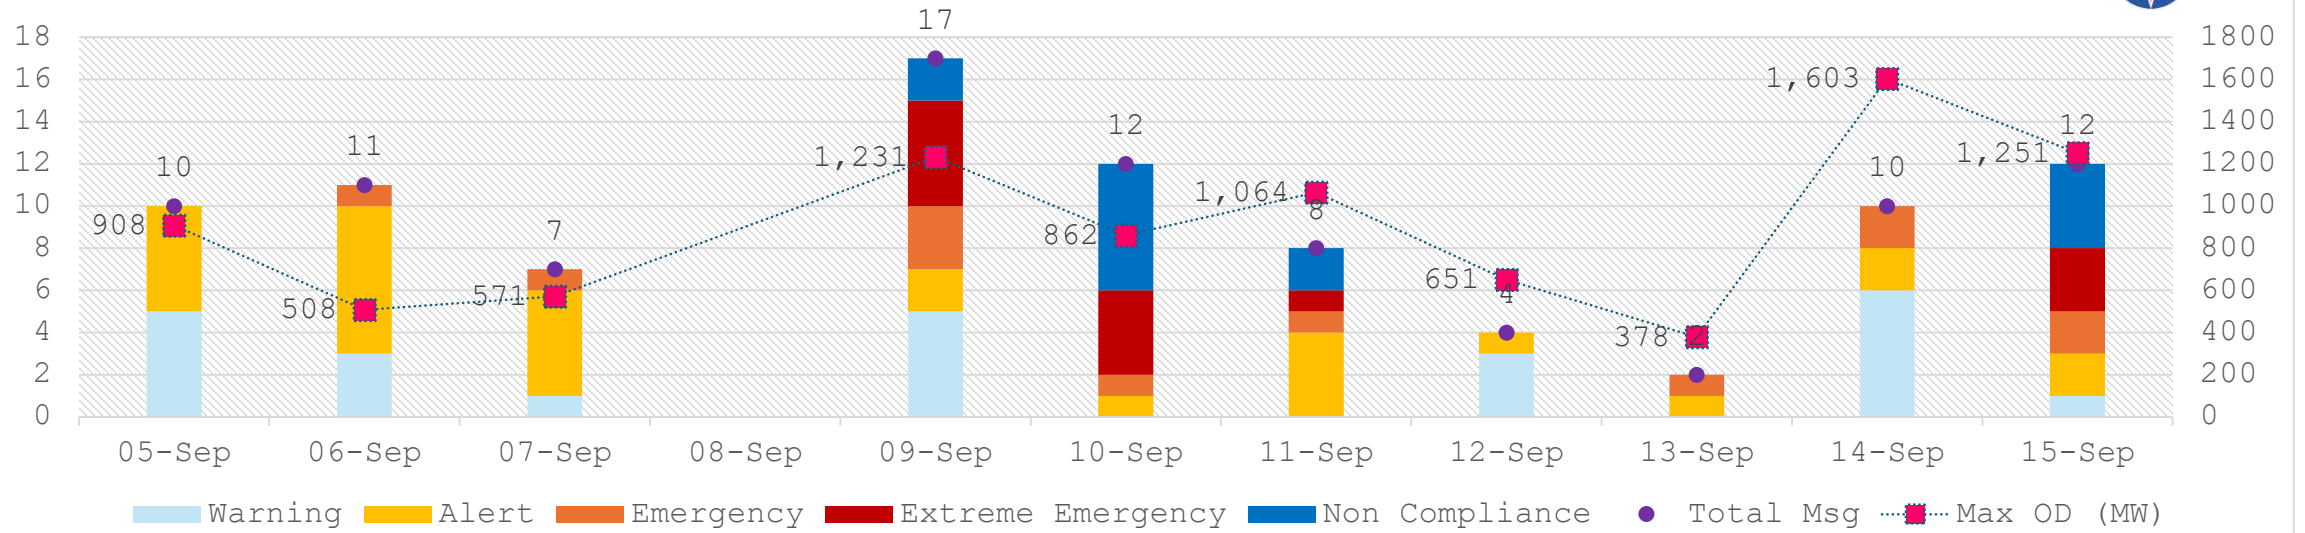
Deliberations in the meeting

Members noted.


Meeting ended with a vote of thanks to the chair.

Annex A


WB Performance 5-15th Sept 2026 (Low Freq period)



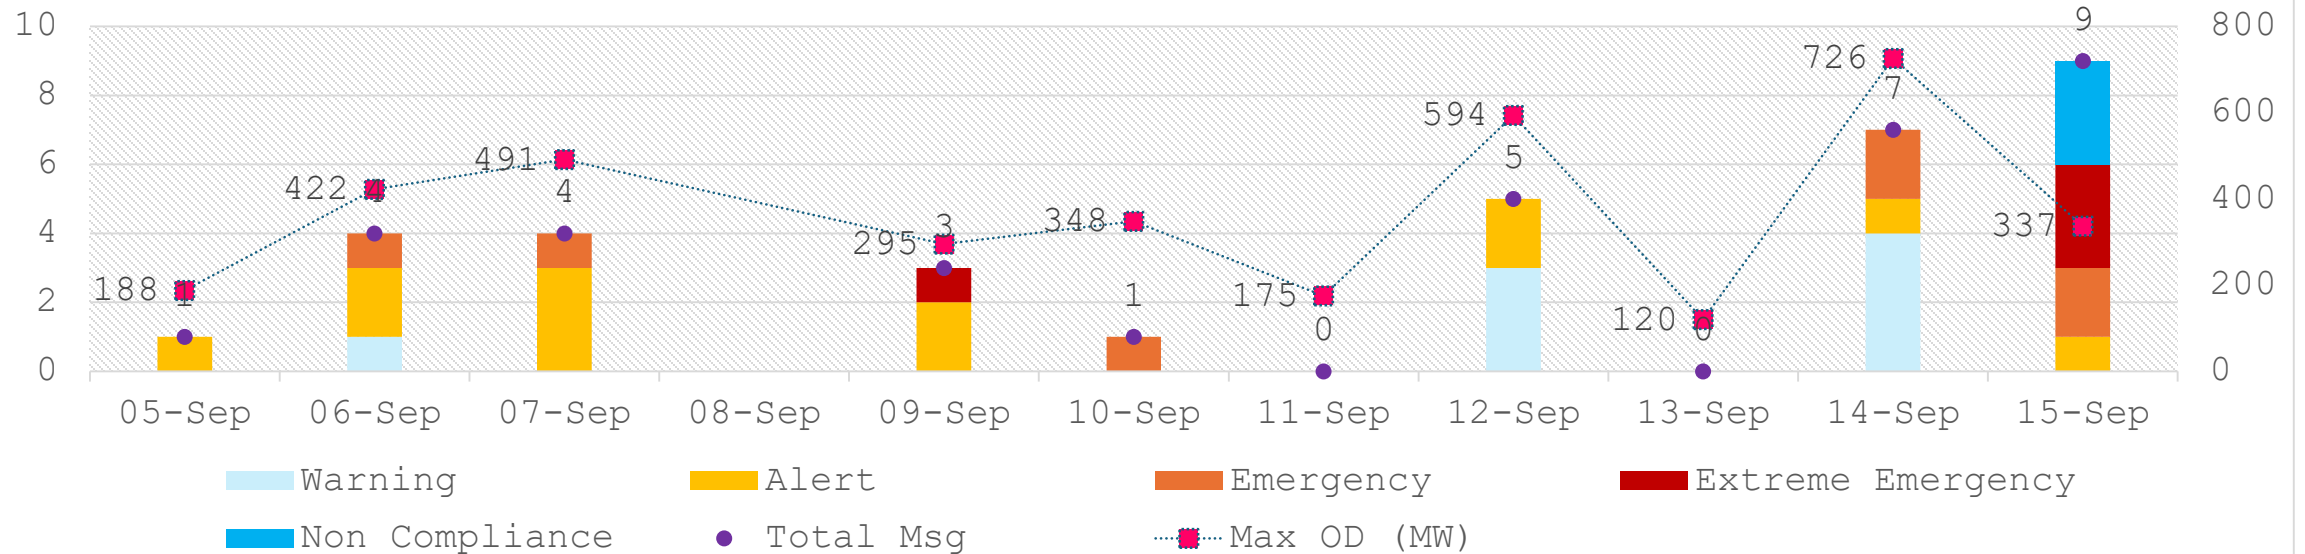
Bihar Performance 5-15th Sept 2026 (Low Freq period)



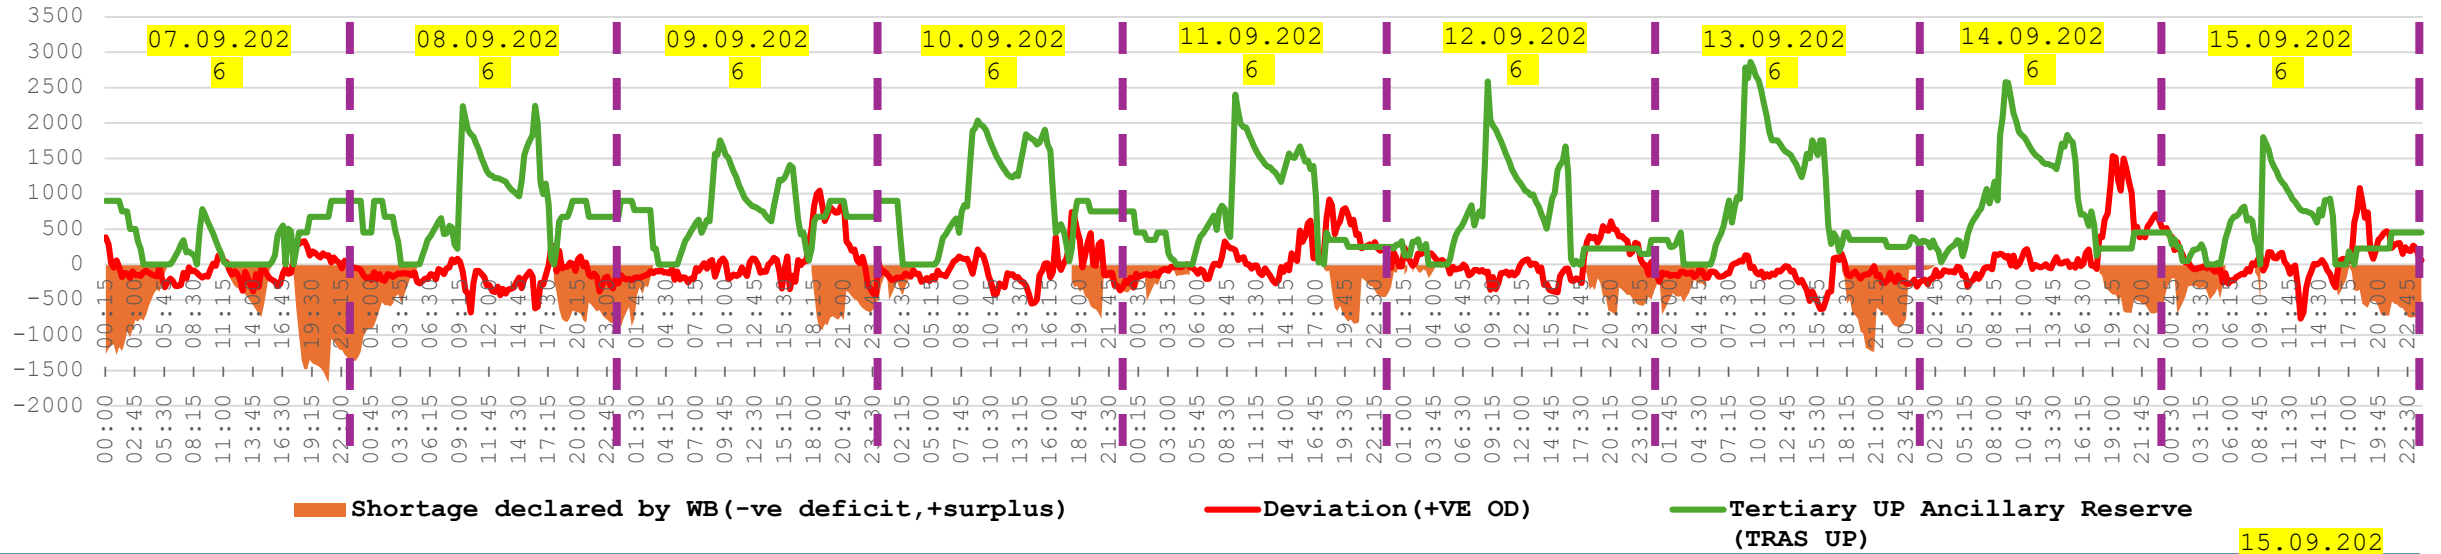WB declared adequacy Vs Deviation during 07.09.26 to 15.09.26



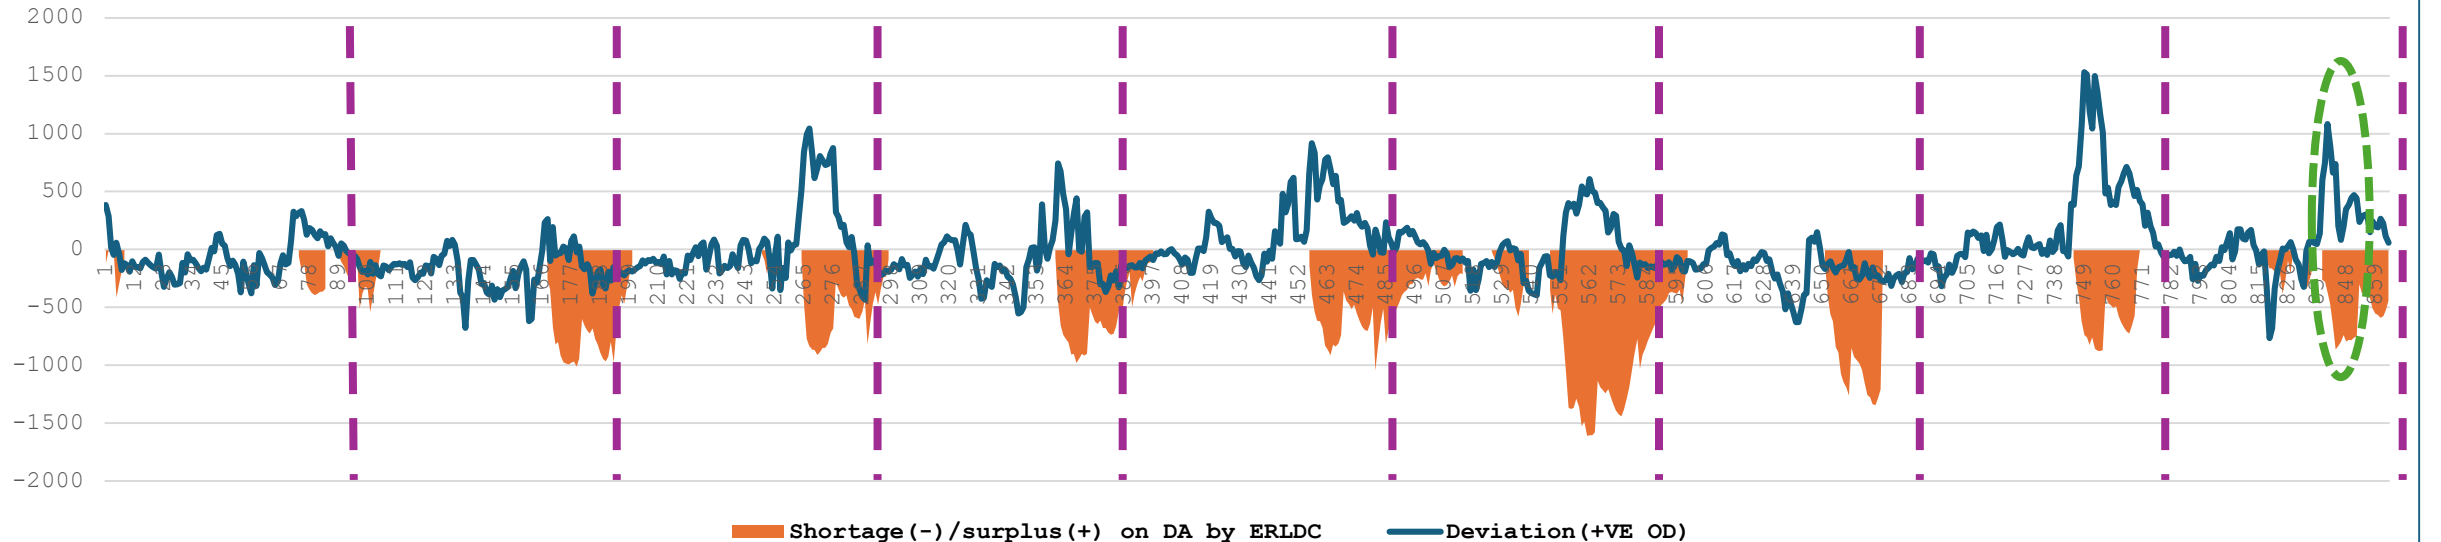ERLDC calculated adequacy Vs Deviation during 07.09.26 to 15.09.26












Annex B

Participants in 243rd OCC Meeting

Venue: ERPC Conference Hall, Kolkata

Time: 10:30 Hrs.

Date: 16.09.2026 (Wednesday)








Sl.	Name	Designation	Organisation	Contact No.	E-mail Id	Signature
1	K. B. Jagtap	Member Secretary	ERPC	8652776033	mserpc-power@nic.in	
2	S Banerjee	Executive Director	ERLDC	9433041823	surajit_banerjee@grid-india.in	
3	Debabrata Dasgupta	GM	ERLDC	9434740041	dbiswas@grid-india.in	
4	Bilash Achari	DGM	ERLDC	7003472016	bilash.achari@grid-india.in	
5	MANAS DAS	DGM	ERLDC, GRID-INDIA	9607070925	manasdas@grid-india.in	
6	Mahavir Prasad Singh	GM	ERLDC, GRID-INDIA	9729872327	mahavir@grid-india.in	
7	KAVITA PARIHAR	GM	ERLDC Grid India	9958114989	kanika@grid-india.in	
8	SOURAV MANDAL	CM	ERLDC GRID-INDIA	9402102353	Souravmandal@grid-india.in	
9	आशुतोष कुमार श्रीवास्तव	ए.जी.एम.	ए.टी.पी.सी. ए.टी.	9650908719	akshirivastava16@ntpc.co.in	
10	Prabanna Kumar Saha	AGM	NTPC Ltd, ER-243 Bhubaneswar	9437962430	prabannasaha@ntpc.co.in	
11	SHYAMAL MONDAL	AGM	NTPC - Kharagpur	9406712572	shyamalmondal@ntpc.co.in	
12	Sumit Narang	SE Mgr	NTPC ER-1 HQ	8005493953	sumitnarang@ntpc.co.in	
13	Rahul Piyadarni	DGM	NTPC Barahi	9472199246	rahulpiyadarni@ntpc.co.in	
14	D.K. MURALI	D.G.M	NTPC BARH	9494800877	kmadasari@ntpc.co.in	
15	Nakka Rambabu	Manager	NTPC Talcher Kandika	9337807358	makkarambabu@ntpc.co.in	

Participants in 243rd OCC Meeting

Venue: ERPC Conference Hall, Kolkata

Time: 10:30 Hrs.

Date: 16.09.2026 (Wednesday)













Sl.	Name	Designation	Organisation	Contact No.	E-mail Id	Signature
16	MANAS MONDAL	AGM (OS)	WBPDCL	8336903808	m.mondal@wbpdcl.co.in	 16.09.2026
17	Rajat Kr. Koley	Sr. Mgr (PS)	WBPDCL	9474860642	rkr.koley@wbpdcl.co.in	 16/9/26
18	Preetan Banerjee	ACE	WBSEDCL	7003871189	preetan72@gmail.com	
19	Roumak Kar	DE (E)	WBSEDCL	8906024332	roumak.kar@wbsecl.in	 16/09/2026.
20	SHOUVIK BANERJEE	CE, SLDC	WBSETCL	9434910379	ce.wbslde@gmail.com	
21	SANJIB ROY	ACE, SLDC	WBSETCL	9434910887	addiceslde@gmail.com	
22	UTSAB ADITYA	SE, SLDC	WBSETCL	9434910880	Utsabadiya@gmail.com	
23	ARNAB BASU	DE, SLDC	WBSETCL	9434910978	arnab.basu@wbsetcl.in	
24	DEBARSHI DE	DGM (SD)	CESC	9230521123	debarshi.de@rpsg.in	 16/09/26
25	SURAJIT ROY	Chief Mgr	HEL	8335067270	surajit.roy@rpsg.in	 16/9/26
26	SHEKHAR MAHAJAN	DGM (ICM)	JSWEUL	9552577251	shekhar.mahajan@jsw.in	
27	Shabari Pramanick	CM (ERLDC)	ERLDC	9007058764	shabari.pramanick@grid-india.in	
28	Animesh Mukhopadhyay	VP	JIPL	9583040198	headonm_orissa@jindalgroup.com	
29	Amit Kr. Gupta	DM	JIPL	9681335196	JIPLScheduling@jindalgroup.com	
30	TUNESHWAR KUMAR	SR. MANAGER	JUSNL	9431190306	tuneshwar.kumar@gmail.com	

Participants in 243rd OCC Meeting

Venue: ERPC Conference Hall, Kolkata

Time: 10:30 Hrs.

Date: 16.09.2026 (Wednesday)


Sl.	Name	Designation	Organisation	Contact No.	E-mail Id	Signature
31	Raju Kachhap	Senior Manager	SLDC, Ranchi (JUSNL)	7783087568	rajmaifme82@gmail.com	
32	Gagan Kumar	E. Ex. E.	SLDC, BSPTCL	7992486100	gaganbushra@gmail.com	
33	Alok Kumar Moharana	GM (EI)	OPTCL	9438907246	ele. akmaharana@optcl.co.in	
34	CHANDAN MALLICK	CM (SO)	ERLDC, GRID-SW DEA	7278756275	chandan.mallik@grid-india.in	
35	ALOK PRATAP SINGH	CM (SS)	ERLDC	8874707077	apbsingh@grid-india.in	
36	S. K. Sharma	Sr. Gen & HOD	DVC	9434533423	sanjay.sharma@dvc.gov.in	
37	S. K. Panda	manager	"	6370134294	sanku.panda@dvc.gov.in	
38	PARITHA GHOSH	Dehon	ER-1	9434748263	partha.ghosh@powergrid.in	
39	RAMESH KR. PRADHAN	DGM	ERLDC, GRID-INDIA	9831337570	rkpradhan@grid-india.in	
40	D. K. Khuntia	AD	ERPC	7683889161	dellip.khunti.cea@gov.in	
41	P P Jena	EE	ERPC	9776198991	ppjena.erpca@gov.in	
42	P. K. DE	SE	ERPC	9831620142	secommf.erpca@gov.in	
43	I. K. MEHRA	SE	ERPC	9810688789	ikmehra@nic.in	
44	J. K. Panda	AEF	ERPC	9151621295	jkpande.cea@gov.in	
45	Diptikanta Panda	Manager	GMR	8114918762	Diptikanta.Panda@gmrgroup.in	

Participants in 243rd OCC Meeting

Venue: ERPC Conference Hall, Kolkata

Time: 10:30 Hrs.

Date: 16.09.2026 (Wednesday)

Sl.	Name	Designation	Organisation	Contact No.	E-mail Id	Signature
46	Abhishek Das	AST	TCS	943385015	das.abhishek2@tcs.co	
47	S C De	CGM	ERLDC	9436385869	sdc@erlde.in	
48	BS Ray	DD	ERPC			
49	A. Chatterjee	AEE	ERPC			
50						
51						
52						
53						
54						
55						
56						
57						
58						
59						
60						

Sr. no.	DISCOM	GSS (Substation)	33kV Feeder	Normal Load (MW)	Site / Controller Action	Already in ADMS feeder list?	New wiring need to do?	feeder addition	EMR Testing	Remarks
1	TPCODL	CHANDAKA	BARANGA	13.16	Reuse ADMS controller	No (new)	no wiring			NO WIRING NEEDED
2	TPCODL	CHANDPUR	CHANDPUR	5.35	Reuse ADMS controller	No (new)	check			
3	TPCODL	CHOUDWAR	IDCO	10.29	Reuse ADMS controller	No (new)	do wiring	DONE	PENDING	
4	TPCODL	CUTTACK	BENTKAR	8.54	Reuse ADMS controller	No (new)	do wiring	DONE	DONE	
5	TPCODL	DHENKANAL	DHENKANAL TOWN	9.29	Reuse ADMS controller	No (new)	do wiring			
6	TPCODL	JAGATSINGPUR	JAGATSINGPUR	13.07	Reuse ADMS controller	No (new)	do wiring	DONE	DONE	
7	TPCODL	KESURA	BALAKATI	12.52	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
8	TPCODL	KESURA	SBI	13.28	Reuse ADMS controller	No (new)	do wiring	DONE	PENDING	
9	TPCODL	KHAJURIAKATA	HINDOL	7.59	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
10	TPCODL	KONARK	BANGURIGAON	2.98	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
11	TPCODL	KONARK	GOP	3.57	Reuse ADMS controller	No (new)	do wiring			
12	TPCODL	KONARK	SUTAN	0.06	Reuse ADMS controller	No (new)	do wiring			
13	TPCODL	MANIA	INDUSTRIAL	5.84	Reuse ADMS controller	No (new)	do wiring	DONE	PENDING	
14	TPCODL	MENDHASAL	GOTHAPATANA	6.81	Reuse ADMS controller	No (new)	do wiring			
15	TPCODL	NARASHINGPUR	MARDAMUKHA	2.01	NEW installation	No (new)	do wiring			
16	TPCODL	NAYAGARH	GODIPADA	1.95	NEW installation	No (new)	do wiring			
17	TPCODL	NAYAGARH	LATHIPADA	2.26	NEW installation	Yes — verify	do wiring			
18	TPCODL	NAYAGARH	MACHIPADA	5.55	NEW installation	No (new)	do wiring			
19	TPCODL	NIMAPADA/DIG HALO	ABHAYAMUKHI	7.96	Reuse ADMS controller	No (new)	do wiring			
20	TPCODL	NIMAPADA/DIG HALO	PIPLI	5.94	Reuse ADMS controller	No (new)	do wiring			
21	TPCODL	NUAPATNA	TIGIRIA	7.55	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
22	TPCODL	OLAVER	RAJAKANIKA	3.91	Reuse ADMS controller	No (new)	no wiring			NO WIRING NEEDED
23	TPCODL	PARADEEP	INDUSTRIAL	11.54	Reuse ADMS controller	No (new)	do wiring	DONE	DONE	
24	TPCODL	PARADEEP	JHIMANI	3.88	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
25	TPCODL	PATTAMUNDAI	PATTAMUNDAI	8.17	Reuse ADMS controller	No (new)	do wiring			NO WIRING NEEDED
26	TPCODL	PATTAMUNDAI	RAJNAGAR	1.96	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
27	TPCODL	PHULNAKHARA	BANAMALIPUR	5.24	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
28	TPCODL	RAJNAGAR/KUNDUPUR	ADHAJORI	5.00	NEW installation	No (new)	do wiring			
29	TPCODL	SALIPUR	JAPAKUDA	6.10	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
30	TPCODL	SAMUKA	CHARINALA	2.21	Reuse ADMS controller	No (new)	do wiring			
31	TPCODL	TIRTOL	GORADA	6.46	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
32	TPNODL	BALASORE	BALGOPALPUR	10.00	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED

33	TPNODL	BALASORE	ODANGI	13.00	Reuse ADMS controller	No (new)	do wiring			
34	TPNODL	BALASORE	RUPSA	11.00	Reuse ADMS controller	No (new)	do wiring			
35	TPNODL	BANGIRIPOS	SARAGCHIDA	3.00	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
36	TPNODL	BARIPADA	CHANCHA (INDUSTRIAL)	8.00	Reuse ADMS controller	No (new)	do wiring			
37	TPNODL	BARIPADA	RAGHUNATHPUR	6.00	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
38	TPNODL	BARIPADA	SHAMAKHUNTA	5.00	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
39	TPNODL	BASTA	BALIAPAL	14.00	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
40	TPNODL	BASTA	RAJGHAT	10.00	Reuse ADMS controller	No (new)	do wiring			
41	TPNODL	BETANOTI	BADASAH	5.00	Reuse ADMS controller	No (new)	do wiring			
42	TPNODL	BETANOTI	BETANOTI-2	14.00	Reuse ADMS controller	No (new)	do wiring			
43	TPNODL	BHOGRAI	KAMARDA NEW	12.00	Reuse ADMS controller	No (new)	do wiring	DONE	DONE	
44	TPNODL	CHANDIPUR	SARAGAN	8.00	NEW installation	No (new)	do wiring			
45	TPNODL	CHANDIPUR	SWADHINPADIA	18.00	NEW installation	No (new)	do wiring			
46	TPNODL	JALESWAR	BARTANA	3.00	Reuse ADMS controller	No (new)	do wiring			NO WIRING NEEDED. BARTANA FEEDER ALREADY CLUBED WITH BHOGRAI
47	TPNODL	JALESWAR	HATIGARH	9.00	Reuse ADMS controller	No (new)	do wiring			NO WIRING NEEDED. HATIGARH FEEDER ALREADY CLUBED WITH BASTA
48	TPNODL	RAIRANGPUR	GORUMAHISANI	4.00	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
49	TPNODL	RAIRANGPUR	KUSUMI	5.00	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
50	TPNODL	SOMNATHPUR	NEW NILAGIRI	6.00	NEW installation	No (new)	do wiring	DONE	PENDING	NEW PANEL INSTALLATION DONE.
51	TPNODL	SORO	JAMUJHADI	7.00	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
52	TPNODL	SORO	KHAIRA	19.00	Reuse ADMS controller	No (new)	do wiring			
53	TPNODL	UDALA	BERHAMPUR	3.00	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
54	TPNODL	UDALA	KHUNTA	8.00	Reuse ADMS controller	Yes — verify	no wiring			NO WIRING NEEDED
			TOTAL	401.04						

TOTAL NO. OF FEERERS	54
NEW FEEDER INTEGRATION (UNDER 5 S/S)	8
NO WIRING REQUIRED	24
WIRING COMPLETED	8
PENDING	22

Annex B.2.1.(b))

Status of DVC Units under Phase-I Implementation

As per the phasing plan notified under the CEA (Flexible Operation of Coal based Thermal Generating Units) Regulations, 2023, BTPS Unit #A (500 MW) and RTPS Unit #2 (600 MW) were covered under Phase-I, with the implementation period from July 2024 to June 2026.

1. Flexible Operation Solutions at BTPS Unit #A (500 MW)

- To enable flexible operation and compliance with CEA requirements, Work Order No. GEMC-511687795492297 dated 19.12.2024 was awarded to M/s BHEL for implementation of flexible operation solutions at BTPS Unit #A.

The following major works have been completed:

- APC system commissioning activities were carried out by BHEL PSER and BHEL-EDN engineers during June 2026.
- **Stable operation at 40% TML without oil support through APC was successfully demonstrated on 15.06.2026 for 1 hour 30 minutes and on 17.06.2026 for 3 hours, with all process parameters remaining within acceptable limits during flexibility trial test in coordination with M/s BHEL.**
- **Ramp rate trials were completed with achieved ramp rates of:**
 - **2.93% in 70% to 100% TMCR range**
 - **2% in 55% to 70% TMCR range**
 - **1% in 40% to 55% TMCR range**
- Stall logic for FD Fans and PA Fans has been incorporated in DCS, along with alarm configuration and display on respective DCS pages.
- In one TDBFP, the existing ON/OFF recirculation valve has been replaced with a modulating control valve, and associated control logic has been implemented.
- Materials for BOSMON system have been received at site. Installation and commissioning are planned during the next scheduled overhauling of the unit from 25.03.2027 to 23.04.2027.

2. Flexible Operation Solutions at RTPS Unit #2 (600 MW)

RTPS Unit #2 is the first 600 MW SEC-manufactured unit in DVC. The Boiler, Turbine and Generator were supplied by Shanghai Electric Corporation (SEC), China. hence, before any upgradation/retrofitting, feasibility test for flexible operation has been

considered before implementing any retrofit or upgradation measures for flexible operation.

Accordingly, Work Order No. GEMC-511687782454419 dated 10.11.2025 was awarded to M/s Siemens Energy India Limited for carrying out a Feasibility Test for Flexible Operation of RTPS Unit #2.

The feasibility test is scheduled to be conducted in Sept 2026, after completion of the ongoing Capital Overhauling of the unit.

Further, in the 56th TCC Meeting held on 25.05.2026, DVC informed ERPC that RTPS Unit #2 is facing challenges due to non-availability of OEM support and tuning for flexible operation has not yet been undertaken. DVC also informed that MTPS Unit #7 has successfully demonstrated 40% MTL operation for 4 hours and requested that MTPS Unit #7 may be considered as a substitute for RTPS Unit #2 for meeting CEA flexible operation requirements.

In the Deliberation, TCC advised DVC to expedite implementation of 40% MTL operation at the earliest and agreed that MTPS Unit #7 may be considered as a substitute for RTPS Unit #2 to meet CEA flexible operation requirements, while ensuring continuous operation of units as per system requirement, particularly during non-solar hours.

3. Flexible Operation Solutions at MTPS Unit #7 (500 MW):

Mejia TPS Unit #7 (500 MW) has successfully demonstrated operation at 40% Technical Minimum Load (TML) and sustained the load continuously for four hours, in line with CEA guidelines for flexible operation.

Present Status:

- APC System installation done. Installation of APC panels has been completed, and control loop configuration and tuning activities carried out.
- **On 26.09.2025, the unit successfully achieved a technical minimum load of 200 MW (40% TML) without oil support and sustained operation continuously for (4) four hours, in compliance with CEA flexible operation guidelines during flexibility trial test in coordination with M/s BHEL.**
- Stall Protection installed in MTPS U#7, Commissioning is to be done.

- In both TDBFP, the existing ON/OFF recirculation valve has been successfully replaced with a modulating control valve, and the associated control logic has been implemented.
- Materials for the BOSMON system have been received and installed at site. Thermocouples have been installed in Boiler during overhauling. Commissioning is to be done.

Issues noted during Flexible operation and running at 40% TML of DVC Units

1. Coal Quality Issues:

DVC units receive coal from multiple sources with significant variations in Gross Calorific Value (GCV), Volatile Matter (VM), ash content, and moisture. These variations adversely affect combustion stability, flame sustainability, and boiler performance at low loads, making it difficult to reliably maintain unit operation at 40% TML on a continuous basis.

2. Although the recommendations given by the OEM, Bharat Heavy Electricals Limited, for flexible operation have been implemented, several operational challenges are noted during operation at 40% Technical Minimum Load (TML) and during ramping operations, as detailed below:
 - During ramp-up and ramp-down operations (2–3% loading/unloading), the Superheater (SH) temperature spray control system continues to face difficulty in maintaining Main Steam (MS) and Reheater (RH) temperatures within the permissible standard deviation limits. This ultimately imposes additional thermal stress on boiler pressure parts, turbine components, and other critical equipment. At 200 MW, the HRH steam temperature reduced to approximately 499–500°C, which was below the design operating requirement.
 - Flame stability issues are frequently encountered during low-load operations with low VM Coal.
 - Consecutive ramp-up and ramp-down operations in successive 15-minute blocks are generally not feasible. The unit requires adequate stabilization time before initiation of the next ramping cycle; hence, a suitable stabilization period is essential between successive ramping operations.
 - During ramp-up and ramp-down operations, Boiler metal temperature excursions have been observed in the Divisional Panel Superheater tubes, which may adversely affect the residual life and long-term reliability of these components.
 - IP Control valve throttling: Below 250 MW, IPCV throttling commenced. At 200 MW, both IPCVs were reported throttled to approximately 65% in MTPS U#7.

- Proper distribution of coal flow among the running feeders could not be maintained. Higher loading of the base mill was required for flame stability.

The above operational constraints associated with frequent ramp-up and ramp-down operations increase the likelihood of Boiler Tube Leakage (BTL) incidents and impose additional thermal and mechanical stresses on critical boiler and turbine components, thereby adversely affecting unit performance, reliability, operational safety, and long-term equipment health.

3. Continuous operation at 40% TML with results in increased thermal and mechanical stress on boiler and turbine components. Such operating conditions accelerate component degradation and fatigue, thereby affecting equipment reliability and potentially reducing the overall service life of the plant.



JINDAL INDIA POWER LIMITED

(Formerly known as Jindal India Thermal Power Limited)
Regd. off: Habitat India, C-3, Qutab Institutional Area,
Katwaria Sarai, New Delhi- 110016, Phone: 011-40841950
Website: www.jitpl.com,

Ref: JIPL/ERPC/Sept'26/09/127

Date:05/09/2025

To
Member Secretary,
Eastern Regional Power Committee,
14, Golf Course Road, Tollygunj,
Kolkata-700033

Sub: Operational Difficulties of Thermal Power Plants in Operating at 40% Technical Minimum – JIPL Inputs

Ref: Mail received from ERPC regarding **Operational difficulties of Thermal power plants in operating at 40% technical minimum** on dated 17.09.2026.

Dear Sir/Madam,

This is with reference to your trailing email regarding submission of specific operational difficulties being faced/envisaged by thermal generating stations operating at **40% Technical Minimum Load**. In this regard, we would like to submit that both units of **Jindal India Power Limited (JIPL)** fall under **Phase-II** of the implementation plan for operation at 40% technical minimum. As per the applicable implementation schedule, **Unit #1 is required to comply by March 2027 and Unit #2 by November 2027.**

Currently, JIPL has taken necessary steps to achieve stable and reliable operation of its units at the prescribed technical minimum limit of 55%. However, based on our assessment of the plant design configuration and operating experience, the following technical and operational difficulties are envisaged while operating the units below 55%:

1. **OEM (BHEL)/APC Support:** Presently, the requisite support from the OEM, M/s BHEL, for operating units below 55% is not available due to ongoing legal issues. In the absence of necessary **technical support from BHEL**, upgradation or migration to any new system through an alternative technology provider would not be prudent for sustainable safe operation.
2. **Flame Stability and Coal Quality:** Maintaining stable combustion at such low load may be difficult due to continuous variations/inconsistency in the quality of domestic coal, which can adversely affect flame stability and will lead to flame failures.
3. **Boiler Metal Temperature Excursions:** Frequent ramp-up/ramp-down operation coupled with sustained low-load operation may result in boiler metal temperature excursions, posing challenges in maintaining the recommended operating parameters and would badly impact equipment reliability as they are not designed to operate to meet flexibility.
4. **Wind-box Pressure:** Maintaining adequate wind-box pressure at below 55% load may be operationally challenging and could adversely affect combustion stability.
5. **Operation of Critical Auxiliaries:** Operation of units at 40% technical minimum will require stopping one set of auxiliaries such as **FD/ID/PA Fans, BFPs, CEPs, etc.,** thereby increasing



JINDAL INDIA POWER LIMITED

(Formerly known as Jindal India Thermal Power Limited)

Regd. off: Habitat India, C-3, Qutab Institutional Area,
Katwaria Sarai, New Delhi- 110016, Phone: 011-40841950
Website: www.jitpl.com,

operational interventions and having implications for unit reliability without modifying system logics and auto loops. Also frequently start and stop of above-mentioned auxiliaries will lead to further unstability of plant.

6. **Mill Trip at Lower Load:** At lower operating load, tripping of any one running coal mill will make it difficult to maintain furnace stability and could expose the unit to operational instability/Tripping
7. **High Exhaust Temperature in HP Turbine:** Sustained low-load operation may result in high exhaust temperature in the HP Turbine, requiring close monitoring and appropriate operational safeguards.
8. **TDBFP/Auxiliary PRDS Operation:** Sustainable operation of the **Turbine Driven Boiler Feed Pump (TDBFP) through Auxiliary PRDS below 50% unit load** is another area of technical concern requiring appropriate system assessment and stabilization.

It is to re-iterate that all above actions require intervention of the BTG-OEM (M/s BHEL) to mitigate various risks for sustainable and safe operation of units. Further, implementation of APC for achieving reliable operation at 40% technical minimum requires a systematic process involving **baseline assessment/mapping, technology finalization, detailed engineering, implementation, commissioning and stabilization which would not be possible without OEM support.**

In addition to the above technical issues, we would also like to highlight the **commercial implications of sustained low-load operation.** Appropriate **Heat Rate and Auxiliary Power Consumption (APC) compensation for operation of units below 55% load is presently not available to Section 63 generating stations.** Operation at 40% technical minimum is expected to result in further deterioration in operating heat rate and auxiliary consumption and will lead to increase in operational & maintenance costs. In the absence of an appropriate compensation mechanism, sustained operation of these units below 55% may therefore will be commercially unviable.

JIPL is committed to meeting the existing prescribed technical minimum requirements and is exploring the necessary technical assessment and preparatory actions to reduce it further. However, the above operational, equipment reliability and commercial aspects may kindly be taken into consideration while finalizing/implementing the framework for sustained operation of thermal generating units at **40% / below 55% technical minimum.**

We request ERPC to kindly take the above input on record for further deliberation at the ensuing NPC meeting.

For Jindal India Power Limited
(Formerly known as Jindal India Thermal Power Limited)

Authorized Signatory

Annex B.2.1.d

ICT status

State	Utility	Voltage Rating (kV)	Capacity (MVA)	Total Installed ICT	Spares required as per CERC guidelines	Spares available	Quantity under procurement	Order Placed (Y/N)	Tentative Delivery (MM-YY)	Remarks
Bihar	BSPTCL	400/220	500							
Bihar	BSPTCL	400/220	315							
Bihar	BSPTCL	400/220	105							
Bihar	BSPTCL	400/132	315							
Bihar	BSPTCL	400/132	200							
Bihar	BSPTCL	220/132	200							
Bihar	BSPTCL	220/132	160							
Bihar	BSPTCL	220/132	100							
Bihar	BSPTCL	132/66	50							
Bihar	PG ER-I	400/220	500							
Bihar	PG ER-I	400/220	315							
Bihar	PG ER-I	400/220	105							
Bihar	PG ER-I	400/132	315							
Bihar	PG ER-I	400/132	200							
Bihar	PG ER-I	220/132	200							
Bihar	PG ER-I	220/132	160							
Bihar	PG ER-I	220/132	100							
Bihar	PG ER-I	132/66	50							
Jharkhand	JUSNL	400/220	500							
Jharkhand	JUSNL	400/220	315							
Jharkhand	JUSNL	400/220	105							
Jharkhand	JUSNL	400/132	315							
Jharkhand	JUSNL	400/132	200							
Jharkhand	JUSNL	220/132	200							
Jharkhand	JUSNL	220/132	160							
Jharkhand	JUSNL	220/132	100							
Jharkhand	JUSNL	132/66	50							
Jharkhand	PG ER-I	400/220	500							
Jharkhand	PG ER-I	400/220	315							
Jharkhand	PG ER-I	400/220	105							
Jharkhand	PG ER-I	400/132	315							
Jharkhand	PG ER-I	400/132	200							
Jharkhand	PG ER-I	220/132	200							
Jharkhand	PG ER-I	220/132	160							
Jharkhand	PG ER-I	220/132	100							
Jharkhand	PG ER-I	132/66	50							
Sikkim	PG ER-II	400/220	500							
Sikkim	PG ER-II	400/220	315							

State	Utility	Voltage Rating (kV)	Capacity (MVA)	Total Installed ICT	Spares required as per CERC guidelines	Spares available	Quantity under procurement	Order Placed (Y/N)	Tentative Delivery (MM-YY)	Remarks
Sikkim	PG ER-II	400/220	105							
Sikkim	PG ER-II	400/132	315							
Sikkim	PG ER-II	400/132	200							
Sikkim	PG ER-II	220/132	200							
Sikkim	PG ER-II	220/132	160							
Sikkim	PG ER-II	220/132	100							
Sikkim	PG ER-II	132/66	50							
Sikkim	Sikkim	400/220	500							
Sikkim	Sikkim	400/220	315							
Sikkim	Sikkim	400/220	105							
Sikkim	Sikkim	400/132	315							
Sikkim	Sikkim	400/132	200							
Sikkim	Sikkim	220/132	200							
Sikkim	Sikkim	220/132	160							
Sikkim	Sikkim	220/132	100							
Sikkim	Sikkim	132/66	50							
Odisha	OPTCL	400/220	500							
Odisha	OPTCL	400/220	315							
Odisha	OPTCL	400/220	105							
Odisha	OPTCL	400/132	315							
Odisha	OPTCL	400/132	200							
Odisha	OPTCL	220/132	200							
Odisha	OPTCL	220/132	160							
Odisha	OPTCL	220/132	100							
Odisha	OPTCL	132/66	50							
Odisha	PG Odisha	400/220	500							
Odisha	PG Odisha	400/220	315							
Odisha	PG Odisha	400/220	105							
Odisha	PG Odisha	400/132	315							
Odisha	PG Odisha	400/132	200							
Odisha	PG Odisha	220/132	200							
Odisha	PG Odisha	220/132	160							
Odisha	PG Odisha	220/132	100							
Odisha	PG Odisha	132/66	50							
West Bengal	CESC	400/220	500							
West Bengal	CESC	400/220	315							
West Bengal	CESC	400/220	105							
West Bengal	CESC	400/132	315							
West Bengal	CESC	400/132	200							

ICT status

State	Utility	Voltage Rating (kV)	Capacity (MVA)	Total Installed ICT	Spares required as per CERC guidelines	Spares available	Quantity under procurement	Order Placed (Y/N)	Tentative Delivery (MM-YY)	Remarks
West Bengal	CESC	220/132	200							
West Bengal	CESC	220/132	160							
West Bengal	CESC	220/132	100							
West Bengal	CESC	132/66	50							
West Bengal	PG ER-II	400/220	500							
West Bengal	PG ER-II	400/220	315							
West Bengal	PG ER-II	400/220	105							
West Bengal	PG ER-II	400/132	315							
West Bengal	PG ER-II	400/132	200							
West Bengal	PG ER-II	220/132	200							
West Bengal	PG ER-II	220/132	160							
West Bengal	PG ER-II	220/132	100							
West Bengal	PG ER-II	132/66	50							
West Bengal	WBSETCL	400/220	500							
West Bengal	WBSETCL	400/220	315							
West Bengal	WBSETCL	400/220	105							
West Bengal	WBSETCL	400/132	315							
West Bengal	WBSETCL	400/132	200							
West Bengal	WBSETCL	220/132	200							
West Bengal	WBSETCL	220/132	160							
West Bengal	WBSETCL	220/132	100							
West Bengal	WBSETCL	132/66	50							

Annex B.2.1.e**ଓଡିଶା ବିଦ୍ୟୁତ୍ ଶକ୍ତି ସଂଚାରଣ ନିଗମ ଲି.8.****ODISHA POWER TRANSMISSION CORPORATION LIMITED**

(A Government of Odisha Undertaking)

O/O THE CHIEF GENERAL MANAGER (O&M), BHUBANESWAR**Registered Office: Janpath, Bhubaneswar- 751007**Telephone: (0674) 2542479 (EPABX), Website: www.optcl.co.inCIN - U40102OR2004SGC007553, e-mail: cgm.onm@optcl.co.in**TW-CGM (O & M)-168/2026/1713⁽³⁾****Dt. 18/09/2026****To**

The Member Secretary
 Eastern Regional Power Committee (ERPC)
 14, Golf Club Road, Tollygunge, Kolkata – 700033

Sub: Submission of progress status of HTLS reconductoring works and ICT new/augmentation plan of OPTCL - compliance to deliberations in the 243rd OCC Meeting.

Ref: 243rd OCC Meeting of ERPC held on 16.09.2026 at Kolkata.

Sir,


With reference to the deliberations in the 243rd OCC Meeting of ERPC held on 16.09.2026 at Kolkata, the progress of HTLS reconductoring works under the OPTCL transmission network and the plan for installation of new Inter-Connecting Transformers (ICTs) / augmentation of existing ICT capacity were apprised during the meeting.

Accordingly, the updated progress status of the HTLS reconductoring works and the ICT new/augmentation plan of OPTCL are enclosed herewith for kind information and onward submission to the appropriate forum.

It is requested that the enclosed status statements may kindly be taken on record as compliance to the deliberations of the 243rd OCC Meeting.

Yours faithfully,

Encl.: As above.


Chief General Manager (O&M)
Copy to:

1. Sr.PS to CMD, OPTCL for kind appraisal of CMD.
2. Director (Operation), OPTCL, Bhubaneswar – for kind information.

HTLS RECONDUCTORING STATUS_OPTCL_18.09.2026		
Sl. No.	Project	Status
1	400kV IB-Lapanga HTLS Up-gradation Estimated Cost: ₹ 97.82 Cr.	LOA Placed to M/s K. Ramachandra Rao on 09.09.2026 (JV with M/s Paramount) Completion Period: 10Months form LOA Cost: 90.23 Cr.
2	220kV Lapanga-Katapali HTLS Up-gradation (47.52RkM) Estimated Cost: ₹ 82.08 Cr.	LOA Placed to M/s K. Ramachandra Rao on 31.08.2026 Completion Period: 10Months form LOA Cost: 72.55 Cr.
3	220kV Lapanga-Budhipadar HTLS Up-gradation (18.2 RKM) Estimated Cost: ₹ 32.75 Cr.	LOA Placed to M/s Paramount on 31.08.2026 Completion Period: 6Months form LOA Cost: 28.56 Cr.
4	HTLS Upgradation in 132kV Burla-Katapali (Ckt-I & II) (OTSSP-II Scheme)	Tender Cancelled
5	Stringing of HTLS Conductor(9.12 rkm) after dismantling of ACSR Panther Conductor in existing 132 KV Lapanga-Aryan Viraj-Shyam DRI SC line along with up-gradation of requisite bay equipment in Jharsuguda District on Turnkey contract basis	LOA Placed on 14.07.02026 to M/s Paramount Schedule for Completion: 06 Months from LOA
6	Stringing of HTLS Conductor after dismantling of twin AAAC Moose Conductor in existing 400 KV Meramundali-Mendhasal DC Line along with up-gradation of equipment and Bus at respective Grid Sub-station ends (Approx. Line Length- 100.5 Route KM) on Turnkey contract basis	Tender floated.
7	132kV Katapali-Thuapali-Bargarh (Awarded to: M/s Paramount Communications Ltd.) Awarded Cost: ₹ 43.76 Cr.)	W.O. Awarded to: M/s Paramount Communications Ltd. on 15.04.2026 Preliminary Survey Completed.
8	132kV Cuttack - Jagatsinghpur line HTLS Up-gradation EPC: M/s Sterlite Power Tr. Ltd., LoA – 31-12-2024, SoC – 30-06-2025 Cost:- ₹23.52 Cr.	Work Under Progress Foundation : 3/3 completed, Erection: 3/3 Stringing: 26.574/35.65 CKM All materials available Target: 31.07.2026
9	132kV Angul-Chainpal line HTLS Up-gradation (14.9KM)	Materials available. 132kV Angul-Chainpal line: Stringing: 12.5/14.9kM

		EPC: M/s Sterlite Power Tr. Ltd.,				
ICT New/Augmentation Plan						
Sl No	Name of Grid Substation	New/ Augmentation	MVA	From	To Be	To be commissioned by
1	Mendhasal	New	500(4 th ICT)	315x3	500x1+315x3	Oct 2026
		Augmentation	315 to 500	500x1+315x3	500x2+315x2	2027-28
2	Lapanga	New	315(3 rd ICT)	500x1+315x1	500x1+315x2	2026-27
		Augmentation	315 to 500	500x1+315x2	500x2+315x1	2028-29
3	New Duburi	New	500(4 th ICT)	500x1+315x2	500x2+315x2	2027-28
		Augmentation	315 to 500	500x2+315x2	500x3+315x1	2029-30

[Handwritten Signature]
18/9/26

Chief General Manager (O&M)
OPTCL, Bhubaneswar

Plan for replacement of defective CLR insulator in PMJTL elements

Annex B.2.2.a

- Status of CLR Supply as on 11.09.2026:-


CLR Rating	Qty under Procurement	Start of progressive supply	Tentative date of end of progressive supply
400kV, 120kN	1682	Jun-26 (Supply started) 7370 Nos. already supplied) 160kN-6670 Nos. 120kN- 700 Nos.	Nov-26
400kV, 160kN	8591		
400kV Total	10273		
765kV, 160kN	3357	Jun-26 (Supply started) 9660 Nos. already supplied) 210kN-7960 Nos. 160kN- 1700 Nos	Dec-26
765kV, 210kN	14428		
765kV Total	17785		

Plan for replacement of defective CLR insulator in PMJTL elements

- Replacement Status & Plan for defective CLR as on 14.09.2026:-

SL No	Name of Line	Total Defective Insulator	Replaced as on Date	Date/Tentative date of start of Replacement work	Tentative No of days required	Tentative date of end of Replacement work
1	400kV New Jeerat-Subhasgram Ckt 1	3382	2900	Jul-26	7	Oct-26
2	400kV D/C New Jeerat-Subhasgram Ckt 2	3382	0	Sept-26	18	Oct-26
3	400kV New Jeerat-Jeerat Ckt 1	1123	0	Oct-26	8	Nov-26
4	400kV New Jeerat-Jeerat Ckt 2	1122	0	Oct-26	8	Oct-26
5	400kV Medinipur-Chanditala Ckt 1	303	0	Sep-26	5	Oct-26
6	400kV Medinipur-Chanditala Ckt 2	303	0	Sep-26	5	Oct-26
7	400kV Medinipur-Kharagpur Ckt 1	329	0	Aug-26	5	Oct-26
8	400kV Medinipur-Kharagpur Ckt 2	329	0	Aug-26	5	Oct-26
9	765kV Ranchi-Medinipur Ckt 1	2530	1800	Aug-26	8	Nov-26
10	765kV Ranchi-Medinipur Ckt 2	2530	1800	Aug-26	8	Nov-26
11	765kV Medinipur-New Jeerat Ckt 1	6362	1700	Aug-26	16	Dec-26
12	765kV Medinipur-New Jeerat Ckt 2	6363	1400	Aug-26	17	Dec-26
TOTAL		28,058	9600			

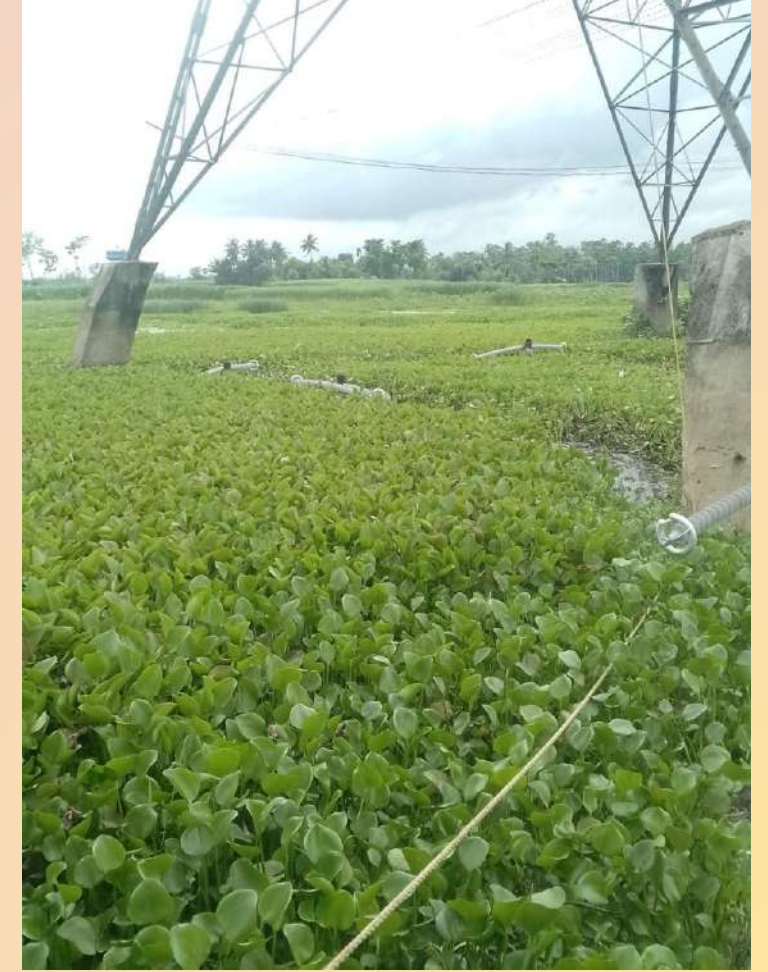Issue faced during Replacement of Defective CLR in PMJTL Lines



WATER LOGGED LOCATIONS

Issue faced during Replacement of Defective CLR in PMJTL



WATER LOGGED LOCATIONS

Issue faced during Replacement of Defective CLR in PMJTL Lines



WATER LOGGED PADDY FIELD

Issue faced during Replacement of Defective CLR in PMJTL Lines



FLOOD LIKE SITUATION

Issue faced during Replacement of Defective CLR in PMJTL Lines



FLOOD LIKE SITUATION

Issue faced during Replacement of Defective CLR in PMJTL Lines



CONTINUOUS HEAVY RAIN

Issue faced during Replacement of Defective CLR in PMJTL Lines



SEVERE ROW ISSUE IN MULTIPLE LOCATIONS

Issue faced during Replacement of Defective CLR in PMJTL Lines




SEVERE ROW ISSUE IN MULTIPLE LOCATIONS

Insulator Replacement Plan in PMJTL Lines for coming weeks (19.09.2026-31.09.2026)



SI No.	Name of TL	Dates		Time		
		From	To	From	To	Remarks
1	400kV New Jeerat-Subhasgram Ckt-2	19.09.2026	25.09.2026	07:00 Hours	16:00 Hours	For TL Insulator
2	400kV New Jeerat-Subhasgram Ckt-1	26.09.2026	28.09.2026	07:00 Hours	16:00 Hours	For TL Insulator
3	400kV Medinipur-Kharagpur Ckt-1	19.09.2026	21.09.2026	07:00 Hours	17:00 Hours	For TL Insulator
4	400kV Medinipur-Kharagpur Ckt-2	22.09.2026	25.09.2026	07:00 Hours	17:00 Hours	For TL Insulator
5	400kV Medinipur-Chanditala Ckt-1	26.09.2026	28.09.2026	07:00 Hours	17:00 Hours	For TL Insulator
6	400kV Medinipur-Chanditala Ckt-2	29.09.2026	31.09.2026	07:00 Hours	17:00 Hours	For TL Insulator

Critical ICTs of Eastern Region


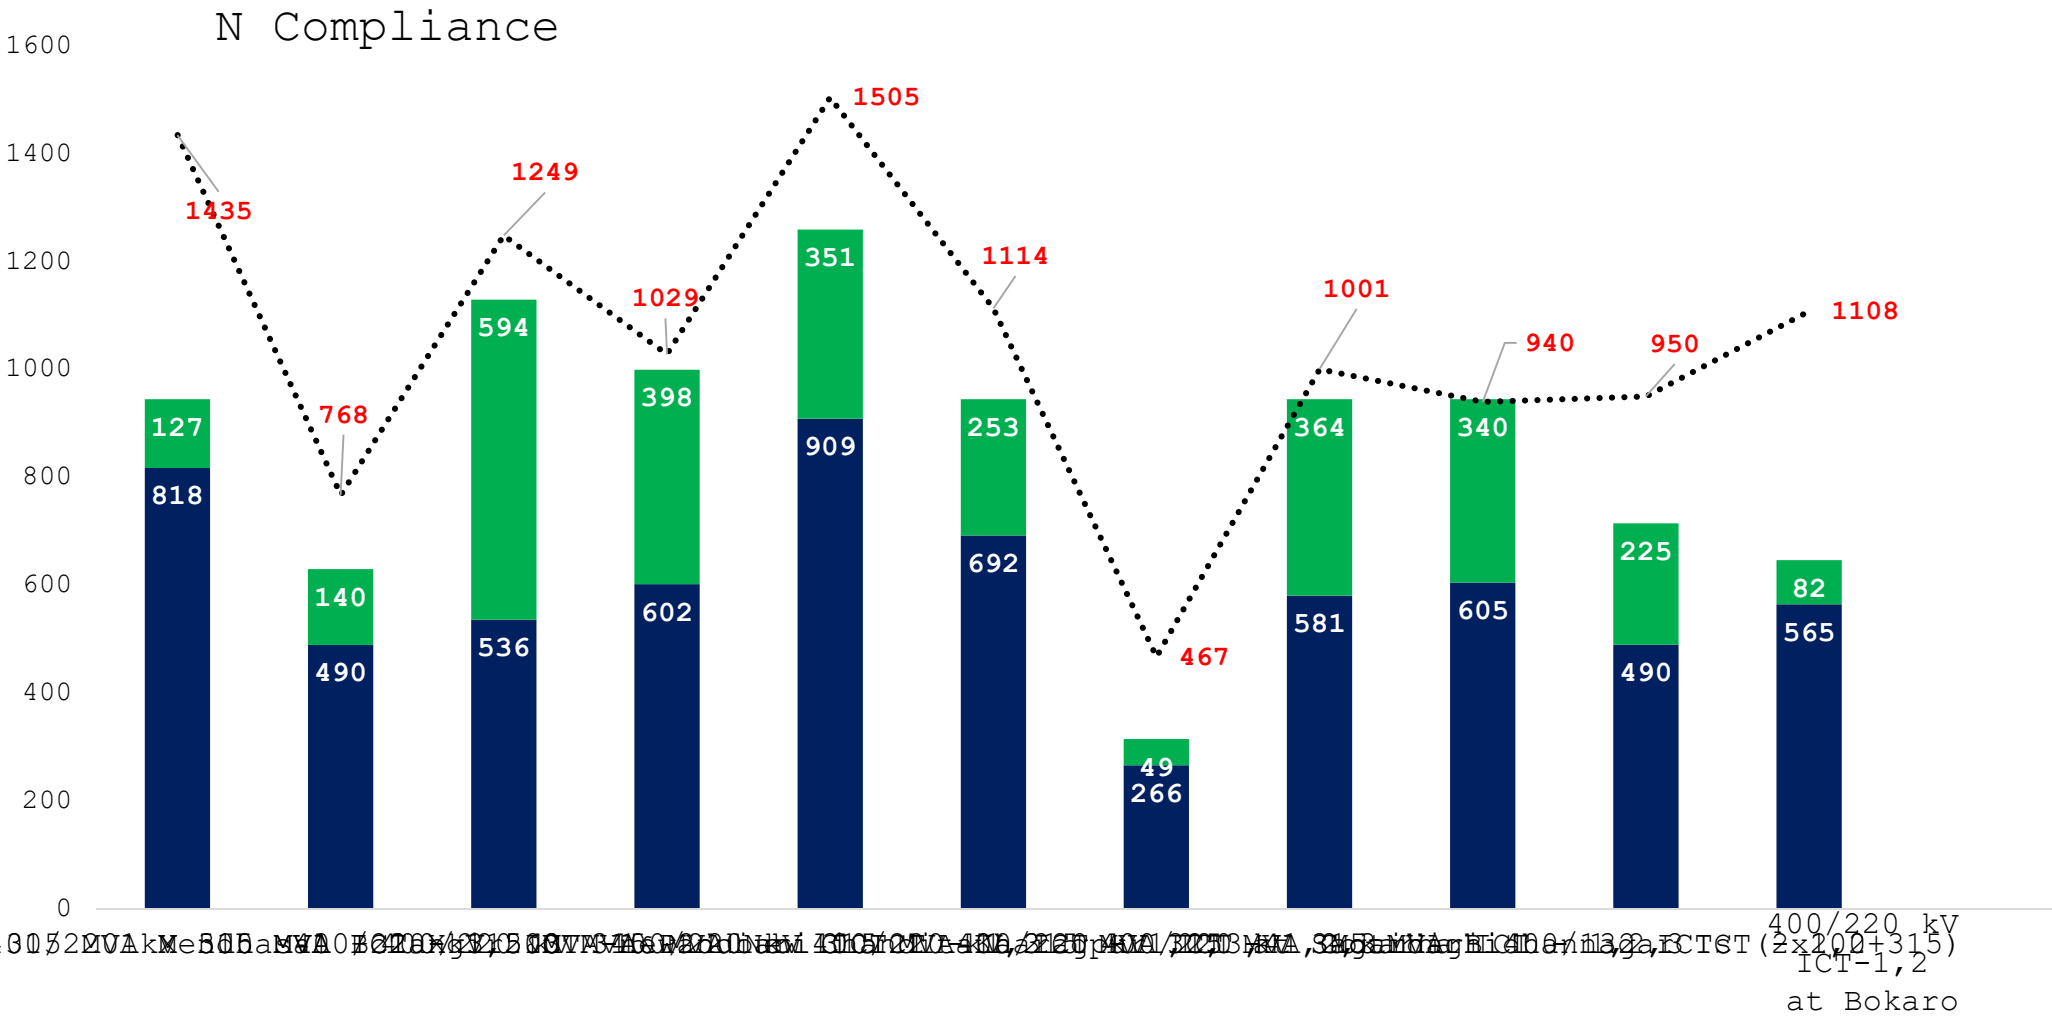
99th Percentile Loading (MW) 2026



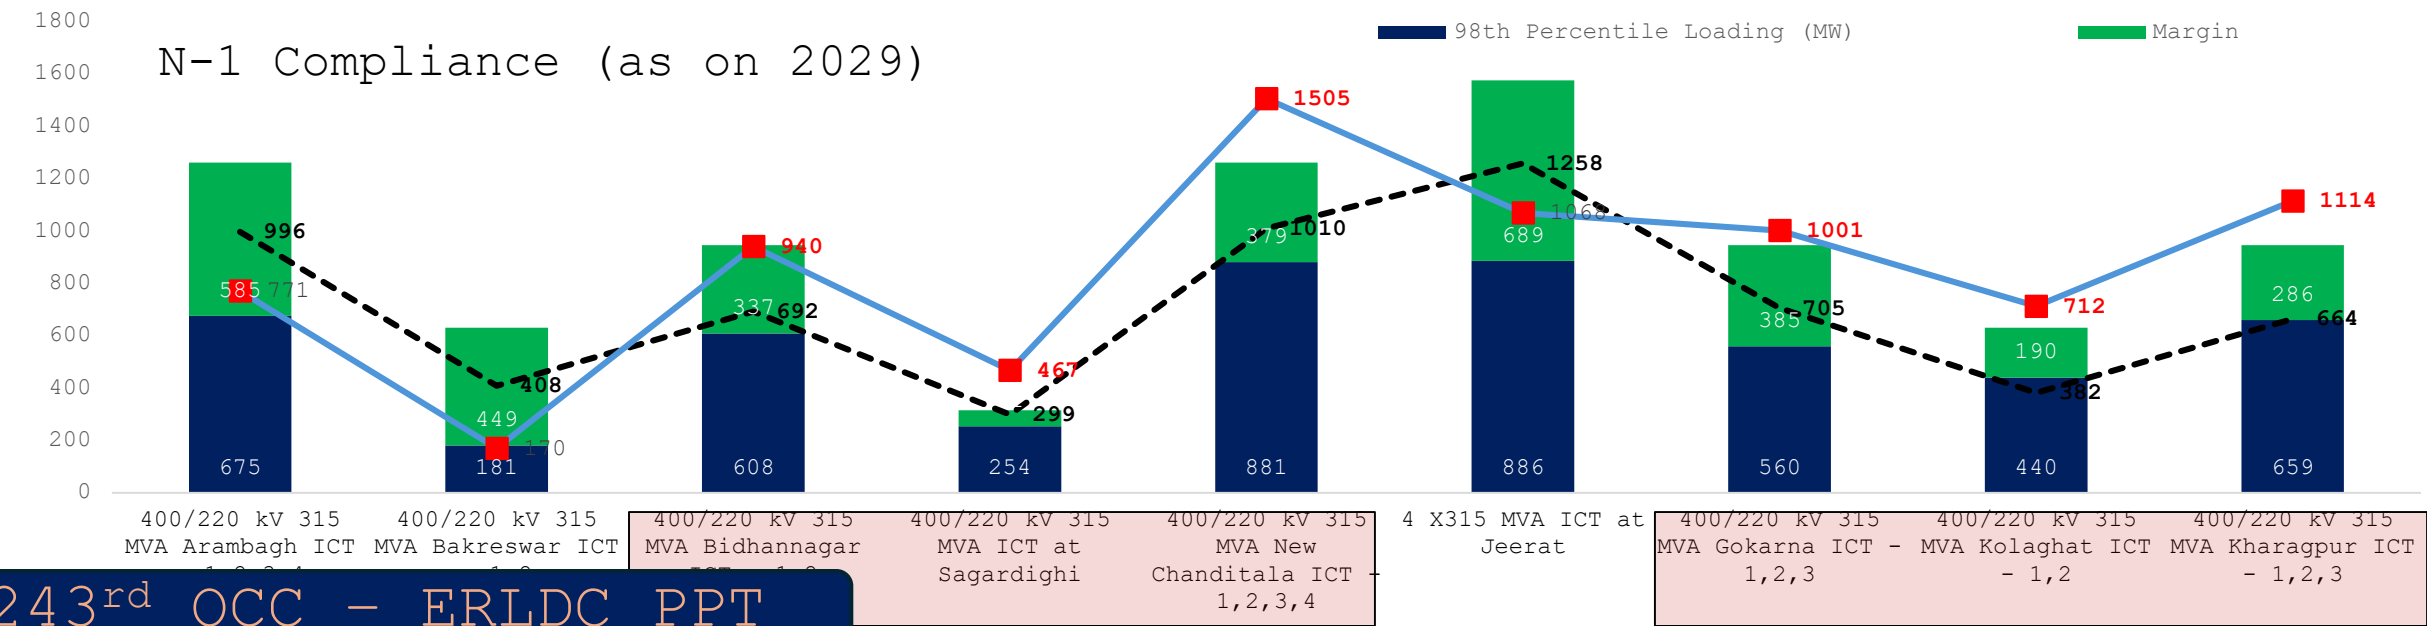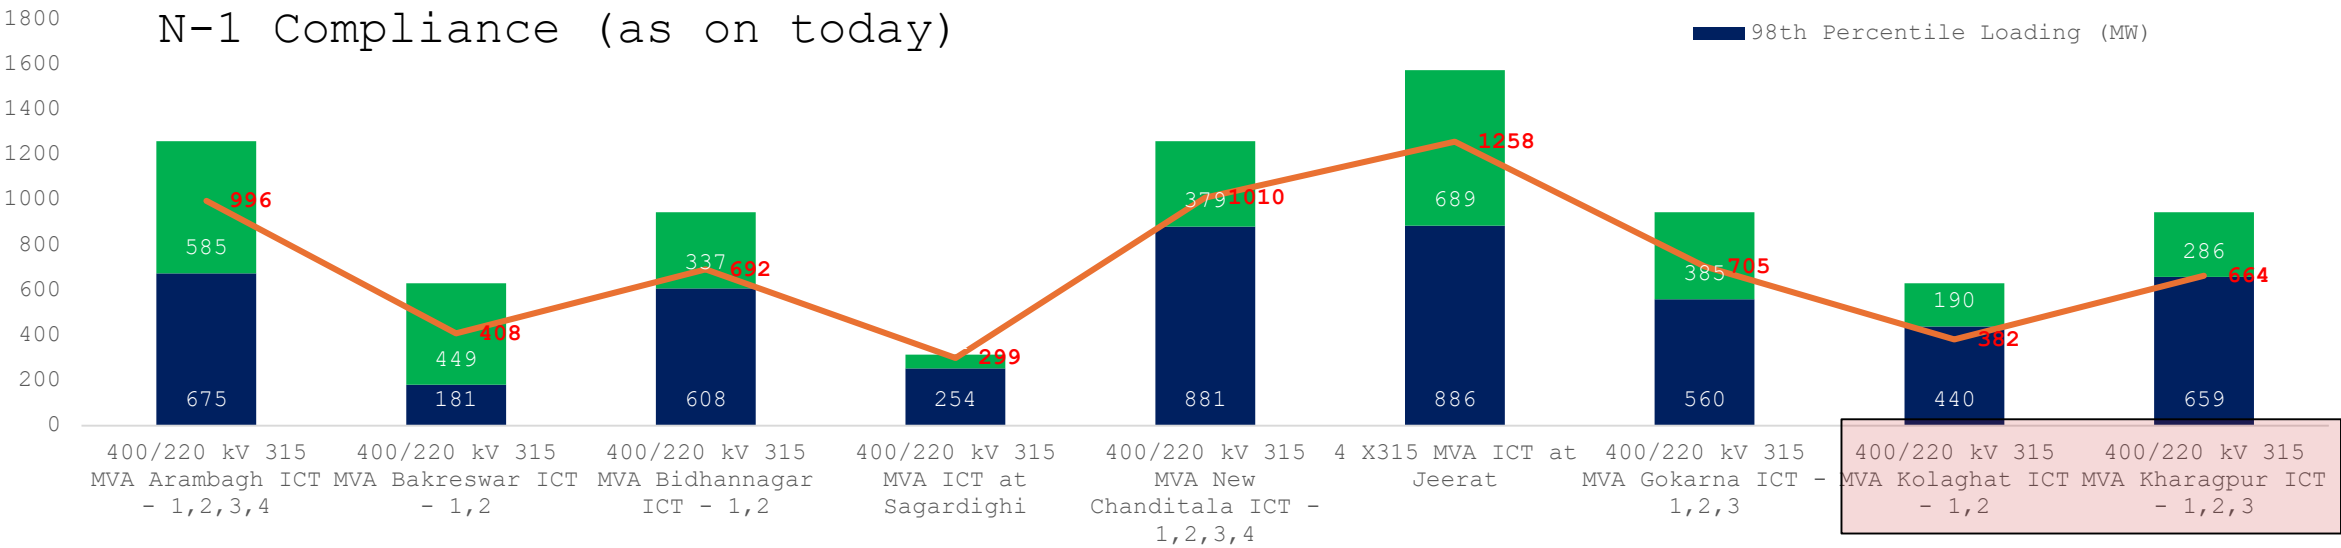Substation wise ICT Loading Scenario - WB (WBSETCL)



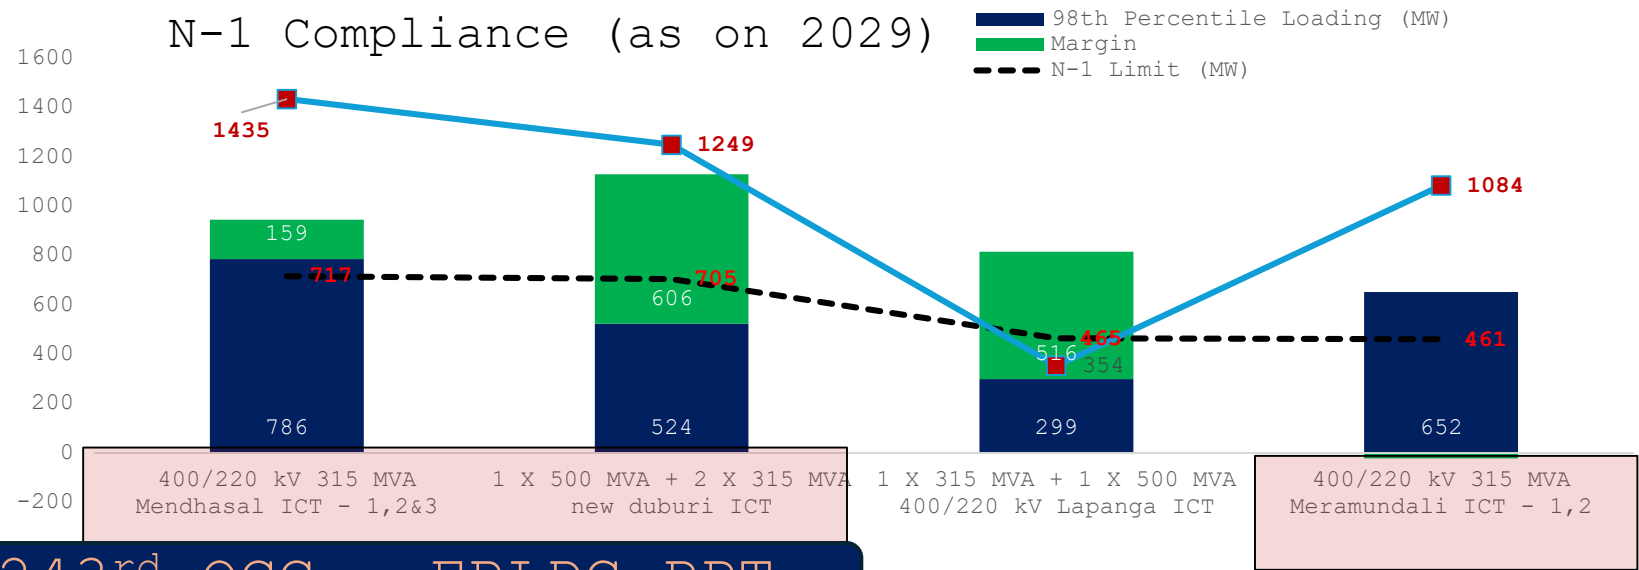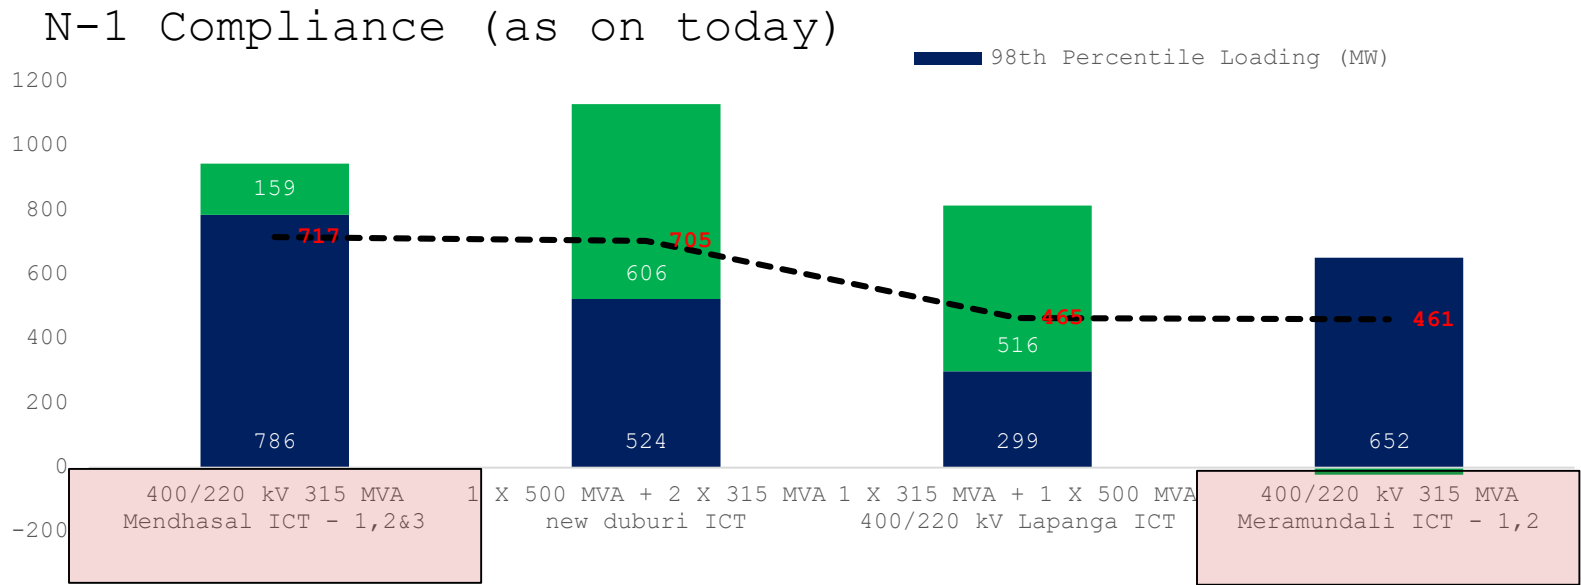Substation wise ICT Loading Scenario - Odisha (OPTCL)



400 KV Pantograph & DBR Isolator Replacement at Malda SS under ADDCAAP

- डेटा वर्गीकरण :
प्रतिबंधित
- Presently Malda 400 KV running with split bus mode. Bus coupler open as new Bus Bar commissioning is pending for S/D.
 - As per 241st OCC Shut down meeting, both 400 KV Bus SD for Bus Bar commissioning can be provided at November-26 (Post completion of festive season).
 - At Malda following isolators required to be replaced under ADDCAP:-

400 KV Malda-Purnea-I	
Main Bus-I Isolator (89M1)	Pantograph
Main Bus-I Isolator (89M2)	Pantograph
Transfer Isolator (89T)	Pantograph
Line Isolator (89L)	HCB

400 KV Malda-Purnea-II	
Main Bus-I Isolator (89M1)	Pantograph
Main Bus-I Isolator (89M2)	Pantograph
Transfer Isolator (89T)	Pantograph
Line Isolator (89L)	HCB

400 KV Bus Coupler	
Main Bus-I Isolator (89M1)	Pantograph
Main Bus-I Isolator (89M2)	Pantograph

- If considered phase wise total Pantograph to be replaced- 24 No's
- If considered phase wise total HCB to be replaced- 06 No's

डेटा वर्गीकरण :
प्रतिबंधित/RESTRICTED

Main Bus

Isolator closed



Isolator in open

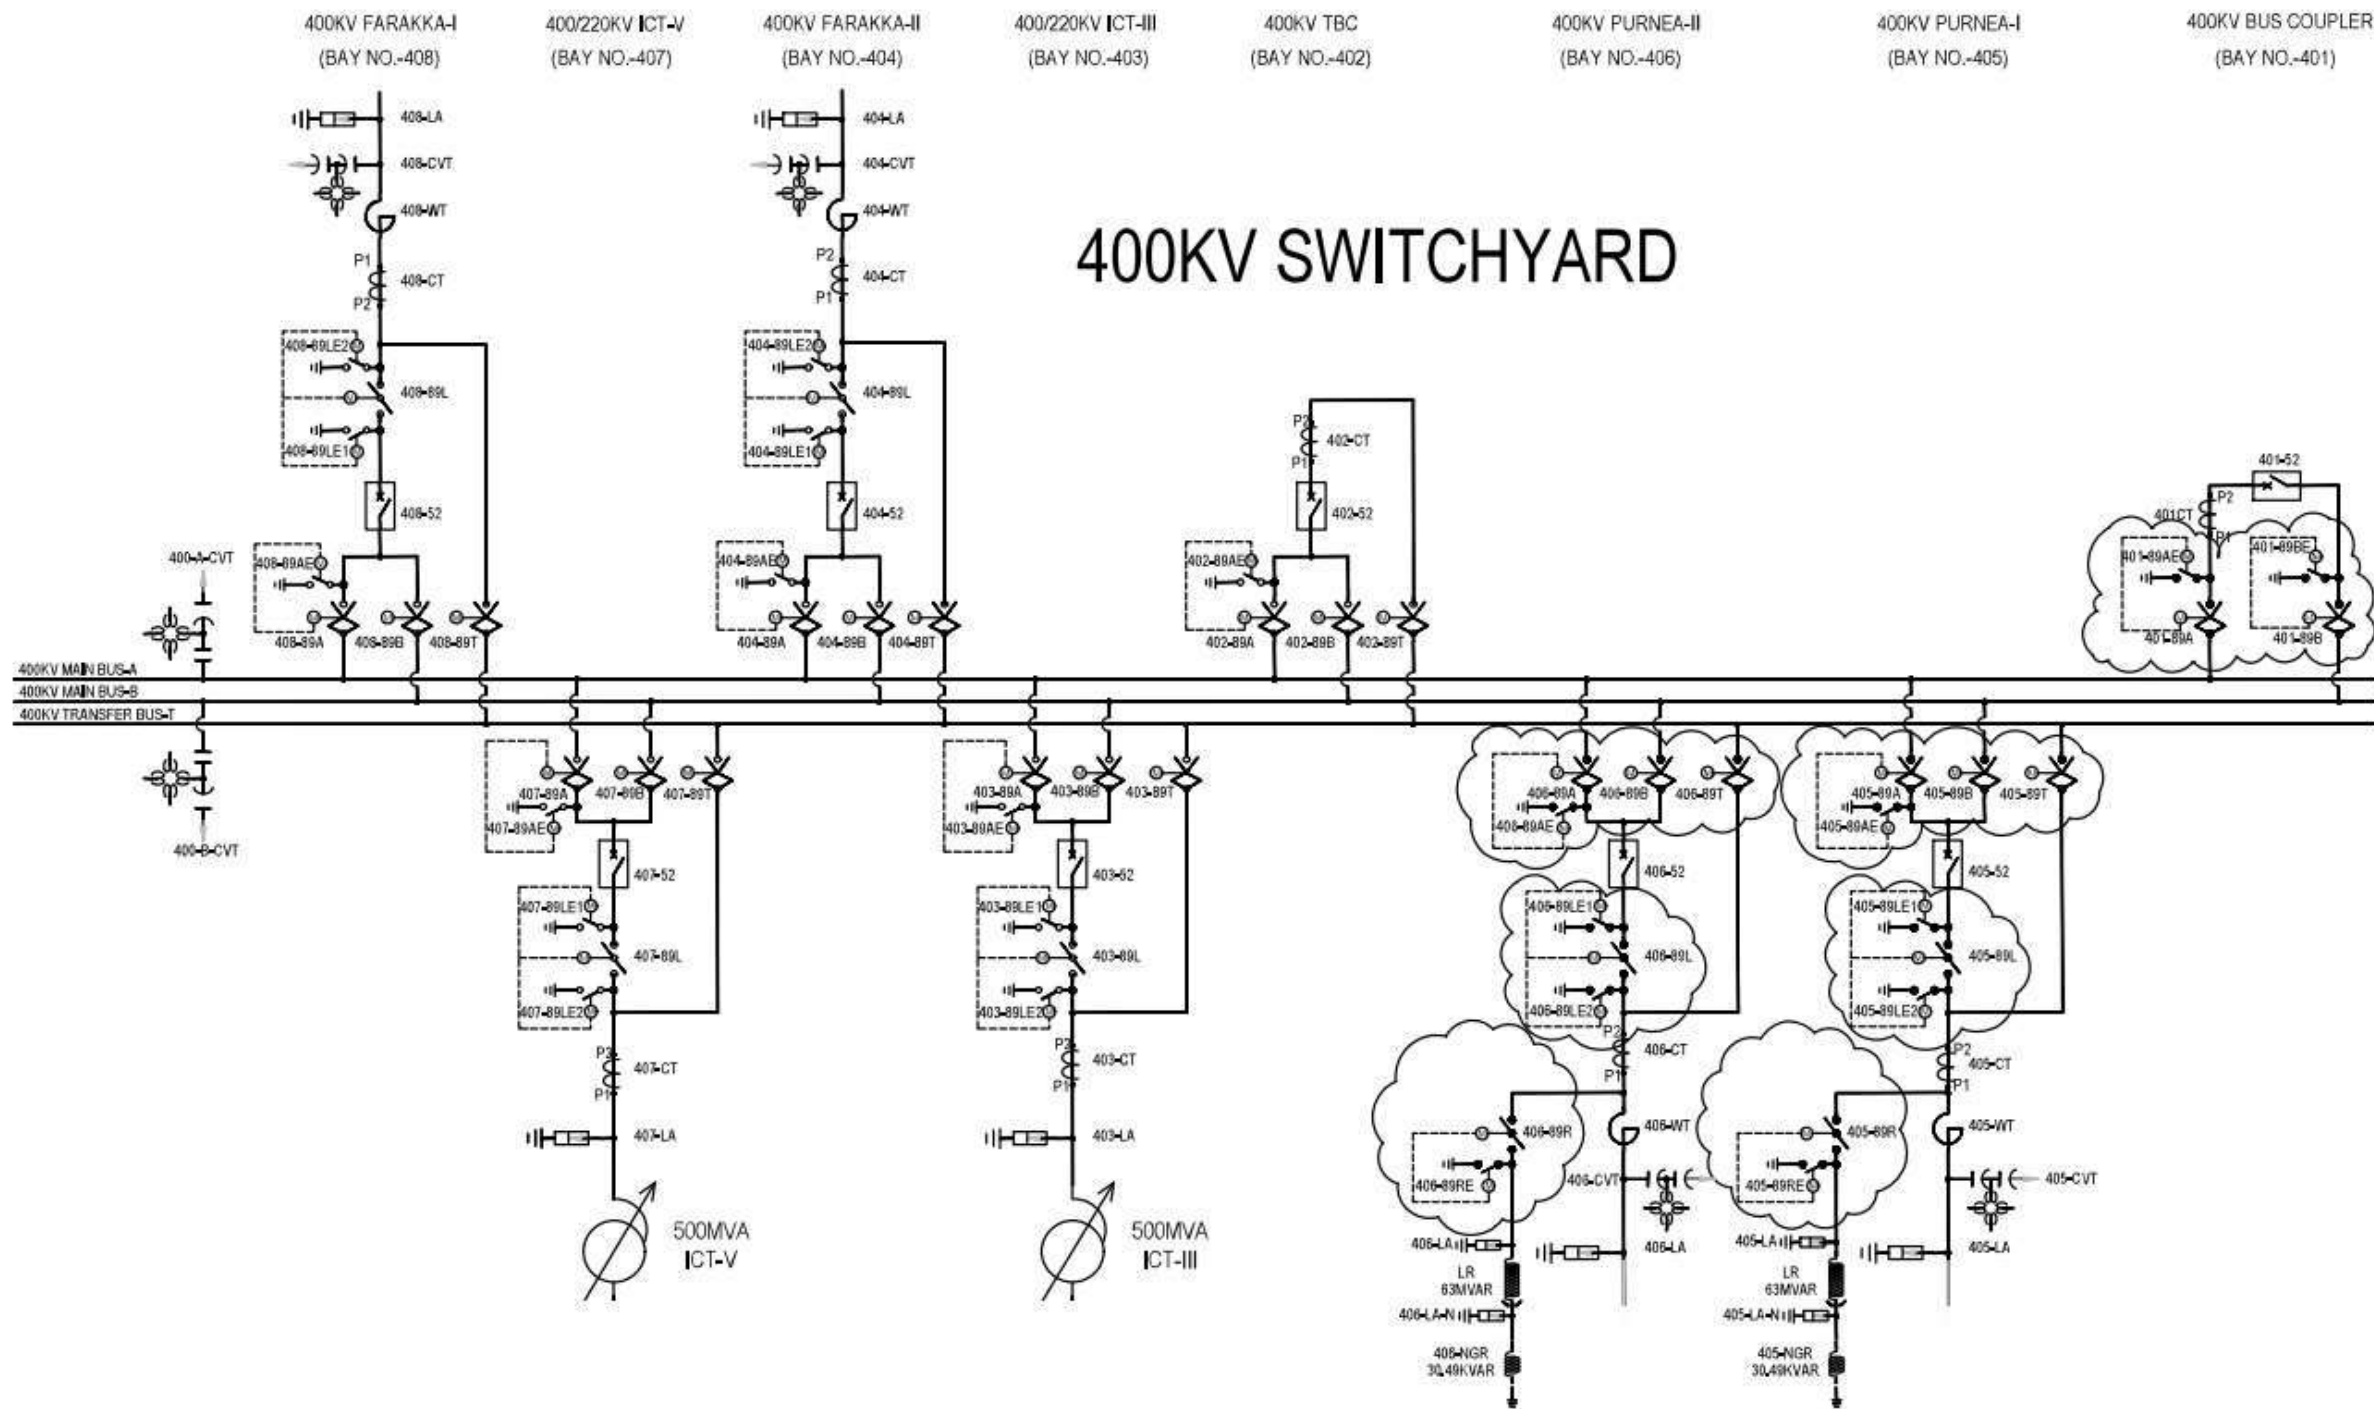


For carrying out any activity in pantograph, corresponding Bus & Feeder SD is required, i.e, 89M1/89M2/89T.

For carrying out any activity in HCB, corresponding ONLY Feeder SD is required, i.e, 89L.

डेटा वर्गीकरण :






• Various options for replacement of Isolators at Malda SS:-

OPTION-1:- (All isolators will be replaced by one go). 30/30 Nos.


Name of Element	SD Duration	Work Details	Isolator for Replacement	Remarks/ Conditions
400 KV BUS-1	ODB	Bus jumper disconnection at Purnea Gantry, to facilitate isolation of Purnea-1/2 & BC from Remaining system.	89M-1/2 of BC + 89M-1/2/T+L of Purnea-1/2	
400 KV BUS-2	ODB			
400 KV Malda-Purnea-1	OCB	Continuous SD for all isolator replacement, for 18 Days.		Only Malda-Farakka-D/C will be in service to cater WB load.
400 KV Malda-Purnea-2	OCB			
400 KV BUS-1	ODB	For returning to normal configuration.		
400 KV BUS-2	ODB			

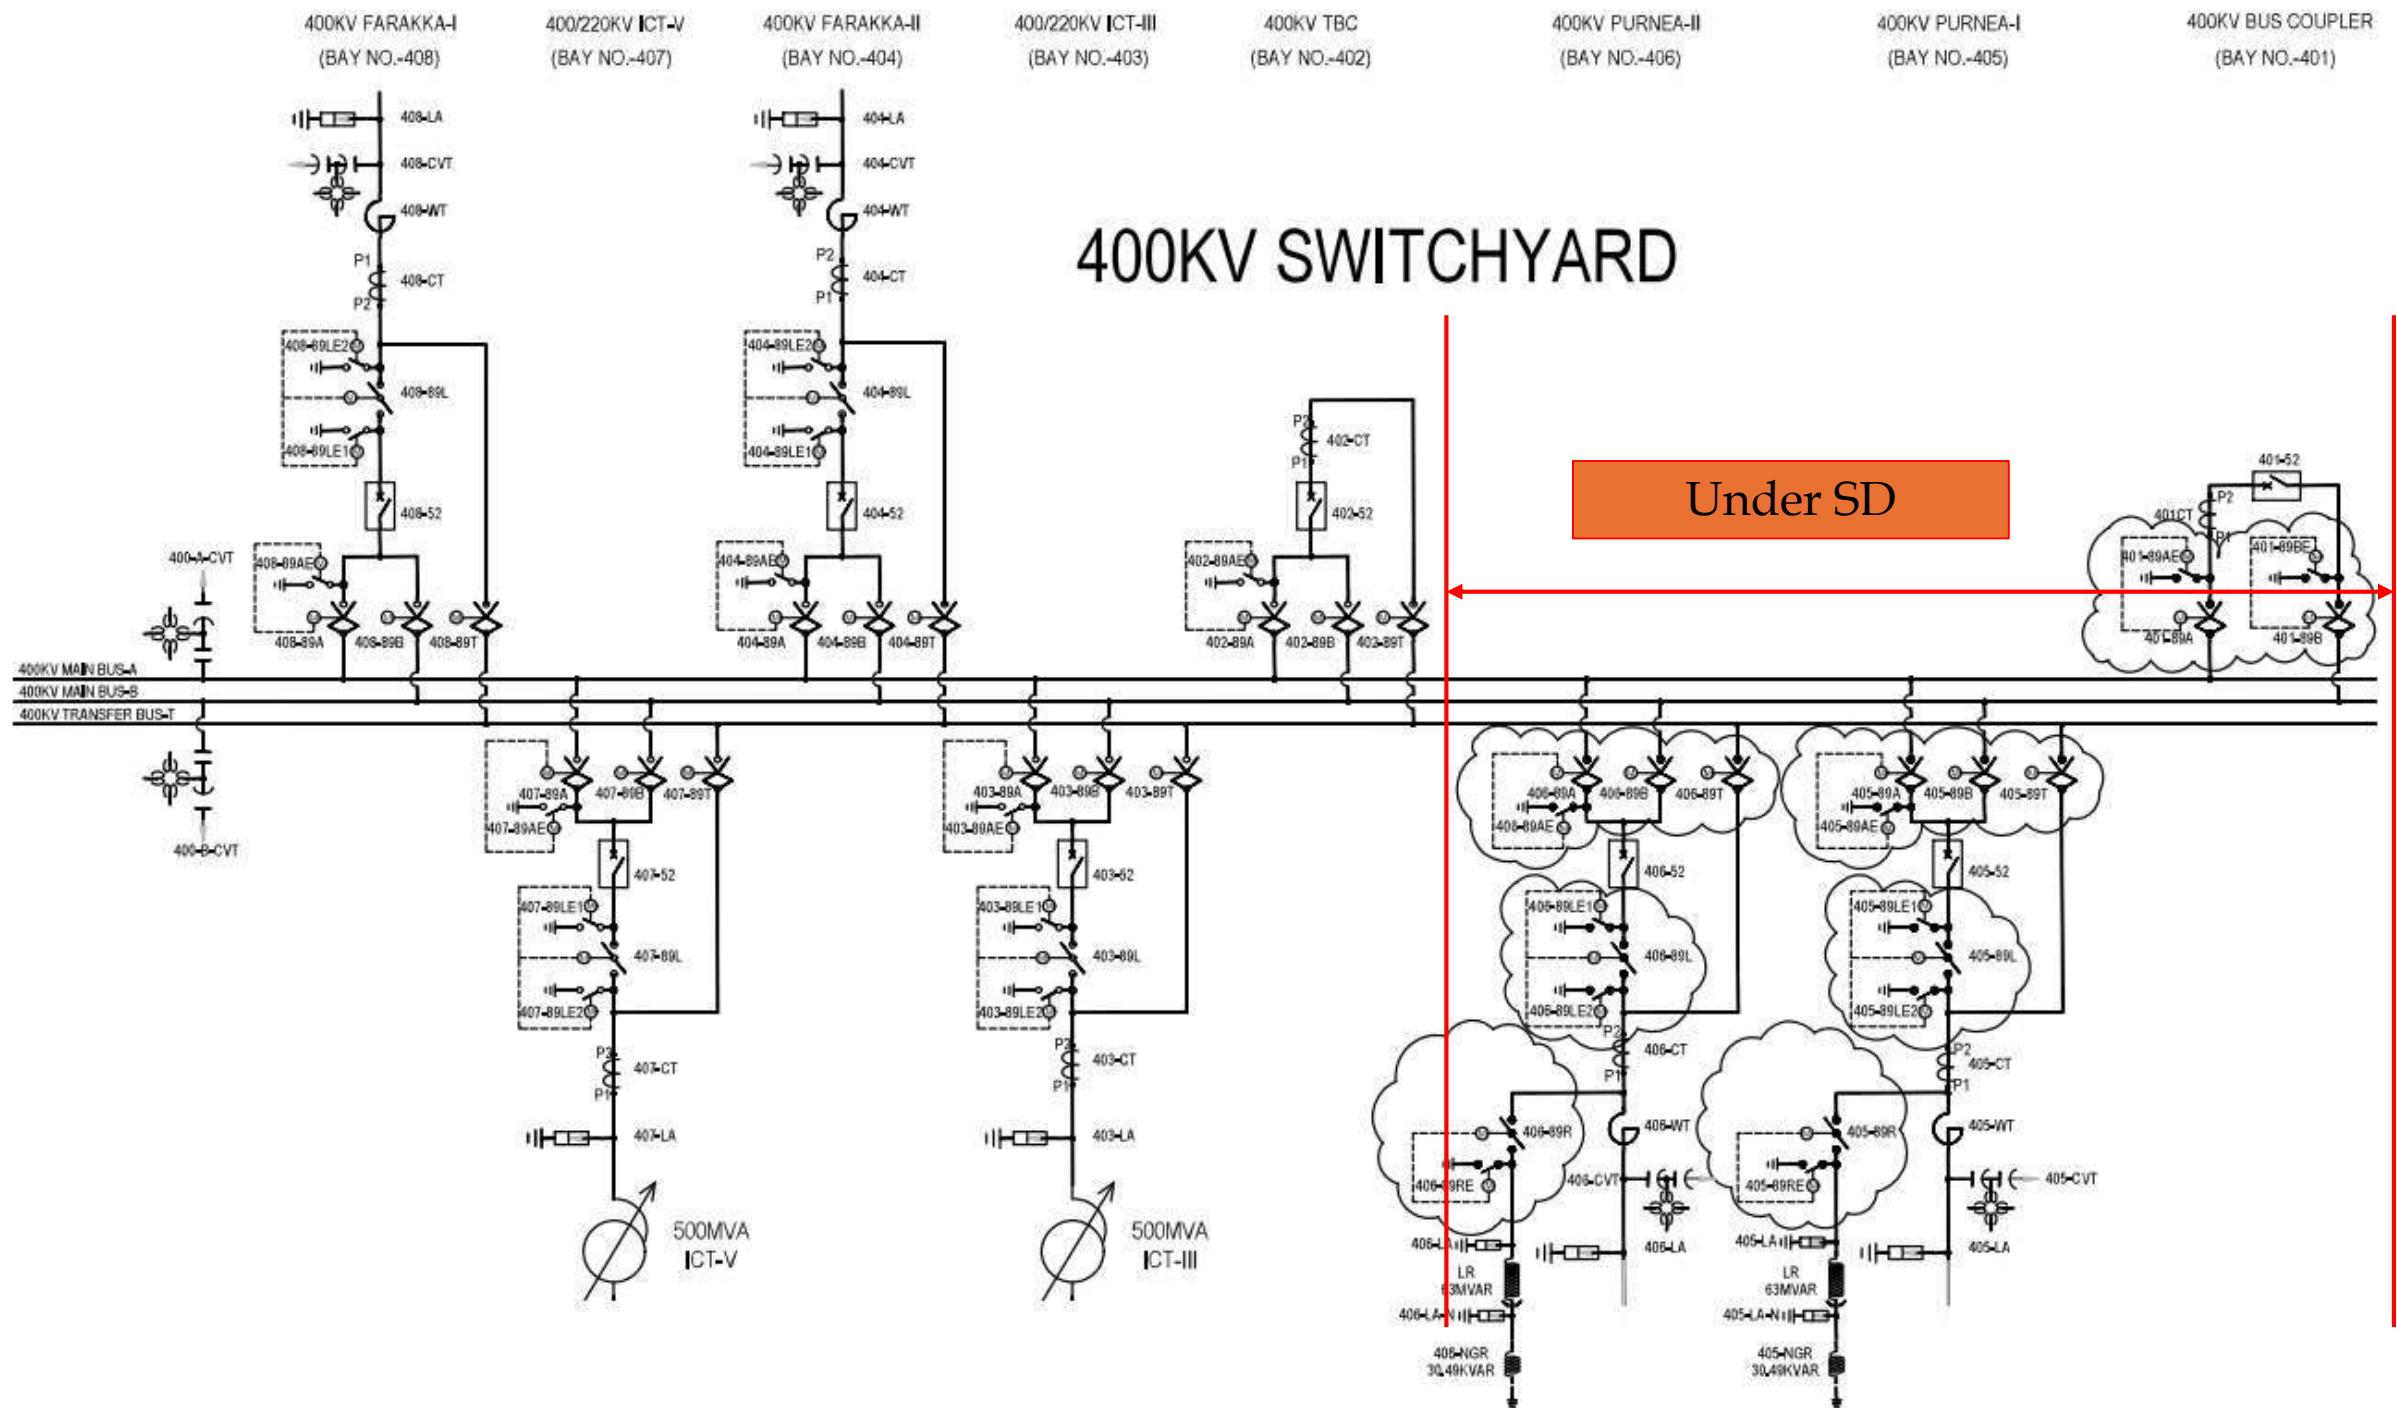

• Various options for replacement of Isolators at Malda SS:-

OPTION-2:- (Only Bus Coupler Isolators and Line side Isolators of Purnea-1/2). (18/30)


Name of Element	SD Duration	Work Details	Isolator for Replacement	Remarks/ Conditions
400 KV BUS-1	ODB	Bus jumper disconnection at Bus Coupler Gantry, to facilitate isolation of BC from Remaining system. BC will be out for 12 Days.	89M-1/2 of BC	Total 06 Pantograph will be replaced. Bus Coupler can not be taken into service in case of any contingency.
400 KV BUS-2	ODB			
400 KV Malda-Purnea-1	OCB	Alternate SD for replacement of 89T/L of one circuit at a time, for 10 Days.	89T+L of Purnea-1/2.	For all cases, at-least 03 400 KV Line Feeders will be in service. Transfer Bus will not be available for entire period.
400 KV Malda-Purnea-2	OCB			
400 KV BUS-1	ODB	For returning to normal configuration.		
400 KV BUS-2	ODB			

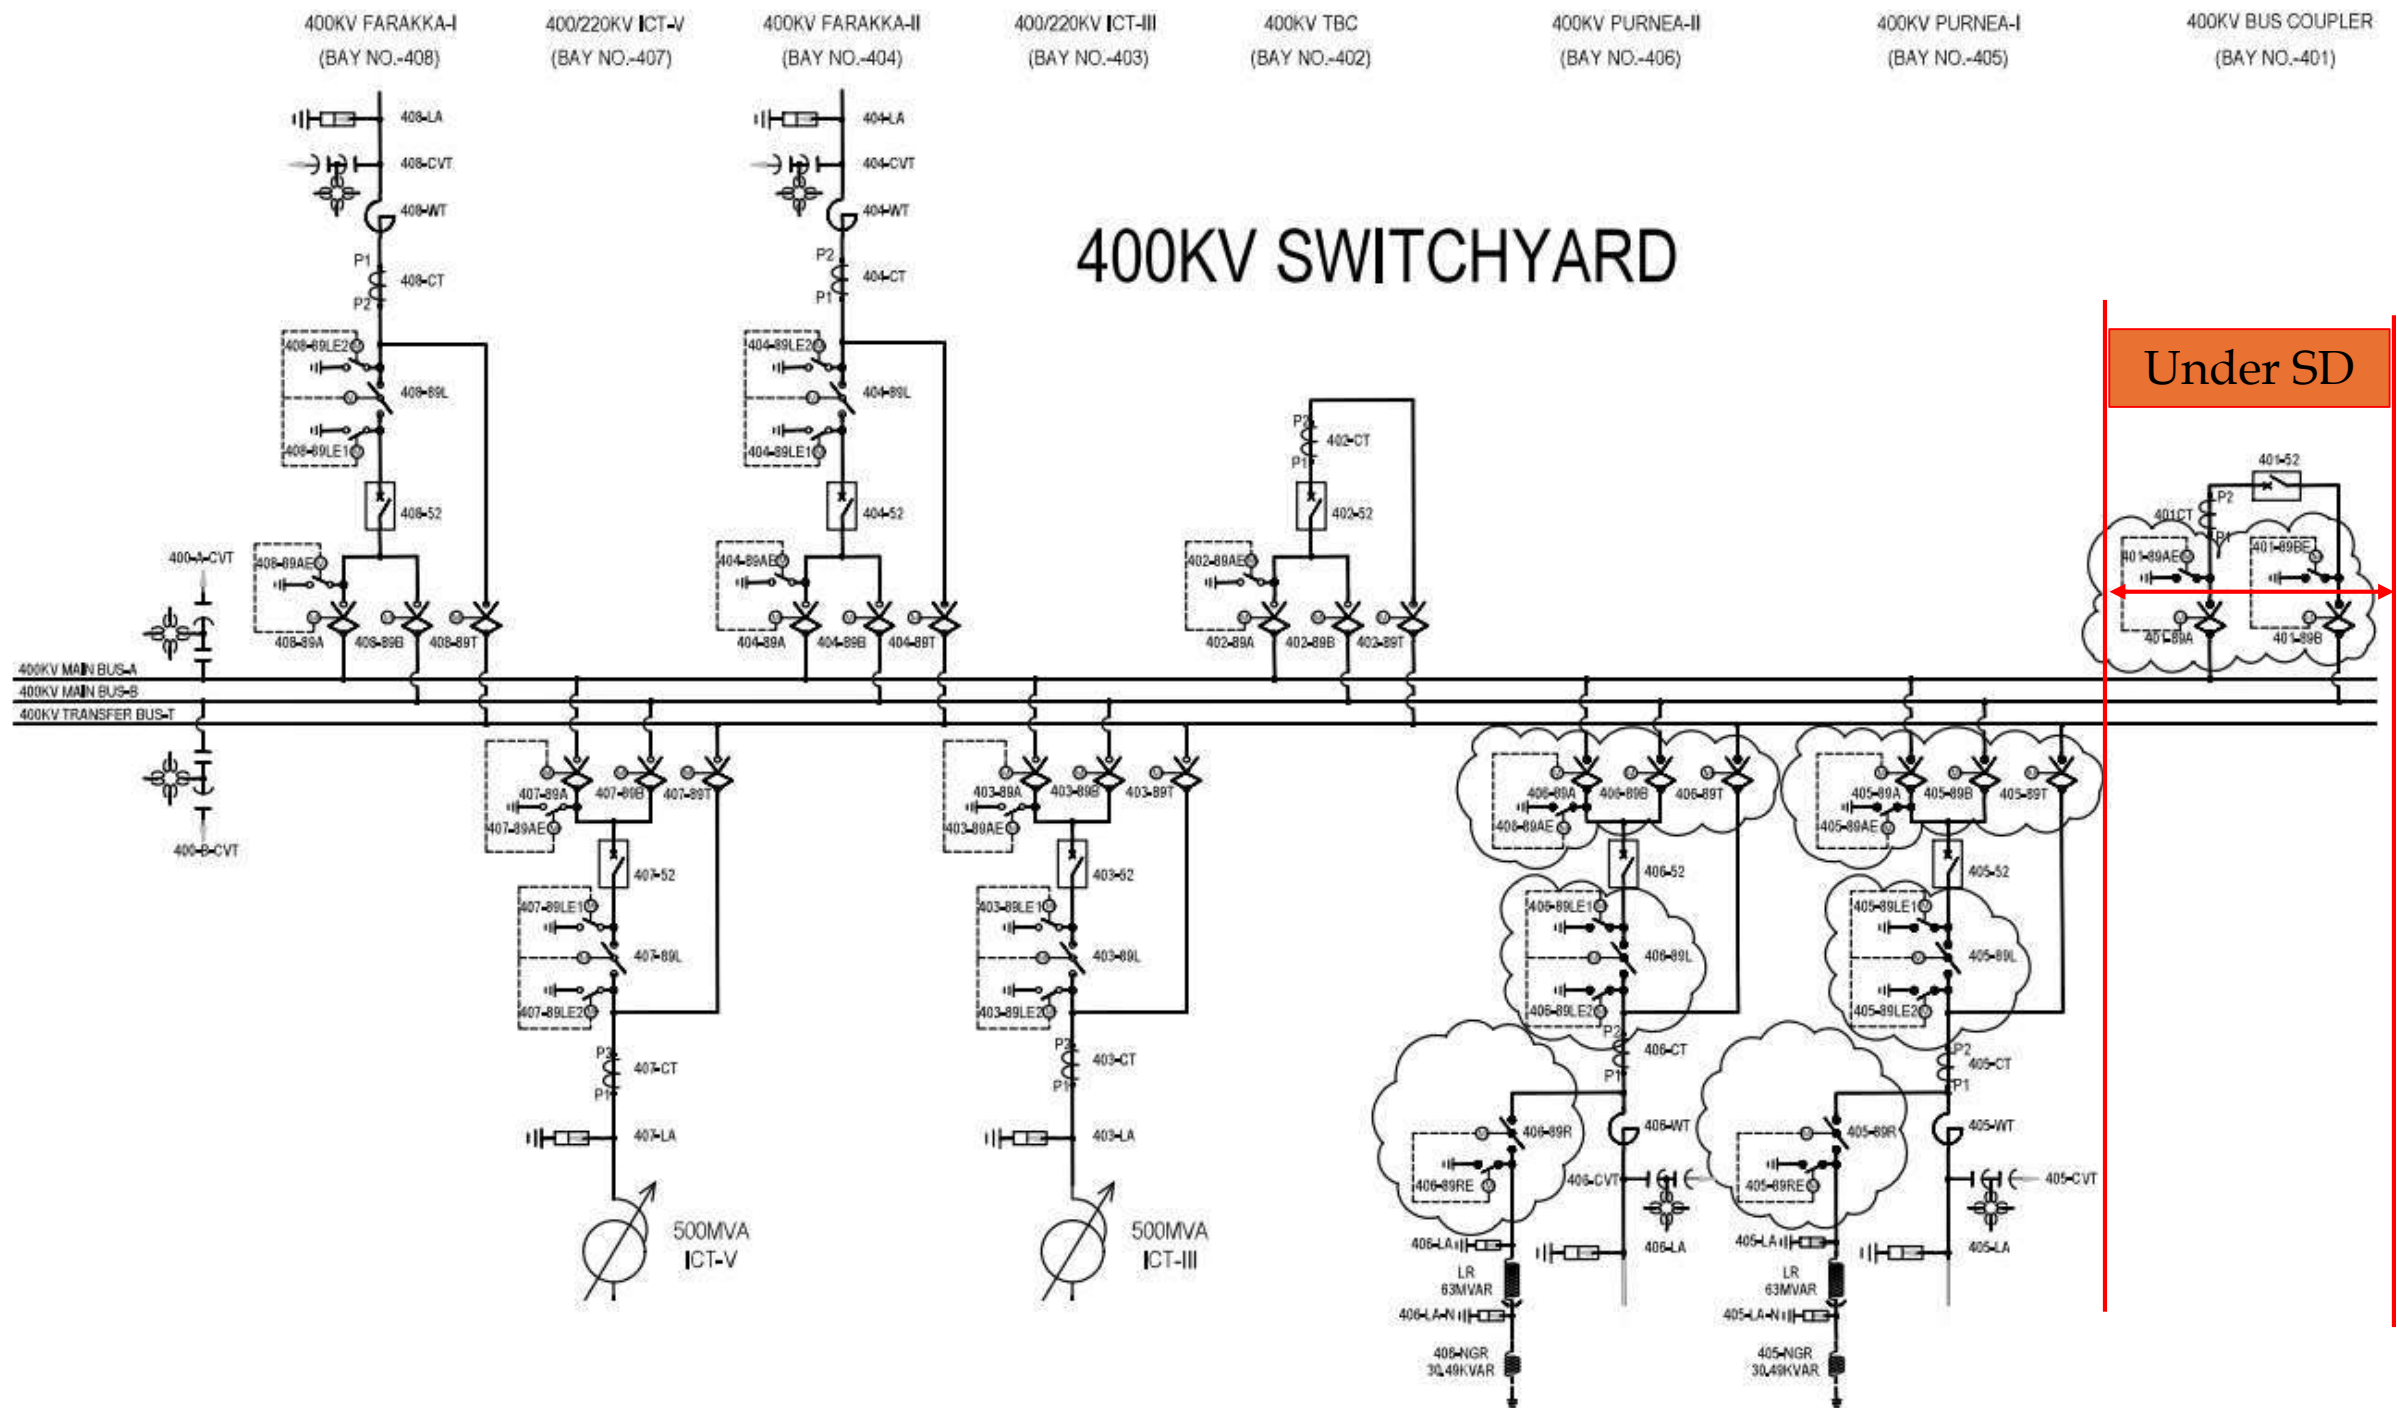

- Various options for replacement of Isolators at Malda SS:-

OPTION-3:- (After completion of Option-2). (12/30)

Name of Element	SD Duration	Work Details	Isolator for Replacement	Remarks/ Conditions
400 KV BUS-1 & 400 KV Malda-Purnea-1.	OCB	For replacement of 89M1 of both Purnea-1/2. Both element will be out for 15 Days.	89M-1 of both Purnea-1/2.	Purnea-2 feeder will be charged through TBC.
400 KV BUS-2 & 400 KV Malda-Purnea-2.	OCB	For replacement of 89M2 of both Purnea-1/2. Both element will be out for 15 Days.	89M-2 of both Purnea-1/2.	Purnea-1 feeder will be charged through TBC.

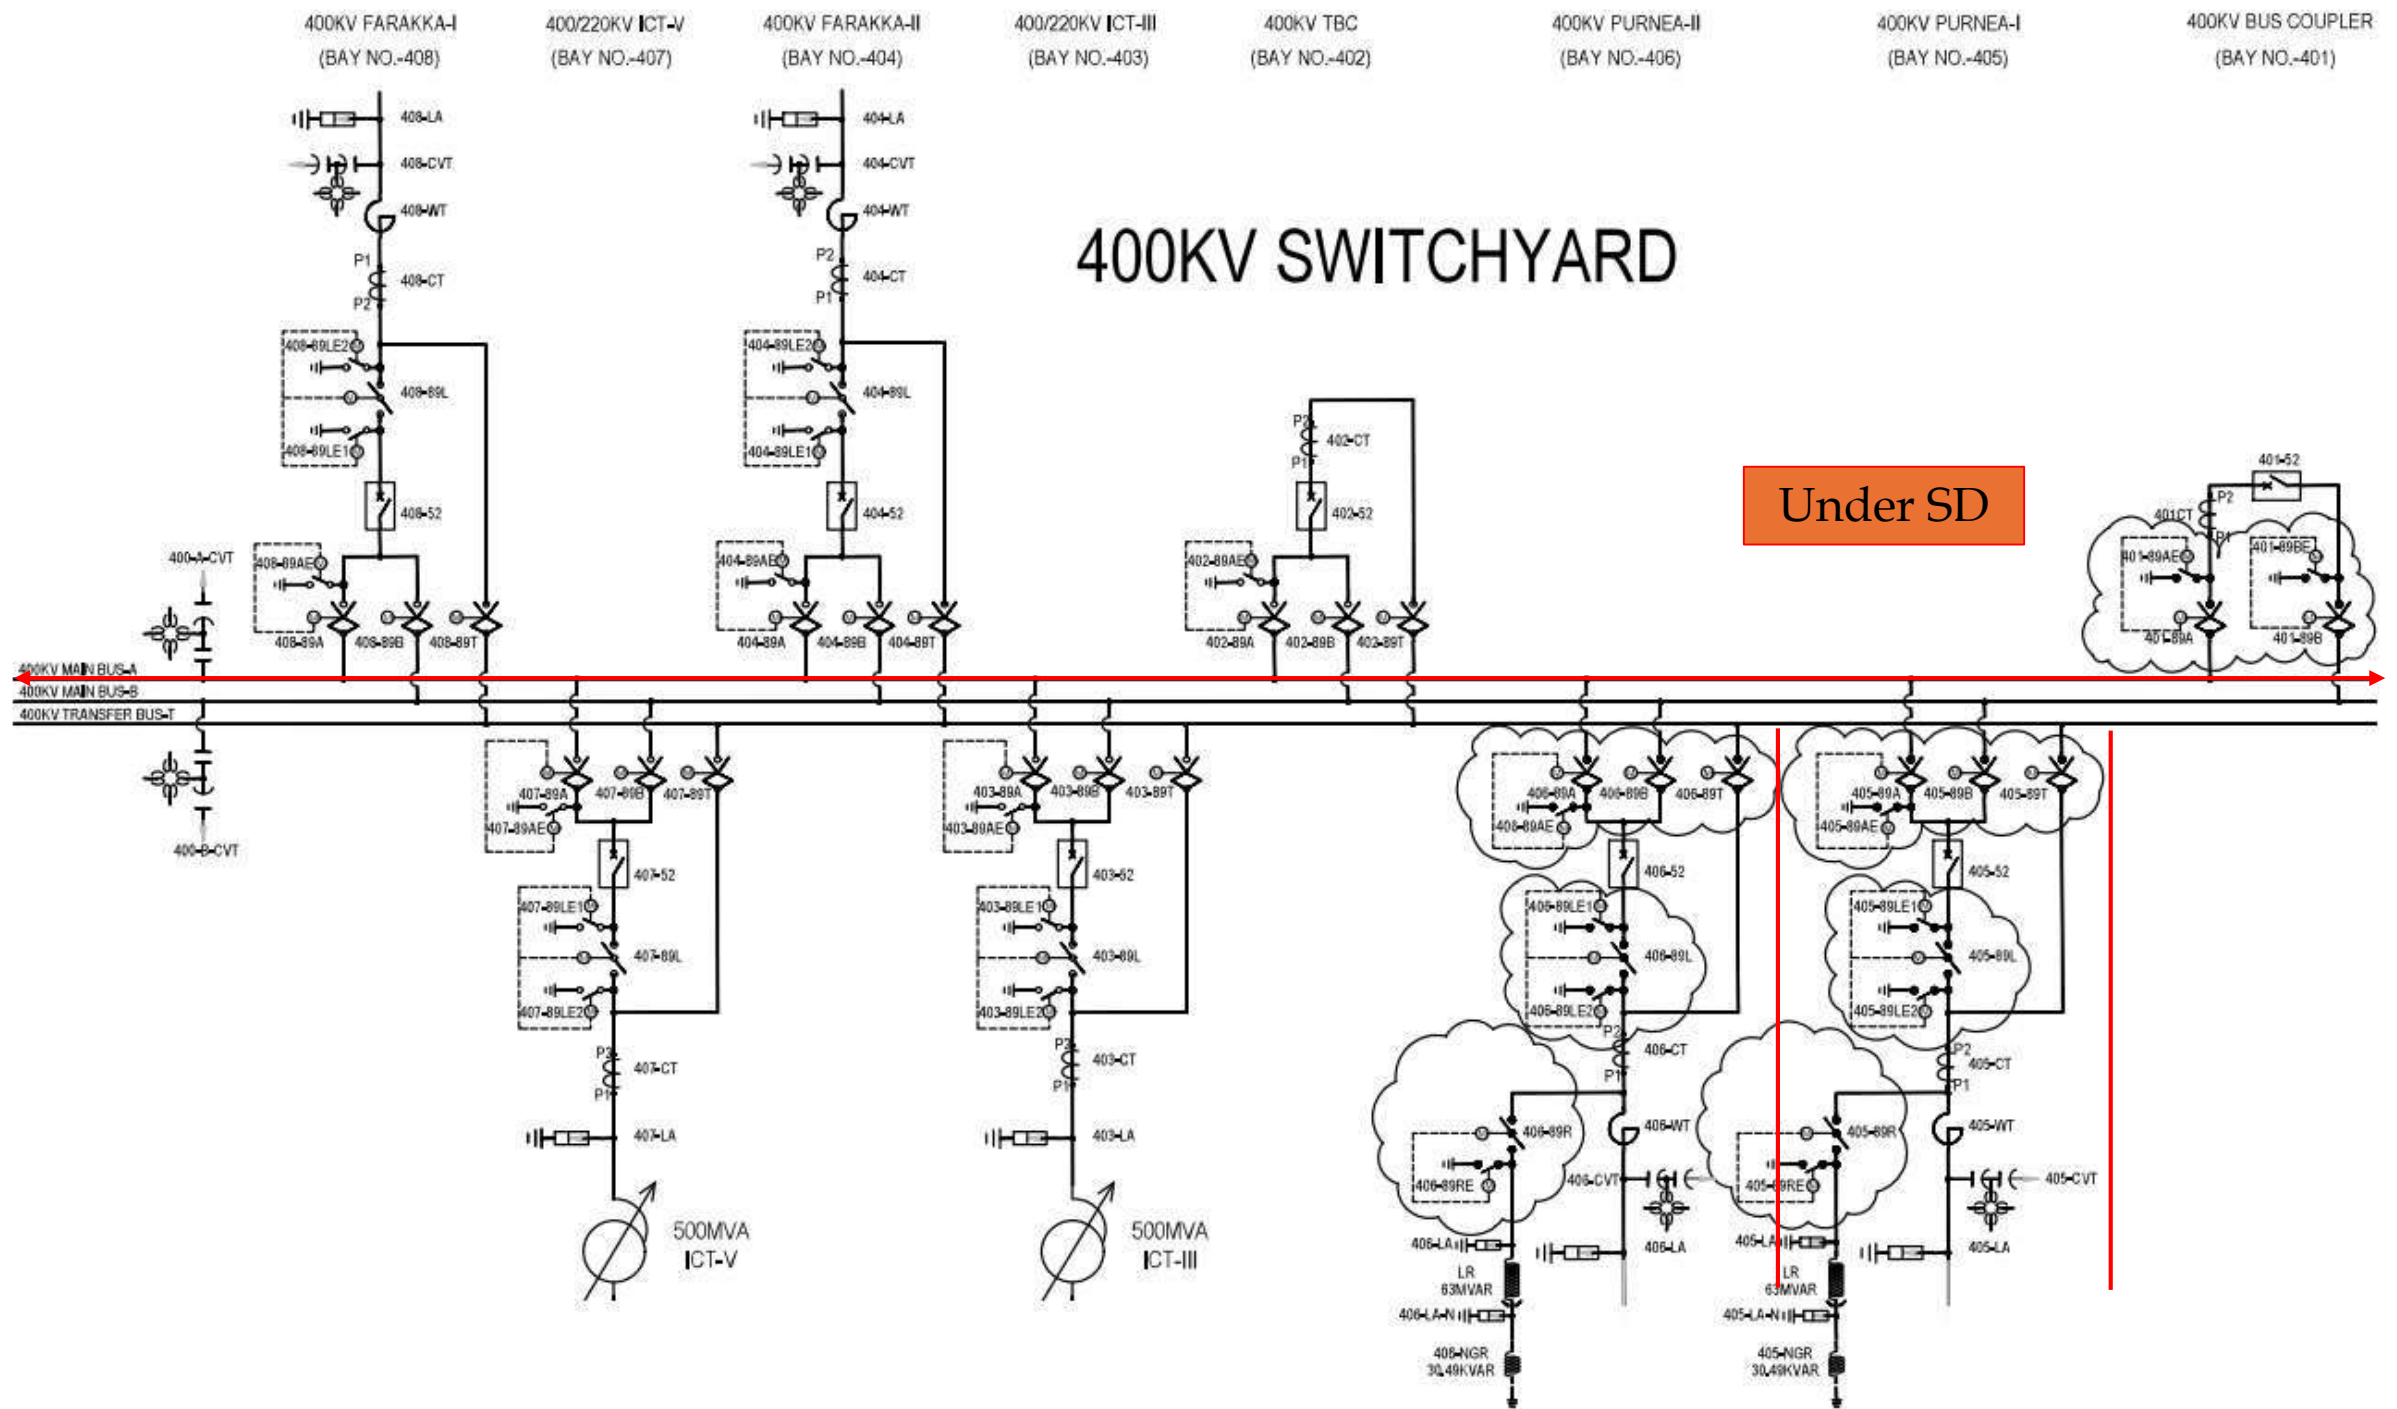



Annex B.2.12.

भारत सरकार/ Government of India
विद्युत मंत्रालय/ Ministry of Power
केन्द्रीय विद्युत प्राधिकरण/ Central Electricity Authority
विद्युत प्रणाली अभियांत्रिकी एवं प्रौद्योगिकी विकास प्रभाग
Power System Engineering & Technology Development Division

Date: 08.09.2026

सेवा में,

<As per attached list>

विषय: Formal Procedure for sharing IMD Wind Sensors' Data with Power Utilities - reg.

महोदया/ महोदय,

You are kindly aware that Standing Committee of Experts under CEA comprising representatives from Power Utilities (central & state), CPRI, academia, IMD, and other stakeholders investigates into the causes of failure of transmission towers of 220 kV & above voltage level, and gives appropriate recommendations to prevent their failures. You are also kindly aware that Wind Speed is one of the foremost critical parameter to be considered by various Power utilities in designing transmission towers suited to different Wind Zones (WZ), terrains & topographies. However, one of the prime reasons for failures is observed to be the huge difference between the design wind speed and the actual wind speed encountered during the failures.

While the design wind speed, obtained from Wind Zone Map of India, is considered by power utilities in designing the transmission towers, the actual wind speed obtained from various sources mainly from IMD field wind sensors is to be used by power utilities for design validation, failure analysis and reliability assessment of transmission line Towers.

In this regard, availability of real-time accurate wind speed data at the location of transmission towers at the time of their failure is essential. However, it has been observed that quite often difficulties have been faced by power utilities in obtaining access to real time wind speed data for specific (failed) transmission tower locations from nearby IMD Wind sensors. The matter was deliberated upon in Standing Committee meetings held from time to time wherein, IMD representative informed that power utilities can obtain such access by entering into Memoranda of Understanding (MoU) with IMD, and requested to address the matter to IMD. The matter was taken up with IMD requesting to share the procedure/guidelines for obtaining real-time wind speed data for specific (failed) transmission tower locations by transmission utilities.

In this regard, IMD, vide its email dated 27.08.2026, has informed that it is open to entering into Memoranda of Understanding (MoUs) with various Power Transmission Utilities across India for collaboration and sharing of meteorological data/services, including wind speed data from IMD Wind Sensors.

IMD has further informed that Power-sector utilities desirous of obtaining meteorological data/services may forward a formal proposal/ request to the Director General of Meteorology, IMD (directorgeneral.imd@imd.gov.in), clearly indicating their specific requirements and the proposed scope of collaboration. The proposal/request may also be forwarded with a copy to the Organization Section and PHT Cell of IMD at organisationsection@gmail.com , imd.pht@gmail.com

In view of the above, all concerned power utilities are requested to take note of the procedure indicated by IMD and initiate necessary action at their end.

This issues with approval of the competent Authority

भवदीय,
Digitally signed by
Kavita Jha
Date: 08-09-2026
13:08:46
(कविता झा)
निदेशक/Director

Copy to:

1. SA to Chairperson, CEA
2. SA to Member (PS), CEA
3. PS to Chief Engineer, PSE&TD, CEA

ADDRESS LIST:

Director General, Central Power Research Institute, P B No.8066, Sadashivnagar PO, Prof. Sir C V Raman Road, Bangalore - 560 080 dgcprici@cpri.in, mchandra@cpri.in	Member-Secretary, Southern Regional Power Committee No. 29, Race Course Cross Road, Bengaluru- 560009 mssrpc-ka@nic.in
Member-Secretary Western Regional Power Committee F-3, MIDC Area, Marol, Opposite SEEPZ, Central Road, Andheri (East), Mumbai-400093 ms-wrpc@nic.in,	Member-Secretary Eastern Regional Power Committee 14, Golf Club Rd, Golf Gardens, Tollygunge, Kolkata, West Bengal- 700033 mserpc-power@nic.in,
Member-Secretary Northern Regional Power Committee, 18-A, Qutab Institutional Area, Shaheed Jeet Singh Marg, Katwaria Sarai, New Delhi110016 ms-nrpc@nic.in,	Member Secretary, North Eastern Regional Power Committee, NERPC Complex, Dong Parmaw, Lapalang, Shillong - 793006 (Meghalaya). nerpc@ymail.com
Director, TCD, CEA, Sewa Bhawan, R.K. Puram, New Delhi tcdcea@nic.in	Head of the Department, Civil Engg., Delhi Technological University, Shahbad Daultpur, Bawana Road, Delhi-110 042 (Fax No.011-27852188) sksinghdce@gmail.com
Director, Structural Engineering Research Centre, CSIR Campus, Taramani, Post Box No.8287, Chennai-600113 (Fax No.044-22641734) director@serc.res.in	Director General, India Meteorological Department, Mausam Bhawan, Lodhi Road, New Delhi- 110 003 (Ph.011-24616051) directorgeneral.imd@imd.gov.in dgmnet@gmail.com m.mohapatra@imd.gov.in
Chairman & Managing Director, Madhya Pradesh Power Transmission Co. Ltd. Block No.2, Shakti Bhawan, Rampur, Jabalpur (M.P.) - 482008. md@mptransco.nic.in kshamashukla@mptransco.nic.in	Chairman, Karnataka Power Transmission Corporation Limited No. 82, Shakti Bhawan, Race Course Road, Bengaluru - 560001 md@kptcl.com mdkptcl@gmail.com ceepnc@kptcl.org etrlinepnc@kptcl.org aee9tech@kptcl.org
Managing Director, Maharashtra State Electricity Transmission Company Ltd.,	Chief Engineer (Transmission), Jharkhand Urja Sancharan Nigam Ltd. (JUSNL) Engineering Buliding, HEC,

C-19, E-Block Prakashganga, Bandra-Kurla Complex Bandra(E), Mumbai 400051. dirop@mahatransco.in md@mahatransco.in	Dhurwa, Ranchi – 834004 mdjusnl@gmail.com
Managing Director, Himachal Pradesh Power Development Corporation Ltd. Barowalia House, Khalini Shimla - 171004 md@hppcl.in	Chairman & Managing Director, Transmission Corporation of Andhra Pradesh Vidyut Soudha, Gunadala, EluruRd, Vijayawada, Andhra Pradesh 520004 ce.trans@aptransco.gov.in surendrababu.karreddula@aptransco.co.in
Chairman, Gujarat Urja Vikas Nigam Ltd. Sardar Patel Vidyut Bhawan, Race Course, Vadodara- 390 007 md.guvnl@gebmil.com	Managing Director, Gujarat Energy Transmission Corporation Ltd. Sardar Patel Vidyut Bhawan, Race Course, Vadodara- 390007 Ph.: 0265-2353085 md.getco@gebmil.com
Chairman & Managing Director, Orissa Power Transmission Corporation Ltd. Janpath, Bhubaneswar- 751 022. cmd@optcl.co.in dir.operation@optcl.co.in	Director (Operations), Rajasthan Rajya Vidyut Prasaran Nigam Ltd. Vidyut Bhawan, Jyoti Nagar, Jaipur (Rajasthan) Ph.: 0141-2740814 dir.oper@rvpn.co.in cmd.rvpn@gmail.com
Chairman & Managing Director, Uttar Pradesh Power Transmission Corporation Ltd. Shakti Bhawan, 14-A, Ashok Marg, Lucknow- 226001 cmd@upptcl.org	Managing Director, Assam Electricity Grid Corporation Ltd. Bijulee Bhawan, Paltan Bazar, Guwahati- 781 001 managing.director@aegcl.co.in md_aegcl@yahoo.co.in cgm.ppd@aegcl.co.in
Chairman & Managing Director, Delhi Transco. Ltd. Shakti Sadan, Kotla Marg, New Delhi – 110002 md@dtl.gov.in gmom1.dtl@gmail.com dgmtoperation1.dtl@gmail.com ram.kumar@dtl.gov.in subhash40285@gmail.com	Managing Director, TANTRANSCO, 10th Floor/NPKRR Malikai, No. 144 Anna Salai, Chennai-600002 Ph.: 044-28521057 mdtantransco@tnebnet.org
West Bengal State Electricity Transmission Company Ltd (WBSETCL), Vidyut Bhawan, Block-DJ, Sector-II, Bidhan Nagar, Kolkata- 700 091. md@wbsetcl.in	Chairman & Managing Director, Chhattisgarh State Power Holding Company Ltd., Vidyut Seva Bhawan P.O. Sunder Nagar, Danganiya, Raipur- 492 013 (Chhattisgarh) mddiscom@gmail.com mddiscom@cspc.co.in
Chairman, Haryana Vidyut Prasaran Nigam Ltd. Shakti Bhawan, Sector No. 6	Chairman, Kerala State Electricity Board Board Secretariat, Vidyuthi Bhavanam Pattom

Panchkula, Haryana - 134109, chairman@hvpn.org.in	Thiruvananthapuram - 695004 cmdksebs@ksebs.in
Chairman & Managing Director, Transmission Corporation of Telangana Ltd. Vidyut Soudha, Khairatabad, Hyderabad - 500082 cmd@tstransco.in	Managing Director, Bihar State Power Transmission Company Ltd. Vidyut Bhawan, Bailey Road Patna - 800021 mdcellbsptcl@gmail.com sunil2008iitd@gmail.com
Managing Director, Power Transmission Corporation of Uttarakhand Ltd. , Vidyut Bhawan, Saharnpur Road, Near I.S.B.T. Crossing, Dehradun, Uttarakhand - 248002 md@ptcul.org ee_tande_ksp@ptcul.org asi_baig@ptcul.org	Chairman & Managing Director, Punjab State Transmission Corporation Ltd. The Mall, Mall Road, Patiala - 147001, Punjab cmd@pstcl.org se-tlsc-pta@pstcl.org
Managing Director, Jammu & Kashmir State Power Transmission Corporation Ltd. Exhibition Ground, Jahangir Chowk, Srinagar (J&K) - 190009 md@jkspdccl.com mdjkptcl1@gmail.com	The Engineer-in-Chief, Power and Electricity Deptt., Govt. of Mizoram, Power House, Bara Bazar, Aizwal, Mizoram- 796 001, eincpower@gmail.com eincplanning@gmail.com mizoplan@gmail.com
Chairman & Managing Director, Meghalaya Energy Corporation Ltd. Lumjingshai Short Round Road, Shillong- 793001. ewnong@yahoo.com directormeptcl@gmail.com cetranzemeptcl@gmail.com meecl.webportal@gmail.com apborkharpan@gmail.com	Chief Engineer (P), Manipur Electricity Department Govt. of Manipur, Manipur Sectt. South Block, Imphal, Manipur- 795 001. md.mspcl@gmail.com ed.tech.mspcl@gmail.com sandei@ymail.com
Chief Engineer, Nagaland Deptt. of Power, Kohima, Nagaland- 797 001 cetransgen@gmail.com asang.dcare@gmail.com secyit-ngl@nic.in vizo123@gmail.com namheu@gmail.com	Chief Engineer (Power), Department of Power, Govt. of Arunachal Pradesh, Itanagar (Arunachal Pradesh) - 791111 setrans26@gmail.com tklara@hotmail.com vidyutarunachal@rediffmail.com vidyutarunachal@gmail.com
Chairman & Managing Director, Tripura State Elec. Corporation Ltd. Govt. of Tripura, Bidyut Bhawan, Agartala- 799 001. managing.director@tsecl.in director.technical@tsecl.in cmd.tsecl@rediffmail.com	Chairman & Managing Director, Chhattisgarh State Power Transmission Company Limited, Vidyut Seva Bhavan, Danganiya, chairman@cspc.co.in mdtransco@cspc.co.in

Chairman & Managing Director, Rajasthan Rajya Vidyut Utpadan Nigam Ltd. Vidyut Bhawan, Jyoti Nagar, Jaipur (Rajasthan) cmd@rrvun.com dir.oper@rvpn.co.in	Managing Director, Jammu & Kashmir State Power Development Corporation Ltd, PDD Building, Exhibition Grounds, Opposite High Court, Jahangir Chowk, Srinagar (J&K) 190009 md@jkspdcl.com
Commissioner-cum-Secretary(P), Andaman and Nicobar Electricity Department, Secretariat, Andaman and Nicobar Islands, Port Blair- 744101 secyship14@gmail.com	Secretary, Dadra & Nagar Haveli, Electricity Department, Dadar Nagar Secretariat, Silvassa- 396230 tapasyaraghav@gmail.com
Secretary, Lakshadweep Elec. Department, U.T. of Lakshyadeep, Kavaratti- 682555 lk-ktelect@nic.in	Secretary, Puducherry Elec. Department Secretariat, Puducherry- 605001 secycs.pon@nic.in secytran.pon@nic.in
Managing Director, Karnataka Power Corporation Limited No. 82, Shakthi Bhavan, Race Course Road, Bengaluru – 560001 mdkpcl@gmail.com	Chairman, Jharkhand Urja Utpadan Nigam Ltd. Engineering Building, HEC Dhurwa, Ranchi-834004 mdjuunl2018@gmail.com
Chairman & Managing Director, West Bengal Development Power Corporation Ltd.(WBPDCL) Bidyut Unnayan Bhaban, plot 3/C, LABlock, Sector-III, Salt Lake City, Kolkata - 700 098 wbpdcl@wbpdcl.co.in	Managing Director, Chhattisgarh State Power Generation Company Ltd., Vidyut Seva Bhawan P.O. Sunder Nagar, Danganiya, Raipur- 492 013(Chhattisgarh) mdgenco@cspc.co.in
Chief Engineer (Elect.), Goa Electricity Department Vidyut Bhawan, Panaji, Goa- 403001 cee-elec.goa@nic.in elec.goa@nic.in	Chairman & Managing Director, U.P. Rajya Vidyut Utpadan Nigam Ltd., Shakti Bhawan,14- Lucknow 226001 cmd@upptcl.org
Managing Director, Bihar State Power Generation Company Limited 5th Floor, Vidyut Bhawan, Bailey Road, Patna (Bihar) md.bspgcl@gmail.com	Managing Director, Sikkim Power Development Corporation Ltd. 31-A, N.H. Way, Gangtok-737101 sikkim.serc@gmail.com
Chairman & Managing Director, TANGEDCO, 10th Floor/NPKR Ramasamy Malikai, No. 144, Anna Salai, Chennai – 600 002 chairman@tnebnet.org	Chairman & Managing Director, POWERGRID, Saudamini, Plot No.2, Sector 29, Near IFFCO Chowk, Gurgaon – 122 001 cmd@powergrid.in
Chairman & Managing Director, NTPC Ltd. NTPC Bhawan, Core 7,	Chairman & Managing Director, THDC INDIA LTD.

Scope Complex 7, Institutional Area, Lodhi Road, New Delhi- 110003 cmd@ntpc.co.in amanna@ntpc.co.in kamalverma@ntpc.co.in shipratyagi@ntpc.co.in dhananjaykumar@ntpc.co.in	Pragatipuram, Bye Pass Road, Rishikesh, Uttarakhand- 249201 cmd@thdc.co.in
Chairman, Bhakra Beas Management Board, Sector -19B, Madhya Marg, Chandigarh – 160019 cman@bbmb.nic.in	Chairman & Managing Director, SJVN LIMITED, Himfed Building, New Shimla 171009 sectt.cmd@sjvn.nic.in nandlal.sharma@sjvn.nic.in
Chairman & Managing Director, NEEPCO Ltd. Brookland Compund, Shillong- 793003 vksnhpc@yahoo.co.in	Chairman & Managing Director, Damodar Valley Corporation (DVC), Head Quarter, DVC Towers, VIP Road Kolkata – 700054 chairman@dvc.gov.in dharmadas.tripathi@dvc.gov.in
Chairman & Managing Director, NLC India Limited, Cuddalore District, Tamilnadu cmd@nlcindia.in	Chairman & Managing Director, NPCIL, Nabhiya Urja Bhavan, Anushaktinagar, Mumbai-400094 npciltecrectt@npcil.co.in
Chairman & Managing Director, National Hydro Power Corporation Ltd. Corporate Office, NHPC Office Complex, Sector 33, Faridabad, Haryana- 121003, cmd@nhpc.nic.in	Shri E.V. Rao, KEC International Limited, RPG House, 463, Dr. Annie Besant Road, Worli, Mumbai-4000 03 raoev@kecrpg.com kecindia@kecrpg.com
Chairman, Resonia Limited (erstwhile Sterlite Power Transmission Ltd.), The Mira Corporate, Suit, Plot No. 1&2, C Block, 2nd Floor, Ishwar Nagar, Mathura Road, New Delhi – 110065 rohit.gera@sterlite.com tan.reddy@sterlite.com kamlesh.garg@sterlite.com arun.sharma1@sterlite.com	Shri Milind Nene, Dy. President, Kalpataru Power Transmission Ltd., Plot No. 101, Part-III, GIDC Estate, Sector-28, Gandhinagar-382028, Gujarat kaushal.thakkar@kalpatarupower.com thakkarkaushal86@yahoo.com ajay.tripathi@kalpatarupower.com milind.nene@kalptarupower.com
Mr. Bipin B. Shah, Vice President-Transmission, Torrent Power Limited, 3rd Floor, Jubilee 2 House, Shahpur, Ahmedabad-380001 NAMANSHAH@torrentpower.com MAYANKGUPTA@torrentpower.com bipinbshah@torrentpower.com kashyapdesai@torrentpower.com	Shri P.G. Suresh Kumar, Director, L&T IDPL, Kudgi Transmission Ltd., 1 st Floor, TCTC Building, Mount Poonamallee Road, Manapakkam, Chennai-600 089 pgsk@Lntidpl.com csr@Intecc.com

Sr. Vice President, M/s Adani Power Limited, 7th Floor, Sambhav Building, Judges Bungalow Road, Bodakdev, Ahmedabad, Gujrat- 380015 Anil.sardana@adani.com praveen.tamak@adani.com sameer.ganju@adani.com sunnykumar.singh@adani.com	Director General, Electric Power Transmission Association (EPTA), First Floor, 6 Basant Lok, Vasant Vihar, New Delhi - 110070 dg.epta@epta.in epta.dg@gmail.com
Shri Suresh Reddy, Director, L&T Infrastructure Development Projects Limited (L&T IDPL), L&T campus TCTC building , First Floor, Mount Poonamalle Road, Manapakkam, Chennai, Tamil Nadu -600089, contactus@lntidpl.com csr@lntecc.com	Chairman & Managing Director, Neyveli Lignite Corporation Limited Corporate Office, Block -1 Neyveli – 607801 cmd@nlcindia.in
Chairman & Managing Director, Reliance Power, Reliance Centre, Ground Floor 19, Walchand Hirachand Marg, Ballard Estate, Mumbai 400 001 reliancepower.investors@relianceada.com rpower.mcafilling@relianceada.com reliancepower.ipo@relianceada.com	Shri Vijayanand Semletty, Associate Director-Commercial Regulatory, Sekura 503A, Windsor, Off CST Road, Kalina Mumbai-400098 Vijayanand.Semletty@Sekura.in Neeraj.Verma@energy-sel.com Nimish.Sheth@energy-sel.com
Director, Darbhanga – Motihari Transmission Co. Ltd. 6th Floor, Plot No. 19 & 20, Film City, Sector 16-A, Noida, Uttar Pradesh-201301 Neeraj.Verma@Sekura.in Nimish.Sheth@Sekura.in Vijayanand.Semletty@Sekura.in	Chairman and Managing Director, M/s Juniper Green Transmission Private Limited rohit.gera@junipergreenenergy.com rohit.gera91@gmail.com
Chairman & Managing Director, Tata Power, NDPL House, Hudson Lines, Kingsway Camp Delhi-110009 BD@tatapower.com neeraj.srivastava@tatapower.com piyushkumar@tatapower.com nitin.kumar@tatapower.com vrshrishande@tatapower.com	Chairman & Managing Director, M/s ReNew Transmission Ventures Private Limited anuj.jain@renewpower.in mohit.jain@renewpower.in amit.kumar1@renewpower.in pankaj.kumar@renew.com
Director, M/s. G.R. Infraproject limited, transmission@grinfra.com ashwin@grinfra.com modassar.a@grinfra.com akul.s@grinfra.com	Chairman & Managing Director, M/s Apraava Energy Private Limited Rajiv.mishra@apraava.com naveen.munjal@apraava.com roshni.shah@apraava.com sumit.sinha@apraava.com siddhartha.ghosh@apraava.com

CMD, M/s Megha Engineering & Infrastructures Ltd., jsrinivaskumar@meilgroup.in	Shri I R Venkatraman (Head & VP - Regulatory & Contracts), Indiegriid Unit No. 101, First Floor, Windsor, Village KoleKalyan, off CST Road, Vidyanagari Marg, Kalina, Santacruz (East), Mumbai - 400098 venkatraman.inumula@indigrid.com vivek.karthikeyan1@indigrid.com
Shri Gulam Mir Mohd., Electric M &RE Division, Choglamsar, Leh-Ladakh194101 cepladakh@gmail.com	Chairman & Managing Director, Pragati Power Corporation Limited, Himadri, Rajghat Power House Complex, New Delhi - 110002 md.ipgpp@nic.in
Sh. Partha Bhattacharya, Essar Power, 27th KM, Surat Hazira Road, District Surat, Hazira, Gujarat 394270 Tamendra.Kumar@essarpower.co.in Rajive.Tiwari@essarpower.co.in Rajat.Bajpai@essarpower.co.in khilendra.pant@essarpower.co.in	Suzlon Renewable Development Limited "Suzlon House", 5 Shrimali Society Near Shree Krishna Centre, Navrangpura, Ahmedabad - 380009. marketing.india@suzlon.com Nilesh.Randave@suzlon.com

Annex B.2.15.

CENTRAL POWER RESEARCH INSTITUTE
CABLES & DIAGNOSTICS DIVISION
P.B. No. 8066, SADASHIVANAGAR SUB P.O
PROF. SIR. C. V. RAMAN ROAD, BANGALORE - 560 080. INDIA.
Tel: +91 80-22072333/2332



REPORT OF ANALYSIS

Test Report No : CPRIBLRCDD25F0029-10B Date: 09.02.2026
Required by : M/s. POWERGRID, SRTS-II RHQ, Bengaluru.
Reference No. & Date : LOA No. SRTS-II/C&M/WC-4140/LOA-3803/2025/4597 dated 28.01.2025 and Amendment-I.

Equipment Assessed	Transformers & Reactors at Odisha
1.	16.67 MVAR, 400 kV, Single Phase, R Phase Keonjhar Line Reactor, 400 kV Baripada Substation, Make: CGL, Sr. No. T8353/8
2.	16.67 MVAR, 400 kV, Single Phase, Y Phase Keonjhar Line Reactor, 400 kV Baripada Substation, Make: CGL, Sr. No. T8353/7
3.	16.67 MVAR, 400 kV, Single Phase, B Phase Keonjhar Line Reactor, 400 kV, Baripada Substation, Make: CGL, Sr. No. T8353/9
4.	50 MVAR, 400 kV, Three Phase, Rengali-Indravati Line Reactor, 400 kV Indravati Substation, Make: BHEL, Sr. No. 6004880
5.	63 MVAR, 420 kV, Three Phase, Bus Reactor, 400 kV Jeypore Substation, Make: BHEL, Sr. No. 6005650
6.	63 MVAR, 420 kV, Sundargarh#1 Line Reactor, Three Phase, 400/220 kV Rourkela Substation, Make: CGL, Sr. No. T8820B/4
7.	50 MVAR, 420 kV, Chaibasha#2 Line Reactor, Three Phase, 400/220 kV Rourkela Substation, Make: BHEL, Sr. No. 6005038

Scope of Work : Analysis and Submitting Final Report on aged Transformers and Reactors

This report consists of the following:

No. of pages (Total) : 9


(DILLIP KUMAR PUHAN)
TEST ENGINEER


(K. P. MEENA)
ADDITIONAL DIRECTOR

FINAL ANALYSIS REPORT

1. Make: CGL, Sr. No. T8353/8, Rating: 400 kV, 16.67 MVAR, Single Phase, R Phase Keonjhar Line Reactor, 400 kV Baripada Substation, Year of Manufacturing: 1993 (**33 Years old**), Date of Re-commissioning: 04.02.2014 Overhauling done: 29.12.2013

The diagnostic test data provided by POWERGRID have been analysed in detail and following are our comments and recommendations:

1. IR and PI values obtained on the winding insulation sections lie in the normal permissible range. IR values obtained on core insulation (CC-G, CC-CL and CL-G) are also normal.
2. Tan delta and capacitance values obtained on the winding insulation lies in the normal permissible range. Tan delta and capacitance values obtained on HV and Neutral bushings lie in the normal permissible range.
3. Moisture content in the solid insulation lies in the permissible range.
4. Measured vibration values lie in the normal permissible range.
5. The oil test results are normal indicating healthy condition of the reactor oil.
6. D.G.A results are normal indicating normal internal condition of the reactor.
7. The calculated Degree of Polymerization value (551.45) shows moderate deterioration indicating reasonably good condition of the solid insulation.

Recommendations:

From the diagnostic test data, it can be inferred that the condition of Reactor is moderate. Close monitoring of Furan needs to be carried out.


(DILLIP KUMAR PUHAN)
TEST ENGINEER


(K. P. MEENA)
ADDITIONAL DIRECTOR

FINAL ANALYSIS REPORT

2. Make: CGL, Sr. No. T8353/7, Rating: 400 kV, 16.67 MVAR, Single Phase, Y Phase Keonjhar Line Reactor, 400 kV Baripada Substation, Year of Manufacturing: 1993 (**33 Years old**), Date of Re-commissioning: 04.02.2014, Overhauling done: 29.12.2013, Filtration done in Jan 2022 due to high moisture content in oil.

The diagnostic test data provided by POWERGRID have been analysed in detail and following are our comments and recommendations:

1. IR and PI values obtained on the winding insulation sections lie in the normal permissible range. IR values obtained on core insulation (CC-G, CC-CL and CL-G) are also normal.
2. Tan delta and capacitance values obtained on the winding insulation lies in the normal permissible range. Tan delta and capacitance values obtained on HV and Neutral bushings lie in the normal permissible range.
3. Moisture content in the solid insulation lies in the permissible range.
4. Measured vibration values lie in the normal permissible range.
5. The oil test results are normal indicating healthy condition of the reactor oil.
6. D.G.A results are normal indicating normal internal condition of the reactor.
7. The calculated Degree of Polymerization value (595.25) shows moderate deterioration indicating reasonably good condition of the solid insulation.

Recommendations:

From the diagnostic test data, it can be inferred that the condition of Reactor is moderate. Close monitoring of Furan needs to be carried out.


(DILLIP KUMAR PUHAN)
TEST ENGINEER


(K. P. MEENA)
ADDITIONAL DIRECTOR

FINAL ANALYSIS REPORT

3. Make: CGL, Sr. No. T8353/9, Rating: 400 kV, 16.67 MVAR, Single Phase, B Phase Keonjhar Line Reactor, 400 kV, 400 kV Baripada Substation, Year of Manufacturing: 1993 (**32 Years old**), Date of Re-commissioning: 04.02.2014, Overhauling done: 29.12.2013, Filtration done in Jan 2022 due to high moisture content in oil.

The diagnostic test data provided by POWERGRID have been analysed in detail and following are our comments and recommendations:

1. IR and PI values obtained on the winding insulation sections lie in the normal permissible range. IR values obtained on core insulation (CC-G, CC-CL and CL-G) are also normal.
2. Tan delta and capacitance values obtained on the winding insulation lies in the normal permissible range. Tan delta and capacitance values obtained on HV and Neutral bushings lie in the normal permissible range.
3. Moisture content in the solid insulation lies in the permissible range.
4. Measured vibration values lie in the normal permissible range.
5. The oil test results are normal indicating healthy condition of the reactor oil.
6. D.G.A results are normal indicating normal internal condition of the reactor.
7. The calculated Degree of Polymerization value (539.86) shows moderate deterioration indicating reasonably good condition of the solid insulation.

Recommendations:

From the diagnostic test data, it can be inferred that the condition of Reactor is moderate. Close monitoring of Furan needs to be carried out.


(DILLIP KUMAR PUHAN)
TEST ENGINEER


(K. P. MEENA)
ADDITIONAL DIRECTOR

FINAL ANALYSIS REPORT

4. Make: BHEL, Sr. No. 6004880, Rating: 400 kV, 50 MVAR, Three Phase, Rengali-Indravati Line Reactor, 400 kV Indravati Substation, Year of Manufacturing: 1987 (**38 Years old**), Date of Commissioning: 16.03.1990 (**35 Years in Service**), Reactor failed in 2004 and recommissioned in 2005 after repair, Oil filtration done in 2018 and 2020 due to bushing replacement, Oil replaced with GTOL in 2017.

The diagnostic test data provided by POWERGRID have been analysed in detail and following are our comments and recommendations:

1. IR and PI values obtained on the winding insulation sections lie in the normal permissible range. IR values obtained on core insulation (CC-G, CC-CL and CL-G) are also normal.
2. Tan delta and capacitance values obtained on the winding insulation lies in the normal permissible range. Tan delta and capacitance values obtained on HV bushings lie in the normal permissible range.
3. Moisture content in the solid insulation marginally exceeds the permissible range indicating moderately wet insulation.
4. Measured vibration values lie in the normal permissible range.
5. The oil test results show lower value of BDV (52.1 kV) and higher water content in the reactor oil.
6. D.G.A results are normal indicating normal internal condition of the reactor.
7. Furan analysis shows increasing trend in furan content from 0.311 mg/kg in 2020, through 0.561 mg/kg in 2023 to 0.778 mg/kg 2024 indicating rapidly deteriorating condition of the solid insulation. The calculated Degree of Polymerization value (530.24) shows moderate deterioration indicating reasonably good condition of the solid insulation.

Recommendations:

Based on the diagnostic test results, it is recommended to carry out drying of the reactor to reduce the high moisture content present in the solid insulation. In addition, furan levels should be closely monitored for at least one year to track the progression of paper insulation degradation. If a further rise in furan concentration is observed despite the drying process, replacement of the reactor should be considered to ensure reliability and prevent potential failure.


(DILLIP KUMAR PUHAN)
TEST ENGINEER


(K. P. MEENA)
ADDITIONAL DIRECTOR

FINAL ANALYSIS REPORT

5. Make: BHEL, Sr. No. 6005650, Rating: 420 kV, 63 MVAR, Three Phase, Bus Reactor-1, 400 kV Jeypore Substation, Year of Manufacturing: 1997 (**28 Years old**), Date of Commissioning: 26.05.1998 (**27 Years in Service**), Major overhauling done in Sept 2020.

The diagnostic test data provided by POWERGRID have been analysed in detail and following are our comments and recommendations:

1. IR and PI values obtained on the winding insulation sections lie in the normal permissible range. IR values obtained on core insulation (CC-G, CC-CL and CL-G) are also normal.
2. Tan delta and capacitance values obtained on the winding insulation lies in the normal permissible range. Tan delta and capacitance values obtained on HV bushings lie in the normal permissible range.
3. Moisture content in the solid insulation lies in the permissible range.
4. Measured vibration values lie in the normal permissible range.
5. The oil test results are normal indicating healthy condition of the reactor oil.
6. D.G.A results show normal concentration of hydrocarbon gases indicating normal internal condition of the reactor. But CO and CO₂ were higher before major overhauling and exhibiting increasing trend after overhauling.
7. Furan analysis shows increasing trend in furan content from 0.346 mg/kg in 2020, to 1.163 mg/kg 2024 indicating rapidly deteriorating condition of the solid insulation. The calculated Degree of Polymerization value (497.1) shows moderate deterioration indicating reasonably good condition of the solid insulation.

Recommendations:

Furan analysis and other diagnostic results reveal Reactor insulation system is in a moderate condition. To ensure reliability, it is recommended to conduct regular furan and DGA monitoring to track the insulation aging trends. A long-term replacement plan needs to be made to address progressive deterioration.


(DILLIP KUMAR PUHAN)
TEST ENGINEER


(K. P. MEENA)
ADDITIONAL DIRECTOR

FINAL ANALYSIS REPORT

6. Make: CGL, Sr. No. T8820B/4, Rating: 420 kV, 63 MVAR, Three Phase, Sundargarh#1 Line Reactor, 400/220 kV Rourkela Substation, Year of Manufacturing: 2002 (**23 Years old**), Date of Commissioning: 02.03.2003 (**22 Years in Service**), Overhauling done in 2020.

The diagnostic test data provided by POWERGRID have been analysed in detail and following are our comments and recommendations:

1. IR and PI values obtained on the winding insulation sections lie in the normal permissible range. IR values obtained on core insulation (CC-G, CC-CL and CL-G) are also normal.
2. Tan delta and capacitance values obtained on the winding insulation lies in the normal permissible range. Tan delta and capacitance values obtained on HV bushings lie in the normal permissible range.
3. Moisture content in the solid insulation lies in the permissible range.
4. The oil test results higher water content in the reactor oil.
5. D.G.A results show normal concentration of hydrocarbon gasses indicating normal internal condition of the reactor. But CO and CO₂ are exhibiting increasing trend.
6. Furan Analysis shows low furan content (0.205 mg/kg) indicating healthy condition of the solid insulation.

Recommendations:

From the diagnostic test data, it can be inferred that the condition of the reactor insulation system is generally healthy. All the bushings are in healthy condition. In view of higher water content in the reactor oil recommended for filtration and hot circulation.


(DILLIP KUMAR PUHAN)
TEST ENGINEER


(K. P. MEENA)
ADDITIONAL DIRECTOR

FINAL ANALYSIS REPORT

7. Make: BHEL, Sr. No. 6005038, Rating: 420 kV, 50 MVAR, Three Phase, Chaibasha#2 Line Reactor, 400/220 kV Rourkela Substation, Year of Manufacturing: 1989 (**36 Years old**), Date of Commissioning: 31.08.1993 (**32 Years in Service**), Recommissioned in 2013 and overhauling done in 2020.

The diagnostic test data provided by POWERGRID have been analysed in detail and following are our comments and recommendations:

1. IR and PI values obtained on the winding insulation sections lie in the normal permissible range. IR values obtained on core insulation (CC-G, CC-CL and CL-G) are also normal.
2. Tan delta and capacitance values obtained on the winding insulation lies in the normal permissible range. Tan delta and capacitance values obtained on HV bushings lie in the normal permissible range.
3. Moisture content in the solid insulation lies in the permissible range.
4. Measured vibration values lie in the normal permissible range.
5. The oil test results are normal indicating healthy condition of the reactor oil.
6. D.G.A results show increasing trend in hydrocarbon gases although concentration is not high. CO and CO₂ were high before overhauling and are exhibiting increasing trend after overhauling indicating deterioration of solid insulation.
7. Furan analysis also shows increasing trend in total furan content from 2.056 mg/kg in 2023 to 2.27 mg/kg in 2024 indicating active deterioration of solid insulation. The calculated Degree of Polymerization shows lower DP values indicating substantial aging of solid insulation.

Recommendations:

From the diagnostic test data, it can be inferred that the condition of the Reactor is critical. Considering the requirement for high system reliability, replacement of the Reactor is recommended to prevent potential failures and ensure continued safe operation.


(DILLIP KUMAR PUHAN)
TEST ENGINEER


(K. P. MEENA)
ADDITIONAL DIRECTOR

CENTRAL POWER RESEARCH INSTITUTE
CABLES & DIAGNOSTICS DIVISION
P.B. No. 8066, SADASHIVANAGAR SUB P.O
PROF. SIR. C. V. RAMAN ROAD, BANGALORE - 560 080. INDIA.
Tel: +91 80-22072333/2332



NOTE

CPRI analysis and recommendations are limited to the diagnostic test data provided by POWERGRID. CPRI accepts no responsibility or liability for in-service failure of the transformers in near future. Occurrence of abnormal operating conditions in the power system can lead to transformer failure. The probability of abnormal operating conditions in the power system cannot be predicted.

(DILLIP KUMAR PUHAN)
TEST ENGINEER

(K. P. MEENA)
ADDITIONAL DIRECTOR

Annex B.2.17

**Review of DSM Charges due to system
issue in WBES Scheduling Portal for
HVDC Pusauli from NTPC Kahalgaon
Stage-1**

By POWERGRID ER-I

Background

- Energy scheduling for HVDC Pusauli is being carried out on a daily **D-1 basis** through the WBES portal (<https://newwb.es.gridindia.in/>).
- Earlier, the portal operated in the "**Full Requisition**" mode by default. It was sufficient to enter **zero (0)** in the **OnBar(n)** column (Manual Input mode) for the time blocks from **08:00 hrs to 16:00 hrs**, as the energy requirement during this period was met through renewable sources.
- Recently (a couple of months back), the portal's default mode has been changed to "**Full Surrender**".

Systemic Issue Explained:

Systemic Issue

Screenshot of the Energy Scheduling Platform (ESG) interface showing a Requisition form and a table of Requisition Details.

Requisition Form Fields:

- Date: 11-08-2026
- Buyer Region: ERLDC
- Buyer: HVDC_PUSAULI
- Seller Region: ERLDC
- Seller: KHSTPPJ
- Revision: 2
- Comments: Enter Comments

Requisition Details Table:

Time Block	Time Desc	OnBar Ent	OffBar Ent	Latest Restrict Req	OnBar (I/P)	RestrictReq(n)	OnBar(n)	OffBar (I/P)	OffBar (n)	Operation
1	00:00-00:15	0.68	0	0	0	0	0	0	0	Manual input
2	00:15-00:30	0.68	0	0	0	0	0	0	0	Manual input
3	00:30-00:45	0.68	0	0	0	0	0	0	0	Manual input
4	00:45-01:00	0.68	0	0	0	0	0	0	0	Manual input
5	01:00-01:15	0.68	0	0	0	0	0	0	0	Manual input
6	01:15-01:30	0.68	0	0	0	0	0	0	0	Manual input
7	01:30-01:45	0.68	0	0	0	0	0	0	0	Manual input
8	01:45-02:00	0.68	0	0	0	0	0	0	0	Manual input
9	02:00-02:15	0.68	0	0	0	0	0	0	0	Manual input
10	02:15-02:30	0.68	0	0	0	0	0	0	0	Manual input
11	02:30-02:45	0.68	0	0	0	0	0	0	0	Manual input
12	02:45-03:00	0.68	0	0	0	0	0	0	0	Manual input
13	03:00-03:15	0.68	0	0	0	0	0	0	0	Manual input

Annotation: Value more than "OnBar Ent" is reduced to "0", without giving any error while saving.

Summary

	July 2026 (03.07.2026 to 31.07.2026)	August 2026 (01.08.2026 to 19.08.2026)
Normative Capacity of NTPC Kahalgaon Stage-1	764.4 MW	764.4 MW
HVDC Pusauli GNA Allocation	0.8 MW	0.8 MW
HVDC Pusauli Actual Consumption	195.053 MWH	216.681 MWH
HVDC Pusauli Consumption considered for DSM charges for zero schedule	94.7 MWH (approx. 48.50% of total consumption)	121.11 MWH (approx. 55.8% of total consumption)
DSM charges paid for the mentioned period	Rs.6,57,010.10	Rs.9,57,597.20
	Total = 16,14,607.00	
Approximate DSM charges payable by POWERGRID for 3 weeks, based on previous week's bills @Rs.2,67,000.00 per week	Rs.8,01,000.00 (@Rs.2,67,000.00 per week)	
Extra DSM charges paid (approx.)	Rs.8,13,607.00	

Hence, it is requested to revise the DSM account schedule of HVDC Sasaram for the mentioned period, considering the fact that the issue arose due to systemic issue.

Thank you



ग्रिड-इंडिया
GRID-INDIA

ग्रिड कंट्रोलर ऑफ इंडिया लिमिटेड
(भारत सरकार का उद्यम)
GRID CONTROLLER OF INDIA LIMITED
(A Government of India Enterprise)



[formerly Power System Operation Corporation Limited (POSOCO)]

पूर्वी क्षेत्रीय भार प्रेषण केन्द्र / Eastern Regional Load Despatch Centre

कार्यालय : 14, गोल्फ क्लब रोड, टॉलीगंज, कोलकाता - 700033
Office : 14, Golf Club Road, Tollygunge, Kolkata - 700033
CIN : U40105DL2009GOI188682, Website : www.erldc.in, Tel. : 033 23890060/0061

No.: ERLDC/MO/ERPC/2026/602

Date: 10.09.2026

To
The Member Secretary
ERPC
Tollygunge, Kolkata-700033

Subject: Regarding lower DC declaration during peak hours as compared to off-peak hours of the same day by ER ISGS under Partial Outage

Sir,

This is to inform you that instances of declaration of lower DC during peak hours as compared to off-peak hours of the same day have been observed in respect of certain ER ISGS, wherein "Partial Outage" has been cited as the reason for such revision.

In this regard, Clause 63(j)(iv) of Hon'ble CERC order in Petition No. 9/SM/2024 dated 05.10.2025 stipulates as follows:

"The generating stations shall not be permitted to declare Peak hours DC less than off-peak hours DC, other than in cases of forced outage or partial outage. Grid India shall strictly monitor the same. In case a generating station provides less DC during peak hours of the day than off-peak hours, the DC for such generating station for the purpose of fixed charges shall be taken as the lower of the two."

During the last six months, several instances of reduced DC declarations during peak hours as compared to off-peak hours have been observed, as detailed in Annexure-I.

ERLDC has sought clarification from Patrattu STPP Stage-I for the period 13.04.2026 to 15.04.2026 and Talcher Stage-I for the period 27.07.2026 to 30.07.2026, vide letters dated 15.04.2026 and 31.07.2026 respectively, regarding the reduction of DC during peak hours and the corresponding higher DC declaration during off-peak hours, wherein "Partial Outage" has been cited as the reason for revision. However, the requisite clarifications, including the specific reason/cause of the partial outage and supporting details/digital records, are yet to be furnished by the generating stations.

पंजीकृत कार्यालय : बी-9, प्रथम तल, कुतुब इंस्टीट्यूशनल एरिया, कटवारिया सराय, नई दिल्ली - 110016
Registered Office : B-9, 1st Floor, Qutab Institutional Area, Katwaria Sarai, New Delhi - 110016
Website : www.grid-india.in

In the absence of reasonable justification for such lower DC declaration during peak hours by the generating stations mentioned in Annexure-I, the reduced DC may be considered for determination of fixed charges for the concerned generating stations for the days on which such instances have been observed, in accordance with the provisions of the aforesaid Hon'ble CERC Order.

Further, the modalities for calculation and furnishing of such reduced DC by ERLDC in the data being furnished for preparation of REA, and the corresponding utilization of such reduced DC by ERPC in publication of REA, may be finalized.

The matter may also be placed for deliberation in the upcoming 243rd OCC meeting, if considered necessary.

भवदीय / Yours faithfully,



सुरजीत बनर्जी

कार्यपालक निदेशक

Annexure-I

Instances of Lower DC During Peak Hours Compared to Off-Peak Hours

Sl No	Date	Generating Station	Peak Avg DC (MW)	Off-Peak Avg DC (MW)	Peak – Off Peak (MW)	Off-Peak > Peak (%)
1	03-04-2026	FSTPP_III	417.66	468.19	-50.53	10.79
2	13-04-2026	PTPS_I	450	701.25	-251.25	35.83
3	14-04-2026	PTPS_I	450	587.5	-137.5	23.4
4	23-04-2026	PTPS_I	500	696.25	-196.25	28.19
5	09-06-2026	FSTPP_I_II	1199.12	1496.48	-297.36	19.87
6	11-07-2026	North_Karanpura_STPS	1020.93	1753.59	-732.66	41.78
7	13-07-2026	KHSTPP_I	676.55	751.85	-75.3	10.02
8	14-07-2026	FSTPP_III	400	465.47	-65.47	14.07
9	21-07-2026	FSTPP_III	260	368.31	-108.31	29.41
10	23-07-2026	FSTPP_III	346.88	402.22	-55.34	13.76
11	27-07-2026	KHSTPP_I	650.62	735	-84.38	11.48
12	27-07-2026	TSTPP_I	750	858.91	-108.91	12.68
13	28-07-2026	North_Karanpura_STPS	1580	1782.38	-202.38	11.35
14	28-07-2026	TSTPP_I	625	804.22	-179.23	22.29
15	19-08-2026	FSTPP_I_II	1270	1490.82	-220.82	14.81
16	20-08-2026	FSTPP_I_II	1070	1403.24	-333.24	23.75
17	24-08-2026	TSTPP_I	725	836.86	-111.86	13.37
18	28-08-2026	PTPS_I	1056.25	1403.12	-346.88	24.72
19	01-09-2026	North_Karanpura_STPS	898	1237.5	-339.5	27.43
20	03-09-2026	FSTPP_III	275	456.53	-181.53	39.76
21	03-09-2026	FSTPP_I_II	823.06	1314.07	-491.01	37.37
22	04-09-2026	FSTPP_III	259.19	389.51	-130.32	33.46
23	04-09-2026	FSTPP_I_II	823.06	1107.3	-284.24	25.67
24	07-09-2026	FSTPP_III	350	459.78	-109.77	23.88
25	08-09-2026	FSTPP_III	323.31	438.56	-115.25	26.28
26	08-09-2026	FSTPP_I_II	823.06	1215.76	-392.7	32.3

Note:

1. The instances mentioned above pertain to the period from 01-04-2026 to 09-09-2026.
2. The instances have been identified where the average DC declared during peak hours is 10% or more lower than the average DC declared during off-peak hours.
