



भारत सरकार / Government of India
विद्युत मंत्रालय / Ministry of Power
पूर्वी क्षेत्रीय विद्युत समिति / Eastern Regional Power Committee

सं /NO. ERPC/EE/OPERATION/2026/ 846

DATE:24.07.2026

सेवा में /To
संलग्न सूची के अनुसार /As per list enclosed.

विषय : 17.07.2026 (शुक्रवार) को ईआरपीसी सचिवालय, कोलकाता में भौतिक रूप से आयोजित 241वीं ओसीसी बैठक के कार्यवृत्त – के संबंध में

Sub: Minutes of 241st OCC Meeting held on 17.07.2026 (Friday) physically at ERPC Secretariat, Kolkata – reg

महोदय/महोदया,
Sir(s)/Madam,

कृपया अपनी जानकारी और आवश्यक कार्रवाई के लिए 17 जुलाई 2026 (शुक्रवार) को आयोजित 241वीं ओसीसी बैठक के कार्यवृत्त संलग्न देखें। यह ईआरपीसी वेबसाइट (www.erpc.gov.in) पर भी उपलब्ध है।

Please find enclosed **Minutes of 241st OCC Meeting** held on 17.07.2026 (Friday) physically at ERPC Secretariat, Kolkata at 10:30 hrs. This is for your kind information and necessary action. The same is also available at ERPC website (www.erpc.gov.in).

टिप्पणियाँ, यदि कोई हों, कृपया यथाशीघ्र इस कार्यालय को अग्रेषित करें।
Observations, if any, may please be forwarded to this office at the earliest.

इसे सदस्य सचिव के अनुमोदन से जारी किया जाता है।
This issues with the approval of Member Secretary.

भवदीय /Yours faithfully


24/07/2026
आर.के.मीना / (R.K.Meena)
एसई (ऑपरेशन)/SE(Operation)

Organization	Category	E-mail
CEA	GM division	gmcea@nic.in
ERPC	RPC	mserpc-power@nic.in
ERPC		secomm1.erpc@gov.in
ERPC		seop-erpc@gov.in
ERPC		erpc-protection@gov.in
ERPC		hoo-erpc@gov.in
CEA	RPSO	hoo-rpso.kol-power@gov.in
DVC	Central GENCO	sanjay.sharma@dvc.gov.in
DVC		santosh.panda@dvc.gov.in
NTPC		jaiprakashverma@ntpc.co.in
NTPC Farakka		sumeetnarang@ntpc.co.in
NTPC		sraybarman@ntpc.co.in
NTPC		ksureshbabu@ntpc.co.in
NTPC		arshadjilani@ntpc.co.in
NTPC Nabi Nagar		skupadhyay@ntpc.co.in
NTPC-Barh		aksrivastava16@ntpc.co.in
NTPC-Barh		abhishekmurari@ntpc.co.in
NTPC-TSTPS		suranjandas@ntpc.co.in
BRBCL/NTPC		bnayadav01@ntpc.co.in
POWERGRID ER-II	Central TRANSCO	partha.ghosh@powergrid.in
POWERGRID ER-II		mithun.gayen@powergrid.in
POWERGRID ER-II		snayek@powergrid.in
POWERGRID ER-II		pmaity@powergrid.in
POWERGRID ER-I		sudeepkumar@powergrid.in
Powergrid, Odisha Project		eswar@powergrid.in
Powergrid, Odisha Project		ajayasahu@powergrid.in
WBSEDCL	DISCOM	preetam72@gmail.com
ERLDC	RLDC	surajit.banerjee@grid-india.in
ERLDC		dbiswas@grid-india.in
ERLDC		bilash.achari@grid-india.in
ERLDC		manasdas@grid-india.in
ERLDC		chandan.mallick@grid-india.in
ERLDC		rkpradhan@grid-india.in
GRIDCO	Others	ele.plsahoo@gridco.co.in
GRIDCO		ele.bpmohapatra@gridco.co.in
CHEMTROLS		anirudhya.saha@chemtrols.com
CHEMTROLS		anish.raigopal@chemtrols.com
CHEMTROLS		shivaji.dewanjee@chemtrols.com
CESC	Private GENCO	koushik.banerjee@rpsg.in
CESC		anupam.biswas@rpsg.in
CESC		debarshi.de@rpsg.in
MPL		rautpv@tatapower.com
GMR, Odisha		swapnajit.panigrahi@gmrgroup.in
GMR, Odisha		diptikanta.panda@gmrgroup.in
JSW		biswanath.patel@jsw.in
JSW		mahendra.malik@jsw.in
APNRL		shiladityachatterjee@adhunikpower.co.in
APNRL		rajukumarsharma@gmail.com
APNRL		rahul.kumar@adhunikpower.co.in
MPL		jetir@tatapower.com
HEL		archita.dutta@rpsg.in

Organization	Category	E-mail
JIPL		jiplscheduling@jindalgroup.com
INDIGRID	Pvt. TRANSCO	abhishek.kukreja@indigrid.com
INDIGRID		dinesh.laha@indigrid.com
SIKKIM POWER TRANSMISSION		ayyappa.y@greenkogroup.com
WBSLDC		arnab.basu@wbsetcl.in
WBSLDC	SLDC/STU	utsab.aditya@gmail.com
WBSLDC		svkbanerjee@yahoo.com
WBSLDC		sanjibroy12235@gmail.com
WBSLDC		cecpwbsetcl@gmail.com
BSPTCL		sldc.bseb@gmail.com
BSPTCL		gagankmishra@gmail.com
SLDC, Ranchi, JUSNL		tuneshwarkumar@gmail.com
SLDC, Ranchi, JUSNL		rimitopno@gmail.com
SLDC, Ranchi, JUSNL		rajmailme82@gmail.com
WBSETCL		sajalkbag74@gmail.com
WBSETCL		ce.wbsldc@gmail.com
WBSETCL		cpd.wbsetcl@gmail.com
OPTCL		ele.smsahoo@optcl.co.in
OPTCL		ele.scdash@optcl.co.in
SLDC, Odisha		ele.dpkar@sldcorissa.org.in
SLDC, Odisha		sanjayasldc@gmail.com
WBPDC	State GENCO	mpodder@wbpdcl.co.in
WBPDC		rk.koley@wbpdcl.co.in
TVNL		bk20tvnl@gmail.com
OHPC		chandan.panda143@gmail.com
OHPC		dasakshaya26@gmail.com



Eastern Regional Power Committee

MINUTES OF 241st OCC MEETING

Venue: ERPC Secretariat, Kolkata

Date: 17.07.2026

Contents

1. PART-A: CONFIRMATION OF MINUTES	2
1.1. Confirmation of Minutes of 240 th OCC Meeting held physically at ERPC Secretariat on 12 th June 2026	2
2. PART-B: ITEMS FOR DISCUSSION.....	2
2.1 Update on follow up agenda: ERPC	2
2.2 Issues for follow-up: ERLDC	19
2.3 Grid Frequency Excursions and Operational Compliance by Regional Utilities: ERLDC	21
2.4 Shutdown proposals for NHAI diversion works: ERLDC	24
2.5 Talcher – Kolar Bipole Shutdown for NHAI Diversion Work at Nayagarh, Odisha: NTPC Talcher	26
2.6 Embargo on Drawal through STPS–Chandil 220 kV Tie Line: WB SLDC	26
2.7 Emergency condition arose for the network around KTPP after sudden outage (long term or may be permanent outage) of KTPP unit 3 since 18.06.26: WB SLDC	28
2.8 Temporary Group Control Operation of 400 kV Bus Reactors at Arambag: WB SLDC	29
2.9 Update on Reconductoring of the lines of Chukha Transmission system under ERES-44 scheme: WB SLDC	30
2.10 Challenges in Grid operation due to upcoming influx of Datacentre load: ERLDC	31
2.11 Status of Operationalization of SAMAST at SLDC Jharkhand for Transition of Scheduling & Accounting Functions of PTPS-I (PVUNL): ERLDC.....	32
2.12 Restoration of 400kV Patna-Naubatpur Ckt#2 and 400kV Patna-Naubatpur-Balia Ckt#1 to its original configuration: ERLDC	33
2.13 Shutdown proposal of Thermal generating units: ERPC	34
2.14 Frequency Response Performance of Eastern Region for May 2026 events: ERLDC	35
2.15 Requirement of Standardized Procedure for Charging of Transmission Lines During Partial Reconductoring Works and Interim Bypass arrangements: ERLDC	37
2.16 ERLDC Operating procedure for ER Grid for 2026-27: ERLDC	38
2.17 Switching off the idle charged 132 kV PTPS–DVC Patratu Tie Line (5C): PVUNL	39
2.18 Implementation of DTPC scheme in place of PLCC Scheme (with updated heavier Pedestal mount Wave trap) due to space constraint in the existing bays: POWERGRID, ER-II	40
2.19 Shutdown of various lines in Sikkim & Noth Bengal for SAG correction, rectification of damage leg and for providing Guy support to protect concerned tower due to Hill shrinking/land slide/ change of river course: POWERGRID, ER-II	41
2.20 Recovery of cost against AMR implementation: POWERGRID, ER-II	44
3. PART-C: ITEMS FOR INFORMATION.....	45
3.1. ER Grid performance during June 2026	45
3.2. Non-Submission of FRC data in stipulated time-frame: ERLDC	45
4. PART-D: OPERATIONAL PLANNING.....	47
4.1. Major Thermal Generating Units/Transmission Element outages/shutdown in ER Grid (as on 09-07-2026)	47
4.2. Long outage report of transmission Element (MORE THAN 01 WEEK) (As on 09.07.2026):	48

4.3.	Commissioning of new units and transmission elements in Eastern Grid in the month of June-2026	52
4.1.	UFR operation during the month of June 2026	54

EASTERN REGIONAL POWER COMMITTEE

MINUTES OF 241st OCC MEETING TO BE HELD ON 17.07.2026 (FRIDAY) AT 10:30 HRS

Member Secretary, ERPC welcomed all OCC members and other participants who were present physically as well as those who had joined virtually to the **241st OCC Meeting**.

Thereafter he requested all the participants to give brief introduction.

□ He outlined the performance of ER grid during **June-2026** highlighting the following points:

- In **June-2026**, energy consumption of ER was **20783 MU** which is **9 % more** than **June -2025**.
- In **June-2026**, Peak demand met of ER was **34324 MW** which is **3.9 % more** than **June -2025**.

❖ Thermal **PLF** of **ER** during **June-2026** was **76.7 %** whereas National average is **72.3%**.

❖ Generating stations whose **PLF** was **90%** or more during **June-2026**:

Utility	Generating station	PLF (%)
IPP	HALDIA TPP (HEL)	99
	JOJOBERA TPS (TATA POWER)	90

❖ During **June-2026**, **74%** of the time, the ER grid frequency was within IEGC Band (49.90Hz-50.05Hz).

Coal stock position (As on 13.07.2026) is as follows:

SL.	Name of States/Power Stns.	% of Actual Stock vis-à-vis Normative Stock
1.	Jharkhand (TVNL)	171%
2.	Odisha (IB TPS)	93%
3.	West Bengal (WBPDCCL)	67%
4.	D.P.L. TPS	18%
5.	DVC	89%
6.	NTPC	82%

Onset of Commercial operation of **TEESTA V HPS (NHPC)** w.e.f 13.07.26 was highlighted while the respective Units 1&2 were synchronized with the grid on 12.07.26.

ED, ERLDC touched upon the following key facets:

- Concern was raised on frequent fluctuations in frequency beyond the prescribed IEGC band. In June and July 2026, frequency has been observed to dip as low as 49.5 Hz as well as shoot up to 50.3 Hz.
- Rising ER demand, especially peak demand of Bihar exceeding 9000 MW in July'26 was highlighted.

List of participants attached at **Annex-A**.

Member Secretary, ERPC requested S.E (Operation) to take up the agenda for discussion.

1. PART-A: CONFIRMATION OF MINUTES

1.1. Confirmation of Minutes of 240th OCC Meeting held physically at ERPC Secretariat on 12th June 2026

The Minutes of 240th Operation Coordination Sub-Committee meeting held on 12.06.2026 was circulated vide letter dated 19.06.2026.

Deliberations in the meeting

Since no comments have been received so far, the Minutes of 240th OCC meeting were confirmed.

2. PART-B: ITEMS FOR DISCUSSION

2.1 Update on follow up agenda: ERPC

a) Intrastate Transmission Network Assessment & Mitigation-Odisha

Reference:

Implementation of the Under Voltage Load Shedding (UVLS) scheme in the Odisha system has been under review since the 231st, 232nd, 233rd, and 234th OCC Meetings held on 22.09.2025, 24.10.2025, 22.11.2025, and 23.12.2025 respectively.

The matter was also discussed in the recently concluded 55th TCC/ERPC meeting held on 16.12.2025 and 17.12.2025 at Kalimpong, West Bengal. As per deliberation in 55th TCC Meeting, **300MW load** has been identified and it will be operationalized before **Summer '26**.

The continued delay in implementation is posing increasing risks not only to the Odisha system but also to the Eastern Region as a whole during the forthcoming Summer-2026 period.

- During a review meeting held on 30.04.2026, OPTCL and SLDC Odisha informed that the quotation from the existing ADMS vendor had been received and was under examination. Further, 31 feeders of TPCODL and 23 feeders of TPNODL have been identified under the scheme. The target date for completion was indicated as June-2026.

As per 56thTCC meeting:

Odisha updated that 400 MW load has been identified for UVLS scheme & the scheme will be implemented by June-2026.

During deliberation, ERLDC highlighted the transmission constraints in Odisha network and stated that the reconductoring of 400 kV OPGC-Lapanga-Meramundali section shall be completed as long-term solution to mitigate the transmission constraint issue in Odisha system.

CEA also pointed out that in transmission RA plan of Odisha, the reconductoring of intra-state lines will be completed by OPTCL in the timeframe of 2026-27. However there is no progress in this regard. CTUIL also submitted the delay in strengthening of intra-state networks by OPTCL will result in ISTS system vulnerable in future.

56th TCC Decision:

Forum advised OPTCL to implement the UVLS scheme by June-2026 without any further delay.

OPTCL would submit a timeline for carrying out reconductoring of their intra-state networks as finalized in the resource adequacy plans.

As per 56th ERPC meeting:

Odisha officials were not present in the preceding (ERPC) discussion.

ERLDC highlighted the urgency of early completion of this scheme for voltage stability of Bhubaneswar region.

56th ERPC Decision:

ERPC forum advised OPTCL to implement the UVLS scheme by June-2026 without any further delay. Detailed work plan for reconductoring of intrastate transmission line shall be shared with ERPC & ERLDC within two weeks.

As per 240th OCC:

OPTCL informed that the work was under progress and would require approximately one additional month for completion. It was stated that the execution is being carried out through the on-going ADMS project.

240th OCC Decision

Forum strongly urged OPTCL to complete the UVLS implementation by June 2026 by treating UVLS as a priority project for the capital region of Bhubaneswar.

Deliberations in the meeting

OPTCL informed:

- *The UVLS scheme is being implemented through ADMS in two phases (200 MW each).*
- *Thirty of the thirty-five Grid Substations are already covered under ADMS while the remaining substations are under integration.*
- *The agency is carrying out logic testing and installation of RTU components.*

OCC Decision

- ✓ *In view of system security, OCC stressed the importance of completing implementation of at least Phase-I of ADMS on priority basis.*
- ✓ *OPTCL shall implement the first phase (200 MW) of UVLS without further delay and complete the balance work by August 2026. Weekly progress reports along with a detailed implementation timeline i.r.o individual feeders shall be submitted to ERPC.*

b) Update on reconductoring of 400kV Talcher-Meramundali D/C & Farakka- Kahalgaon D/C.

Reconductoring of 400kV Talcher-Meramundali D/C & Farakka- Kahalgaon D/C:

As per update in 237th OCC dated 17.03.2026:

- ✓ 42Ckm out of 51Ckm reconductoring work of ckt 1 was completed and line had to be restored with this partial reconductoring on 03.03.2026 due to system constraint. Later on, POWERGRID requested to avail shutdown of LILO (Angul bypass) portion of ckt 2 bypassing the LILO part upto 11th April'2026 to complete balance 20 Ckm (out of 35Ckm).
- ✓ In this regard, one meeting was convened on 06.03.26 involving SRPC, SRLDC, ERPC, ERLDC, SLDC Odisha. After detailed deliberation, the forum concluded that the shutdown request submitted by POWERGRID for bypassing the LILO section of the 400 kV Talcher–Meramundali line cannot be approved at present due to prevailing system security concerns and high SR demand. It was also decided that the said request will be reassessed after peak demand scenario of SR tentatively end of April 2026 or 1st Week of March 2026.

Deliberations in the meeting

Powergrid informed:

- *The deployment of agency for the reconductoring/bypass work has been delayed and the agency is expected to be mobilised by end-July'26.*
- *The work sequence involves taking a shutdown of the Talcher–Meramundali Circuit-2, isolating the LILO point, and directly connecting Talcher–Meramundali so that both circuits remain in service while reconnection work proceeds at the LILO point thereafter.*

OCC Decision

Powergrid was advised to ensure agency mobilisation without further delay by end-July'26 and to share a firm date-wise execution schedule with ERPC/ERLDC.

Reconductoring of 400KV Farakka-Kahalgaon D/C (Important for WB System):

As per update in 237th OCC dated 17.03.2026:

- It was decided in the meeting dated 26th Feb'26 that the Shutdown be extended up to 08.03.2026. Further, an update received from ER-1 POWRGRID via mail dated 09-03-2026 that 92kM out of 94kM has been completed.
- At KHSTPP end, upgradation work of FSTPP-I main bay (being done by KHSTPP) and line bay upgradation work (being done by POWERGRID) are also expected to be completed.
- At FSTPP end, line bay upgradation works are in progress and expected to be completed. Moreover, material supply for carrying out the jack bus reconductoring work has reached FSTPP. The jack bus reconductoring work will be taken up in last week of March and will be completed in 18 days as per plan shared by FSTPP.

Record Notes of Discussion (RNoD) among CTUIL, POWERGRID, NTPC, ERLDC and ERPC for resolution of issues related to the Reconductoring works of Farakka –Kahalgaon 400kV D/c transmission line and Talcher – Meramundali 400kV D/Ctransmission line under Eastern Region Expansion Scheme-XXXXIII (ERES-43) , held on **1st July 2026** attached at **Annex B.2.1.(b)**

Deliberations in the meeting

Powergrid updated:

- *Reconductoring/conductor-replacement work could not commence as originally planned due to non-availability of material at site, material is expected to reach site by September 2026. So, reconductoring of ckt-2 is being planned from October 2026.*

WB SLDC submitted :

- *In view of the festival period, it is proposed that shutdown may commence after the festival, i.e., from November 2026 in place of the earlier October 2026 and the same may be carried out in phase-wise manner.*
- *ERLDC was requested to study the effects of simultaneous shutdown of multiple 765 kV lines on ER network in November 2026.*
- *Concern was raised on potential vulnerability of WB network in absence of 765 kV support and with only one circuit of 400KV Farakka-Kahalgaon D/C.*

ERLDC apprised that shutdown of 765 kV New Ranchi–Medinipur section can not be allowed concurrently with 400KV Farakka-Kahalgaon. However, shutdown of 765 kV Medinipur-New Jeerat can be availed at the same time. November will be the most suitable period for allowing the shutdown so that loading of 400 KV Farakka-Kahalgaon remains well within thermal limit.

OCC Decision

- ✓ *OCC agreed for shutdown for reconductoring of 400KV Farakka-Kahalgaon (ckt-2) from November 2026. The appropriate section of 765 kV corridor may be clubbed with this S/D as submitted by ERLDC.*
- ✓ *OCC highlighted the significance of bay upgradation at NTPC Farakka end for optimal utilization of the 400KV Farakka-Kahalgaon (ckt-1).*
- ✓ *It was also advised that a special meeting may be convened involving NTPC Farakka, NTPC Kahalgaon, Powergrid (ER-I & II), WB SLDC and WBSEDCL to finalize the time line for long-pending bay upgradation works at NTPC Farakka end.*

c) Urgent Review of Phase I Compliance for CEA Flexible Operation Regulations, 2023

- ☐ *CEA has issued a gazette notification dated January 30, 2023, regarding flexible operation of coal-fired generating units.*
- ☐ *As per CEA gazette notification extraordinary, part III, section 4, no. 61 (CG-DL-E-31012023-243299), the coal-based power generating units shall have flexible operation capability with minimum power level of 55%. This capability includes a ramp rate of 2% between 55%-70% and a ramprate of 3% above 70%. This capability was mandated within one year of the notification, i.e., by Jan 2024. Further, the regulation mandates that generating units not capable of achieving a minimum power level of 40% shall achieve the same as per the CEA phasing plan.*
- ☐ *It may be noted that CEA's flexible operation regulations were notified after successful pilot test/study conducted across the country in association with international partners and BHEL.*
- ☐ *In this regard, it is pertinent to mention that 91 Units of total installed Capacity 51,080 MW in aggregate of various thermal power plants have been notified under Phase I (July 2024 – June 2026) for operation at 40% MTL (Minimum Technical Load). These units are required to carry out the necessary retrofitting/modifications as recommended by the respective OEMs so as to be fully prepared for sustained operation at 40% MTL by June 2026, as mandated under the provisions of the aforesaid Regulations.*

- ❑ It may also be noted that successful and sustained operation at 40% MTL with Indian coal has been demonstrated by other generating utilities (Under Pilot Phase) such as West Bengal Power Development Corporation Limited (WBPDCCL) at Sagardighi Unit-8 and Damodar Valley Corporation (DVC) at Mejia Unit-8, following suitable retrofits as advised by the OEMs.
- ❑ Further, in order to compensate the losses on account of flexible operation, CERC has already incorporated most of the recommendations of CEA's compensation methodology such as for additional Capex, oil consumption, additional auxiliary power consumption, and heat rate degradation.
- ❑ Therefore, all generating utilities are requested to complete the retrofit, control system tuning, trial runs etc. of all units under Phase I by June 2026 in consultation with the OEM positively.
- ❑ It is also requested to furnish the progress and updates (as per attached format) of First Phase units by the end of November 2025 and thereafter every month.

As per 56th TCC meeting

DVC informed that 40% MTL can be achieved only with higher grade of coal. As coal is arranged from various sources having different grades, the sustained operation of boilers at 40% MTL with different grades of coal has not yet been demonstrated.

DVC representative further highlighted that many of the state generators has not yet implemented 55% technical minimum norm.

56th TCC Decision:

TCC advised DVC & JSWEUL to send their inputs & difficulties faced by them in achieving 40% MTL on sustained basis to ERPC.

As per 56th ERPC meeting

- ✓ MS, ERPC stated that considering the projected increase in penetration of RE power (rooftop solar, Solar parks, wind power), there is a need of operating all thermal generators at their technical minimum (including intra-state TPPs).
- ✓ Representatives of Thermal generators (identified under Phase I) expressed the technical constraints due to non-availability of quality coal for operating at 40% technical minimum.
- ✓ Member (GO&D), CEA inquired about whether there is any compensation mechanism at state level for operation of intra-state thermal generators at technical minimum in ER.
- ✓ WB informed that they have prepared a draft regulation regarding compensation for intra-state TPPs for operating at technical minimum which is yet to be approved by WBERC.

56th ERPC Decision:

- ✓ ERPC advised all thermal generating stations to intimate their preparedness as well as technical difficulties, if any, in achieving 40% MTL to ERPC Secretariat. ERPC Secretariat would subsequently forward the issues to CEA.
- ✓ The forum also advised to ER states to operate intra-state TPPs at MTL(55%) to assist in grid stability in view of increasing RE penetration and to introduce compensation mechanism for operation of intra-state thermal generators at technical minimum through respective SERCs.

Deliberations in the meeting

WB SLDC stated that compensation mechanism for operating at 55% technical minimum has been incorporated in the recently drafted tariff regulations of WBERC and accordingly necessary changes shall be done in the SAMAST scheduling software for enabling all intra-state generators (WB) to operate at 55% technical minimum as per respective schedules.

WBPDCCL confirmed technical readiness to operate at the compensated level; the earlier outstanding issue of compensation for operation below normal technical minimum has since been addressed in the new regulation.

OCC Decision

OCC forum was apprised that most inter-state generating stations are presently operating at around 55% technical minimum, and are now required to move towards 40% MTL flexible operation. It is also advised to state generating stations to operate at 55% Technical minimum level.

All thermal generators were advised to furnish specific operational difficulties, if any, in operating at 40% technical minimum to ERPC secretariat before the ensuing NPC meeting (scheduled in September 2026).

d) Upgradation of 66/11 kV Bulbuley Sub-station to 132 kV Level and Associated Transmission Infrastructure works in Gangtok

Upgradation of 66/11 kV sub-station at Bulbuley (Gangtok) to 132 kV voltage level, establishment of AIS extension bay at POWERGRID 132/66 kV sub-station at Lagyap and GIS bays at Bulbuley along with installation of 132/66 kV, 2x25 MVA transformers at Bulbuley along with construction of 132 KV LILLO arrangement at 132 kV D/C transmission line. Estimated Cost = Rs. 167.42 Crore. Bulbuley is the only major substation within Gangtok proper that still has scope for upgradation and availability of ROW corridor for construction of transmission line. Capacity augmentation is not possible in remaining two other 66/11 kV sub-stations within Gangtok proper, i.e. Tadong and Sichey, owing to space and ROW constraints. These areas are now completely built up and commercialized. Urgent need to upgrade the main power supply to main Gangtok city area to 132 kV voltage level due to current condition of the existing lines all of which are 66 kV lines. Need to undertake the work soon since there will not be any ROW availability or space for expansion of sub-station in Gangtok proper in the near future.

Deliberation in 56th TCC meeting:

MS, ERPC informed that as per CEA recommendation, instead of upgrading Bulbuley S/s to 132 kV level, Perbing S/s has been recommended for early commissioning to cater to the load of Gangtok area.

Powergrid informed that the Perbing S/s will be commissioned by **5th June, 2026**.

56th TCC Decision:

TCC noted.

56th ERPC Decision:

ERPC noted.

Deliberations in the meeting

Powergrid updated:

The Perbing S/S has already been charged at 132 kV level. ICT has also been charged. Charging at 66 kV level is still pending that shall be done by 31st July 2026.

OCC Decision

OCC noted.

e) Spare Reactor procurement under Eastern Regional Pool as per CEA norms

In **52nd ERPC** meeting, estimated expenditure of **Rs. 55.67 Crores** (exclusive of GST but including transportation cost) was concurred towards procurement of spare reactors in ER pool by Powergrid ER-II as per CEA spare norms.

STATE	VOLTAGE	SIZE	STORAGE PLACE
WEST BENGAL	400 KV	125 MVAR	DURGAPUR SS
		80 MVAR	BINAGURI SS
SIKKIM	220 KV	31.5 MVAR	NEW MELLI SS
JHARKHAND	400 KV	125 MVAR	NEW RANCHI SS
ODHISSA	400 KV	63 MVAR	ROURKELLA SS

In **54th TCC** meeting, Powergrid intimated that the tender evaluation is on progress.

As per 55th TCC meeting:

- ✓ POWERGRID updated that tender has been awarded for the reactors except 31.5 MVAR reactor.
- ✓ Since the 31.5 MVAR reactor is seldom used at present, hence they have segregated it from the rest of the population and it will be done separately.

As per 240th OCC:

Powergrid updated the status of procurement as follows:

240th OCC Decision

OCC advised Powergrid to keep all spare reactors at designated substations of respective states as per submitted delivery schedule, i.e. within 2 years. At the same time procurement of 63 MVAR reactor at Rourkela S/s needs to be expedited. Monthly update on spare reactor procurement to be shared with ERPC.

Deliberations in the meeting

Powergrid updated the status of procurement as follows:

STATE	VOLTAGE	SIZE	STORAGE PLACE	UPDATE
WEST BENGAL	400 KV	125 MVAR	DURGAPUR SS	LOA is awarded with delivery schedule of 2 years
		80 MVAR	BINAGURI SS	
SIKKIM	220 KV	31.5 MVAR	NEW MELLI SS	
JHARKHAND	400 KV	125 MVAR	NEW RANCHI SS	
ODHISSA	400 KV	63 MVAR	ROURKELLA SS	NOA has been placed and negotiation is under process.

OCC Decision

OCC advised Powergrid to keep all spare reactors at designated substations of respective states as

per submitted delivery schedule, i.e. within 2 years. At the same time procurement of 63 MVAR reactor at Rourkela S/s needs to be expedited. Monthly update on spare reactor procurement to be shared with ERPC.

f) Restoration of 220KV FSTPP LALMATIA Line.

The line is out of service since long due to tower collapse. Presently 220 kV Farakka-Lalmatia line is charged(from loc no 241 to loc 84) at 132 kV voltage level for anti-theft purpose by tapping at loc. No. 100-101.

As per 56th TCC :

- ✓ JUSNL informed that the line will be completed by 10th June.
- ✓ ERLDC suggested that JUSNL may take all requisite FTC clearances beforehand so that the line may be charged at the earliest.

56th TCC Decision:

TCC noted the work progress by JUSNL and advised NTPC to check healthiness of the bay equipment of the line at Farakka end.

56th ERPC Decision:

ERPC noted.

As per 240th OCC:

JUSNL updated:

- ✓ Erection of one tower and stringing over a span of 450 meters is pending. Expected timeline of completion is **25th June 2026**.
- ✓ Bay upgradation is pending at NTPC Farakka end.

240th OCC Decision

- OCC advised JUSNL to adhere to the schedule of line restoration i.e. by 25th June 2026.
- NTPC was advised to keep the bay ready at Farakka STPS end to facilitate charging of the 220kV FSTPP-LALMATIA Line.
- Implementation of Farakka islanding scheme is to be taken up after restoration of 220KV FSTPP LALMATIA Line.

Deliberations in the meeting

NTPC submitted:

- *Through Agreement dtd. 25.10.2021(attached at **Annex B.2.1.f**) Farakka–Lalmatia Transmission System (FLTS) was handed over to JUSNL by ECL on “as is where basis at ZERO cost and relieving NTPC from O&M responsibility.*
- *As per the agreement, JUSNL shall have the ownership of FLTS and shall maintain FLTS at their own cost. Responsibility for operation and maintenance shifts to JUSNL.*
- *JUSNL will bear all costs related to Overhauling, Upgradation ,Replacement ,Maintenance and any incidental expenses.*

Communications were sent to JUSNL as per details below:

- *Vide letter dated 31.01.2026, NTPC requested JUSNL to update the bay equipment and*

protection system along with the new transmission line. Requisite AC and DC supply source for the Bay and CRP will be made ready by NTPC.

- Vide letter dated 14.02.2026, NTPC requested JUSNL to update the complete bay equipment and protection system along with the new transmission line. Necessary AC and DC supply source for the Bay and CRP will be made ready by NTPC.

OCC Decision

- ✓ The forum advised JUSNL and NTPC to decide the ownership of bay at Farakka end bilaterally. Accordingly, bay works at Farakka end may be initiated at the earliest.

g) A review of the Flue Gas Desulfurization (FGD) installation, in consultation with beneficiaries, is required for ongoing and operational Category 'C' thermal power projects of NTPC: GRIDCO

- It is to mention that MoEF&CC has notified Environment (protection) Rules on 11.07.2025 wherein applicability of SO₂ emission standards in thermal power plants has been revised based on their location/category. As per the above amendment, Sulphur dioxide emission standards shall not be applicable to all Category C thermal power plants subject to ensuring compliance of stack height criteria notified vide notification number GSR 742 (E) dated 30th August 1990.
- As understood CEA vide letter dtd 20.08.2025 intimated all RPCs that the generating utilities would be required to review the FGD installation in consultation with Discoms at the ongoing projects at Category C TPPs.
- In the said letter, CEA referred a meeting that was held with GENCOs on 18.07.2025 and with vendors on 08.08.2025 with a request to RPCs to convene a special TCC/RPC meeting at the earliest and deliberate the matter and various proposals furnished by CEA.
- Further, as per the minutes of the meeting Dtd 25.07.2025, the generating companies were advised to discuss various aspects with the beneficiary Discoms their willingness to have FGD installed and pay for the cost attributable to FGD (CAPEX+OP-EX) or stop the project and pay the fixed cost (CAPEX) incurred so far.
- In this regard this is to be mentioned that, Darlipalli STPS of NTPC is coming under category 'C' as per MOEF Notification dtd 11.07.2025. FGD has been already installed and commissioned from 01.07.2024 for unit#2 and 27.01.2025 for unit#1.

NTPC has been raising bills approx. 1.5 Crs/month to 1.8 Crs/month towards secondary energy charges (OP-EX) as Odisha has 50% allocation from the said project. Hence, GRIDCO vide letter dtd 02.09.2025 requested NTPC for discontinuation of supplementary energy charge (ECS) towards FGD for Darlipalli STPS to which NTPC replied that "FGD system has been declared Commercial Operation in accordance with the provision of CERC Tariff Regulation 2019, and the bills of supplementary variable charges are also being raised accordingly to all the constituent beneficiaries of the station. The matter is being looked into by concerned statutory authorities and any decision and subsequent direction issued in such cases will be duly complied by NTPC."

In view of the exemption for Category 'C' TPPs from SO₂, standards GRIDCO raises the following points for discussion:

1. Discontinuation of FGD Operation: NTPC is requested to stop the operation of the FGD system at Darlipali STPS, as it is no longer mandatory under the revised MoEF&CC notification.
2. Assessment and Financial Justification: NTPC should furnish the project-wise status of

FGD implementation for all its generating stations in the Eastern Region. Furthermore, a detailed financial assessment must be conducted to compare the cost benefit of operating with FGD versus without FGD; ensuring beneficiaries are not burdened with unnecessary CAPEX and OP-EX.

Deliberation in 56th TCC meeting

- ✓ NTPC stated that the units where FGD has already been commissioned, not keeping the FGD operational might result in deterioration of the equipment.
- ✓ WBSEDCL suggested that NTPC may run FGD on intermittent basis to prevent such an outcome and not burden the beneficiaries with higher OPEX that results due to continuous operation. The matter of aux consumption issue will be resolved by adopting suitable methodology.

56th TCC Decision:

TCC advised NTPC to adhere to the decision taken in the meeting held on 12.12.2025, chaired by Secretary, Power GoI, for TPPs which have already installed FGD, where it has directed that the future course may be mutually decided by respective stakeholders. TCC opined that the matter, being a national level issue, may be referred to NPC and referred the matter to ERPC for concurrence.

Deliberation in 56th ERPC meeting

- ✓ GRIDCO emphasized that NTPC needs to discontinue the operation of the FGD system at Darlipalli STPS immediately, in strict compliance with the MoEF&CC Environment (Protection) Rules dated 11.07.2025. Such unilateral operation of FGD by NTPC Darlipalli is imposing an unjustified financial burden on GRIDCO and subsequently on consumers.
- ✓ WBSEDCL agreed with the submission of GRIDCO and stated that NTPC should discontinue the operation of the FGD system at Darlipalli STPS. As an alternative measure, WBSEDCL suggested that FGD can be run intermittently to keep the FGD in serviceable condition. They also submitted that without any clear directives to run the FGD, the same may attract audit observations.
- ✓ NTPC representative informed that keeping the FGD system idle for a prolonged period (6 months) might result in deterioration of the FGD components.
- ✓ Member (GO&D), CEA opined that as CAPEX is already being paid by the constituents and since OPEX constitutes a relatively small portion of overall tariff, NTPC may be allowed to run the FGD as it helps in reduction of the pollution level in the nearby area of power plant and also keep the FGD in working condition.

ERPC Decision:

ERPC forum suggested that NTPC should submit the cost-benefit analysis report of running the FGD by considering the sale of gypsum to ERPC Secretariat by 30th June, 2026 and the matter will be deliberated in sub-committee meeting of ERPC for taking the further course of action.

Deliberations in the meeting

NTPC informed:


Report on Cost-benefit analysis for FGD installation is under approval stage at Corporate Commercial and the same shall be shared in the next OCC.

OCC Decision

NTPC was advised to positively submit cost benefit analysis along with inputs from concerned OEM at the earliest.

h) High loading and N-1 violation of 400/220kV ICTs at Bolangir (POWERGRID):

Bolangir S/S is one of the major 400/200kV S/S in western Odisha catering load to Bolangir, Kesinga, Bargarh & Katapalli areas. In recent part, demand in this part of Odisha has increased significantly, which ultimately impacts the loading of ICTs of Bolangir. Supporting source of these areas is 220kV-Lapanga-Katapalli -D/C, which also operating at high loading mainly during summer period. ICT loading further increases with opening of 220 kV Katapalli-Bolangir(PG) and 220kV Katapalli-Bargarh lines to limit the loading of 220 kV Budhipadar-Lapanga D/c and 220 kV Lapanga-Katapalli D/c which are not N-1 compliant.

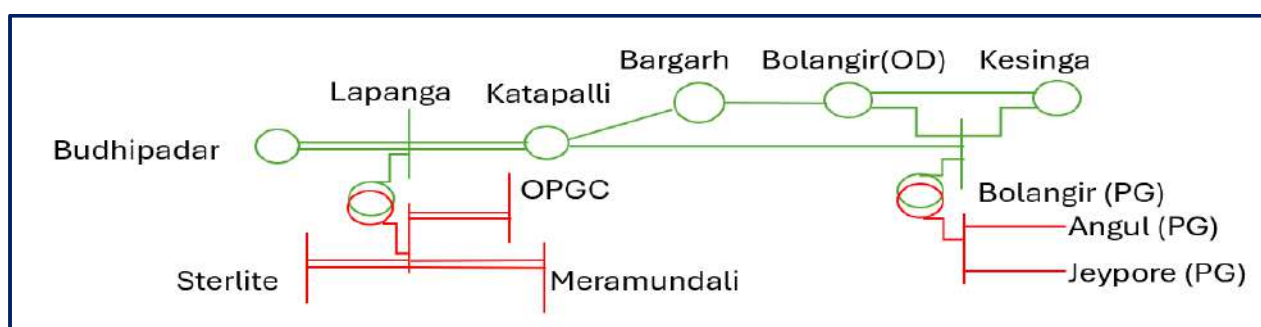

As per 56th ERPC meeting

Chief Engineer, CEA informed that upgradation of this line has already been approved under RA plan for 2026-27. Further, he also pointed out that in transmission RA plan of Odisha, the reconductoring of intra-state lines is to be completed by OPTCL in the timeframe of 2026-27. However, there is no progress in this regard. CTUIL also submitted the delay in strengthening of intra-state networks by OPTCL will result in ISTS system vulnerable in future.

56th ERPC Decision:

The forum advised OPTCL to plan the reconductoring of lines as proposed in the RA plan for 2026-27 at the earliest and submit a timeline of the same to ERPC secretariat.

Deliberations in the meeting

OPTCL informed that proposal of reconductoring of 220 kV intra-state lines connecting Bolangir(PG) is still in planning stage.

OCC Decision

- ✓ *OCC opined that persistent delay in strengthening of intra-state network of Odisha may render the ISTS network vulnerable in near future and thereby took a serious note on the issue.*
- ✓ *OCC urged OPTCL to submit a firm timeline and detailed work schedule for reconductoring of associated 220 kV lines from Bolangir(PG) S/S in the next OCC.*

i) Diversion of RPC approved Spare Transformers and Reactors to the constituents / State Transmission Utilities

- ❑ **Chairperson, CEA/NPC** opined that private Transmission Service Providers (TSPs) may be considered for diversion of RPC approved spare transformers and reactors on a case-to-case basis, subject to discussion in the respective Regional Power Committee (RPC) forum.
- ❑ **Chairperson, CEA/NPC** further suggested that a suitable mechanism for periodic rotation/usage of spare transformers and reactors within the utility or among the constituents / State Transmission Utilities (STUs) may be explored. This would ensure that spare transformers and reactors do not remain unused for prolonged periods and become too old without operational utilization.
- ❑ It was suggested that all RPCs may review the existing Standard Operating Procedures (SOPs) prepared by SRPC and NRPC (attached at **Annexure-B.2.1.i**) in their respective forums, obtain comments from stakeholders, and submit their suggestions. The matter may thereafter be deliberated in the Operation Sub-Group of the NPC for finalization of a uniform SOP at the national level.

As per 17th NPC decision:

All RPCs to explore a suitable mechanism for periodic rotation/usage of spare transformers and reactors within the utility or among the constituents / State Transmission Utilities (STUs) and also examine the inclusion of Private Transmission Service Providers in the scheme. All RPCs may also review the existing Standard Operating Procedures (SOPs) prepared by SRPC and NRPC in their respective RPC forums.

56th TCC Decision:

Forum suggested all the utilities to submit their comments regarding the diversion of spares as well as the penal provision to ERPC secretariat at the earliest so that the matter may be deliberated in the next NPC.

As per 56th ERPC meeting

WBSLDC suggested that the penalty may be levied after duration of 36 months as procurement of new ICTs is taking around 3 years.

Further, representative of Powergrid suggested that penalty of 15% of approved tariff may be adjusted in the procurement of new spare ICTs & reactors.

Member Secretary stated that the spare available in the regional pool should be used in case of exigency and the state should maintain their spare as per extant norms of CEA/CERC.

56th ERPC Decision:

After detailed deliberation, Forum decided that all the concerned utilities will submit their inputs on draft SOPs to ERPC secretariat by 30th June, 2026. The input of ERPC based on the feedbacks received from concerned stakeholders will be submitted in the forthcoming NPC.

Deliberations in the meeting

Regarding the diversion of spares including penal provisions, WBSETCL submitted comments as stated below:

1) Date of effect of penalty related order, if any, should be after the issuance of such order only. It

should not be effective retrospectively.

2) It would be prudent that the penalty may be levied after a duration of 36 months as procurement of new ICTs is taking around 3 years.

3) A penalty of 10% of approved tariff for the diverted equipment may be imposed on the borrower for the duration of deployment beyond 36 months.

4) Periodic energization/testing of idle spares may also be considered to prevent deterioration.

5) Collected penalty amounts may accrue in any separate reliability fund for proper use in future for necessary inspection, testing etc.

6) After release of equipment by the constituents, the equipment may be kept as spare in the nearest location, if possible. It will reduce the cost of transportation otherwise.

OCC Decision

✓ All ER utilities (except WBSETCL) were advised to share their inputs/comments (if any) on the SOP (**Annex B.2.1.i**) on diversion of spares to ERPC by 31st July 2026.

✓ The forum opined that the respective inputs will be placed in the ensuing NPC meeting for consideration and subsequent finalization of the SOP.

j) Update on islanding schemes in ER.

The list of existing Islanding schemes in ER is as under:

Eastern Region (ER)		
1	Kolkata (CESC) IS	City/Major Town/ Strategic Load
2	Howrah (Bandel) IS	City/Major Town/ Strategic Load
3	Bakreswar TPS IS	Industrial and Railway load
4	Haldia (Tata Power) IS	Industrial areas of Haldia and Port
5	Chandrapura (CTPS DVC) IS	Industrial areas

As per 238th OCC:

OCC suggested for formation of a sub group committee under chairmanship of S.E. (Operation), ERPC comprising members from ERPC, ERLDC, concern SLDC and Generating company for regular monitoring of islanding scheme formation and implementation in the ER States. **The committee shall coordinate with stakeholders and submit progress report in OCC.**

A special sub-group has been constituted for the identification and implementation of islanding schemes in the capital cities of ER states.

56th ERPC Decision:

The forum advised that the matter may be regularly followed up in OCC meetings.

1. Ranchi Islanding Scheme

- ☐ Nomination for ER sub-group of islanding scheme implementation was received from JUSNL.
- ☐ The kick-off meeting for the implementation of the Ranchi City Islanding Scheme was held on **23rd April 2026** under chairmanship of ERPC.
- ☐ To accurately define the electrical boundaries and load behaviour of the island, SLDC

Jharkhand was requested to share:

- **Island Boundary & Feeder Logic:** Clearly define the islanded area and provide a comprehensive list of feeders that must be disconnected to ensure successful island formation.
- **Load Profiles:** Node-wise load data (Maximum, Minimum, and Average) for the identified area to ensure generation-load balancing.
- **Defense Mechanism Data:** Current node-wise loads of Jharkhand that are already covered under **AUFLS** (Automatic Under Frequency Load Shedding) and **ADMS** (Automatic Demand Management System).
- **Infrastructure Timeline:** Confirmation of the expected commissioning date for the **400kV Latehar New – Patratu New D/C** line, as this must be integrated into the islanding model.

As per 56th TCC meeting

JUSNL informed that they have already provided data regarding Ranchi islanding scheme.

As per 240th OCC:

ERLDC informed:

Required data from the concerned SLDCs has been received. A base case has been prepared for dynamic/transient study.

240th OCC Decision

- ✓ ERLDC was advised to carry out dynamic study on the base case and share relevant inputs with SLDC Jharkhand.
- ✓ After the finalization of logic, the concerned utility i.e. JUSNL to prepare DPR and implementation plan.

Deliberations in the meeting

ERLDC highlighted some constraints faced in the dynamic study of Ranchi islanding scheme, such as, low voltage issues being faced due to feeding large load segment. This is due to inadequacy of power evacuation corridor from PVUNL. Presently, only few 220 kV lines are feeding all the identified loads and thus, getting overloaded. 400 kV Patratu-Latehar line needs to be commissioned for N-1 compliance in islanding condition.

OCC Decision

- ✓ The forum advised ERLDC to carry out dynamic study considering the upcoming 400 kV Patratu-Latehar line and recommend the study results within a week.
- ✓ JUSNL was advised to expedite commissioning of 400 kV Patratu-Latehar line and submit detailed execution plan in next OCC.

2. Patna Islanding Scheme under PSDF

- In 54th TCC meeting held on 23.06.2025, BSPTCL had proposed to implement Patna Islanding Scheme through Internal Resource Fund.
- However, a meeting was held on 24th June 2025 under the chairmanship of the Hon'ble Minister of Power and Housing & Urban Affairs, wherein the matter of Islanding Patna city was discussed. In the meeting, it was decided that the State of Bihar would submit a proposal for funding the Islanding scheme by the Ministry of Power).

- In compliance to minutes of the meeting held on dt. 24.06.2025, Board of Directors, BSPTCL has approved for implementation of Patna Islanding Scheme through PSDF in 131st BOD meeting held on dt. 17.07.2025 vide its resolution no. 131-06.
- In line with the above, a proposal has been submitted for Implementation of Patna Islanding Scheme under PSDF to NLDC vide this office letter no. 549 dt. 18.07.2025 along with all the required documents in compliance to minutes of meeting held on dt. 24.06.2025.
- Further, Chief Engineer (Generation), CEA has requested the recommendation of ERPC for implementation of Patna Islanding Scheme through PSDF.

As per 56th TCC meeting

SLDC Bihar informed that the PSDF Appraisal committee approved the PSDF grant proposal of Patna islanding scheme and the approval from the PSDF monitoring committee is awaited.

As per 240th OCC:

SLDC Bihar apprised that LOA shall be placed once sanction of PSDF funds is received from NLDC.

240th OCC Decision

OCC noted.

Deliberations in the meeting

SLDC Bihar updated that in-principle approval has been obtained from NLDC on 10th June 2026 while sanction of funds is still awaited.

OCC Decision

OCC noted.

3. IB Valley TPS Islanding Scheme (Odisha)

IB valley TPS Islanding scheme has also been put on hold for long time. The status regarding the same has been sought on urgent basis by Ministry of Power (Govt of India).

As per 56th TCC meeting

OPGC informed that those necessary lines have been identified for Ib valley islanding scheme but base data is required from SLDC Odisha for further action.

240th OCC Decision

ERLDC was advised to carry out revised study on the modified base case recently submitted by OPGC. OPTCL was advised to submit identified loads and detailed implementation logic in the next OCC.

Deliberations in the meeting

SLDC Odisha informed that planning of Bhubaneswar Islanding Scheme (meant for Bhubaneswar & Cuttack area) is being taken on priority as of now. Once the Bhubaneswar islanding scheme gets implemented, IB valley TPS islanding scheme will be taken up for further proceedings.

OCC Decision

OCC noted.

4.Bhubaneswar Islanding Scheme (Odisha)

Nomination for sub-group of islanding scheme implementation in ER is still awaited.

240th OCC Decision

OPTCL was advised to finalize the load and generation philosophy (essential loads, startup power, etc.) and submit detailed technical feasibility including unit capabilities, protection scheme, and control logic within one month.

Deliberations in the meeting

SLDC Odisha updated:

- *Work order for preparation of the Detailed Project Report (DPR) has been issued and a kick-off meeting is planned within the next two weeks.*
- *Three generating units have tentatively been identified as potential islanding sources — two units of GMR and one unit at NTPC Kaniha — though final selection is pending.*
- *The DPR preparation is expected to take about 3–4 months once the generation source is finalized.*

OCC Decision

SLDC Odisha was advised to finalise the generation source for the Bhubaneswar–Cuttack–Puri scheme and share the exact load-shedding quantum with ERPC/ERLDC before proceeding to DPR finalization.

5. Farakka islanding scheme

This is presently not in service due to long outage of 220 kV Farakka-Lalmatia line.

240th OCC Decision

Implementation of Farakka islanding scheme shall be taken up after restoration of 220KV FSTPP LALMATIA Line.

Deliberations in the meeting

OCC Decision

Implementation of Farakka islanding scheme shall be taken up after restoration of 220KV FSTPP LALMATIA Line.

k) Review of AUFLS in Eastern Region: SCADA Integration & Data Updation

- ◆ Based on the recommendation and decisions in 14th NPC meeting held on 05.02.24, 214th OCC meeting and special meeting on 10.07.2024, a load relief quantum of 6916 MW was finalized for Eastern Region. UFR Feeders real time monitoring has been discussed in NPC as well as various fora of ERPC.
- ◆ Further, with new IEGC 2023 the same has been mandated as quoted below: IEGC 2023, Clause 13.d: “SLDC shall ensure that telemetered data of feeders (MW power flow in real time and circuit breaker status) on which UFR and df/dt relays are installed is available at its control centre. SLDC shall monitor the combined load in MW of these feeders at all times.
- ◆ SLDC shall share the above data with the respective RLDC in real time and submit a monthly exception report to the respective RPC. RLDC shall inform SLDCs as well as the concerned RPC on a quarterly basis, durations during the quarter when the combined load in MW of these feeders

was below the level considered while designing the UFR scheme by the RPC. SLDC shall take corrective measures within a reasonable period and inform the respective RLDC and RPC, failing which suitable action may be initiated by the respective RPC.”

As per 56th TCC meeting

Both Bihar & Jharkhand updated that they will Complete AUFLS implementation as well as SCADA integration by end of June 2026.

56th TCC Decision:

TCC urged early completion of AUFLS implementation as well as SCADA integration.

56th ERPC Decision:

ERPC advised concerned ER states for early completion of AUFLS as well as SCADA integration.

Update:

The load relief quantum to be implemented at each stage of AUFLS for FY 2026-27 is computed by NPC based on the regional peak demand met in FY 2025-26. Details enclosed in [Annex B.2.1.g](#).

Stage-wise Load relief= Stage-wise relief (%) * RPRegion * AP/RP

AP: All India Peak Demand Met in MW

RP: Regional Peak Demand Met

As per this methodology, total load relief quantum for ER comes out as 7195 MW against 6916 MW in preceding year.

This 7195 MW of load relief has to be distributed among all ER states as per methodology to be finalized in OCC forum.

As per 240th OCC meeting:

- ✓ SLDC Jharkhand updated that pending 35 MW of AUFLS quantum to be implemented by July 2026.
- ✓ SLDC Bihar updated that out of 1578 MW quantum, 1000 MW has been integrated with SCADA while rest 578 MW is still pending.

240th OCC Decision

- Bihar and Jharkhand utilities shall expedite RTU rectification and SCADA integration works. Completion target is latest by July 2026.
- OCC consented to the methodology of distributing the stage-wise AUFLS load quantum among individual states based on respective contribution in annual energy consumption and peak demand met. All ER states are advised to note the revised AUFLS allocation as communicated in **Annex B.2.1.g**, identify and configure additional AUFLS load quantum and the same needs to be integrated with SCADA accordingly.

Deliberations in the meeting

SLDC Bihar updated that identification of new feeders for the revised load relief quantum is under approval stage

OCC Decision

- ✓ All SLDCs were advised to ensure implementation of adequate stage-wise load relief quantum as detailed below by August 2026. Entire number of feeders should also be integrated in SCADA.

Control Area	Required Load Relief					Implemented Load Relief					Pending Installation
	Stage –I (49.4 Hz)	Stage –II (49.2 Hz)	Stage–III (49.0Hz)	Stage–IV (48.8Hz)	Total Relief by Control Area	Stage –I (49.4 Hz)	Stage –II (49.2 Hz)	Stage–III (49.0Hz)	Stage–IV (48.8Hz)	Total Relief by Control Area	
	(MW)	(MW)	(MW)	(MW)		(MW)	(MW)	(MW)	(MW)		
BSEB	345	399	466	466	1676	316	373	409	424	1522	154
JSEB	103	130	151	151	535	85	111	133	110	439	96
DVC	159	208	243	243	853	173	209	242	239	863	-10
Odisha	304	372	434	434	1544	374.5	377.5	370	452	1574	-30
WB & CESC	523	613	715	715	2567	560	574	712	715	2561	6
Sikkim	5	5	5	5	20	0	0	0	0	0	20
TOTAL	1439	1727	2015	2015	7194	1508.5	1642.5	1848	1927	6959	276

2.2 Issues for follow-up: ERLDC

a) Replacement of CLR insulators of PMJTL lines

- Replacement of faulty Decan make CLR insulators in the 765 kV New Ranchi–Medinipur–New Jeerat corridor and associated 400 kV PMJTL lines has been under discussion in various OCC/TCC meetings owing to the strategic importance of these transmission corridors for reliable power supply to Kolkata and adjoining areas of South Bengal. While replacement activities in the 400 kV system have substantially reduced outage incidences, frequent shutdown requests continue to be received for the 765 kV corridors.
- During FY 2025-26, POWERGRID availed 63 shutdowns on the 765 kV New Ranchi–Medinipur–New Jeerat corridor for replacement of failed CLR insulators. Further, during the ongoing summer period, several additional emergency shutdown requests have already been processed. Such frequent outages, particularly during periods of high demand in West Bengal, pose operational challenges and increase the risk to reliability and security of power supply to Kolkata and surrounding areas. Shutdown of one circuit followed by any contingency on the parallel circuit may lead to a highly stressed system condition.
- In 239th POWERGRID informed that around 5,000 faulty Decan make CLR insulators in the 400 kV system have been replaced, significantly reducing trippings compared to the previous year. However, procurement of replacement insulators for the identified 765 kV corridors has been delayed, with completion now targeted by October 2026. OCC directed POWERGRID to expedite replacement of defective insulators, undertake comprehensive condition assessment of vulnerable locations, improve shutdown planning through consolidated weekly outages, and minimize emergency shutdowns, particularly during the summer.

As per 240th OCC meeting:

Powergrid informed:

- Approximately 28,000 insulators (400 & 765 kV combined) are planned for replacement. For 400 kV system: about 10,000 insulators to be replaced and for 765 kV system: about 17,000 insulators to be replaced.
- Total 10273 Nos (400KV) and 17785 Nos (765KV) CLR insulators are under procurement. As of 30th June 2026, 700 (at 400 kV level) and 850 (at 765 kV level) insulators have been supplied at site and progressive supply will continue.
- Replacement work will be prioritized on critical lines (e.g. 765 kV D/C Ranchi- Medinipur) and shall be carried out progressively, aiming to complete both supply and replacement by October-November 2026.

OCC opined that a special meeting may be convened by ERPC involving stakeholders from Powergrid, WB & ERLDC to finalize a detailed plan for replacement of CLR insulators in a phased manner.

Update:

Special meeting was convened on **10th July, 2026** and relevant details enclosed at **Annex B.2.2(a)**.

Deliberations in the meeting

Powergrid updated the detailed Plan as well as current status for replacement of defective CLR insulator in PMJTL elements as follows:

SL. No.	Name of Line	Total defective insulator	Replaced as on 08.07.2026	Replaced as on 08.07.2026	Date / Tentative date of start of Replacement work	Tentative No of days required	Tentative date of end of Replacement work
1	400kV New Jeerat-Subhasgram Ckt 1	3382	2400	2680	Jul-26	5	Aug-26
2	400kV D/C New Jeerat-Subhasgram Ckt 2	3382	0		Aug-26	18	Sep-26
3	400kV New Jeerat-Jeerat Ckt 1	1123	0		Aug-26	8	Sep-26
4	400kV New Jeerat-Jeerat Ckt 2	1122	0		Aug-26	8	Sep-26
5	400kV Medinipur-Chanditala Ckt 1	303	0		Sep-26	5	Sep-26
6	400kV Medinipur-Chanditala Ckt 2	303	0		Sep-26	5	Sep-26
7	400kV Medinipur-Kharagpur Ckt 1	329	0		Sep-26	5	Oct-26
8	400kV Medinipur-Kharagpur Ckt 2	329	0		Sep-26	5	Oct-26
9	765kV Ranchi-Medinipur Ckt 1	2530	0		Aug-26	15	Nov-26
10	765kV Ranchi-Medinipur Ckt 2	2530	0		Aug-26	15	Nov-26
11	765kV Medinipur-New Jeerat Ckt 1	6362	0	975	Jul-26	30	Dec-26
12	765kV Medinipur-New Jeerat Ckt 1	6363	0	320	Jul-26	30	Dec-26
TOTAL		28,058	2400	3975			

OCC Decision

OCC advised Powergrid to strictly adhere to the submitted schedule of insulator replacement in the 765 kV & 400 kV transmission corridors and urged that the replacements in the 765 kV New Ranchi–

Medinipur section should be completed before commencement of reconductoring in 400KV Farakka-Kahalgaon(ckt-2).

b) SPS for ACCP-II/JSPL

- ❑ Following the 233rd OCC meeting, a special meeting was held on November 26, 2025, to discuss the implementation of System Protection Schemes (SPS) for the new ACCP-II plant, during which OPTCL was advised to assess existing protection adequacy at the JSPL site. Although the site visit was eventually conducted on January 11, 2026, the overall implementation remains significantly delayed. While JSPL has implemented one SPS for injection control, a second scheme designed to restrict drawal at the Meramandali end is currently pending the transmission of Talcher-Meramandali power flow data from OPTCL. Consequently, OPTCL has apprised that installing the necessary RTU at Meramandali for data visibility will require approximately two months.
- ❑ In 235th OCC meeting, forum directed both JSPL and OPTCL to expedite the finalization and implementation of the remaining scheme to ensure grid stability. In 237th OCC meeting, it was advised to SLDC/OPTCL to expedite the implementation.

238th OCC meeting

OPTCL updated that JSPL has placed purchase order for procurement of RTU required for data telemetry of 400kV Talcher-Meramundali lines to JSPL for SPS action. The delivery of the RTU is expected in two weeks. Thereafter, SPS for drawl restriction would be configured at JSPL end.

239th OCC Meeting

- ✓ RTU procurement order has already been placed, and materials are in delivery stage. The RTU will be installed within 10 days after its receipt.
- ✓ Subsequently, implementation of the SPS for shedding JSPL load to limit 400 KV TSTPSMMND flow on sudden loss of ACCP-II generation, will be completed.

240th OCC meeting:

- ✓ OPTCL informed that the data transmission-related works including procurement and installation of RTUs have been completed. However, JSPL informed that issues related to data integration and communication are still persisting.
- ✓ OCC advised JSPL to implement the SPS at the earliest in coordination with OPTCL. Both utilities were advised to resolve the persistent issues bilaterally.

Deliberations in the meeting

OPTCL submitted:

Data pertaining to load flow in 400kV Talcher-Meramundali lines can now be easily accessed by JSPL for SPS implementation.

JSPL was absent in the meeting.

OCC Decision

OCC noted the progress in data telemetry as submitted by OPTCL.

2.3 Grid Frequency Excursions and Operational Compliance by Regional Utilities: ERLDC

- ❑ Increasing penetration of renewable energy (RE), coupled with its inherent variability and uncertainty, has posed greater challenges in maintaining grid frequency. Although the ER currently has a relatively lower share of RE in its generation mix, grid frequency deviations continue to be

influenced by deviations in state drawl and over/under-injection by conventional generating stations. This has made real-time load-generation balancing more challenging.

- ER constituents have generally maintained grid discipline. However, during recent sustained low-frequency events, some constituents exhibited significant deviations from their scheduled drawl, highlighting the need for improved resource adequacy planning, advance resource portfolio management, and timely operational interventions.


Recent Low Frequency Events: Two sustained low-frequency events were observed during **June 2026**:

- **2nd June 2026 (20:00 hrs) to 3rd June 2026 (02:00 hrs)**
- **26th June 2026 (19:00 hrs) to 27th June 2026 (00:00 hrs)**


- Both events occurred during the non-solar evening peak period and were primarily driven by resource shortages, further aggravated by persistent over-drawl (OD) by several constituents across PAN INDIA.
- The maximum OD and the percentage duration of overdraw by ER Constituents during the low-frequency period are summarized below:

State Name	BIHAR	WEST BENGAL	ODISHA	DVC	JHARKHAND
2nd June 2026	Max OD: 151 MW (OD: 4.8%)	Max OD: 633 MW (OD: 48.2%)	Max OD: 103 MW (OD: 10.8%)	Max OD: 299 MW (OD: 74.7%)	Max OD: 120 MW (OD: 56.9%)
26th June 2026	Max OD: 1055 MW (OD: 61.5%)	Max OD: 546 MW (OD: 81.7%)	Max OD: 532 MW (OD: 64.1%)	Max OD: 204 MW (OD: 51.1%)	Max OD: 135 MW (OD: 85.9%)

Frequency plot 2nd June 2026

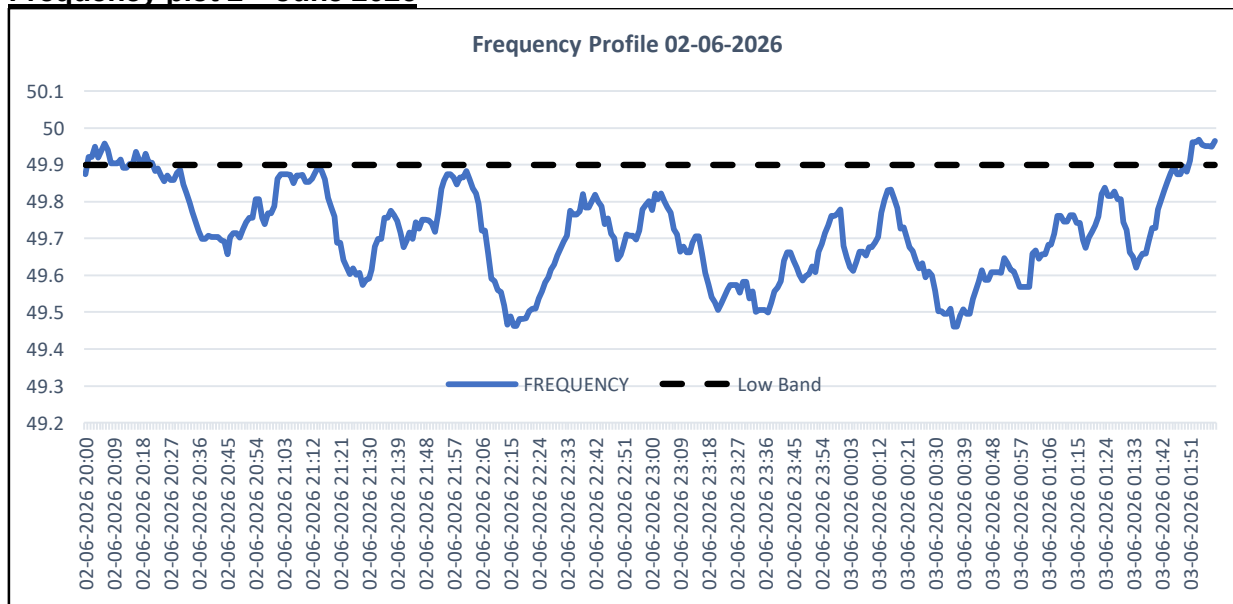

Frequency plot 26th June 2026

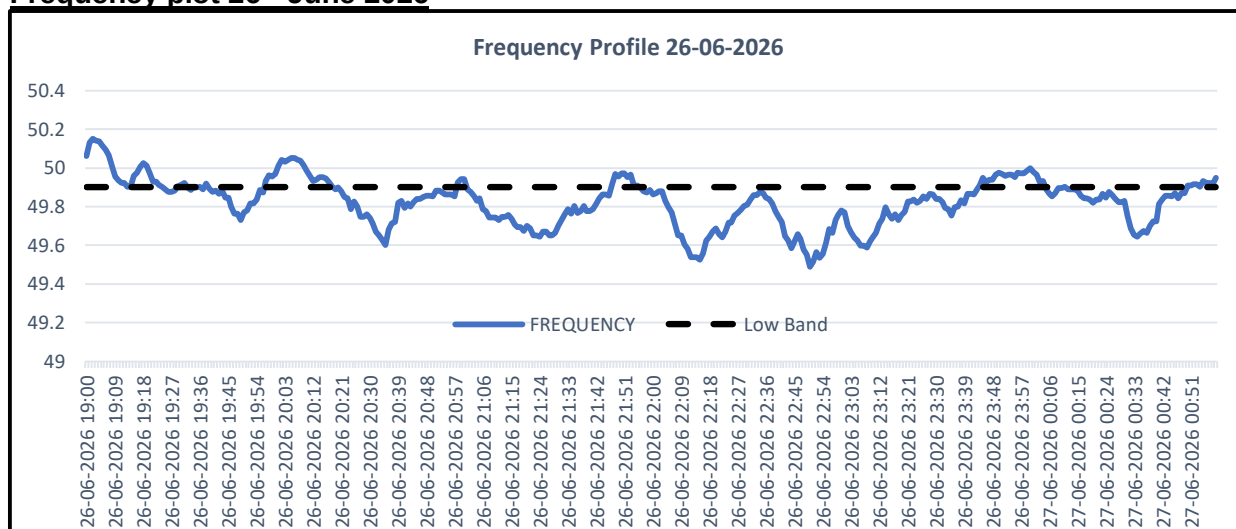

- During these events, ERLDC Control Room issued multiple violation messages to the concerned constituents. Despite repeated pursuance, over-drawl (OD) continued in some cases.
- To safeguard overall grid security and prevent further deterioration of system frequency, system operators, in certain instances, were left with no alternative but to resort to opening interconnecting tie-line feeders, as mutually agreed with the concerned constituents, to curb persistent overdrawal as a measure of last resort. Such actions were necessary to preserve grid security and maintain the reliability of the system.

Deliberations in the meeting

ERLDC presented case studies on the sustained low-frequency events that occurred on 2nd and 26th June 2026, wherein the system frequency remained below 49.90 Hz for a considerable time during the non-solar peak period. Minimum system frequency recorded was 49.46 Hz at 22:14 hrs on 02.06.2026 and 49.49 Hz at 22:50 hrs on 26.06.2026. The detailed presentation is enclosed as **Annexure-B.2.3**.

- It was highlighted that during these sustained low-frequency events, all available generation resources were maximized to the extent possible through optimal scheduling and dispatch including available ancillary services such as TRAS and SRAS with the objective of restoring the system frequency within the IEGC operating band.
- It was further pointed out that, on both occasions, a significant gap existed between the purchase and sell bids in the power market, resulting in the market clearing price reaching the max. ceiling price of ₹10/kWh. This situation underscored the necessity for utilities to maintain adequate reserves in the States so that they can fully meet their demands without resorting to over-drawl.
- It was reiterated that, as per the prevailing practice, Violation Messages shall be issued to overdrawing States and under-injecting generating stations as per prevailing practices.

OCC Decision

- ✓ Member Secretary, ERPC advised to maintain resource adequacy in order to avoid overdrawl from the grid.

- ✓ All ER constituents should strictly adhere to scheduled drawls and avoid overdrawling when system frequency drops below the IEGC band (especially below 49.9 / 49.5 Hz). The need for strictly adhering to the schedule interchange during extreme grid emergency conditions, particularly when the system frequency falls to 49.70 Hz was emphasized.
- ✓ All ER SLDCs were advised to abide by respect ERLDC real-time dispatch instructions or emergency control messages to prevent widespread frequency fluctuations and safeguard regional grid security.
- ✓ As mandated in the IEGC Clause: 36(3)

Quote

Whenever the power system is in an alert state or emergency state as assessed by SLDC or advised by RLDC.

The respective distribution licensee or bulk consumer under the regional control area shall abide by the directions of the RLDC to secure the system, and extreme measures like load shedding may be carried out as a last resort...

Unquote

In line with the above, in the event of sustained overdrawal by the drawee entities under low-frequency conditions despite issuance of non-compliance messages, ERLDC Control Room shall issue a Physical Regulatory Message to reduce the drawl of the concerned entity by disconnecting its tie-lines already identified, as the last resort, in the interest of maintaining security of the integrated power system.

2.4 Shutdown proposals for NHAI diversion works: ERLDC

- NHAI is undertaking several road widening/diversions works under the PM Gati Shakti & Bharatmala Pariyojana initiative, many of which require transmission line long shutdowns for diversion work.

In ER, Shutdown request has been received for the following lines so far:

Sr. No.	Name of the Line	Duration of Shutdown	Executing Agency/Consultancy	Present Status
1	400kV Jeypore-Gazuwaka D/C	15.05.26 till 05.06.26 (22 days)	Executing Agency: NHAI Consultant: POWERGRID Odisha	Shutdown taken on 15.05.26 and time extension requested up to 20.07.2026
2	500kV HVDC Talcher-Kolar HVDC line	Nov'2026 (15 days)	Executing Agency: PG Odisha-	
3	765kV Gaya-Balia S/C	01.07.26-20.07.26 (20 days)	Executing Agency: NHAI Consultant: POWERGRID ER-I	A special meeting involving NHAI to be convened to allow the SD
4	400kV Kahalgaon-Banka D/C	05.07.26 – 20.07.26 (16 days)	Executing Agency: NHAI Consultant: POWERGRID ER-I	Matter to be discussed in 241 st OCC.
5	400KV-Patna-Balia-1 & 2	16.08.26-30.08.26 (15 days for each circuit)	Facilitate critical piling work related Diversion on account of " Four Laning of Patna-Gaya-Dobhi section of NH 22"	Matter to be discussed in 241 st OCC.

6	400KV-Chandauti (PMTL)-Nabinagar (NPGC) D/C	01.08.26 – 20.08.26 (20 days)	Line diversion work for construction of Amas-Derbhanga Expressway (NH-119D).	Matter to be discussed in 241st OCC.
---	---	-------------------------------	--	--------------------------------------

- ❑ The shutdown of 400 kV Jeypore–Gazuwaka D/C was initially approved from 15.05.26 till 05.07.26 (22 days) after detailed deliberation in the Outage OCC Meeting held on 12.05.26. The outage resulted in a 650 MW reduction in ER–SR TTC/ATC, impacting inter-regional transfer capability and grid operational flexibility. Subsequently, multiple extensions in the restoration schedule were observed, resulting in prolonged outage of this critical inter-regional corridor. The delayed restoration has affected transmission system reliability, deferred several interdependent shutdowns and constrained outage planning during the upcoming lean maintenance period.
- ❑ While timely shutdowns are essential for the expeditious execution of these nationally important infrastructure projects, prolonged outages beyond the approved schedule adversely impact transmission system reliability, operational flexibility and overall grid security.
- ❑ Accordingly, it is essential that all stakeholders including the concerned Transmission Licensees and beneficiaries shall ensure meticulous planning and execution of the diversion works so that transmission lines are restored within the approved shutdown period. It is advised concerned transmission licensee to restore the line within approved timeframe.

Deliberations in the meeting

Powergrid Odisha apprised that 400kV Jeypore-Gazuwaka D/C will be restored latest by 25th July 2026.

NHAI representatives intimated that diversion work in different transmission lines are taken up by separate Project Implementing Units. They requested for earliest facilitation of shutdown of 765kV Gaya-Balia S/c and 400kV Chandauti-NPGC D/C citing availability of material and manpower to start the work.

ERLDC raised concern regarding inordinate delay in completing the diversion works affecting reliability and security of the network necessitating TTC/ATC curtailment in some cases. Many related shutdowns are also deferred due to non-revival of the line already under shutdown. While the diversion works are carried out by NHAI, the transmission licensee also needs to coordinate for earliest restoration of the lines.

It also highlighted that the shutdown of 400kV Chandauti-NPGC D/C requires generation restriction up to 1500MW for transient stability of the units. Hence, the diversion may preferably be planned during annual overhauling work of any unit of NPGC.

OCC Decision

- ✓ OCC Forum expressed discontent over prolonged outage of important transmission lines , such as 400kV Jeypore-Gazuwaka D/C, beyond the approved shutdown timelines. After a lot of deliberation, the forum accorded modus operandi for facilitating such diversion proposals.
- ✓ NHAI and transmission licensee need to make a joint site visit 7 days before the proposed shutdown date to assess material availability along with site working condition to commence the work. Upon

receipt of the report of joint site visit by NHAI and transmission licensee, shutdown will be facilitated considering ongoing network conditions.

- ✓ In case the diversion work involves a double circuit line, deployment of ERS to be explored by transmission licensee to make at least one circuit available during the period of shutdown.
- ✓ A committee comprising representatives from ERPC, ERLDC, NHAI, Transmission licensee to be formed for monitoring the diversion work. The Transmission licensee shall intimate progress of work to the monitoring committee on weekly basis.
- ✓ Considering prevailing grid conditions, shutdown of 500kV HVDC Talcher-Kolar HVDC line can't be allowed in August 2026 rather it can be availed from November 2026.
- ✓ OCC opined that the diversion proposal of any transmission line needs to be discussed in OCC or OCC outage meeting for detailed deliberation and concurrence of the forum.

2.5 Talcher – Kolar Bipole Shutdown for NHAI Diversion Work at Nayagarh, Odisha: NTPC Talcher

- With reference to the proposed shutdown of the HVDC Talcher – Kolar Bipole by PGCIL for NHAI diversion work at Nayagarh, Odisha, and as discussed in the special meeting convened on 23 June 2026 under the aegis of ERPC, the proposal was reviewed.
- It is submitted that the HVDC outage may be taken up during the planned outage period of Unit-2, which is scheduled for 50 days, to minimize generation curtailment to TSTPS units.
- It is requested that minimal load support may be ensured for carrying out soot blowing in Stage-I and Stage-II boilers to maintain reliable boiler operation. Curtailment upto technical minimum throughout the shutdown period may kindly be avoided for safe and reliable unit operation.

Deliberations in the meeting

NTPC requested for shutdown of TSTPP U#2 from 20.08.2026 citing urgency of boiler license renewal.

ERLDC stated that as S/D of 400kV Talcher-Meramundali D/C and 500kV HVDC Talcher-Kolar can't be allowed simultaneously, TSTPP U#2 S/D can be taken from November 2026. In view of prevailing peak demand Odisha and potential overloading of 400kV Talcher-Meramundali D/C, 500kV HVDC Talcher-Kolar should not be allowed in Aug'2026.

SLDC Bihar raised objection to the proposed S/D timeline.

OCC Decision

OCC opined to convene a special meeting involving ERPC, ERLDC, NTPC, concerned beneficiaries and respective SLDCs to finalize the planned S/D of TSTPP U#2.

2.6 Embargo on Drawal through STPS–Chandil 220 kV Tie Line: WB SLDC

- Since 03.06.2026, an embargo restricting drawal to 100 MW through the STPS–Chandil 220 kV tie line has been in force due to upstream network constraints beyond Chandil, primarily arising from overloading of the New Ranchi–Chandil and Ramchandrapur–Chandil transmission lines.
- As a result, West Bengal has been compelled to restrict drawal through the Chandil tie line to nearly 50% of its thermal capacity. Such prolonged underutilization of an inter-State tie line is undesirable from both operational and system planning perspectives. The restriction has also led to operational

difficulties and increased congestion in the WB transmission network, particularly around STPS and the associated transmission corridor.

- It is, therefore, requested that the concerned utilities may expedite the necessary transmission strengthening works to remove the prevailing constraint and restore full utilization of the tie line.

Deliberations in the meeting

West Bengal SLDC apprised the forum:

- *Critical loading condition in the Durgapur & Chandil-fed zone, driven by unusually high load growth (from about 300 MW to 575 MW over roughly five-and-a-half to six years) on account of new and migrating industrial load, including announced semiconductor and fertiliser-sector investments in the area.*
- *With only two 250 MW generating units locally available, the zone is heavily dependent on the Chandil tie-lines from Jharkhand. An embargo imposed by Jharkhand/ERPC currently restricts loading on this tie-line to about 100 MW, effectively meeting only 55–60% of the zone's expected demand and creating a near-emergency situation.*
- *Augmentation of the incoming 220 kV lines to Chandil, i.e. from New Ranchi and Ramchandrapur as well as from Chandil to 220 kV Santaldih bus was requested for urgent consideration as with present configuration, load management in the periphery of Santaldih bus may not be feasible in near future.*
- *220 kV Maithon–Asansol line is expected to be commissioned by Oct'2026, though this support will be sufficient it can reliably cater to the current load around 220 kV Santaldih bus and not the upcoming load. Thus, upgradation of incoming 220 kV lines to Chandil is essential, factoring in future load growth in the vicinity.*

Jharkhand representative explained that the Ranchi–Chandil and Chandil–Santaldih corridor is operating in a largely radial configuration and is already supporting an additional ~100 MW beyond its formal rating for more than 50% of the time. Still support is being extended to WB system to the best feasible extent. A new 400 kV double-circuit connectivity project (400 kV sub-station with a 220 kV double-circuit tie) was cited as a medium-term solution, which is expected to be commissioned around October 2026 but with full benefit is only likely to be available by 2027 once further downstream network augmentation is complete. Also, this new connectivity alone will largely be absorbed by incoming new industrial load (estimated 300–350 MW) rather than relieving the existing constraints.

ERLDC supplemented that at present support is being provided to WB network by Jharkhand by violating line loading limits, so there is no scope of extending further support from Jharkhand as per present network configuration.

OCC Decision

- ✓ *Considering bidirectional power flow in 220 kV Chandil-Santaldih line and N-1 violation at 220 kV Chandil even without drawl from WB, JUSNL was advised to submit a detailed plan for HTLS upgradation of all 220 kV incoming lines to Chandil.*
- ✓ *OCC opined that detailed load flow study may be carried out by CTU i.r.o 220 kV Chandil-Santaldih ISTS line and accordingly the same was referred to CMETS-ER for further deliberation.*

2.7 Emergency condition arose for the network around KTPP after sudden outage (long term or may be permanent outage) of KTPP unit 3 since 18.06.26: WB SLDC

- KTPP Unit-3 was de-synchronized at 19:37 hrs on 18.06.2026 reportedly due to a natural calamity and fire hazard. An initial intimation regarding the outage was received from the KTPP Control Room on 19.06.2026 at 16:41 hrs.
- Thereafter, SLDC, WB issued repeated communications seeking the expected restoration timeline of the affected unit. However, no further communication or restoration update has been received from the KTPP Control Room.
- Meanwhile, the daily generation summary reports issued by WBPDCCL Headquarters initially mentioned the outage reason as "Occurrence of Fire Hazard" and the restoration status as "Unit Breakdown Due to Natural Calamity." Following repeated follow-up by SLDC, the report was revised to indicate the outage reason as "Occurrence of Fire Hazard & Unit Breakdown Due to Natural Calamity" and the restoration status as "Extent of damage is being assessed. Estimated timeline for restoration will be intimated shortly." However, no formal technical assessment report or estimated restoration schedule has yet been communicated by KTPP.
- The prolonged outage of Unit-3 has created a critical system security concern. In the absence of any generating unit connected to the **220 kV bus** at KTPP, the **400/220 kV ICT configuration does not satisfy the N-1 contingency criterion**. A single tripping of an ICT at KTPP may result in:
 - Load loss of approximately 680 MW (only if 220 kV Food Park–Junglepur D/C disconnected), along with
 - Generation loss of about 420 MW due to unit tripping of Hiranmoyee Energy Ltd. and TPH. (considering auxiliary of KTPP units are not from the 400/220 kV ICTs).

Under the normal network configuration with 220 kV KTPP–Food Park–Junglepur–Howrah connected, the cascading impact could be significantly more widespread up to New Chanditala 400 kV sub-stn even, posing a serious threat to grid security.

- a) Earlier SLDC have requested KTPP for ICT augmentation from 315 MVA to 500 MVA.
- b) Also, WBSETCL felt shifting of one unit (out of unit 4,5,6) from 400 kV side to 220 kV side is the fastest and most justified decision to combat the issue. Accordingly for the first part of this proposal, WBSETCL had already submitted a quotation with the detailed drawing to the GM (OS), WBPDCCL Headquarters on **30.12.2024**, for execution of the connectivity part as a deposit work, as requested by WBPDCCL. However, no response has been received till date.

For the second part, WBPDCCL has to replace the existing 16/400 kV GT by their spare GT of 16/220 kV ICT in respect of the chosen unit (anyone out of 4, 5, 6).

- c) On 76th SLCF held on 10.09.2025, SLDC WB advised KTPP to take up with STU for installation of 3rd ICT at KTPP.

Representative of KTPP is requested to apprise the forum of:

1. The detailed cause of the outage and extent of damage;
2. The expected timeline for restoration of Unit-3.
3. The status and expected timeline to complete proposal (b) of WBSETCL.
4. Also, the decision on either of point (a) or (c) as proposed by SLDC WB may please be intimated.

Deliberations in the meeting

West Bengal SLDC presented Network security concerns around Kolaghat TPP subsequent to prolonged outage of unit-3(Annex B.2.7).

Following key concerns were highlighted:

- *Detailed cause of occurrence of the event as well as restoration plan of the unit is not being received from WBPDC.*
- *With only two machines at KTPP 400 kV bus and with U#3(connected to 220 kV bus) under outage, the entire 220 kV load is met through two no:s of 315 MVA transformers causing severe violation of N-1 contingency criterion.*

WBPDC attributed the incident to deficiency in WB STU network & lack of augmentation of existing ICT at KTPP by WBSETCL.

OCC Decision

OCC advised that all operational constraints leading to such sudden generation outage need to be resolved bilaterally between WBPDC and WBSETCL at the earliest so as to prevent recurrence of such incident posing threat to regional grid stability.

2.8 Temporary Group Control Operation of 400 kV Bus Reactors at Arambag: WB SLDC

- ☐ The 400 kV, 50 MVAR Bus Reactor Bay at Arambag 400 kV Substation has remained out of service since 12.06.2026 due to failure of the associated 400 kV Circuit Breaker. Restoration of the bay is dependent upon procurement and replacement of the faulty breaker, which is expected to require considerable time.
- ☐ Under the prevailing circumstances, WBSETCL proposes to operate the existing 50 MVAR Bus Reactor in group control mode along with the existing 125 MVAR Bus Reactor, utilizing the 125 MVAR Bus Reactor Bay, until the defective circuit breaker is replaced and the dedicated reactor bay is restored.
- ☐ The matter is placed before the OCC for appraisal and necessary operational consent please.
- ☐ In view of the persistently high loading on the **220 kV Malda (PG)–Gajol D/C** corridor and the transmission constraint in the **New Purnea–Old Purnea** section, SLDC, WB has repeatedly requested in the OCC and TCC forums that the shutdown required for HTLS reconductoring work for 220 KV Malda(PG)-Gajol(WBSETCL) D/C lines under the "**Chukha Transmission System (CTS) Strengthening Scheme under ERES-44**" be scheduled during the **mid-November to 31st December 2026** window.
- ☐ SLDC has categorically stated that, owing to the critical loading of this corridor, shutdown outside this period cannot be permitted without risking **prolonged load shedding (PLS)**. In the event the work is not completed within the said window, its execution is likely to be deferred by another year.
- ☐ Considering the strategic importance of this strengthening work for meeting the **Summer 2027** demand and the abnormal delay already experienced in tender finalization, it is considered necessary to closely monitor the implementation progress against a time-bound schedule.

Deliberations in the meeting

WB SLDC informed:

- *Owing to the temporary unavailability of a dedicated breaker, the utility proposed to operate the 125 MVAR and 50 MVAR reactors in parallel through a common (125 MVAR) bay under group control, rather than keeping either reactor out of service, until the breaker is made available.*

- *As per normal practice, reactors of this class are typically kept in service during winter months and taken out of service during summer, so the interim group-control arrangement is not expected to materially affect operations in the near term.*

OCC Decision

OCC consented to the interim group-control arrangement for the 125 MVAR & 50 MVAR reactors while at the same time replacement of defective breaker and restoration of dedicated reactor bay needs to be expedited.

2.9 Update on Reconductoring of the lines of Chukha Transmission system under ERES-44 scheme: WB SLDC

- ☐ Powergrid has been entrusted with the reconductoring work of various lines of Chukha Transmission system under ERES-44 scheme.
- ☐ The lines of Chukha Transmission System are more than 37 years old and are prone to outages. Further, reconductoring of some of the lines is critical for ensuring reliability of the supply in West Bengal system. Among the lines, reconductoring of 220 kV Malda-Gazole section(18 kM) is essential for operational flexibility of WB system and early completion of the reconductoring work on this section is critical for ensuring reliability of supply in Gazole and adjoining areas. It is worth mentioning that at present bus splitting is in operation at 220 kV Gazole S/s compromising the reliability of the supply.
- ☐ The inordinate delay in carrying out the reconductoring work of Chukha Transmission system would pose challenge to smooth & secure grid operation and reliable power supply to adjoining areas of West Bengal.

Deliberation in 56thTCC meeting

Powergrid informed that the technical specification for HTLS reconductoring of the Malda–Gazole–Dalkhola transmission section has been finalized and the tender will be awarded by August, 2026.

56th TCC Decision:

TCC advised Powergrid to complete the reconductoring of the Malda–Gazole–Dalkhola transmission section at the earliest.

56th ERPC Decision:

ERPC noted the importance of early reconductoring of the Malda–Gazole–Dalkhola transmission section and urged Powergrid to ensure early completion of the same.

Deliberations in the meeting

Powergrid updated that pursuant to a request received from a bidder, the Bid submission timeline for the subject tender has been extended up to 28th July 2026.

OCC Decision

- ✓ *OCC noted the extension of bid due date.Outcome of the bid opening to be intimated by Powergrid in the next OCC(August 2026).*
- ✓ *Powergrid was also advised to expedite finalisation of the tender and confirm a firm shutdown/execution schedule so that reconductoring work can commence from November 2026.*

2.10 Challenges in Grid operation due to upcoming influx of Datacentre load: ERLDC

- ❑ Large-scale data centres are expanding rapidly driven by the growing demand for cloud computing, artificial intelligence (AI) and digital services. Recognizing their strategic importance, GoI has introduced measures such as infrastructure status for data centres above 5 MW IT load, dedicated data centre parks, renewable energy facilitation and simplified approvals to accelerate investments.
- ❑ Based on report titled “Scaling India’s Data Centre Ecosystem” by CEEW published in February 2026, it is projected that connected demand by data centres would reach 4.5-6.5 GW by 2030 in India. In the Eastern Region, Kolkata has 16MW connected capacity and it will increase with 48% CAGR up to 2030.
- ❑ Further, as experiences gathered from power systems worldwide, it indicates that large data centres will possess new operational challenges for power system due to their concentrated, power-electronic-based loads and extensive cooling systems. These intensified cooling loads predominantly induction motor’s load may also aggravate fault-induced delayed voltage recovery (FIDVR) event which we already experienced in Kolkata and Bhubaneswar areas. All these developments could significantly influence future resource adequacy assessments, demand forecasting, transmission planning, and grid reliability studies, particularly around Kolkata, Bhubaneswar, Patna and Ranchi.
- ❑ To facilitate the connectivity of the DATA CENTRE to the grid, it is needed to conduct a detailed study on transmission adequacy with necessary data. The information may include, but need not be limited to:
 - Connected load (existing and ultimate planned capacity).
 - Phased capacity addition and expected commissioning schedule.
 - Load composition (% IT load, % cooling load, rest auxiliary loads, etc.).

Detailed format for data sharing is attached as **Annexure B.2.8**.

Currently, ERLDC doesn’t have any details about existing data centres in Eastern regions. Details of existing data centre are required to be shared with ERLDC, and the same is required to be shared whenever an application for new data centres is received. Availability of the above information will enable to undertake advance comprehensive planning and operational studies, including load flow, short-circuit, voltage stability, dynamic performance, contingency analysis, protection coordination, and restoration studies.

Deliberations in the meeting

ERLDC gave a brief presentation flagging the operational challenges expected from the rapid growth of data-centre load in the region, distinguishing between traditional IT/storage data centres, AI-inference data centres, AI-training data centres, and crypto-mining loads — the latter three categories being associated with sharp, fast power ramps that can affect grid voltage, reactive power and frequency.

Following aspects were also highlighted:

- *As per applicable bulk-load interconnection/technical guidelines, data centres of 5 MW and above are required to comply with prescribed technical standards; cooling load alone can constitute 35–40% of a data centre's total demand, with associated inductive/reactive-power (UPS) characteristics.*

- A recent event was cited as an illustrative example, where multiple transmission-line faults in the vicinity of large data centres led to cascading load trips within 3–4 seconds, causing sudden frequency and reactive-power swings.
- Presently there is inadequate visibility/reporting of data-centre loads and their load-composition (IT load vs. cooling load) at the regional level.

OCC Decision

All SLDCs and utilities were advised to compile and furnish details of data centres (5 MW and above), including load composition, connected or proposed to be connected in their respective areas, to ERPC/ERLDC in a prescribed format. **(Annexure B.2.8).**

2.11 Status of Operationalization of SAMAST at SLDC Jharkhand for Transition of Scheduling & Accounting Functions of PTPS-I (PVUNL): ERLDC

- ❑ The Hon'ble CERC, vide ROP for the hearing dated 16-06-2026 in Petition No. 658/MP/2025, has directed that the interim arrangement for scheduling and accounting of power from Patratu Thermal Power Station, Phase-I (3×800 MW) of PVUNL by ERLDC shall continue till the end of June 2027 or till operationalization of the SAMAST portal by SLDC Jharkhand, whichever is earlier.
- ❑ ERLDC is presently carrying out the scheduling, metering, and accounting of PTPS-I based on the modalities finalized during the online meeting held on 23-07-2025 in the presence of representatives from ERPC, CTU, SLDC Jharkhand, JBVNL, and NLDC, which were subsequently endorsed in the 229th OCC meeting of ERPC held on 25-07-2025. ERLDC has been carrying out the scheduling, metering, and accounting of PTPS-I based on the requisite NOCs received from Jharkhand, in accordance with the agreed modalities.
- ❑ Upon operationalization of SAMAST by SLDC Jharkhand, these functions are to be transferred to SLDC Jharkhand in accordance with the directions of the Hon'ble Commission.
- ❑ ERLDC conducted three-day training and handholding session from 18th to 20th May 2026 at ERLDC, Kolkata, for officials of SLDC Jharkhand covering scheduling, metering, accounting, and other operational activities to be undertaken by SLDC Jharkhand following the transfer of the control area jurisdiction of PTPS-I from ERLDC to SLDC Jharkhand.
- ❑ In this regard, SLDC Jharkhand is requested to inform the target date for operationalization of the SAMAST portal for scheduling and accounting, considering readiness in all respects. The information is required to facilitate appropriate planning for continuation of the interim scheduling arrangement and the eventual transition of scheduling and accounting functions from ERLDC to SLDC Jharkhand.
- ❑ In this regard, ERLDC had already issued a letter to SLDC Jharkhand on 01.07.2026 seeking the target date for operationalization of the SAMAST portal and their readiness for taking over the scheduling and accounting functions of PTPS-I. However, no response has been received from SLDC Jharkhand so far.
- ❑ Therefore, SLDC Jharkhand is requested to apprise the OCC of the present status and expected timeline for operationalization of SAMAST so that necessary actions may be initiated by all concerned stakeholders well in advance for a smooth transition of the scheduling and accounting functions from ERLDC to SLDC Jharkhand.

Deliberations in the meeting


SLDC Jharkhand intimated that SAMAST will be made operational within next six months.

OCC Decision

SLDC Jharkhand was advised to strictly abide by the submitted timeline.

2.12 Restoration of 400kV Patna-Naubatpur Ckt#2 and 400kV Patna-Naubatpur-Balia Ckt#1 to its original configuration: ERLDC

Bypassing of 400kV Patna-Naubatpur Ckt#1 and 400kV Naubatpur-Balia Ckt#1 at Naubatpur(BGCL) was accorded in **206th OCC meeting** held on **31.08.2023** for drawl of start-up power of 2x660 MW Buxar Thermal Power Project by connecting one circuit of the Buxar–Naubatpur line using the 400kV Balia-1 bay at Naubatpur. Subsequently, with the interim arrangement, 400KV Buxar–Naubatpur Ckt#2 was charged on 11.05.24 and Buxar started drawing start up power. After commissioning of Buxar Unit#1, the interim arrangement was continued.

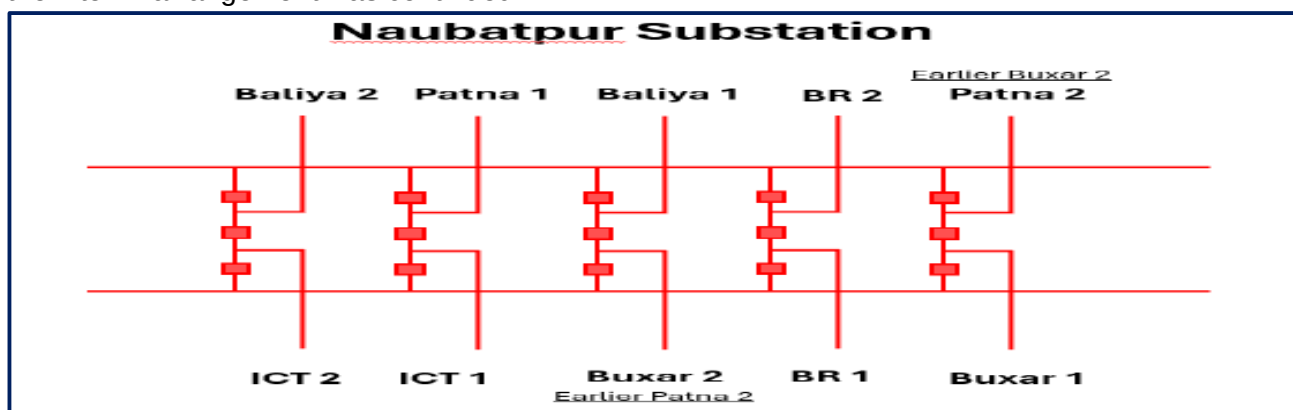

- ❑ The termination bays (2 nos) of Buxar at Naubatpur were ready in April'26. Thereafter, BSPTCL submitted shutdown proposals for swapping of bays of Buxar-2 and Patna-2 at Naubatpur (for enhanced reliability of power evacuation of Buxar) and restoration of 400kV Patna-Naubatpur-Balia Ckt#1 bypassed at Naubatpur to its original LILO configuration.
- ❑ Shutdown of 400kV Patna-Naubatpur Ckt#2 was allowed on 09.05.26 to facilitate bay swapping with 400kV Patna-Buxar Ckt#2 at Naubatpur. While the FTC of 400kV Buxar-Naubatpur#2 was done on 08.06.26 after rerouting works, 400kV Patna-Naubatpur Ckt#2 is yet to be restored even after 2 months of outages. Besides, restoration of 400kV Patna-Naubatpur-Balia Ckt#1 bypassed at Naubatpur to its original LILO configuration was also not followed upon. As Buxar connectivity at 400kV level with Naubatpur is commissioned now, restoration of other ISTS lines at Naubatpur is highly desired for enhancing system reliability and security.

Deliberations in the meeting

SLDC Bihar updated that Patna-Naubatpur ckt-2 has been charged on 17.07.26 and a meeting will be held with PGCIL and BSPTCL in first week of August to resolve the issue.

OCC Decision

OCC noted.

2.13 Shutdown proposal of Thermal generating units: ERPC

✓ Annual Overhauling of Unit–1 of Buxar Thermal Power Project (2×660 MW): SJVN Thermal Private Limited

Minutes of Meeting (MoM) held between Bihar State Power Holding Company Limited (BSPHCL) and SJVN Thermal Private Limited (STPL). (Attached at **Annex B.2.11**)

Background:

- Unit–1 (660 MW) of the Buxar Thermal Power Project (2×660 MW) was first synchronized on 21 August 2025 for trial operation. Following the successful completion of all mandatory performance tests, the unit achieved its Commercial Operation Date (COD) on 14 November 2025.
- In accordance with the prescribed maintenance philosophy for thermal power stations, each generating unit is required to undergo an annual planned overhauling of approximately 30 days to ensure reliable, safe, and efficient operation during the subsequent operating cycle.

Proposal:

- As the proposed annual overhauling schedule could not be accommodated during the LGBR planning process, the matter was subsequently discussed with the beneficiary utility, Bihar State Power Holding Company Limited (BSPHCL). As recorded in the Minutes of Meeting, BSPHCL advised STPL to schedule the annual overhauling after 20 October 2026.
- Accordingly, considering the availability of resources and operational requirements, STPL proposes the following schedule for the Annual Overhauling of Unit–1 for approval by the Operational Coordination Committee (OCC).

Unit	Capacity (MW)	From	To	Duration	Reason
Unit-1	660 MW	20.11.2026	19.12.2026	30 Days	Planned Overhauling

✓ Rescheduling of Start of Overhauling of Unit-3 of NTPC Kahalgaon: NTPC

- Planned overhauling of Unit-3 (210 MW) of Stage-I, NTPC Kahalgaon, which was scheduled to commence on 15 July 2026, is proposed to be postponed due to issues related to the BMD Overhauling Contract.
- Accordingly, the overhauling schedule may be revised to 28th July, 2026 as the tentative date for taking Unit-3 under overhauling subject to the readiness of the Contract and site conditions.

✓ Rescheduling of Start of Overhauling of Unit-2 of NTPC Talcher: NTPC

TSTPS LGBR Proposed : 20-Aug-2026 to 03-Oct 2026 (45 Days)

Approved by MoP/CEA: 01 Sept-2026 to 15-Oct-2026 (45 Days)

- Due to liability in unit, the scope of work has increased. Hence additional 5 days beyond the proposed 45 days may be allowed to restore the reliability of the unit after overhaul.
- Considering the festive season, with Durga Puja Festival commencing from 10 October 2026, it was proposed in the LGBR to start the overhaul from 20 August 2026 so that the unit can be brought back on bar before the festival period. Therefore, the starting date of the planned outage may be approved as **20 August 2026 and upto 08-Oct-2026 (50 Days)**.

✓ **Shutdown request of NTPC Farakka Unit-5: NTPC**

- With Reference to LGBR 2026-27 scheduled Overhaul of Farakka unit-5(500 mw) in July -August had been deferred in **240th OCC** as requested by NTPC
- It is proposed that **FSTPS Unit-5** Annual overhauling may be rescheduled from **01.01.2027 for 30 days**.

Deliberations in the meeting

- *SJVN representative appealed for S/D of Buxar Thermal Power Plant(Unit-1) and supplemented the discussion held with the beneficiary utility,i.e Bihar State Power Holding Company Limited (BSPHCL) SLDC Bihar representative agreed to the proposal.*
- *Owing to persistent contractual issues & site readiness, NTPC Kahalgaon requested to postpone shutdown of U#3 to 28th July 2026 for 45 days that was earlier approved from 15th July 2026(45 days).*

OCC Decision

OCC forum agreed with the following planned overhauling shutdowns:

1. *NTPC Kahalgaon U#3 from 28th July 2026 for 45 days.*
2. *NTPC Farakka U#5 overhauling is rescheduled from 01.01.2027 (30 days)as requested by NTPC.*
3. *Buxar TPP may avail shutdown of Unit-1 from 20.11.2026 for 30 days.*

2.14 Frequency Response Performance of Eastern Region for May 2026 events: ERLDC

Frequency Response Performance of Eastern Region for Jun 2026 events:

Event 1 : Date and Time of the Reportable Event: 16:47 Hrs. of 12th June 2026 (Friday)

Brief Details of the Grid Event: Generation loss event of 1266 MW in 400kV NKSTPP, ER at 16:47 hrs. on 12.06.2026.

Event 2 : Date and Time of the Reportable Event: 14:50 Hrs. of 16th June 2026 (Tuesday)

Brief Details of the Grid Event: Generation loss event of 1106 MW in JIPL, ER at 14:50 hrs. on 16.06.2026

Event 3 : Date and Time of the Reportable Event: 19:23 Hrs. of 18th June 2026 (Thursday)

Brief Details of the Grid Event: Generation loss event of 1760 MW in Rihand SS, NR at 19:23 hrs. on 18.06.2026

Event 4 : Date and Time of the Reportable Event: 03:24 Hrs. of 30th June 2026 (Tuesday)

Brief Details of the Grid Event: Generation loss event of 1290 MW in 400 kV Akal S/S, NR at 03:24 hrs. on 30.06.2026

Event 5 : Date and Time of the Reportable Event: 04:14 Hrs. of 30th June 2026 (Tuesday)

Brief Details of the Grid Event: Generation loss event of 1065 MW in 400 kV Akal S/S, NR at 04:14 hrs. on 30.06.2026

Generator Wise Performance Summary

Generator Name	Event 1		Event 2		Event 3		Event 4		Event 5	
	% Based on Droop	Grade	% Based on Droop	Grade	% Based on Droop	Grade	% Based on Droop	Grade	% Based on Droop	Grade
Adhunik	-12.6%	Poor	-104.7%	Poor	31.7%	Average	61.4%	Good	-22.0%	Poor
BARH ST-1	172.6%	Excellent	463.4%	Excellent	45.6%	Average	84.5%	Excellent	21.7%	Below Avg
BARH ST-2	46.6%	Average	187.1%	Excellent	14.6%	Below Avg	-16.1%	Poor	32.6%	Average
BRBCL	179.6%	Excellent	103.4%	Excellent	43.3%	Average	205.7%	Excellent	209.6%	Excellent
DARLIPALLI	38.2%	Average	263.4%	Excellent	18.6%	Below Avg	112.2%	Excellent	121.3%	Excellent
DIKCHU	557.2%	Excellent	945.1%	Excellent	119.5%	Excellent	761.6%	Excellent	350.0%	Excellent
FSTPP I&II	69.3%	Good	77.7%	Excellent	9.7%	Below Avg	580.4%	Excellent	113.1%	Excellent
FSTPP III	248.3%	Excellent	252.8%	Excellent	8.6%	Below Avg	43.2%	Average	289.1%	Excellent
GMR	386.8%	Excellent	582.8%	Excellent	7.4%	Below Avg	126.1%	Excellent	13.7%	Below Avg
INDBHARAT	-0.3%	Poor	69.1%	Good	18.5%	Below Avg	0.0%	Below Avg	0.0%	Below Avg
JITPL	23.4%	Below Avg	-24412.3%	Poor	4.9%	Below Avg	-69.1%	Poor	-18.1%	Poor
KhSTPP I	156.9%	Excellent	-54.9%	Poor	-59.9%	Poor	-109.8%	Poor	-186.5%	Poor
KhSTPP II	116.2%	Excellent	253.1%	Excellent	-1.6%	Poor	-22.2%	Poor	67.8%	Good
MPL	126.3%	Excellent	241.3%	Excellent	1.6%	Below Avg	-39.4%	Poor	17.6%	Below Avg
NORTH KARANPURA	-8004.6%	Poor	101.6%	Excellent	-7.2%	Poor	-10.0%	Poor	47.0%	Average
NPGC	215.1%	Excellent	-31.0%	Poor	-7.3%	Poor	75.0%	Excellent	92.0%	Excellent
PVUNL	105.4%	Excellent	0.0%	Below Avg	0.0%	Below Avg	0.0%	Below Avg	64.1%	Good
TSTPS-I	20.2%	Below Avg	130.0%	Excellent	3.9%	Below Avg	-38.5%	Poor	15.3%	Below Avg

Grade: poor < 50%; below average >= 50% and < 75%; average >= 75% and < 85%; good >= 85% and < 100%; excellent >= 100%.

State Wise FRO Performance Summary

State Name	Event 1		Event 2		Event 3		Event 4		Event 5	
	% Based on FRO	Grade	% Based on FRO	Grade	% Based on FRO	Grade	% Based on FRO	Grade	% Based on FRO	Grade
Bihar	619.4%	Excellent	-293.2%	Poor	-20.9%	Poor	350.1%	Excellent	-138.1%	Poor
DVC	1703.7%	Excellent	-416.3%	Poor	-269.3%	Poor	229.3%	Excellent	106.0%	Excellent
Jharkhand	725.9%	Excellent	314.4%	Excellent	131.1%	Excellent	264.5%	Excellent	-658.7%	Poor
Odisha	502.4%	Excellent	1993.2%	Excellent	-200.6%	Poor	-1277.0%	Poor	-1091.1%	Poor
Sikkim	0.0%	Below Avg	0.0%	Below Avg	0.0%	Below Avg	0.0%	Below Avg	0.0%	Below Avg
West Bengal	-48.6%	Poor	32.6%	Average	-1.0%	Poor	-346.5%	Poor	71.2%	Good

Grade: poor < 50%; below average >= 50% and < 75%; average >= 75% and < 85%; good >= 85% and < 100%; excellent >= 100%.

All concerned generating stations and entities are requested to review their frequency response performance and take necessary corrective measures to enhance frequency response performance during future frequency events.

Deliberations in the meeting

OCC reviewed the tripping/event performance of all ER generating units for the month of June 2026 , It was observed that generating stations such as BRBCL and Dikchu demonstrated consistently high performance. Certain other generating stations exhibited intermittent performance across different frequency events.

ERLDC flagged consistent poor frequency response for APNRL, JIPL, NTPC BARH Stage-II, JSWEUL and NTPC Kahalgaon stage I units. During the meeting held on 24.04.2026 regarding Frequency Response Performance of ER Generating Stations, Kahalgaon had informed that the inadequate performance of its Stage-I units was primarily attributable to the ageing of the units, which are presently operating in hydraulic governing mode without Coordinated Master Control (CMC). Kahalgaon further informed that a proposal for installation of CMC had been initiated; however, its implementation was linked with the Renovation and Modernization programme scheduled during 2028-29.

ERLDC had requested NTPC Kahalgaon to immediately take up the matter with the Commission, clearly indicating the prevailing technical constraints, since continued grid-connected operation of the units is subject to compliance with the prescribed Primary Frequency Response requirements.

NTPC informed that the mechanical governing system of the LMZ turbine-generator unit at Kahalgaon is proposed to be modified under a Renovation & Modernisation (R&M) scheme, currently at the initial design/budgetary estimation stage.

OCC Decision

- ✓ OCC decided that the concerned generating stations shall schedule periodic testing (as per IEGC 2023) of the generating units for the recurring frequency events such that timely corrective measures may be taken for poor frequency performance.
- ✓ In view of time consuming process for modification of the turbine governing system under R&M, NTPC was advised to seek exemption for desired frequency response i.r.o KHSTPP I from Hon'ble CERC.

2.15 Requirement of Standardized Procedure for Charging of Transmission Lines During Partial Reconductoring Works and Interim Bypass arrangements: ERLDC

- ☐ During execution of reconductoring works, it is often necessary to restore or temporarily charge a partially reconducted transmission line so that shutdown of the alternate circuit can be availed for completion of the remaining work. Such situations arise due to phased execution of reconductoring works and are operationally necessary for timely completion of critical transmission projects.
- ☐ Recently, charging of 400 kV Talcher–Meramundali Ckt-I was undertaken under such operational circumstances after considering system security requirements and based on the undertaking furnished by the concerned transmission licensee. The matter was deliberated in the 237th OCC Meeting considering the criticality of maintaining reliable power evacuation from Talcher generating station.
- ☐ Further, ERLDC has observed that similar situations are likely to arise frequently during phased reconductoring of EHV transmission lines across the region.
- ☐ The existing provisions under CEA (Measures relating to Safety and Electric Supply) Regulations, 2023 and the Minutes of Meeting held at CEA on 03.08.2023 provide a dispensation for ERS, Interim Bypass Arrangements and restoration/modification of transmission towers. However, no explicit procedure is presently available regarding temporary charging of partially reconducted transmission lines during phased reconductoring works.
- ☐ Accordingly, ERLDC has sought guidance/clarification from RIO/CEA on this matter vide ERLDC Letter dtd. 22-06-2026, regarding the applicable procedure and any additional statutory requirements in such cases. However, clarification from RIO/CEA is still awaited.
- ☐ Interim bypass arrangements are occasionally required during execution of critical transmission works to facilitate construction activities while maintaining continuity of supply and system security.

- Recently, 400 kV Maithon–Koderma D/C line was charged through an interim bypass arrangement at Gaya to facilitate erection of new towers and associated stringing works. The charging was carried out considering system requirements after receipt of the required documents, certifications and undertakings from the concerned transmission licensee.
- CEA Minutes of Meeting dated 03.08.2023 provide specific dispensation for charging under ERS, Interim Bypass Arrangements and restoration/modification of transmission towers. However, the subsequent correspondence received from RIO vide letter dtd. 17-06-2026 has indicated the need for further clarification regarding the applicable inspection and charging procedure in such cases.
- Accordingly, ERLDC has already sought guidance/clarification from RIO/CEA on this matter vide Letter dtd. 22-06-2026, regarding the applicable procedure and any additional statutory requirements in such cases. However, clarification from RIO/CEA is still awaited.
- Since similar interim bypass arrangements are expected to arise in future during execution of major transmission projects, absence of a uniform procedure may lead to uncertainty in implementation and delay in completion of critical transmission works.
- It may be noted that obtaining the necessary CEA safety clearance is the sole responsibility of the concerned Transmission Licensee/Asset Owner. The Transmission Licensee/Asset Owner shall coordinate with the concerned RIO office and arrange the RIO inspection based on the readiness and progress of the work at site.
- The ERPC/OCC Forum may kindly take note of the issue and consider taking up the matter with the appropriate authority for issuance of suitable guidelines/clarification regarding the procedure to be followed for RIO safety clearance in cases of Partial Reconductoring Works and Interim Bypass arrangements, to ensure consistency in all such cases.

Deliberations in the meeting

ERLDC appealed to the forum that in case of partial reconductoring works, either transmission licensee proactively obtains clearance from CEA or the clearance may be granted by CEA based on undertaking by the licensee. This may eliminate operational delay in restoration of the important transmission lines.

OCC Decision

OCC suggested to take up the matter with Chief Electrical inspector,CEA for finalizing standard operating procedure for Transmission line charging after Partial reconductoring Works or Interim Bypass arrangements.

2.16 ERLDC Operating procedure for ER Grid for 2026-27: ERLDC

- As mandated by IEGC 2023, Reg. 28(4) each RLDC has to update Operating Procedure of regional grid Annually in consultation with all stakeholders. Accordingly, ERLDC has updated the Operating Procedure for the Eastern Region for the financial year 2026-27. The draft operating procedure was circulated among the stakeholders vide mail dated 08th July,2026 for their comments.
- In this regard a meeting is scheduled on July 13, 2026, at 15:00 hrs involving all stakeholders of ER to discuss and finalize the operating procedure.

Deliberations in the meeting

ERLDC updated that draft Operating Procedure of Eastern regional grid has been prepared in consultation with all stakeholders. A consultation meeting was also held on 13th July in this regard. The operating procedure for 2026-27 can be accessed via the following link: <https://erldc.in/systemoperation/operating-procedure-of-er>

OCC Decision

OCC noted and advised all concerned stakeholders to furnish their comments/suggestions on the draft Operating procedure at the earliest.

2.17 Switching off the idle charged 132 kV PTPS–DVC Patratu Tie Line (5C): PVUNL

- ☐ The PTPS Switchyard is presently **idle charged**.
- ☐ The Switchyard is being charged through the **132 kV Hatia–PTPS Transmission Line (Circuits 8C & 9C)**.
- ☐ The **132 kV PTPS–DVC Patratu Tie Line (Circuit 5C)** is also **idle charged**.
- ☐ The **132 kV Hatia–PTPS Transmission Line (8C & 9C)** is a **major hindrance to the construction of the PVUNL Ash Mound**, and its dismantling in the Ash Mound area is **urgently required**.
- ☐ JUSNL / DVC have awarded the work for diversion of the **8C, 9C, and 5C transmission lines** to the newly constructed **400/220/132/33 kV GSS, Katia, Patratu**. However, execution of the diversion is expected to take considerable time.
- ☐ Approval is required for **switching off the idle charged 132 kV PTPS–DVC Patratu Tie Line (5C)**.
- ☐ The matter was discussed during the **240th OCC meeting**, where it was opined that the proposal should be placed before the **CEA** and also referred to the forthcoming **CMETS-ER** meeting.
- ☐ **No resolution has been achieved so far**, resulting in continued delay in the dismantling of the transmission line and impacting the progress of the PVUNL Ash Mound construction.

Deliberations in the meeting

- *PVUNL raised concern over switching off of DVC feeder connected to PTPS old switchyard. Subsequent upon which hatia-PTPS 132 kV both circuits could be deenergized & disconnected as these lines crossing over PVINL ash mound area and is a major hindrance for taking of erection activities inside ashmound area by PVUNL agencies.*
- *It was apprised that CEA has already given consent regarding switching off of DVC feeder.*

SLDC DVC also confirmed that they have also given consent to JUSNL and joint MoM has been signed by both parties.

OCC Decision

In line with the resource adequacy report of CEA, DVC may do the needful action at the switchyard of Patratu TPS .

2.18 Implementation of DTPC scheme in place of PLCC Scheme (with updated heavier Pedestal mount Wave trap) due to space constraint in the existing bays: POWERGRID, ER-II

Approval: Vide Ref No CEA-PS-12-13/3/2019-PSPA-II Division dated 22.11.2024 of CEA of GOI, 24th MOM of NCT was held, where ERES-43 for Re-conductoring of the lines of Chukha Transmission System (CTS) through RTM was approved by NCT, and subsequently it was discussed in the 56th TCC & ERPC meeting held on 15.06.2026 for completing the Reconductoring of the CTS at the earliest.

Change in scope for ERES-43 (CTS Reconductoring) for Substation portion

- For the existing lines in the substation portion, there are two communication cum protection channels, viz;
A. DTPC Scheme
B. PLCC Scheme with Wavetrap in th Y-phase/Circuit/Line
- As per the said NCT, TCC & ERPC approval, the existing Suspended installed Wavetraps are to be replaced with updated Pedestal Mount Wavetraps which are much more heavier than the existing scheme. Since, all the CTS Substations are 40 years old and are having old DMT scheme with minimal space in between the equipments, hence construction of structure for Pedestal Mount Wavetrap is not feasible due to space constraint (**photograph attached**) within the existing bays.
- In view of the above, it is proposed to incorporate the DTPC scheme in place of existing PLCC scheme, which is much more updated, reliable, accurate and feasible with the existing bays without any further modifications and economically there will be no major deviation in the approved cost estimate for implementation of DTPC scheme in comparison to the PLCC with pedestal mount Wavetrap scheme.



Reference photograph

Deliberations in the meeting

Powergrid submitted:

- *On account of space constraints at the existing base/substation, a pedestal-mounted wave trap arrangement is being proposed in place of the existing overhead/hanging wave-trap arrangement, which currently lacks a dedicated support structure at the 220 kV bay.*

- The equipment presently available in the market corresponds to the hanging-type design, and the specification would need to be revisited to suit the pedestal-mounted requirement.
- The proposed (pedestal-mounted) arrangement is cost-effective compared to any other available alternative.

OCC Decision

- ✓ OCC decided that Powergrid shall finalize the design/specification for the pedestal-mounted wave trap in consultation with CTU. Accordingly, the same may be placed in CMETS-ER for concurrence.
- ✓ Cost-sharing aspects also need to be examined by Powergrid and to be placed in TCC/ERPC forum for approval.

2.19 Shutdown of various lines in Sikkim & North Bengal for SAG correction, rectification of damage leg and for providing Guy support to protect concerned tower due to Hill shrinking/land slide/ change of river course: POWERGRID, ER-II

POWERGRID, ER-II, are maintaining several important 400KV, 220 KV & 132 KV transmission lines in Sikkim & North Bengal. The transmission lines are passing through several stiff terrain and river crossing. The nature of hills in Sikkim is growing hills and soils are loose soils, therefore, the towers are regularly subjected to hill shrinking and land slide. Also change of course of small rivers and sudden flash flood due to cloudburst are observed very often, and causing creation of vulnerable condition. In recent past monsoon has affected following towers which take many months to recover in normal shape:-

1. Tower No- 127 of 132 KV D/C Siliguri-Melli & Rangit-Kurseong damage due to hill shrinking on 04.10.2024.



2. Tower No-73 of 132 KV Rangit-Rammam TL due to hill shrinking on 23.06.2025.



3. Tower No-94 of 400 KV D/C Binaguri-New Purnea TL due to change of parman rive coarse change in 14.03.2026.



Due to recent monsoon many roads in hills also affected damage of roads and hill shrinking and land sliding occurs in Sikkim & north Bengal. Therefore, following lines of POWERGRID are affected due to hill shrinking/ land slide/ change of river coarse-

1. 400 KV D/C Rangpo-Teesta V.
2. 400 KV D/C Rangpo-Binaguri.
3. 400 KV D/C Tala-Binaguri-1
4. 400 KV D/C Tala-Binaguri-2
5. 400 KV D/C Binaguri-New Purnea
- 6. 220 KV D/C Rangpo-New Melli**
7. 132 KV D/C Rangpo-Ganktok
8. 132 KV Rangit-rammam
9. 132 KV Rangit-Kurseoung
10. 132 KV Rangpo-Melli
11. 132 KV Siliguri-Melli
12. 132 KV Siliguri-Kurseong

Similarly in recent findings as discussed in 241st SD meeting, affected towers of 220 KV Rangpo-New Melli required sudden attention and given below for reference:-

Tower No-9 & 10 of 220 KV D/C Rangpo-New Melli damage due to change of river coarse.



Tower No-10



Tower No-09



SPAN-09-10

2. Tower No-01 of 220 KV D/C Rangpo-New Melli damage due to Land slide



3. Tower No-13 & 14 of 220 KV D/C Rangpo-New Melli affected due to Hill shrinking-



Tower No-13



Tower No-14

In view of above, the agenda submitted in 241 shutdown meeting for assessment of severity & grand shut down of various lines of north Bengal & Sikkim as mentioned above lines of POWERGRID in time to time for SAG correction, rectification of damage leg and for providing Guy support to protect the tower and avoid long unwanted outage during high hydro period.

Further if forum require, a suitable committee also may be formed for site visit to asses the condition and S/D may be allowed accordingly.

Deliberations in the meeting

Powergrid flagged the vulnerable transmission line locations in the Sikkim and North Bengal region, susceptible to landslides and riverbank erosion, along with the need for rectification of damaged towers at these locations.

OCC Decision

- ✓ OCC acknowledged the importance of rectification of the Powergrid lines affected due to hill shrinking/ land slide/ change of river course as these lines are essential for reliable power evacuation from adjoining hydro generating units.
- ✓ The forum agreed that shutdown of all identified lines shall be availed on daily(non-continuous) basis in coordination with concerned hydro generating stations.

2.20 Recovery of cost against AMR implementation: POWERGRID, ER-II

- POWERGRID has been entrusted with the implementation, subsequent maintenance, and troubleshooting of the AMR system across the Eastern Region. To integrate meters with the AMR system and execute necessary enhancements and upgradations, various LOAs were placed in a phased manner.
- Referring to the minutes of 51st ERPC Meeting, the last approved value of AMR expenditure was INR 7,87,31,547/-. The period of this approved cost was considered from Mar-2019 till Jun-2023.
- For the next lot of cost recovery, expenditure was considered for the period of 01.07.2023 to 31.03.2025. In the 54th ERPC meeting, an amount of INR 6,60,09,667 /- was approved for the said period. However, the cost incurred was re-calculated and it was found that few items were left out in the initial cost calculation. Including those items and the tax components and the consultancy charges, the revised cost amount stands at INR 7,03,73,728.85.
- It is requested to approve the revised cost of INR 7,03,73,728.85/ - for the period between 01.07.2023 to 31.03.2025.

Deliberations in the meeting

Powergrid submitted :

*The originally approved estimate (as per 54th ERPC) has been revised including few left over items, GST and consultancy charges. Auditor certificate enclosed at **Annex B.2.20**.*

OCC Decision

OCC noted and referred to Commercial sub-committee for financial concurrence.

3. PART-C: ITEMS FOR INFORMATION

3.1. ER Grid performance during June 2026

The average and maximum consumption of Eastern Region and Max/Min Demand (MW), Energy Export for the month June-2026 were as follows:

AVERAGE CONSUMPTION (MU)	MAXIMUM CONSUMPTION(MU)/ DATE	MAXIMUM DEMAND (MW)	MINIMUM DEMAND (MW)	SCHEDULE EXPORT	ACTUAL EXPORT
		DATE / TIME	DATE / TIME	(MU)	(MU)
690 MU	737 MU, 17.06.2026	34324 MW, 17.06.2026 at 23:23 Hrs.	23114 MW, 11.06.2026 at 07:47 Hrs.	1515	1726

Deliberations in the meeting

The grid performance of ER for the month of June 2026 was highlighted.

3.2. Non-Submission of FRC data in stipulated time-frame: ERLDC

Adhering to IEGC clauses 30.8 and 30.10.(a) to 30.10.(q), generating stations within the Eastern region are required to submit essential data to ERLDC within two days of receiving a notification regarding a reportable frequency event. Additionally, according to clause 30.10.(n), all control areas within the eastern region must assess their frequency response characteristics and share the evaluation, along with high-resolution data, with the ERLDC. Therefore, timely submission of primary response data is crucial for compliance with the IEGC.

Hence all are again requested to follow the stipulated timeline and submit the data to ERLDC and also fill the google sheet below to include the email address where notifications of reportable events should be sent.

The latest data receipt status is given below for **Jun-2026** events: (as on 08.07.2026):

STATIONS		12.06.2026 16:47 hrs	16.06.2026 14:50 hrs	18.06.2026 19:23 hrs	30.06.2026 04:14 hrs	30.06.2026 03:24 hrs
FSTPP #STG 1 & 2						
FSTPP # STG 3						
KhSTPP #STG 1						
KhSTPP #STG 2						
TSTPP #STG 1						
Barh stage-1						
Barh stage-2						
BRBCL						
Darlipalli						
North Karanpura						
NPGC						
TEESTA V						
PVUNL						
Dikchu						
IBEUL (JSW UTKAL)/INDBHARAT						
GMR						
MPL						
ADHUNIK						
JITPL						
TEESTA III						
Updated as on	08.07.2026					
	Received					
	Not Received					
	Plant Out					
	Data freeze at plant					

Hence all are again requested to follow the stipulated timeline and submit the data to ERLDC and also fill in the google sheet below to include the email address where notifications of reportable events should be sent.

https://docs.google.com/spreadsheets/d/1slvAOmQIEQVIMn0LnB78eKMa2sz2QYICZ-sPEpeV_jk/edit?usp=sharing

Deliberations in the meeting

OCC Decision: -

- All generators were advised to regularly share high resolution data against each reportable frequency event with ERLDC on time to facilitate accurate assessment of FRP for respective control areas.
- All generating utilities were also urged to update the google sheet (link mentioned above) with email address where notifications of reportable events will be shared.

4. PART-D: OPERATIONAL PLANNING

4.1. Major Thermal Generating Units/Transmission Element outages/shutdown in ER Grid (as on 09-07-2026)

SL No	STATION	STATE	AGENCY	UNIT NO	CAPACITY (MW)	REASON(S)	OUTAGE DATE
1	BARH	BIHAR	NTPC	2	660	Initially unit was out due to Boiler tube leakage, later unit was taken under Annual Overhauling from 00:00 hrs of 01.07.2025	26-Jun-2026
2	GMR	ODISHA	GMR-KEL	2	350	Annual Overhauling	21-Jun-2026
3	FSTPP	WEST BENGAL	NTPC	2	200	Drum level high	08-Jul-2026
4	DARLIPALI	ODISHA	NTPC	1	800	Boiler Tube Leakage	08-Jul-2026
5	NABINAGAR(NPGC)	BIHAR	NTPC	2	660	Initially tripped on Flame Failure later leakage developed in LP Bypass Dump Tube	06-Jul-2026
6	Sterlite	ODISHA	SEL	4	600	APH Problem	08-Jul-2026
7	IB.TPS	ODISHA	OPGC	2	210	Ash pond issue	06-Jul-2026
8	MEJIA TPS	DVC	DVC	3	210	Both ESP passes will be taken into service	05-Jul-2026
9	KOLAGHAT	WEST BENGAL	WBPDC	3	210	Due to Fire hazard in boiler	18-Jun-2026
10	RTPS	DVC	DVC	2	600	High Turbine Vibration	14-Apr-2026

Major Generating stations Out on Reserve Shutdown due to low system demand:

SL No	STATION	STATE	AGENCY	UNIT NO	CAPACITY (MW)	REASON(S)	OUTAGE DATE
NA							

Hydro Unit Outage Report: -

S. NO	STATION	STATE	AGENCY	UNIT NO	CAPACITY (MW)	REASON(S)	OUTAGE DATE
1	BURLA HPS/HIRAKUD I	ODISHA	OHPC	5	43.65	Annual Maintenance	19-Jan-2026

2	BALIMELA HPS	ODISHA	OHPC	5	60	Repair and maintenance work	16-Jan-2025
3	BALIMELA HPS	ODISHA	OHPC	6	60	Initially unit was out due to Severe water leakage from turbine, later unit was taken under Repair and maintenance work from 00:00 hrs of 16.01.25	06-Jan-2025
4	TEESTA HPS	SIKKIM	NHPC	1	170	Commercial operation started w.e.f 13.07.26. Units 1&2 synchronized with grid on 12.07.26	04-Oct-2023
5	TEESTA HPS	SIKKIM	NHPC	2	170		04-Oct-2023
6	TEESTA HPS	SIKKIM	NHPC	3	170		04-Oct-2023
7	TEESTA STG III Hep	SIKKIM	TUL	1	200	Sudden cloudburst at glacier fed LOHNAK Lake followed by huge inrush of water in Teesta River and damage of Teesta III Dam & downstream Powerhouses	04-Oct-2023
8	TEESTA STG III Hep	SIKKIM	TUL	2	200		04-Oct-2023
9	TEESTA STG III Hep	SIKKIM	TUL	3	200		04-Oct-2023
10	TEESTA STG III Hep	SIKKIM	TUL	4	200		04-Oct-2023
11	TEESTA STG III Hep	SIKKIM	TUL	5	200		04-Oct-2023
12	TEESTA STG III Hep	SIKKIM	TUL	6	200		04-Oct-2023
13	U. KOLAB	ODISHA	OHPC	4	80	Tripped on Over Frequency	05-May-2026
14	U. KOLAB	ODISHA	OHPC	2	80	Heavy Leakage in guide vane	22-Jan-2026

4.2. Long outage report of transmission Element (MORE THAN 01 WEEK) (As on 09.07.2026):

Transmission Element / ICT	Outage From	Reasons for Outage
220KV-FSTPP-LALMATIA-I	21-04-2021	Two nos. of tower collapsed on 29.05.2024 near to Lalmatia GSS in the Loc. No. 246 & 247. 220KV S/C Farakka-Lalmatia Transmission Line is in anti-theft charging condition from Loc no 248 (Lalmatia end) to Loc no 24. Foundation, erection and stringing progress from loc 1 to 24. Line expected to be charged by Jul 2026.
132KV-BARHI-RAJGIR-1	25-03-2023	Dismantling of tower no. 227, 228, and 229 crossing the premises of Mahabodhi Cultural centre along with

		Destringing of conductor of both circuits and Earthwire between tension tower no. 218-237 in same line. The lines from Barhi(DVC) will be terminated at Barachatti (BH) and new line to be constructed from Barachatti to Rajgir(BH)
132KV-NALANDA-BARHI(DVC)-1	25-03-2023	Dismantling of tower no. 227, 228, and 229 crossing the premises of Mahabodhi Cultural centre along with Destringing of conductor of both circuits and Earth wire between tension tower no. 218-237 in same line. The lines from Barhi(DVC) will be terminated at Barachatti(BH) and new line to be constructed from Barachatti to Nalanda(BH)
400KV-RANGPO-TEESTA-V-1	04-10-2023	Tower near gantry of Teesta V HEP collapsed during GLOF event in Oct 2023 also leading to damage in powerhouse. Tower subsequently erected on 15.06.2024. Teesta V HEP GIS damaged due to hill sinking on 20.08.2024. Presently, tower work done, GIS under restoration and generation expected by July 2026.
400KV-RANGPO-TEESTA-V-2	04-10-2023	Tower near gantry of Teesta V HEP collapsed during GLOF event in Oct 2023 also leading to damage in powerhouse. Tower subsequently erected on 15.06.2024. Teesta V HEP GIS damaged due to hill sinking on 20.08.2024. Presently, tower work done, GIS under restoration and generation expected by July 2026.
132KV-CHANDIL-MANIQUEI-1	05-06-2024	Line is closed when power assistance required by either party. Presently, line is opened as power assistance not required by any party.
400KV/220KV 315 MVA ICT 1 AT NORTH KARANPURA	12-09-2024	Tripped on Differential protection.
400KV/220KV 315 MVA ICT 1 AT TSTPP	01-11-2024	Tripped on PRD protection. The failed transformer has reached the vendor, the repair scope has been finalized, with the ICT likely to be available by Jul'26.
400KV/220KV 315 MVA ICT 2 AT MEJIA-B	20-01-2025	315 MVA ICT-2 at MTPS-B got damaged while charging from 220kV GIS bay. New procurement of ICT has been taken up & installation of the same may complete by end of Mar'28.
400KV-DIKCHU-RANGPO-2	05-08-2025	Shutdown taken for damaged insulator replacement work. While

		charging the line, bus bar protection operated at Dikchu. Issue in GIS chamber of Y ph. Isolator between line CB and bus 2. Powder formation inside isolator chamber has occurred. Restoration work delayed. Current Status: Line is anti-theft charged from Rangpo end to Dikchu extended via Teesta-III, Unable to take in service due to issue in tie bay at Dikchu.
400KV MAIN BUS - 2 AT DIKCHU	05-08-2025	Bus bar protection operated while charging 400kV Dikchu-Rangpo 2. Issue in GIS chamber of Y ph. Isolator between Rangpo ckt 2 line CB and bus 2. Powder formation inside isolator chamber has occurred. Restoration work delayed. Current Status: Negotiation with GE for procurement is under process, further 6 to 8 months required by GE for order delivery.
220KV-PATNA-KHAGAUL-1	24-09-2025	LBB relay operated during rectification of DC grounding defect by M/S KRR at GSS Khagaul. Earlier w.e.f 02-08-2025 12:06 Hrs, Tower No. 63 has bent significantly on one side. As on 18.06.2026, Tower No. 63 has bent significantly on one side, tender has been awarded. Foundation work for tower has been completed. Approximate completion date is 15th July 2026
220KV-BIDHANNAGAR-WARIA-2	29-10-2025	Initially line was opened to control line loading. In between B-phase CT Blasted at Bidhannagar end. Now Line is charged as anti-theft from Waria end to control loading of 220 kV Waria-Mejia D/C.
220KV-BALIMELA-UPPER SILERU-1	21-11-2025	Idle charged from U. Sileru end. Power drawl by Odisha halted due to non-concurrence by Andhra Pradesh.
132KV-MADHEPURA (BH)-SAHARSA-1	18-12-2025	To control the line loading. Line kept idle charged from Saharsa.
400KV/220KV 315 MVA ICT 1 AT KODERMA	10-02-2026	ICT out due to rising acetylene trend. ICT will be sent to factory for rectification. Meanwhile, one ICT from DSTPS is being diverted and expected to be charged by 10th July 2026
132KV-RANGIT-SAGBARI-1	28-02-2026	Line was taken out to carry out necessary jumpering modification at Sagbari station to connect directly to Legship 220/132/66kV. The FTC of

		the line is pending in absence of necessary statutory clearance.
400KV-TEESTA-III-RANGPO-1	15-03-2026	Line is anti-theft charged from Rangpo end to Dikchu extended via Teesta-III
400KV/220KV 315 MVA ICT 2 AT LAPANGA	14-04-2026	Differential Protection Operated causing tripping of ICT. As reported multiple bushings damaged. New 500 MVA ICT commissioning is under progress. Expected charging timeline yet to be intimated by OPTCL.
132KV-ARRAH (PG)-JAGDISHPUR-1	23-04-2026	Site initiated Hand Trip
400KV/220KV 315 MVA ICT 2 AT DSTPS(ANDAL)	03-05-2026	ICT has been shifted to KTPS.
400KV-PATNA-NAUBATPUR(BH)-2	09-05-2026	For Destraining of Quad from AP-01 TO Ext. MC-02 OF 400kV Naubatpur - Patna(PG) ckt-02, residual quad jumpering work from AP-01 TO AP-78, Twin stringing from AP -78A to Ext MC-02 .
400KV-JEYPORE-GAZUWAKA-1	15-05-2026	NH-130CD NHAI Diversion work at location 131,133, 151-153 and 179-180. Expected revival by 20th Jul'26.
400KV-JEYPORE-GAZUWAKA-2	15-05-2026	NH-130CD NHAI Diversion work at location 131,133, 151-153 and 179-180. Expected revival by 20th Jul'26.
765KV-DHARAMJAIGARH-JHARSUGUDA-2	21-05-2026	For diversion of existing 765kV D/C Jharsuguda – Dharamjaygarh Ckt 1&2, due to upcoming railway line of IRCON. Expected revival by 15th Jul'26.
765KV-DHARAMJAIGARH-JHARSUGUDA-1	21-05-2026	For diversion of existing 765kV D/C Jharsuguda – Dharamjaygarh Ckt 1&2, due to upcoming railway line of IRCON. Expected revival by 15th Jul'26.
220KV-KHAGARIA-NEW PURNEA-2	25-05-2026	Khagaria: RYB Fault , Ir-2.821kA ,Iy- 3.130kA ,Ib-2.992kA : New Purnea :R- Y-B FAULT, Z1, FD- 84.2KM, FC: IR- 2.99KA, IY- 3.07KA, IB- 3.04KA; 03 Nos of towers at Loc Nos- 320(DA+0 type), 321(DA+0 type) and 322(DB+0 type) has collapsed and 01 Nos of tower at Loc No- 323 (DB+6 type) has bent from first Cross arm during heavy cyclonic storm on 25-05-2026. Out of 4 deformed towers, repair of 3 towers has been completed. Repair of Tower No. 322 (DB+0) is in progress.
220KV-KHAGARIA-NEW PURNEA-1	25-05-2026	Khagaria: RYB Fault , Ir-2.821kA ,Iy- 3.130kA ,Ib-2.992kA : New Purnea :R- Y-B FAULT, Z1, FD- 84.2KM, FC: IR-

		2.99KA, IY- 3.07KA, IB- 3.04KA; 03 Nos of towers at Loc Nos- 320(DA+0 type), 321(DA+0 type) and 322(DB+0 type) has collapsed and 01 Nos of tower at Loc No- 323 (DB+6 type) has bent from first Cross arm during heavy cyclonic storm on 25-05-2026. Out of 4 deformed towers, repair of 3 towers has been completed. Repair of Tower No. 322 (DB+0) is in progress.
400/220 KV 315 MVA ICT 4 AT ARAMBAGH	29-05-2026	Tripped on Buchholz protection.
400KV-GOKARNA-NEW PURNEA-1	07-06-2026	FOR TOWER ERECTION, DE-STRINGING & RE-STRINGING TO SHIFT THE EXISTING LINE INTO NEW TOWERS AFTER PILING WORK, Expected Revival 12.07.2026
400KV-NEW PURNEA-FARAKKA-1	07-06-2026	FOR TOWER ERECTION, DE-STRINGING & RE-STRINGING TO SHIFT THE EXISTING LINE INTO NEW TOWERS AFTER PILING WORK, Expected Revival 12.07.2026
400KV-GAYA-KODERMA-1	13-06-2026	For installation of 03 nos. new tower in multi circuit portion between location no. 39 to 41; charged as 400 kV Maithon Koderma - 1, Expected Revival 16.07.2026
400KV-MAITHON-GAYA-1	13-06-2026	For installation of 03 nos. new tower in multi circuit portion between location no. 39 to 41; charged as 400 kV Maithon Koderma - 1, Expected Revival 16.07.2026
400KV-MAITHON-GAYA-2	14-06-2026	For installation of 03 nos. new tower in multi circuit portion between location no. 39 to 41, Expected Revival 16.07.2026
400KV-GAYA-KODERMA-2	14-06-2026	For installation of 03 nos. new tower in multi circuit portion between location no. 39 to 41, Expected Revival 16.07.2026
132KV-KHSTPP-SABOUR-1	18-06-2026	for Height raising work associated with the ongoing NHAI Highway

Deliberations in the meeting

Members noted.

4.3. Commissioning of new units and transmission elements in Eastern Grid in the month of June-2026

The details of new units/transmission elements commissioned in the month of June-2026 based on the inputs received from beneficiaries:

NEW ELEMENTS COMMISSIONED DURING June, 2026							
उत्पादन इकाइयाँ / GENERATING UNITS							
क्र. सं. Sl. No.	स्थान Location / Pooling Station	मालिक/यूनिट का नाम OWNER/UNIT NAME	यूनिट संख्या/स्रोत Unit No/Source	संकलित क्षमता (मेगावाट) Capacity added (MW)	कुल/स्थापित क्षमता (मेगावाट) Total/Installed Capacity (MW)	दिनांक DATE	टिप्पणी Remarks
1	NA						
आई.सी.टी./जी.टी./एस.टी. / ICTs/ GTs / STs							
क्र. सं. Sl. No.	एजेंसी/मालिक Agency/ Owner	उप-केन्द्र SUB-STATION	आईसीटी संख्या ICT NO	वोल्टेज (केवी) Voltage Level (kV)	क्षमता (एमवीए) CAPACITY (MVA)	दिनांक DATE	टिप्पणी Remarks
1	NIL						
प्रेषण लाइन / TRANSMISSION LINES							
क्र. सं. Sl. No.	एजेंसी/मालिक Agency/ Owner	लाइन का नाम LINE NAME	लंबाई (किमी) Length (KM)	कंडक्टर प्रकार Conductor Type	दिनांक DATE	टिप्पणी Remarks	
NIL							
लिलो / प्रेषण लाइन की पुनर्व्यवस्था / LILO/RE-ARRANGEMENT OF TRANSMISSION LINES							
क्र. सं. Sl. No.	एजेंसी/मालिक Agency/ Owner	लाइन का नाम / लिलो पर Line Name/LILO at	लंबाई (किमी) Length (KM)	कंडक्टर प्रकार Conductor Type	दिनांक DATE	टिप्पणी Remarks	
1	PGCIL	400KV-KODERMA-MAITHON-1	264	ACSR MOOSE	15-06-2026 02:52	Interim Bypass Arrangement - Shorting of 400 kV Koderma–Gaya D/C and 400 kV	
2	PGCIL	400KV-KODERMA-MAITHON-2	264.2	ACSR MOOSE	15-06-2026 12:58	Maithon–Gaya D/C lines after bypassing Gaya S/S	
3	PGCIL	400KV-FARAKKA-GOKARNA-1	299.5	ACSR Snowbird	08-06-2026 19:59	Shorting of 400 kV New Purnea–Farakka and 400 kV New Purnea–Gokarna T/L to form the temporary 400 kV Farakka–Gokarna transmission line, bypassing New Purnea Substation.	
4	PGCIL	400KV-NEW RANCHI-RTPS-1	155	ACSR MOOSE	15-06-2026 14:57	Charging of the 400 kV New Ranchi–RTPS-1 transmission line through the tie-bay bypass	

5	PGCIL	400KV-NEW RANCHI-RTPS-2	155	ACSR MOOSE	12-06-2026 16:33	arrangement at Ranchi Substation reduces the fault level at Ranchi Substation from approximately 51 kA to 39 kA.
बस/लाइन रिएक्टर / BUS/LINE REACTOR						
क्र. सं. Sl. No.	एजेंसी/मालिक Agency/Owner	एलेमेंट का नाम Element Name	उप-केन्द्र SUB-STATION	रेटिंग (एमवीएआर) Rating (MVA)	दिनांक DATE	टिप्पणी Remarks
1	PGCIL	80MVAR 400KV SWITCHABLE L/R OF 400KV-NEW RANCHI-RTPS-1 AT NEW RANCHI	400	80	14-06-2026 01:09	PGCIL
एच.वी.डी.सी/ए.सी फिल्टर बैंक/फैक्ट्स डिवाइस संबद्ध प्रणाली / HVDC / AC Filter bank / FACTS DEVICE associated System						
क्र. सं. Sl. No.	एजेंसी/मालिक Agency/Owner	एलेमेंट का नाम Element Name	उप-केन्द्र SUB-STATION	वोल्टेज (केवी) Voltage Level (kV)	दिनांक DATE	टिप्पणी Remarks
NIL						
बस - बे / BUS - BAYS						
क्र. सं. Sl. No.	एजेंसी/मालिक Agency/Owner	एलेमेंट का नाम Element Name	उप-केन्द्र SUB-STATION	वोल्टेज (केवी) Voltage Level (kV)	दिनांक DATE	टिप्पणी Remarks
NIL						

Deliberations in the meeting

Members noted.

4.1. UFR operation during the month of June 2026

Frequency profile for the month as follows:

MONTH	MAX (DATE/TIME)	MIN (DATE/TIME)	% LESS IEGC BAND	% WITHIN IEGC BAND	% MORE IEGC BAND
June 2026	50.34 (on 14-June-26 at 07:57 Hrs.)	49.45 (on 03-June-26 at 00:36 Hrs.)	9.2	74.0	16.8

Hence, no report of operation of UFR has been received from any of the constituents.

UFR details for the month as follows:

Control Area	Required Load Relief					Implemented Load Relief				
	Stage –I (49.4 Hz)	Stage –II (49.2 Hz)	Stage– III (49.0Hz)	Stage– IV (48.8Hz)	Total Relief by Control Area	Stage – I (49.4 Hz)	Stage –II (49.2 Hz)	Stage– III (49.0Hz)	Stage– IV (48.8Hz)	Total Relief by Control Area
	(MW)	(MW)	(MW)	(MW)		(MW)	(MW)	(MW)	(MW)	
BSEB	345	399	466	466	1676	316	373	409	424	1522
JSEB	103	130	151	151	535	85	111	133	110	439
DVC	159	208	243	243	853	173	209	242	239	863
Odisha	304	372	434	434	1544	374.5	377.5	370	452	1574
WB & CESC	523	613	715	715	2567	560	574	712	715	2561
Sikkim	5	5	5	5	20	0	0	0	0	0
TOTAL	1439	1727	2015	2015	7194	1508.5	1642.5	1848	1927	6959

Deliberations in the meeting

Members noted.

Meeting ended with a vote of thanks to the chair.

Annex-A

Participants in 241st OCC Meeting

Venue: ERPC Conference Hall, Kolkata

Time: 10:30 Hrs.

Date: 17.07.2026 (Friday)

Sl.	Name	Designation	Organisation	Contact No.	E-mail Id	Signature
1	K. B. Jagtap	Member Secretary	ERPC	8652776033	mserpc-power@nic.in	
2	S Banerjee	Executive Director	ERLDC	9433041823	swrajit.banerjee@ncl-india.in	
3	R.K. Meena	Director	ERPC	8800764840	rkmeena@erpc.in	
4	P.K. DE	SE	ERPC	9831620142	secommnt.erpc@gov.in	
5	A. Das	EE	"	9681214774	anupdas@erpc.in	
6	D.K. Khuntia	AD-I	ERPC	7683889161	delip.khuntia@erpc.gov.in	
7	P P Jena	EE	ERPC	9776198991	ppjena.erpc@gov.in	
8	PRATHAM KUMAR	EE	ERPC	8076873558	PrathamKumar.cea@gov.in	
9	DEVASHISH	Dy. Manager	NHAI PIU-Aurangabad (BR)	6202336330	devashish@nhai.org	
10	PANKAJ KUMAR	DY. MANAGER	MEILON BEHAT OF NHAI	8077012505	Pankaj_Kumar@rajghar.com	
11	S.K. Sharma	SGM	DVC LDC	9434539423	Sanjay.Sharma@dvc-sa.in	
12	S.K. Panda	manager	DVC LDC	6370134794	Santosh.panda@dvc.gov.in	
13	Raju Kachhap	Sr. Manager	SLDC Ranchi	7783087568	rajmailme82@gmail.com	
14	TUNESHWAR KUMAR	Sr. Manager	STU, JUSNL	9431190306	tuneshwar.kumar@gmail.com	
15	Rajendra Prasad	E.E.E.	TVNL	9031049936	rajendra.prasad@tvnl.in	

Participants in 241st OCC Meeting

Venue: ERPC Conference Hall, Kolkata

Time: 10:30 Hrs.

Date: 17.07.2026 (Friday)

Sl.	Name	Designation	Organisation	Contact No.	E-mail Id	Signature
16	She Fozar Ali	Asst	APNRL	9771454984	sfm2power@gmail.com	M
17	Mahendra S. Malik	AGM	JSWEUL	6376355214	mahendra.malik@jsw.in	M Malik
18	Mr. Pimtu Das	GM	SJVN, Buxar	9418475284	pimtu.das@svn.nic.in	P Das
19	Nishant Kumar	DGM	DMTCL/SEPL	7987210324	nishant.kumar@energy-sel.com	N Kumar
20	Prateek Sharma	DGM	POWERGRID ER-1	7352669384	prateeksharma@powergrid.in	Prateek
21	SURAJIT ROY	Chief Manager	HEL	8335067270	surajit.roy@bpsg.in	S Roy
22	DEBARSHI DE	DGM	LESC	9163312742	debarshi.de@bpsg.in	D De
23	Manas Guha	DGM	DPL	8509267341	m.guha@dpl.net.in	M Guha
24	Rajat K. Koley	Sn. Mgr(OS)	WBPDCL	9474860642	rk.koley@wbpdcl.co.in	R Koley
25	MANAS MONDAL	AGM(OS)	WBPDCL	8536903808	m.mondal@wbpdcl.co.in	M Mondal
26	UTSAB ADITYA	SE(E)	SLDC_WB	9434910880	utsabadiya@gmail.com	U Aditya
27	ARNAB BASU	DE(E)	SLDC_WB	9434910978	arnab.basu@wbsetcl.in	A Basu
28	PREETAM BANERJEE	A.C.E.	WBSEDCL	7003871189	preetam72@gmail.com	P Banerjee
29	SHOUVIK BANERJEE	CE, SLDC, WB	WBSETCL	9434910379	svkbanerjee@yahoo.com	S Banerjee
30	RANJAN DAS	CE, CPO	WBSETCL	9434910740	cpd.wbsetcl@gmail.com	R Das

Participants in 241st OCC Meeting

Venue: ERPC Conference Hall, Kolkata

Time: 10:30 Hrs.

Date: 17.07.2026 (Friday)

Sl.	Name	Designation	Organisation	Contact No.	E-mail Id	Signature
31	Suprat Chakrabarty	Asstt. Engg	NTPC/Darjiling	9424140785	schakrabarty02@ntpc.co.in	
32	S.R. Dowl	Asstt. Engg	NTPC/PUNL	9437960620	sdowl@ntpc.co.in	
33	Prasanna Kumar Sahoo	Asstt. (OS)	NTPC/ER-221A Kharagpur	8118052430	prasannasahoo@ntpc.co.in	
34	CHANDAN MALLICK	CM(SO)	ERLDC/ GRID-INDIA	7278756275	chandamallik@grid-india.in	
35	ALOK PRATAP SINGH	CM(SO)	ERLDC GRID-INDIA	9007285390	apsingh@grid-india.in	
36	RAKESH KUMAR PRADHAN	DGM(SO)	"	9831337570	rkpradhan@grid-india.in	
37	MANAS DAS	DGM	ERLDC, GRID-INDIA	9007070925	manasdas@grid-india.in	
38	BILASH ACHARI	DGM	ERLDC GRID-INDIA	7003472016	bilash.achari@grid-india.in	
39	DEBABRATA BISWAS	GM	"	9434740041	dbiswas@grid-india.in	
40	Shabari Pramanick	CM	ERLDC GRID-INDIA	9007058764	shabari.pramanick@grid-india.in	
41	Avinash Mishra	DGM	ERLDC	9453017986	AVINASHMISHRA@NTPC.CO.IN	
42	Gagan Kumar	EEE	SUC, BSATCL	7763817782	gagankumishra@gmail.com	
43	B S Ray	DD	ERPC			
44	A. Chatterjee	AD-I	ERPC			
45						



Receipt of Online Payment of Stamp Duty

Receipt Number : d1c447bacf71dc7c1a7d

Receipt Date : 21-Oct-2021 06:25:27 pm

Receipt Amount : 500/-

Amount In Words : Five Hundred Rupees Only

Document Type : Agreement or Memorandum of an Agreement

District Name : Ranchi

**Stamp Duty Paid By : TAPAS DATTA GENERAL MANAGER
AND M ECL**

Purpose of stamp duty paid : HANDING OVER FARAKKA LALMATIA TRANSMISSION SYSTEM TO JHARKHAND URJA SANCHAR NIGAM LIMITED BY EASTERN COALFIELDS LIMITED

First Party Name : EASTERN COLFIELDS LIMITED

Second Party Name : JHARKHAND URJA SANCHAR NIGAM LIMITED

GRN Number : 2108042118

-: This stamp paper can be verified in the jharnibandhan site through receipt number :-



*This Receipt is to be used as proof of payment of stamp duty only for one document. The use of the same receipt as proof of payment of stamp duty in another document through reprint, photo copy or other means is penal offence under section-62 of Indian Stamp Act, 1899

इस स्वीच का उपयोग केवल एक ही दस्तावेज पर मुद्रांक शुल्क का भुगतान के प्रमाण हेतु ही किया जा सकता है। पुनः प्रिंट

[illegible]



Government of Jharkhand

Receipt of Online Payment of Stamp Duty

NON JUDICIAL

Authorised under Notaries Act-1956
and Notaries Rules 1956 by
Govt of India (Jharkhand)

Receipt Number : fd151d3ac9387122d3ea

Receipt Date : 21-Oct-2021 06:17:26 pm

Receipt Amount : 500/-

Amount In Words : Five Hundred Rupees Only

Document Type : Agreement or Memorandum of an Agreement

District Name : Ranchi

Stamp Duty Paid By : TAPAS DATTA GENERAL MANAGER E AND M ECL

Purpose of stamp duty paid : HANDING OVER FARAKKA LALMATIA TRANSMISSION SYSTEM TO JHARKHAND URJA SANCHAR NIGAM LIMITED BY EASTERN COALFIELDS LIMITED

First Party Name : EASTERN COALFIELDS LIMITED

Second Party Name : JHARKHAND URJA SANCHAR NIGAM LIMITED

GRN Number : 2108042007

:- This stamp paper can be verified in the jharnibandhan site through receipt number :-



25 OCT 2021

This Receipt is to be used as proof of payment of stamp duty only for one document. The use of the same receipt as proof of payment of stamp duty in another document through reprint, photo copy or other means is penal offence under section-62 of Indian Stamp Act, 1899

इस रसीद का उपयोग केवल एक ही दस्तावेज पर मुद्रांक शुल्क का भुगतान के प्रमाण हेतु ही किया जा सकता है। पुनः प्रिन्ट

Sumit Chandra X
25/10/21

Signature
25/10/21

Signature
25/10/21

कर अथवा फोटो कॉपी आदि द्वारा इसी रसीद का दुसरे दस्तावेज पर मुद्रांक शुल्क का भुगतान के प्रमाण हेतु उपयोग भारतीय मुद्रांक अधिनियम, 1899 की धारा 62 अन्तर्गत दण्डनीय अपराध है।



Government of Jharkhand

Receipt of Online Payment of Stamp Duty

Authorised under Notaries Act-1956
and Notaries Rules 1956 by
Govt of India (Jharkhand)

25 OCT 2021



25 OCT 2021

NOTARY PUBLIC RANCHI

Sunil Chandra Das
25/10/21
सुनिल चन्द्र दास
SUNIL CHANDRA DAS
General Manager (E.M.)
महाप्रबन्धक (ई.एम.)
Jharkhand Urja Sancharan Nigam Limited

General Manager (E & M)
Eastern Coalfields Ltd
Sanctoria, Dishergarh

Jharkhand Urja Sancharan Nigam Limited

कर अथवा फोटो कॉपी आदि द्वारा इसी रसीद का दुसरे दस्तावेज पर मुद्रांक शुल्क का भुगतान के प्रमाण हेतु उपयोग भारतीय मुद्रांक अधिनियम, 1899 की धारा 62 अन्तर्गत दण्डनीय अपराध है।



Government of Jharkhand

Receipt of Online Payment of Stamp Duty

WITHOUT PREJUDICE

Rec/FMA No. 641 of 2019 (NTPC Limited –versus- Eastern Coalfields Limited & Others)
Presently pending before the Hon'ble High Court at Calcutta.


Re: 280/MP/2019, ECL vs ERPC before Hon'ble Central Electricity Regulatory Commission (hereinafter "CERC") and order of Hon'ble CERC dated: 21.07.2020.

Re: The Minutes of Meeting dated: 10.08.2021 chaired by Hon'ble Secretary, Ministry of Power – circulated by Under Secretary, MoP vide OM ref no. 10/07/2021-Th.I, dated: 12.08.2021.

Sub: Agreement for relieving NTPC Limited for the responsibility of Operation and Maintenance (O&M) of Farakka Lalmatia Transmission System (FLTS) and handing over the asset of FLTS to Jharkhand Urja Sanchar Nigam Limited (JUSNL) on "as is where is" basis at zero cost.

This agreement is made on 25th day of October, 2021 between:

a) Eastern Coalfields Limited, having its registered office at Sanctoria, P.O.- Dishergarh, Pin Code - 713333, District : Paschim Burdwan, West Bengal, hereinafter referred to as the "ECL";



25 OCT 2021

NOTARY PUBLIC, RANCHI

General Manager (E & M)
Eastern Coalfields Ltd
Sanctoria, Dishergarh
Pin 713333

Signature of General Manager (E & M)
Jharkhand Urja Sanchar Nigam Limited

Signature of Sunil Chandra Das
SUNIL CHANDRA DAS
Addl. General Manager (EM)
Farakka Limited Farakka

(b) Jharkhand Urja Sanchar Nigam Limited, having its registered office at JUSNL Building, Kusai Colony, Doranda, Ranchi - 834002, hereinafter referred to as the "JUSNL"; and

(c) NTPC Limited (Formerly known as National Thermal Power Corporation Ltd.), having its registered office at NTPC Bhawan, SCOPE Complex, Institutional Area, Lodhi Road, New Delhi - 110003, hereinafter referred to as the "NTPC".

Farakka-Lalmatia Transmission System (hereinafter referred to as the "FLTS") includes 82 km long intra state Power transmission line connecting Farakka Thermal Power Plant of NTPC and Lalmatia Sub-Station of ECL- Rajmahal Area along with 220/132kV Lalmatia Sub-Station of ECL-Rajmahal Area. Earlier, this FLTS was constructed by NTPC at the cost of ECL and being maintained by NTPC till date on payment of O&M charges by ECL. The ownership of the FLTS is with ECL till date.

However, disinclination of the NTPC in continuing with the O&M job of the FLTS, disputes cropped up between the parties leading to filing of a writ petition being W.P. No. 17044 (W) of 2015 by the ECL in the Hon'ble High Court at Calcutta and the said writ petition was disposed of by the Hon'ble Court by the judgement dated 23rd September 2016,.

NTPC preferred an appeal being MAT 1981 of 2016 (subsequently numbered as FMA 641 of 2019), hereinafter referred to as the "said appeal", before the Hon'ble Division Bench of the High Court at Calcutta against the aforesaid judgement dated 23rd September 2016 wherein, the Hon'ble Court, by an order dated 10th June 2019, referred the matter to the Central Electricity Regulatory Commission (hereinafter referred to as the "CERC") to consider all aspects of the disputes and decide on them and place before the Hon'ble Division Bench.

Pursuant to the aforesaid order dated 10th June 2019, ECL as petitioner made an application to the CERC whereupon the CERC had heard the parties and passed an order on 21st July 2020, the relevant portions whereof are as follows:

25 OCT 2021
25/10/2021
General Manager (E & M)
Eastern Coalfields Ltd
Sanctoria, Dishergarh
Pin-713333

25 OCT 2021
25/10/2021
General Manager (E & M)
JUSNL
Jharkhand Urja Sancharan Nigam Limited -5-

25 OCT 2021
25/10/2021
SUNIL CHANDRA DAS
अपर महाप्रबन्धक (ई.एम.)
Addl. General Manager (EM)
एनटीपीसी लिमिटेड, फरक्का
NTPC Limited Farakka

"45 (d) ...FLT System be transferred from the Petitioner to JUSNL on "as is where is" basis at zero cost without the Petitioner's claim towards transmission charge for past use of FLT System by JUSNL and depreciation charge of FLT System.

(e) The management of the Petitioner and JUSNL shall work out a transfer plan containing preparation of inventories, inspection of assets, legal transfer of title and physical transfer of FLT system and execute the same within a six months from the date of this order.

(f) After transfer, JUSNL shall have the ownership of FLT System.


(g) JUSNL shall bear the necessary cost for overhauling/ upgradation/ replacement of FLT system.

(h) After the transfer, JUSNL shall file the tariff petition before JSERC for determination of the tariff of FLT System."

"47. ...FLTS System shall be transferred by the Petitioner to JUSNL on "as is where is" basis at zero cost within a period of six months from the date of this order. The responsibility for operation and maintenance of FLT System shall vest in JUSNL. NTPC will be relieved from the responsibility of O&M of FLT System, once FLT System is transferred to JUSNL."

The aforesaid order dated 21st July 2020 of the CERC was therefater placed before the Hon'ble Division Bench of the High Court at Calcutta and the Hon'ble Court by its orders dated 9th July 2021 and 30th July 2021 appointed the Hon'ble Secretary, Ministry of Power, Government of India, as the Nodal Officer to discuss the findings of the CERC with all the parties and take such findings forward to their logical conclusion.

A meeting was held on 10th August 2021 by the Hon'ble Secretary, Ministry of Power, Government of India, pursuant to the aforesaid orders dated 9th July 2021 and 30th July 2021, the minutes whereof was communicated on 12.08.2021, inter-alia, directing ECL to handover the FLTS assets on "as is where is basis" to JUSNL, the Operation and Maintenance whereof as was with the NTPC is also to be transferred to the JUSNL without any further delay and latest by 20th August 2021 and further directing JUSNL to comply with all other directions of the CERC's order dated 21.07.2020, after the transfer of the FLTS from ECL.



[Signature]
25/10/21
General Manager (E & M)
Eastern Coalfields Ltd
Sanctoria, Dishergarh
Pin-713333

[Signature]
25/10/21
Jharkhand Urja
DGM/STU
JUSNL

[Signature]
25/10/21
SUNIL CHANDRA DAS
अपर महाप्रबन्धक (ई.एम.)
Addl. General Manager (EM)
एनटीपीसी लिमिटेड, फरक्का
NTPC Limited Farakka

Also, as directed, ECL shall take up the issue of land lease with Ministry of Coal Separately, independent of immediate asset transfer of FLTS to JUSNL. Decision of the Ministry of Coal will be binding on all the parties.

The parties have jointly consented that, vide this agreement:

- a. NTPC is being relieved from the O&M of the FLTS henceforth from the date of signing of this agreement.
- b. ECL is handing over the asset of FLTS including 220 kV Transmission Line (DCSS) emanating from Farakka NTPC substation, towers, sub-station equipment, 100 MVA transformers, switchgear and control room building with control panel etc to JUSNL on "as is where is" basis at zero cost without its claim towards transmission charge for past use of FLT System by JUSNL and depreciation charge of FLT System.
- c. On and from the date of signing of this agreement, JUSNL shall have the ownership of FLTS and shall maintain the line at their own cost as per the Regulations. JUSNL shall ensure availability of quality and reliable power supply to Rajmahal Area.
- d. JUSNL shall bear the necessary cost for overhauling/ upgradation/ replacement of FLTS and all incidentals relating thereto.
- e. After the transfer, JUSNL shall file the tariff petition before JSERC for determination of the tariff of FLT System.
- f. ECL shall take up the issue of land lease with Ministry of Coal, Government of India, separately and independent of immediate asset transfer of FLTS to JUSNL under this agreement. Decision of the Ministry of Coal, Government of India, will be binding on all the parties.
- g. The associated jobs of preparation of inventories/ inspection of asset shall be completed subsequently by a committee of representatives of all concerns (ECL, NTPC and JUSNL) and the parties shall submit the list/ inspection report within a period of I (one) month from date unless such time is required to be extended due to unavoidable circumstances. The same shall constitute a part of this agreement.
- h. All available relevant documents regarding FLT System may be handed over to JUSNL.

[Signature]
25/10/2021
General Manager (E & M)
Eastern Coalfields Ltd
Sanctoria, Dishergarh
Pin-713333

[Signature]
25/10/2021
Dmytro
Ranchi

Jharkhand Urja Sancharan Nigam Limited

NOTARY PUBLIC RANCHI

[Signature]
25/10/2021
SUNIL CHANDRA DAS
अपर महाप्रबन्धक (ई.एम.)
Addl. General Manager (EM)
एनटीपीसी लिमिटेड, फरक्का
NTPC Limited Farakka



- i. The parties herein declare that they have unequivocally accepted the observations and directions contained in the order dated 21st July 2020 passed by the CERC and if any issue in terms of the said order dated 21st July 2020 of the CERC has not been dealt with in this agreement, then the same will be complied with by the parties in accordance with the directions contained in the said order dated 21st July 2020 of the CERC.
- j. The parties herein hereby undertake to abide by the terms and conditions of this agreement.

JUSNL
 25/10/2021
 Jharkhand
 Jharkhand Urja Nigam Limited

NTPC
 25/10/2021
 Sunil Chandra Das
 SUNIL CHANDRA DAS
 अपर महाप्रबन्धक (ई.एम.)
 Addl. General Manager (EM)
 एनटीपीसी लिमिटेड, फरक्का
 NTPC Limited Farakka

ECL
 25/10/2021
 General Manager (E & M)
 Eastern Coalfields Ltd
 Sanctoria, Dishergarh
 Pin-713333

1. Subhajyoti Jana, Manager (E&M), ECLHQ
 2. Ajit Kumar Yadav, Asst. Manager Law, NTPC-Farakka
 3. Anup Kumar Lall, Sr. Manager (STU), JUSNL.

Date: 25th October, 2021.



25 OCT 2021

NOTARY PUBLIC, RANCHI

Identified by
 25/10/2021
 Identification Verification
 of Lawyers.

Final SoP/ Guidelines for diversion of RPC approved Spare Transformers and Reactors to the constituents / state transmission utilities

A. Background:

1. In line with the recommendations of committee formed under the direction of CERC in Petition No. 38/TT/2017, requirement of regional spare transformers and reactors is being assessed by POWERGRID and agreed in RPCs based on the population of existing transformers and reactors in POWERGRID substations.
2. POWERGRID procures & maintains the RPC approved spare transformers and reactors as Regional Spares to meet any contingency in its existing Substations to ensure the reliability of the grid and to minimise downtime.
3. These spares are approved primarily for use of POWERGRID in its ISTS Substations. However, in some of the cases, requests are being received by POWERGRID from constituents/ state utility to divert Regional spare transformer(s)/ reactor(s) on temporary basis for their use considering certain exigencies, to maintain continuity of power supply and also considering the grid stability & reliability. Further, in past, in few of the cases regional spare transformers/ reactors have been diverted to constituents/ state utilities after necessary approval of concerned RPC.

B. General Condition:

4. As Regional spares are approved primarily for use of POWERGRID in its ISTS Substations, its diversion to regional state transmission utility may be considered under exceptional circumstances considering the gravity of requirement to the constituent and its beneficiaries on expeditious replenishment basis. Further, Inter Regional diversion of equipment to the constituent shall not be considered.

C. Utilities eligible for diversion: Following utilities (hereinafter referred as Borrower) shall be eligible for diversion of Regional spares as per the conditions specified;

- i) **State Transmission Utility:** Diversions can be considered in case of failure of existing equipment in use of respective RPC constituents and diversion required in the interest of Grid security and reliability. It is clarified that under normal circumstances, a regional spare shall not be diverted for commissioning of new assets.
- ii) **Other Utilities:** For utilities other than State Transmission Utilities, under normal circumstances, such diversions are not envisaged. However, if agreed by RPC forum, such diversions may be allowed only under the exceptional circumstances.

D. Modalities for diversion of Regional spare transformer(s)/ reactor(s) to State Transmission Utility:

5. In case of requirement of Regional spare transformer/ reactor by the Borrower i.e. State Transmission Utility, the requirement shall be put up for consent of the respective RPC forum.
6. In this regard, the concerned Borrower shall submit the following to the RPC for consideration:
 - i) Contingency situations describing the requirement of spare equipment from POWERGRID.
 - ii) Action plan along with timeline for return/ replenishment of the spare equipment to POWERGRID.
7. Decision of diversion along with associated terms and conditions for diversion will be based on the agreement reached in RPC Forum after considering the merit of the request. It is clarified that regional spare transformer/ reactor can be diverted only in case of restoration of failed equipment and generally not for commissioning of new equipment.
8. Upon approval in the RPC, the Spare transformer/ reactor shall be diverted to the Borrower only on usage/replenishment basis and the same shall not be sold to the Borrower under any circumstances.

E. Signing of agreement:

Upon approval in the RPC Forum & before diversion of Regional spare transformer/ reactor, an agreement shall be signed between POWERGRID and the Borrower. The agreement shall cover the terms and conditions for the diversion of equipment in line with this SOP and as discussed below broadly.

a) Time period:

The Borrower shall return the Spare transformer/ reactor within the timeframe agreed by the RPC which in all cases shall not exceed a maximum of 24 months from the date of diversion. The spare transformer/ reactor is to be lifted within 3 months of signing of agreement. Failing which the consent for diversion as agreed in the RPC shall be deemed to be withdrawn.

POWERGRID shall monitor the list of such diverted equipment and coordinate to ensure that the replenishment by the borrower is done as per agreed timeframe and keep the RPC forum-informed.

b) Cost Implications:

The equipment shall be diverted on zero cost basis/ cost neutral basis to POWERGRID. On account of the diversion, POWERGRID shall remain revenue

neutral i.e. there shall be no change in CERC approved tariff or its sharing due to diversion of the concerned regional spare transformer/ reactor. The sharing of cost of the asset shall be as per Sharing Regulations. Tariff of the asset shall be borne by the requestor for the period of usage and charges of the asset shall be recovered bilaterally and adjusted back to pool.” Tariff of the asset would be put up to borrower and RPC by POWERGRID in advance.

c) Responsibility of Borrower:

- i) The Borrower shall be responsible for dismantling, to & fro transportation, transit insurance, statutory expenses, erection, testing & commissioning charges (including at POWERGRID station after return) etc., any other incidental expenditure associated with the diversion of equipment or any loss to POWERGRID on account of diversion and all such charges shall be borne by the Borrower.
- ii) Borrower shall verify the condition of equipment at POWERGRID substation before taking the equipment on loan basis. After verification, the equipment shall be handed over to the Borrower.
- iii) The Borrower shall be responsible for transportation/ erection/ commissioning/ operation & maintenance.
- iv) The Borrower shall be responsible to maintain the equipment in healthy condition as per the standard maintenance practices.
- v) The Borrower shall be responsible to ensure that the equipment is returned to POWERGRID in healthy condition as per the commitment/ action plan agreed prior to diversion.
- vi) Any damage/failure of the equipment shall be the responsibility of the Borrower till the equipment is taken over by POWERGRID in healthy condition.
- vii) In case of failure/ breakdown of equipment during transportation/ erection/ commissioning/ operation & maintenance or during any other activity, the Borrower shall return the equipment after repair/ refurbishment of the same rating as per the POWERGRID specification. Alternatively, new equipment matching with the POWERGRID specifications and from POWERGRID approved vendors shall be replenished. All cost for repair/ refurbishment/ replacement as applicable shall be borne by the Borrower.
- viii) After returning of equipment, all pre-commissioning tests shall be jointly performed at POWERGRID station to ascertain healthiness. In case of any deviation, POWERGRID shall take up the repair of equipment and cost of the repair shall be borne by the Borrower.

d) Return of equipment:

In case of any exigency or if required in the interest of the Grid, POWERGRID reserves the right to demand the diverted Spare from the Borrower prior to the time period as agreed in the RPC after intimation to RPC. Once consented in RPC Forum, Borrower shall return the diverted spare to POWERGRID on immediate basis.

e) Penalty clause:

In the event of a delay in the return or replenishment of spare equipment beyond the agreed timeframe (which is a maximum of 24 months from the date of diversion), a penalty of 15% of the approved tariff for the diverted equipment will be imposed on the Borrower for the duration of the deployment. However, this penalty will not be applied if an extended return or replenishment period is approved by the Regional Power Committee (RPC), subject to maximum extension period of 12 months.

.....

Annex B.2.1.i

Annex B.2.1.i

GUIDELINES on DIVERSION of REGIONAL COLD SPARES (TRANSFORMERS and REACTORS)



November 2025

NORTHERN REGIONAL POWER COMMITTEE

1. Background & Objective

POWERGRID procures and maintains regional spares- transformers and reactors- to ensure the continuity of power supply and grid stability in the event of a contingency, such as the sudden failure of an in-service transformer or reactor. The primary purpose of these spares is to meet contingencies/emergencies within ISTS substations of the region. Regional spares are primarily sanctioned for use in Inter-State Transmission System (ISTS) substations. However, diversion of such spares to a State Transmission Utility (STU) may be permitted only under exceptional circumstances, based on the criticality of the requirement and subject to expeditious replenishment by the Borrower.

These Guidelines sets out the framework, eligibility, processes, roles, responsibilities, and conditions under which regional spares- transformers and reactors-maintained by POWERGRID may be diverted to eligible utilities. These Guidelines seeks to balance the need to extend emergency support to constituents with the responsibility of ensuring adequate spare availability for the ISTS network.

2. Scope & Applicability

These Guidelines applies exclusively to transformers and reactors approved by the respective Regional Power Committee (RPC) as *Cold Regional Spares* for use in Inter-State Transmission System (ISTS) substations within the region. These spares are procured, owned, and maintained by POWERGRID to ensure operational continuity of the ISTS network during contingencies. Diversion of Regional Spares may be considered for the following eligible beneficiaries within the same Region:

- o **ISTS Substations.**
- o **State Transmission Utility (STU) Substations**

Diversion may be considered only in case of failure of existing in-use equipment and where diversion is essential for grid security and reliability. Diversion for commissioning of new assets or Inter-regional diversion of equipment to any constituent may not be permitted. All diversions may be executed strictly on a replenishment basis and may not amount to sale or transfer of ownership of the equipment.

3. Roles and Responsibilities

3.1. Lender (POWERGRID): POWERGRID may ensure that the cold regional spares- Transformers and Reactors- are maintained in operationally ready condition and available for deployment during contingencies. POWERGRID may:

- Maintain a central inventory of all Regional Spares with technical particulars and locations.
- Implement the diversion only after RPC or its sub-forum's approval, as the case may be, and in accordance with these guidelines.
- Record every approved diversion in the central register, including date of diversion, borrower, and approved return timeline.

- Monitor adherence to approved diversion timelines and report deviations to the respective RPC Secretariat.

3.2. Borrower: The Borrower may be responsible for safe custody and operation of the diverted Regional Spare during its possession. The Borrower may:

- Submit a formal diversion request to the respective RPC Secretariat with required technical and contingency details.
- Jointly verify the equipment condition at POWERGRID substation prior to MoU signing.
- Bear all expenses associated with transportation (both ways), transit insurance, erection, testing, commissioning, and related statutory charges, as applicable, and any incidental expenditure or loss to POWERGRID.
- Ensure site readiness and compatibility of the spare equipment before diversion.
- Furnish a valid Bank Guarantee equal to the prevailing cost of the equipment, effective till 45 days after return or replenishment is completed.
- Maintain and operate the equipment in accordance with applicable technical standards and POWERGRID's guidelines.
- Return or replenish the equipment in healthy condition within the approved timeframe and bear any repair or replacement cost arising from damage or failure.
- After returning of equipment, all pre-commissioning tests may be jointly performed at POWERGRID station to ascertain healthiness. In case of any deviation, POWERGRID may take up the repair of equipment and cost of the repair may be borne by the Borrower.

3.3. RPC Secretariat: The concerned RPC Secretariat may facilitate deliberation of the diversion proposal in the RPC or its sub-forum and place the Borrower's request before the members for decision. It may record all decisions, including timelines for return or replenishment. RPC Secretariat may communicate the decision of the forum to borrower and Powergrid within one week of decision in RPC or its sub-forum meeting.

4. Procedure for Diversion

4.1. Submission of Request: The Borrower may submit a written request to the concerned RPC Secretariat, specifying:

- The nature of contingency or failure necessitating diversion, including details of affected substation and equipment.
- Technical parameters of the failed equipment and the matching requirement from the Regional Spare pool.
- A detailed action plan and proposed timeline for return or replenishment of the diverted equipment.

4.2. Evaluation and Approval: The RPC or its sub-forum may evaluate the request on merit, considering:

- The severity and genuineness of the contingency.
- Availability of the Regional Spare and its necessity for ISTS grid reliability.
- Impact on overall system stability and adequacy of remaining spares.

The decision of the RPC or its sub-forum will be final and binding on all concerned entities. Upon approval, the forum may record the diversion details and the agreed period of utilization in its proceedings.

4.3. Execution of Memorandum of Understanding (MoU)

- Following the approval of diversion by the respective RPC or its sub-forum, the Borrower and POWERGRID may execute a Memorandum of Understanding (MoU) within forty-five (45) days from the date of RPC or its sub-forum. *For the purpose of these Guidelines, date of communication by RPC secretariat of the decisions of the forum to borrower and Powergrid as defined in para 3.3 shall be treated as the date of RPC or its sub-forum approval, as the case may be.*
- The MoU may specify all terms and conditions of diversion, including equipment details, responsibilities of both parties, financial implications, Bank Guarantee (BG) requirements, maintenance and reporting obligations, timelines for return/replenishment, and applicable penalties for default.

4.4. Condition Assessment and Testing

- Before diversion, a joint inspection of the equipment may be carried out by POWERGRID and the Borrower at the designated POWERGRID substation. The physical condition and test results may be documented and signed jointly.
- Upon return, the equipment may undergo joint pre-commissioning testing at the POWERGRID station to ascertain its healthiness. Any deviation, defect, or damage observed during inspection may be rectified at the Borrower's cost. Where repair or refurbishment is necessary, the Borrower may carry it out through the OEM or other approved agency as per POWERGRID specifications.

5. General Conditions of Diversion

5.1. Timeframe for Diversion and Return

- The Borrower should take the physical handover of the equipment from the designated POWERGRID substation within forty-five (45) days from the date of execution of the MoU.
- Failure to take the physical handover of the equipment within the ninety-days (90) days from RPC or its sub-forum approval, as applicable, may be treated as revocation the diversion approval.

- The maximum diversion period may not exceed twenty-four (24) months from the Zero Date of Diversion.
- The Borrower may ensure return or replenishment of the diverted equipment within this period as per the action plan approved by the RPC or its sub-forum, as applicable, and the provisions of the MoU.
- Any request for extension of the diversion period beyond twenty-four (24) months or delay in taking the physical handover of the equipment may require prior approval of the respective RPC or its sub-forum, as applicable, supported by written justification.
- On completion of the diversion period, the Borrower should return the equipment in healthy condition to POWERGRID to POWERGRID's technical specifications.
- *The "Zero Date of Diversion" shall be the date recorded in the joint handover certificate signed by representatives of POWERGRID and the Borrower at the time of physical transfer from the designated POWERGRID substation or storage location.*
- *The "Date of Return" shall be the date recorded in the joint handover certificate signed by representatives of POWERGRID and the Borrower, after successful healthiness checking, at the time of physical transfer at the designated POWERGRID substation or storage location.*

5.2. Early Recall

- RPC Forum may recall any diverted equipment at any time before the expiry of the approved period if required in the interest of grid security or system reliability.
- The Borrower should return the equipment immediately upon receipt of such recall notice, and the RPC Secretariat may be intimated accordingly.

5.3. Financial Provisions: Diversion of Cold Regional Spares may be carried out on a cost-neutral basis, ensuring that POWERGRID neither incurs financial loss nor earns additional revenue on account of such diversion. The diversion should not result in any change in the Yearly Transmission Charges recoverable by POWERGRID as per the approved tariff against the diverted asset and financial adjustments, if any, may be settled within the regional pool mechanism as approved by the RPC forum. The Borrower may bear all direct and incidental costs, including transportation, loading/unloading, insurance, erection, testing, and commissioning charges. The Borrower may be fully liable for any loss, damage, theft, or deterioration of the equipment during the diversion period. Insurance coverage may be obtained in the joint name of POWERGRID and the Borrower, with POWERGRID designated as the primary beneficiary.

In line with these principles, the financial treatment for diversion may be as follows:

- **ISTS Substations:** Diversion to any ISTS substation, should be without financial liability to Powergrid/DIC. Such diversion should not affect the Regional tariff or cost-sharing framework.
- **STU Substations:** For diversions to STU substations, the equivalent Yearly Transmission Charge (YTC) of the diverted asset on pro-rate basis, along with any applicable penalty, may be credited to the Regional ISTS Pool for the diverted period.

For this purpose, POWERGRID may raise bilateral bills to the borrower to recover the equivalent YTC of the diverted asset on pro-rate basis, along with any applicable penalty. The YTC may be computed in accordance with the prevailing Tariff Regulations, Sharing Regulations, or any other rules or regulations notified by CERC or the Ministry of Power, and all provisions relating to due dates, late payment surcharge, interest, or other billing conditions may likewise be governed by the applicable rules or regulations. The amount so recovered may be adjusted in the Regional ISTS Pool through the Second Bill mechanism under sharing regulations, and the corresponding credit shall be passed on to the DICs of the Region in the same Second Bill.

5.4. Bank Guarantee (BG) requirements:

- Borrower may furnish a valid Bank Guarantee equal to the prevailing cost of the equipment, effective till 45 days after return or replenishment is completed.
- The BG may be invoked by POWERGRID to recover any financial loss or liability arising from events such as failure to return or replenish the equipment within the agreed timeframe, or failure to repair, refurbish, or replace the equipment in the event of damage, failure, or loss during transit, erection, or operation.

5.5. Penalty and Default:

- If the Borrower fails to return or replenish the diverted equipment within the agreed timeframe, which may not exceed 24 months, a penalty of 15% of the approved Yearly Transmission Charge (YTC) of the diverted asset may be levied on a pro-rata basis for the delayed duration.
- The penalty amount may be credited to the Regional Component of ISTS charges for the corresponding period. In case of continued default or non-replenishment, POWERGRID may report the matter to the RPC forum for further decision, which may include encashment of the Bank Guarantee and/or regulatory intervention.

5.6. Record-Keeping and Monitoring: POWERGRID may maintain a centralized and up-to-date register of all diversions, containing the following information:


- Borrower entity name and category.
- Equipment details (type, rating, make, serial number).
- Date of diversion and expected return date.
- Physical and test condition at dispatch and upon return.
- Financial treatment and applicable YTC adjustments.
- Status of replenishment or replacement.

6. Review and Amendment: These Guidelines may be reviewed from time to time to incorporate operational experience, regulatory updates, or changes in system requirements.



7. Power to Relax: RPC forum may relax any of the provisions of these guidelines on its own or on an application made before it by the affected party.

Corrective Action – PAN INDIA


2nd June & 26th June 2026 low frequency event

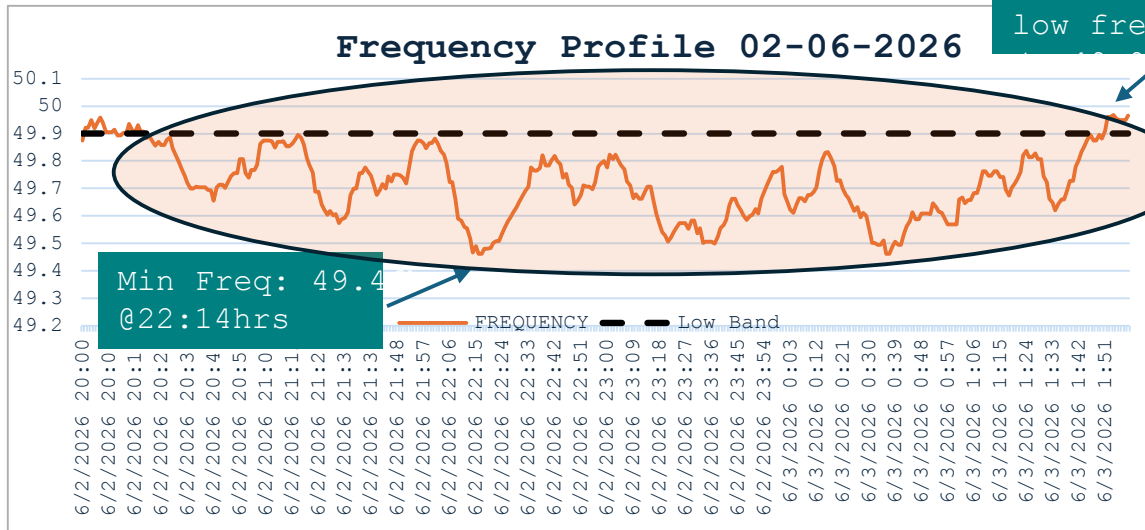

All India Non Solar Max Demand met:

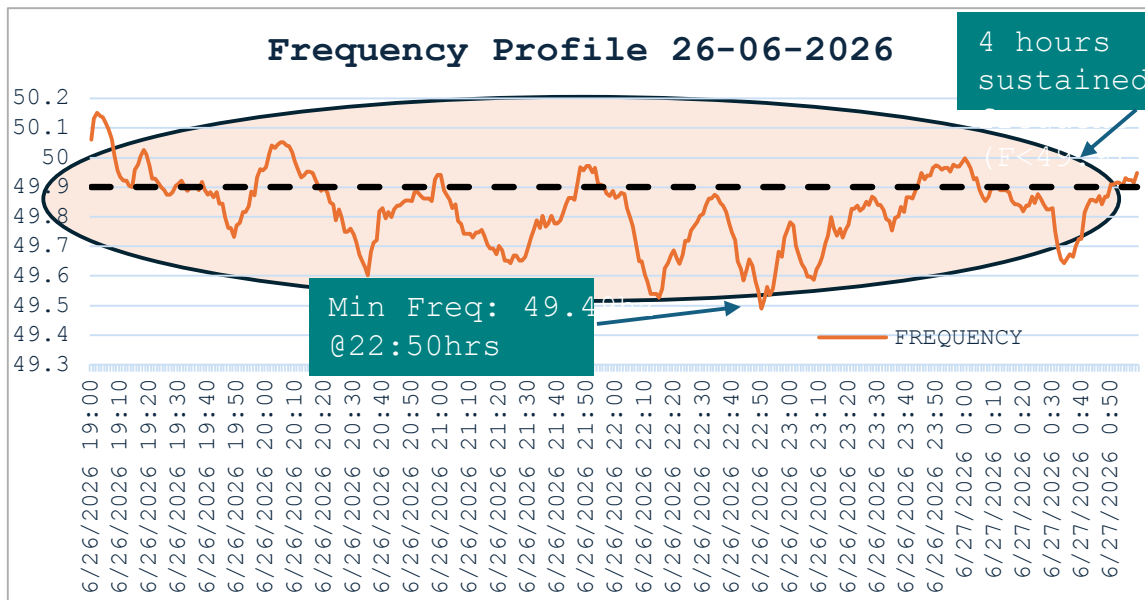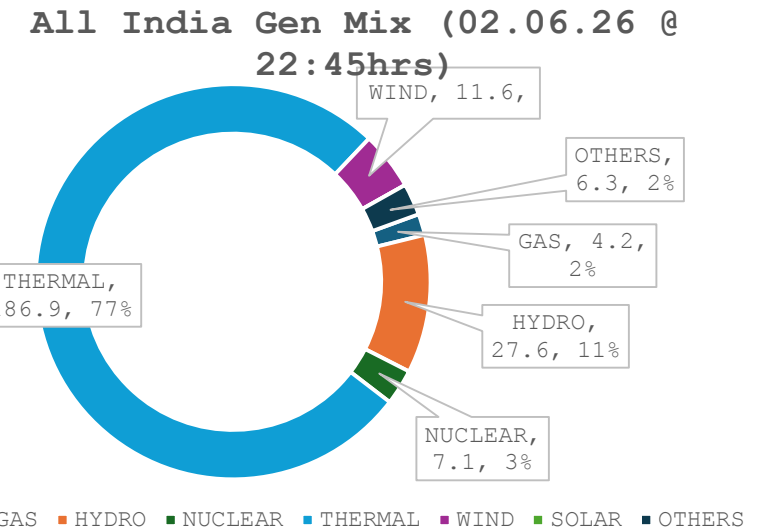


All India Non Solar Max Demand met:

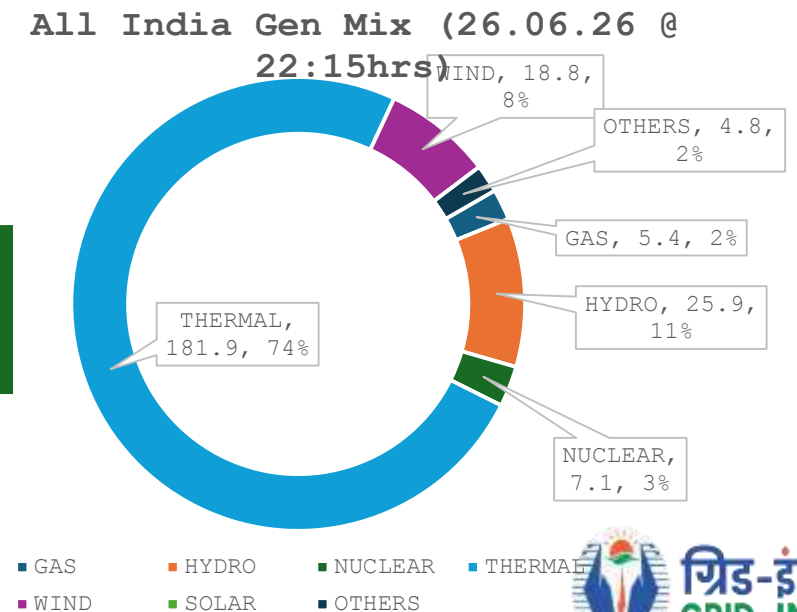

Ancillary Service Despatch– PAN INDIA


2nd June & 26th June 2026 low frequency event

TRAS Despatch 2nd June 2026

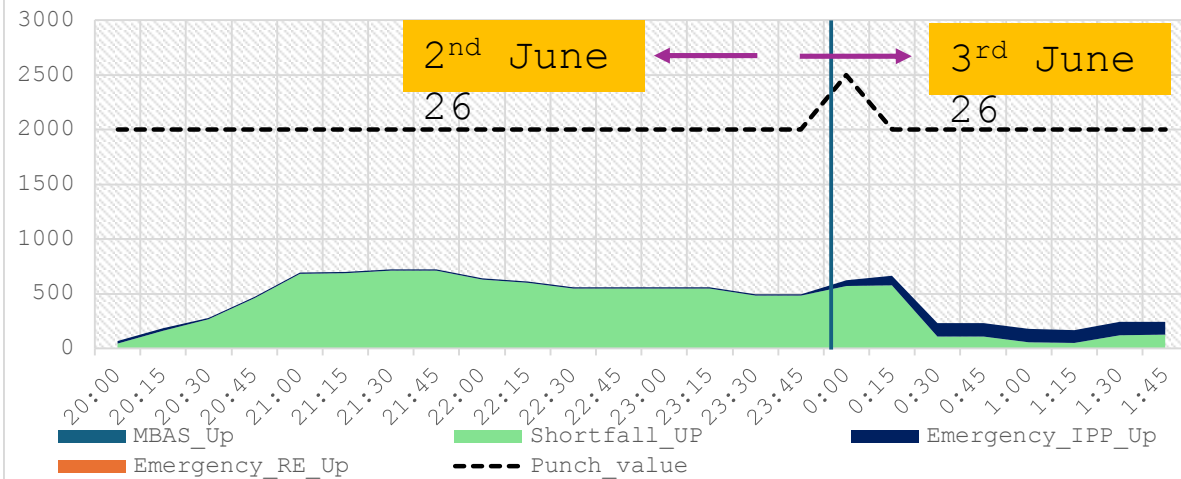

Max **721MW** TRAS up despatched out of 2000MW instruction due to Less Reserve

TRAS Despatch 26th June 2026

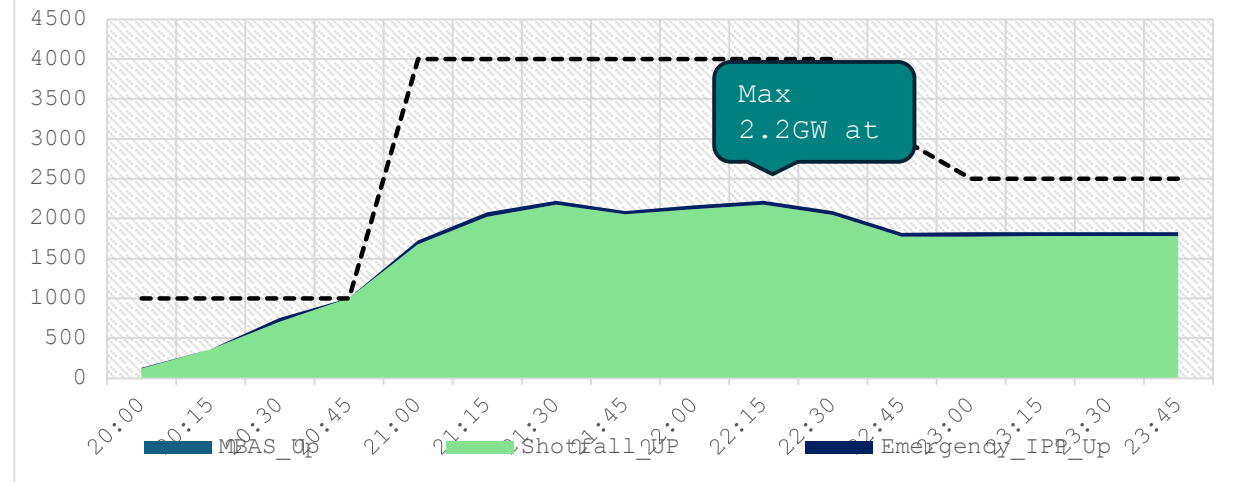


Max **2.2GW** TRAS up despatched out of 4GW instruction due to Less Reserve

Power Market scenario – Exchange


2nd June & 26th June 2026 low frequency event

IEX RTM Snapshot 2nd & 3rd June

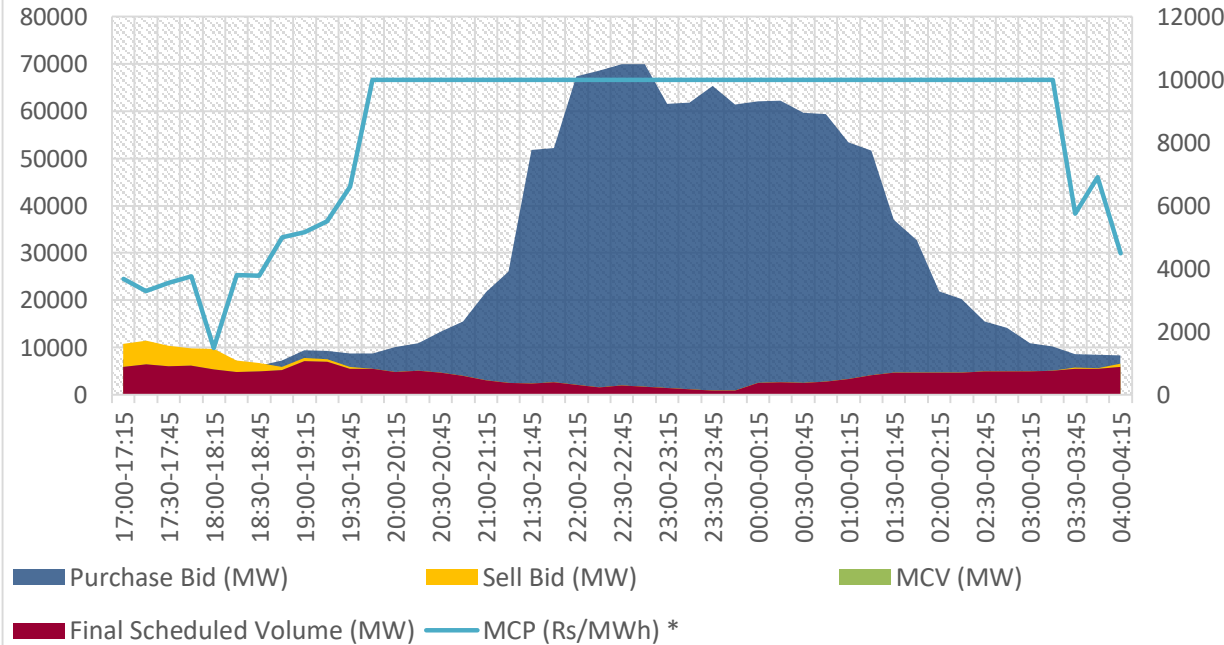

Cleared volume: 2.5GW
against 65GW Purchase bid
(Max) in IEX RTM

IEX RTM Snapshot 26th June

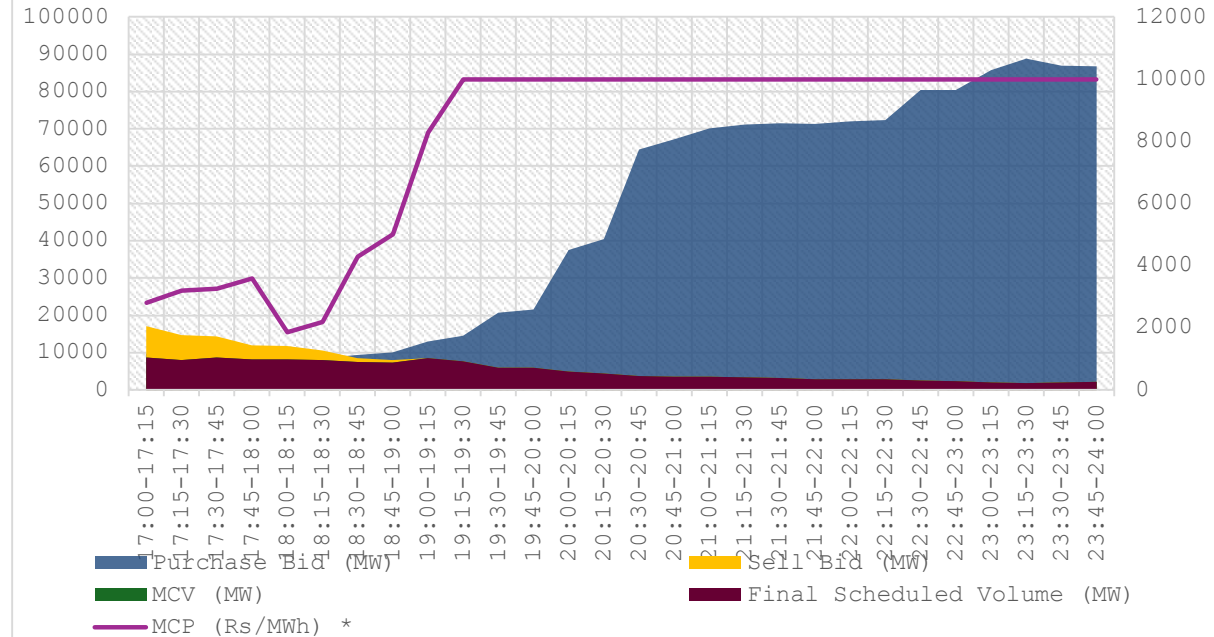

Cleared volume: 1.9GW
against 88GW Purchase bid
(Max) in IEX RTM

Low Frequency event 2nd & 26th June 2026

State Name	BIHAR	WEST BENGAL	ODISHA	DVC	JHARKHAND
2nd June 2026	Max OD: 151 MW (OD: 4.8%)	Max OD: 633 MW (OD: 48.2%)	Max OD: 103 MW (OD: 10.8%)	Max OD: 299 MW (OD: 74.7%)	Max OD: 120 MW (OD: 56.9%)
26th June 2026	Max OD: 1055 MW (OD: 61.5%)	Max OD: 546 MW (OD: 81.7%)	Max OD: 532 MW (OD: 64.1%)	Max OD: 204 MW (OD: 51.1%)	Max OD: 135 MW (OD: 85.9%)

Corrective Action – PAN INDIA


2nd June Deviation by states



Corrective Action – PAN INDIA

2nd June Deviation by states

ODISHA: Frequency (Hz) vs Deviation (MW)
Low Frequency Operation: 02-06-26 20:00 to 03-06-26 01:59

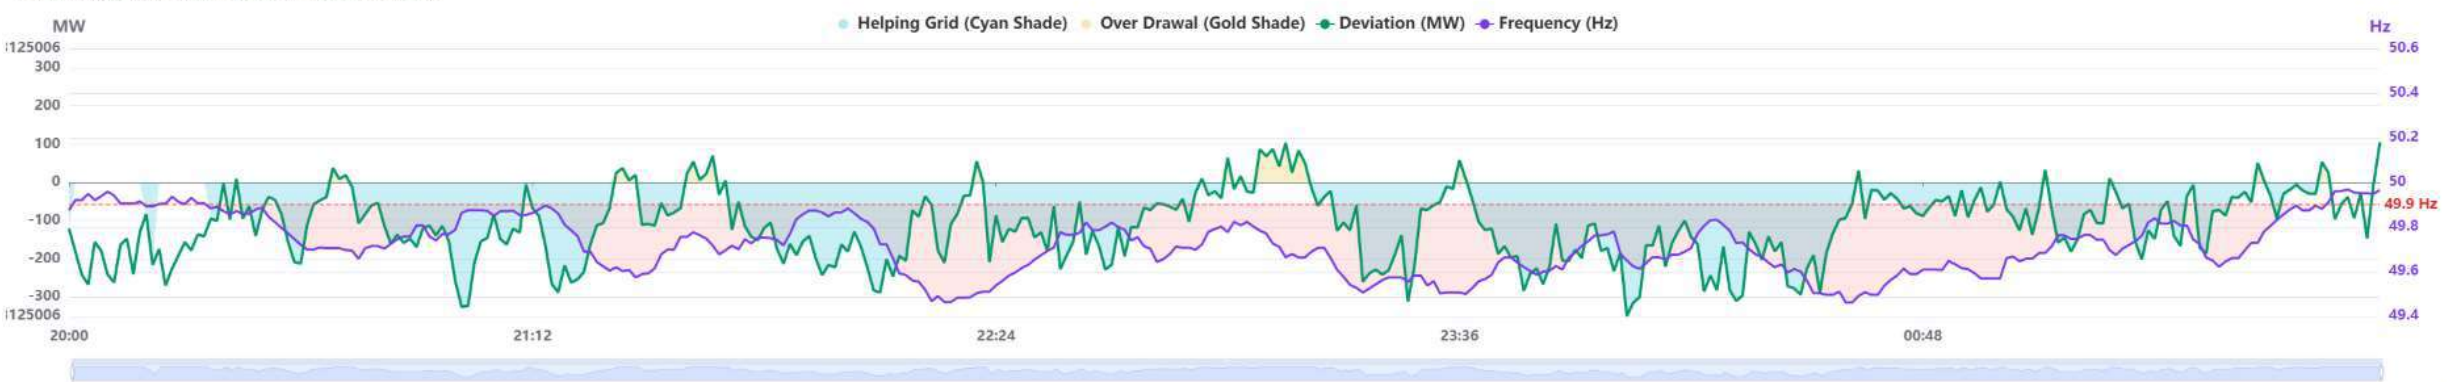

- Annexure 1: ODISHA
- Annexure 1: WEST BENGAL

WEST BENGAL: Frequency (Hz) vs Deviation (MW)
Low Frequency Operation: 02-06-26 20:00 to 03-06-26 01:59




Corrective Action – PAN INDIA

26th June Deviation by states



Corrective Action – PAN INDIA

26th June Deviation by states

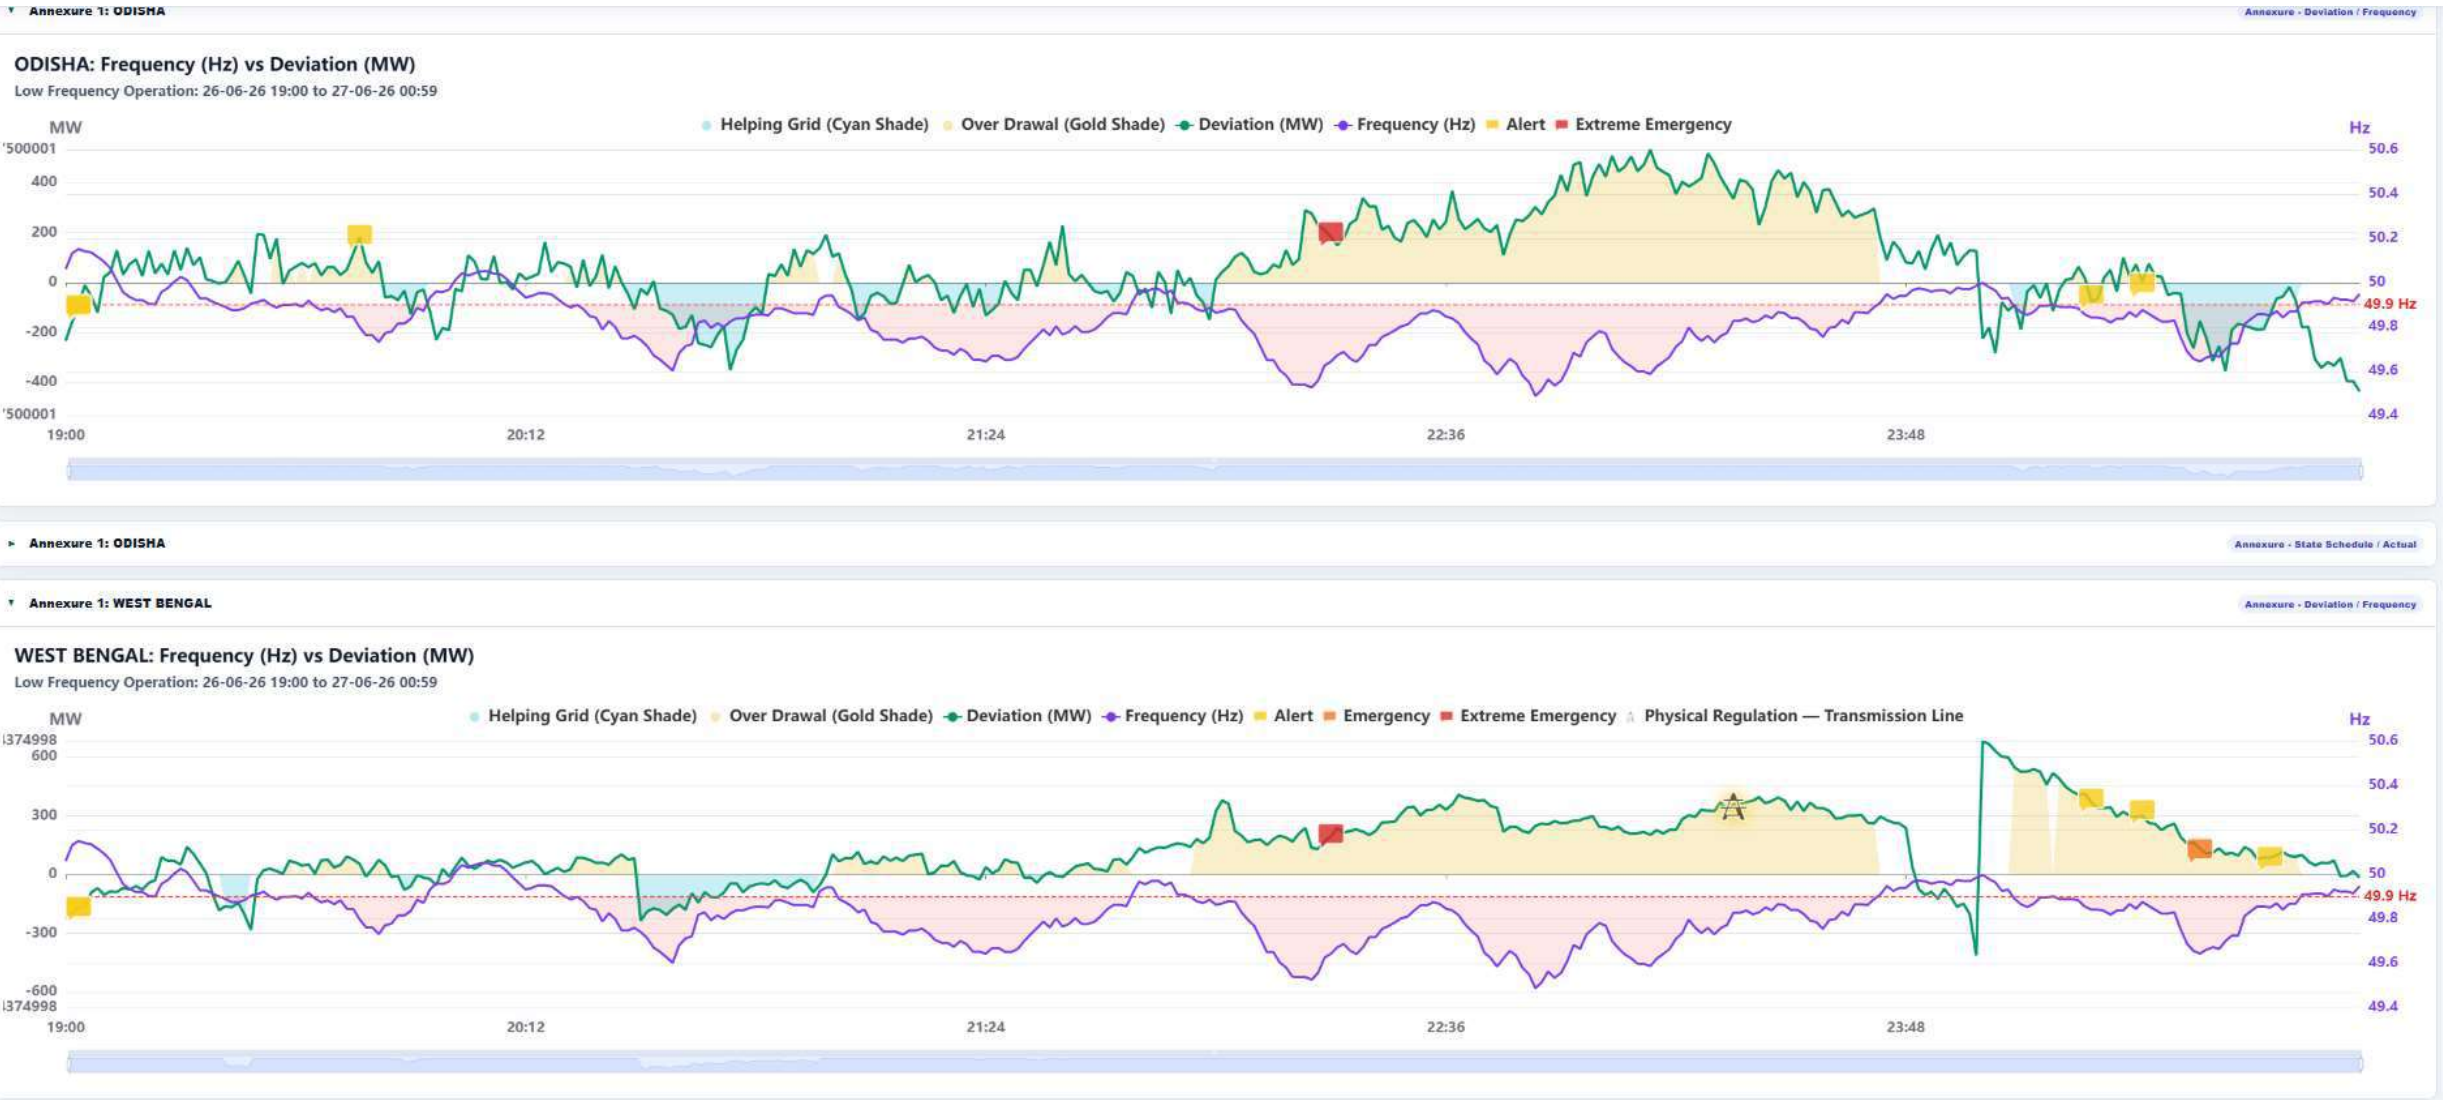

Corrective Action – PAN INDIA

2nd June & 26th June 2026 low frequency event

Action taken in PAN-INDIA

Physical Regulatory measure by WRLDC on 26th June

- 220KV-BHILAD-VAPI-1
- 220KV-BACHAU-MORBI-1
- 220KV-Wardha-BADNERA-1
- 220KV-Wardha-PUSAD-1

Physical Regulatory measure by SRLDC on 2nd June

- 400/220kV Khamman (PG) ICT 1, 2 & 3 for Tamilnadu
- 400/220kV Pagalur (PG) ICT 1, 2 & 3 for Telengana

On 16th July 2026 400/220kV Thrissur ICT 1 & 2 was also opened during low frequency event

Network security concerns around KTPP arising from the prolonged outage of unit 3

Annex B.2.7


Presented by

State Load Despatch Centre,
West Bengal




West Bengal State Electricity Transmission Company Limited


The diagram shows a horizontal red line representing a busbar. Above the busbar, there are three circles labeled U#4, U#5, and U#6. U#6 has a lightning bolt symbol next to it. Below the busbar, there are two large circles representing generators, labeled 246 MW and 230 MW. A thick red vertical bar is positioned between the two generator circles. To the right of the busbar, the text 'KTPP' is written in red. Below the busbar, the text 'Unit#6 & 3 out of bus' is written in red.

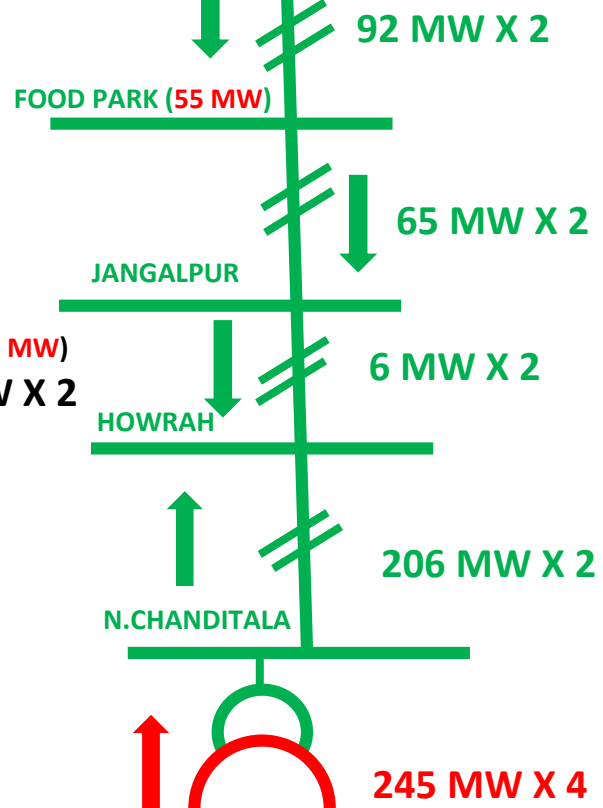

The diagram shows a horizontal red line representing a busbar. Above the busbar, there are three circles labeled U#4, U#5, and U#6. U#6 has a lightning bolt symbol next to it. Below the busbar, there are two large circles representing generators, labeled 246 MW and 230 MW. A thick red vertical bar is positioned between the two generator circles. To the right of the busbar, the text 'KTPP' is written in red. Below the busbar, the text 'Unit#6 & 3 out of bus' is written in red.

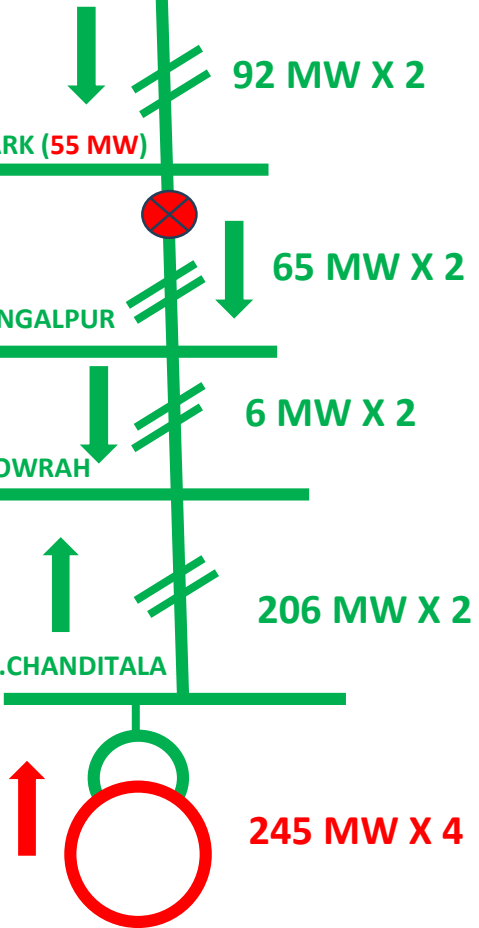

29.06.26//14.08 hrs
WBSEDCL=9506 MW
CESC= 2140 MW(293MW)
STATE=11712 MW

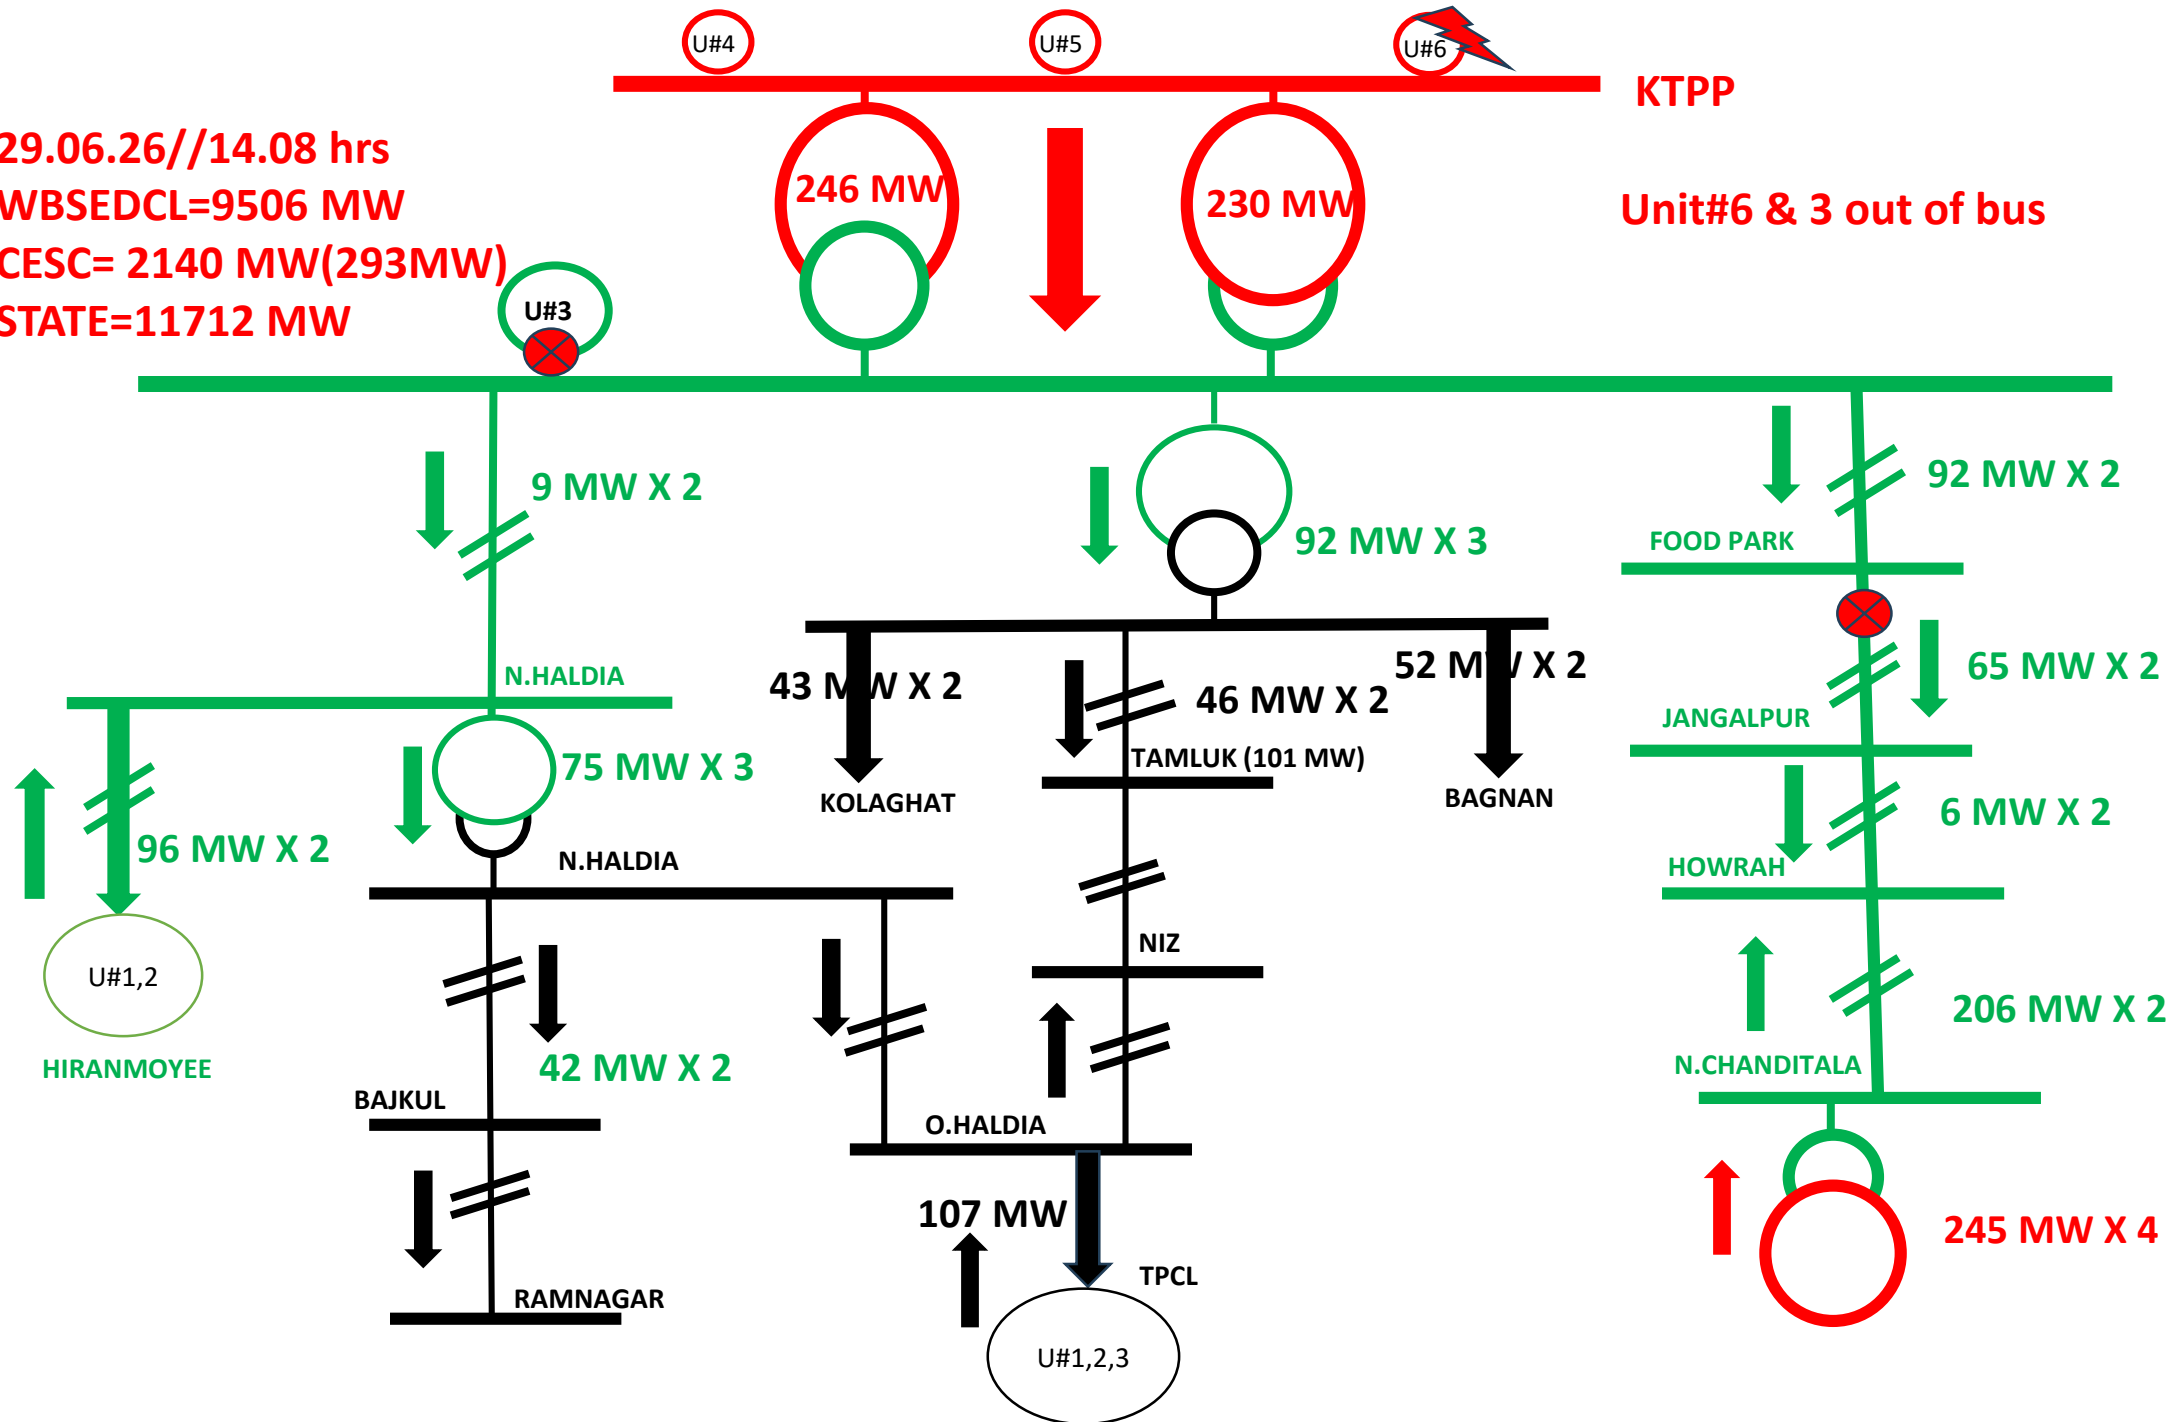

Memo No. : DGM(OPN)/ 9296

Date : 01/4/17

To

The Addl. Chief Engineer,

SLDC, WBSETCL

Sub:- Failure of S.P.S. (Special Protection Scheme) at K.T.P.S. to avoid tripping of one IBT in case of tripping of another IBT

Sir,

It has been observed that during some part of a day (mainly during evening peak hours) the loading on IBTs is such that if one IBT trips the second IBT will not survive even if all the feeders, as designated by you for implementation of SPS, get isolated through SPS. This may result into tripping of all the Units of Stage II.

Placed before you for kind verification of our above observation and taking further necessary action so that tripping of second IBT through overload can be avoided in case of tripping of other IBT otherwise the main aim of SPS implementation will not serve.

Thanking you,

Yours faithfully,

(Prakash Kumar Gupta)
DGM(Operations)/K.T.P.S.
WBPDCL

Date 05.04.17
T.O.O. 14.00 Hrs.

To : DGM(OP), K.T.P.S.

Under present scenario, intention of introduction of special Protection Scheme i.e. 315 MVA IBTs at K.T.P.S. is to offer protection against overloading of each IBT beyond a specified limit, when both are in service. With present load pattern of evening shift and available redundancy, it may not be possible to sustainability of other IBT in case of tripping of one IBT. This SPS will save IBTs from sudden overloading (like outage of TPH unit etc.), not to combat N-1 situation.

So you are requested to avail shut down of 315 MVA IBT #2 which is deferred waiting for synchronisation of u#4 at Sg TPP along with u#1 & 2.

05/04/17
Additional Chief Engineer,
STATE LOAD DESPATCH CENTRE
WBSETCL, HOWRAH

Annexure B.2.8

Sl. No.	Information / Data Required	Details / Remarks
1	Connected load (existing and ultimate planned capacity).	
2	Phased capacity addition and expected commissioning schedule.	
3	Load composition (% IT load, % cooling load, balance auxiliary loads, etc.).	
4	Nature and rating of power electronic interfaces and UPS systems.	
5	Battery Energy Storage System (BESS) and backup diesel generator configurations and operating philosophy.	
6	Load operating characteristics, average load factor, diversity factor, and expected load ramp rates.	
7	Demand response, load curtailment, and load flexibility capabilities.	
8	Grid connectivity details, including voltage level, dedicated transmission infrastructure, redundancy philosophy, and protection arrangements.	
9	Power quality requirements, harmonic mitigation measures, and reactive power compensation facilities.	
10	Black-start capability, restoration philosophy, and operational constraints, if applicable.	
11	Renewable energy integration and captive generation arrangements, if any.	

Annex B.2.20

JAIN PARAS BILALA & CO

CHARTERED ACCOUNTANTS

MARSHALL HOUSE, 33/1, NETAJI SUBHAS ROAD, 5TH FLOOR, ROOM NO. 507, KOLKATA - 700001

CERTIFICATE

THIS IS TO CERTIFY THAT WE HAVE VERIFIED THE AUDITED ACCOUNTS AND OTHER RELEVANT RECORDS OF POWERGRID CORPORATION OF INDIA LIMITED, ERTS-II, KOLKATA IN RESPECT OF EXPENDITURE INCURRED FOR SUPPLY AND ERECTION OF AUTOMATED ENERGY METERS AND DATA COLLECTION DEVICES FOR EASTERN REGION II (WEST BENGAL). WE FURTHER CERTIFY THAT THE EXPENDITURE INCURRED IN THIS REGARD IS AS FOLLOWS.

(In ₹)

S.No	Particulars	Amount
Upto 28.02.2019		
1	Actual Expenditure incurred upto 28.02.19	3,87,31,776.60
2	Consultancy charges @ 15% on Sr No. 1	58,09,766.49
3	GST @ 18% on Consultancy Charges (on Sr No 2)	10,45,757.97
4	Total Upto 28.02.19- A	4,55,87,301.06
01.03.2019-30.06.2023		
5	Actual Expenditure incurred upto 01.03.19-30.06.23	6,68,91,714.00
6	Consultancy charges @ 15% on Sr No. 6	1,00,33,757.10
7	GST @ 18% on Consultancy Charges (on Sr No 7)	18,06,076.28
8	Total For 01.03.19-30.06.23- B	7,87,31,547.38
01.07.2023-31.03.2025		
9	Actual Expenditure incurred upto 01.07.23-31.03.25	5,71,77,229.27
10	Consultancy charges @ 15% on Sr No. 9	85,76,584.39
11	GST @ 18% on Consultancy Charges (on Sr No 10)	15,43,785.19
12	Total	6,72,97,598.85
13	Add: Unrecovered amount against earlier billing	30,76,130.00
14	Total for 01.07.23-31.03.25 - C	7,03,73,728.85
15	Grand Total (A+B+C) upto 31.03.25	19,46,92,577.29
Projected 01.04.2025-31.03.2027		
16	Projected expenditure from 01.04.2025 to 31.03.2027	11,22,34,091.66

IT IS FURTHER CERTIFIED THAT THE ESTIMATED EXPENDITURE AT SL. NO. 16 IS IN ACCORDANCE WITH THE STATEMENT FURNISHED BY THE MANAGEMENT OF THE COMPANY TO US.

WE HAVE OBTAINED ALL THE INFORMATION AND EXPLANATION, WHICH TO THE BEST OF OUR KNOWLEDGE AND BELIEF WERE NECESSARY FOR THE PURPOSE OF OUR EXAMINATION.

Place:- Kolkata
Date:- 02.04.2026

JAIN PARAS BILALA & CO
Chartered Accountants
FRN No-011046C

ASHIS
TOSHNIWAL

Digitally signed by ASHIS
TOSHNIWAL
Date: 2026.04.02 16:49:38 +05'30'

CA Ashis Toshniwal
Mem No-058521
UDIN - 26058521SYDEAF4917
