



भारत सरकार
Government of India
विद्युत मंत्रालय
Ministry of Power
पूर्वी क्षेत्रीय विद्युत समिति
Eastern Regional Power Committee
14 गोल्फ क्लब रोड, टॉलीगंज, कोलकाता 700033
14 Golf Club Road, Tollygunj, Kolkata-700033

Tel. No.: 033-24239651. 24239658

FAX No.: 033-24239652. 24239653 Web: www.erpc.gov.in

सं /NO. ERPC/EE/OPERATION/2025/ 594

दिनांक / DATE: 19.06.2025

सेवा में /To,

संलग्न सूची के अनुसार /As per list enclosed.

विषय : 17 जून 2025 (मंगलवार) को ईआरपीसी, कोलकाता में आयोजित 228वीं ओसीसी बैठक का कार्यवृत्त-संबंध में।
Subject: Minutes of 228th OCC Meeting held on 17.06.2025 (Tuesday) at ERPC, Kolkata -regd.

महोदय महोदया,
Sir(s)/Madam,

कृपया अपनी जानकारी और आवश्यक कार्रवाई के लिए 17 जून 2025 ((मंगलवार) को ईआरपीसी, कोलकाता में 10:30 बजे आयोजित 228वीं ओसीसी बैठक का कार्यवृत्त आयोजित बैठक के संलग्न कार्यवृत्त देखें। यह ईआरपीसी वेबसाइट (www.erpc.gov.in) पर भी उपलब्ध है।

Please find enclosed Minutes of 228th OCC Meeting held on 17.06.2025 (Tuesday) virtually through M.S Office at ERPC Kolkata at 10:30 hrs for your kind information and necessary action. The same is also available at ERPC website (www.erpc.gov.in).

टिप्पणियाँ, यदि कोई हों, कृपया यथाशीघ्र इस कार्यालय को अग्रेषित करें।

Observations, if any, may please be forwarded to this office at the earliest.

इसे सदस्य सचिव के अनुमोदन से जारी किया जाता है।

This issues with the approval of Member Secretary.

भवदीय /Yours faithfully

(S.Kejriwal)

SE(Operation)

एसई (ऑपरेशन)

LIST OF ADDRESSES:

1. CHIEF ENGINEER (TRANS., O&M), BSPTCL, PATNA, (FAX NO. 0612-2504557/2504937)
2. CHIEF ENGINEER (System Operation), BSPTCL, PATNA, (FAX NO. 0612-2504557/2504937)
3. CHIEF ENGINEER, TRANSMISSION (O&M), JUSNL, RANCHI (FAX NO.-0651-2490486/2490863)
4. CHIEF ENGINEER, TVNL, DORANDA, RANCHI - 834102 (FAX NO. 06544-225414)
5. CHIEF LOAD DISPATCHER, SLDC, OPTCL, BHUBANESWAR (FAX NO.0674-2748509)
6. CHIEF GENERAL MANAGER (O&M), OPTCL, BHUBANESWAR7. SR. GENERAL MANAGER (PP), GRIDCO, JANPATH, BHUBANESWAR (0674-2547180)
8. DIRECTOR (OPERATION), IB TPS, AT/PO BANHARPALI, JHARSUGUDA, (FAX NO. 06645-222225/222230)
9. GENERAL MANAGER, TTPS, TALCHER, (FAX NO. 06760-243212)
10. SR. GENERAL MANAGER (ELECTRICAL), OHPC LTD., BHUBANESWAR, (FAX NO.0674-2542102)
11. CHIEF ENGINEER, CLD, WBSETCL, HOWRAH, (FAX NO. 033-26886232)
12. CHIEF ENGINEER, CENTRAL PLANNING WING, WBSETCL, SALT LAKE (FAX NO.:033-23591955)
13. CHIEF ENGINEER (PTR), WBSEDCL, SALT LAKE, KOLKATA (FAX:033-23345862)14. CHIEF GENERAL MANAGER (OS), WBPDC, KOLKATA-98 (FAX NO. 033-23393286/2335-0516)
15. GM, KOLAGHAT TPS, WBPDC, KOLAGHAT (FAX NO.03228231280)
16. DGM (OPERATION), DPL, DURGAPUR, (FAX NO. 0343-2555052)
17. GM (SYS OPERATION), CESC, CHOWRINGHEE SQUARE, KOLKATA (FAX NO.033-22253756/22129871)
18. CHIEF ENGINEER, SLDC, DVC, HOWRAH (FAX NO. 033-2688-5094)
19. ADDL.CHIEF ENGINEER, SLDC, POWER DEPT., GOVT. OF SIKKIM, GANGTOK, (FAX NO. 03592-228186/201148/202284)
20. EXECUTIVE DIRECTOR, ERLDC, POSOCO, KOLKATA, (FAX NO. 033-2423-5809)
21. GENERAL MANAGER, FSTPP, NTPC, FARAKKA, (FAX NO. 03512- 224214/226085/226124)
22. GENERAL MANAGER , KhSTPP, NTPC, KAHALGAON (FAX NO.06429-226082)
23. GENERAL MANAGER, TSTPP, NTPC, TALCHER, (FAX NO. 06760-249053)
24. GENERAL MANAGER (OS), POWERGRID, ER-II, KOLKATA (Fax no: 033-23572827)
25. GENERAL MANAGER, POWERGRID, ER-I, PATNA, (FAX NO.0612-2531192)
26. GENERAL MANAGER (O&M), POWERGRID, ODISHA PROJECTS, SAHID NAGAR, BHUBANESWAR – 751 007
27. EXECUTIVE DIRECTOR (O&M), NHPC, FARIDABAD (FAX No.:0129-2272413)
28. GENERAL MANAGER, TEESTA –V POWER STATION, NHPC, SINGTAM, EAST SIKKIM (FAX 03592 - 247377)
29. CHIEF ENGINEER, RANGIT POWER STATION, NHPC, P.O. RANGIT NAGAR, SOUTH SIKKIM (FAX NO.03595-259268)

30. SENIOR VICE PRESIDENT, PTC LTD., NBCC TOWERS, 15-BHIKAJI KAMA PLACE, NEW DELHI- 110066 (FAX NO. 011-41659504)
31. PLANT HEAD, ADHUNIK POWER & NATUARAL RESOURCES, JHARKHAND(FAX NO.: 0657-6628440)
32. AGM (OPERATION), MAITHON POWER LTD, DHANBAD (FAX: 08860004758)
33. VICE PRESIDENT(POWER), VEDANTA LIMITED, BHUBANESWAR- 751023 (FAX NO 0674-2302920)
34. CHIEF ELECTRICAL ENGINEER, EASTERN RAILWAY, KOLKATA-700 001 (FAX NO.: 033-22300446)
35. CHIEF ELECTRICAL ENGINEER, SOUTH EASTERN RAILWAY, KOLKATA-43 (FAX: 033-24391566)
36. DEPUTY DIRECTOR, EASTERN RPSO, 14, GOLF CLUB ROAD,TOLLYGUNJ, KOLKATA-700033
37. GENERAL MANAGER (O&M), NHPC LTD, FARIDABAD, FAX: 0129-2272413
38. ASSOCIATE VICE PRESIDENT, GMR KEL, BHUBANESWAR-751007. (FAX NO: 0674- 2572794)
39. GM (SO & COMML), NTPC VVNL, NEW DELHI-110033. Fax:011-2436702140. SHRI D. P. BHAGAVA, CHIEF CONSULTANT (O&M), TEESTA URJA LIMITED, NEW DELHI-110 001 (FAX:011-46529744)
41. SHRI BRAJESH KUMAR PANDE, PLANT HEAD, JITPL. (FAX:011-26139256-65)
42. DIRECTOR (NPC), CEA, NRPC BUILDING, KATWARIA SARAI, NEW DELHI- 11001643. VP (OS), HALDIA ENERGY LIMITED, BARIK BHAWAN, KOKATA-700072, FAX: 033-22360955
44. GENERAL MANAGER(O&M), BRBCL, NABINAGAR, BIHAR-824003, FAX-06332- 233026

CC:

Chief Engineer, OPM, CEA	Chief Engineer, NPC, CEA	ASSISTANTSECRETARY, ERPC
--------------------------	--------------------------	--------------------------

ERPC:: Kolkata

पतों की सूची:

1. मुख्य अभियंता (ट्रांस., ओ एंड एम), बीएसपीटीसीएल, पटना, (फैक्स संख्या 0612-2504557/2504937)
2. मुख्य अभियंता (सिस्टम ऑपरेशन), बीएसपीटीसीएल, पटना, (फैक्स संख्या 0612-2504557/2504937)
3. मुख्य अभियंता, ट्रांसमिशन (ओ एंड एम), जेयूसएनएल, रांची (फैक्स संख्या-0651-2490486/2490863)
4. मुख्य अभियंता, टीवीएनएल, डोरंडा, रांची - 834102 (फैक्स संख्या 06544-225414)
5. मुख्य लोड डिस्पैचर, एसएलडीसी, ओपीटीसीएल, भुवनेश्वर (फैक्स नं.0674-2748509)
6. मुख्य महाप्रबंधक (ओ एंड एम), ओपीटीसीएल, भुवनेश्वर 7. एसआर. महाप्रबंधक (पीपी), ग्रिडको, जनपथ, भुवनेश्वर (0674-2547180)
8. निदेशक (ऑपरेशन), आईबी टीपीएस, एटी/पीओ बनहरपाली, झारसुगुड़ा, (फैक्स नंबर 06645-222225/222230)
9. महाप्रबंधक, टीटीपीएस, तालचेर, (फैक्स संख्या 06760-243212)
10. वरिष्ठ महाप्रबंधक (विद्युत), ओएचपीसी लिमिटेड, भुवनेश्वर, (फैक्स संख्या 0674-2542102)
11. मुख्य अभियंता, सीएलडी, डब्ल्यूबीएसईटीसीएल, हावड़ा, (फैक्स संख्या 033-26886232)
12. मुख्य अभियंता, केंद्रीय योजना विंग, डब्ल्यूबीएसईटीसीएल, साल्ट लेक (फैक्स संख्या: 033-23591955)
13. मुख्य अभियंता (पीटीआर), डब्ल्यूबीएसईडीसीएल, साल्ट लेक, कोलकाता (फैक्स: 033-23345862) 14. मुख्य महाप्रबंधक (ओएस), डब्ल्यूबीपीडीसीएल, कोलकाता-98 (फैक्स नंबर 033-23393286/2335-0516)
15. जीएम, कोलाघाट टीपीएस, डब्ल्यूबीपीडीसीएल, कोलाघाट (फैक्स नंबर 03228231280)
16. डीजीएम (ऑपरेशन), डीपीएल, दुर्गापुर, (फैक्स नंबर 0343-2555052)
17. जीएम (एसवाईएस ऑपरेशन), सीईएससी, चौरंगी स्क्वायर, कोलकाता (फैक्स नंबर 033-22253756/22129871)
18. मुख्य अभियंता, एसएलडीसी, डीवीसी, हावड़ा (फैक्स नंबर 033-2688-5094)
19. अतिरिक्त मुख्य अभियंता, एसएलडीसी, विद्युत विभाग, सिक्किम सरकार, गंगटोक, (फैक्स संख्या 03592-228186/201148/202284)
20. कार्यकारी निदेशक, ईआरएलडीसी, पोसोको, कोलकाता, (फैक्स संख्या 033-2423-5809)
21. महाप्रबंधक, एफएसटीपीपी, एनटीपीसी, फरक्का, (फैक्स नंबर 03512- 224214/226085/226124)
22. महाप्रबंधक, खएसटीपीपी, एनटीपीसी, कहलगांव (फैक्स नंबर 06429-226082)
23. महाप्रबंधक, टीएसटीपीपी, एनटीपीसी, तालचेर, (फैक्स नंबर 06760-249053)

24. महाप्रबंधक (ओएस), पावरग्रिड, ईआर-II, कोलकाता (फैक्स नंबर: 033-23572827)
25. महाप्रबंधक, पावरग्रिड, ईआर-I, पटना, (फैक्स) नं.0612-2531192)
26. महाप्रबंधक (ओ एंड एम), पावरग्रिड, ओडिशा परियोजनाएं, शहीद नगर, भुवनेश्वर - 751 007
27. कार्यकारी निदेशक (ओ एंड एम), एनएचपीसी, फरीदाबाद (फैक्स नं.: 0129-2272413)
28. महाप्रबंधक, तीस्ता-V पावर स्टेशन, एनएचपीसी, सिंगताम, पूर्वी सिक्किम (फैक्स 03592 - 247377)
29. मुख्य अभियंता, रंगित पावर स्टेशन, एनएचपीसी, पी.ओ. रंगीत नगर, दक्षिण सिक्किम (फैक्स नं. 03595-259268)
30. वरिष्ठ उपाध्यक्ष, पीटीसी लिमिटेड, एनबीसीसी टावर्स, 15-भीकाजी कामा प्लेस, नई दिल्ली- 110066 (फैक्स नं. 011-41659504)
31. प्लांट हेड, आधुनिक पावर एंड नेचुरल रिसोर्सेज, झारखंड (फैक्स नं.: 0657-6628440)
32. एजीएम (ऑपरेशन), मैथन पावर लिमिटेड, धनबाद (फैक्स: 08860004758)
33. उपाध्यक्ष (पावर), वेदांता लिमिटेड, भुवनेश्वर- 751023 (फैक्स नं. 0674-2302920)
34. मुख्य विद्युत अभियंता, पूर्वी रेलवे, कोलकाता-700 001 (फैक्स नं.: 033-22300446)
35. मुख्य विद्युत अभियंता, दक्षिण पूर्वी रेलवे, कोलकाता-43 (फैक्स: 033-24391566)
36. उप निदेशक, पूर्वी आरपीएसओ, 14, गोल्फ क्लब रोड, टॉलीगंज, कोलकाता-700033
37. महाप्रबंधक (ओ एंड एम), एनएचपीसी लिमिटेड, फरीदाबाद, फैक्स: 0129-2272413
38. एसोसिएट वाइस प्रेसिडेंट, जीएमआर केईएल, भुवनेश्वर-751007। (फैक्स नं: 0674-2572794)
39. जीएम (एसओ एवं सीओएमएल), एनटीपीसी वीवीएनएल, नई दिल्ली-110033। फैक्स:011-2436702140। श्री डी. पी. भागवा, मुख्य सलाहकार (ओ एंड एम), तीस्ता ऊर्जा लिमिटेड, नई दिल्ली-110 001 (फैक्स:011-46529744)
41. श्री ब्रजेश कुमार पांडे, प्लांट हेड, जीतपीएल। (फैक्स:011-26139256-65)
42. निदेशक (एनपीसी), सीईए, एनआरपीसी बिल्डिंग, कटवारिया सराय, नई दिल्ली-11001643. वीपी (ओएस), हल्दिया एनर्जी लिमिटेड, बारीक भवन, कोकाता-700072, फैक्स: 033-22360955
44. महाप्रबंधक (ओ एंड एम), बीआरबीसीएल, नबीनगर, बिहार-824003, फैक्स-06332-233026

सीसी:

मुख्य अभियंता, ओपीएम,	सीईए मुख्य अभियंता, एनपीसी	सीईए सहायक सचिव, ईआरपीसी
-----------------------	----------------------------	-----------------------------



228th OCC MEETING

Date: 17.06.2025

**Eastern Regional Power
Committee**

Contents

1. PART-A: CONFIRMATION OF MINUTES	2
1.1. Confirmation of Minutes of 227 th OCC Meeting held on 26 th May,2025 physically at ERPC Kolkata.....	2
2. PART-B: ITEMS FOR DISCUSSION.....	3
2.1 Endangering Grid connectivity, security & stability of 400 KV Sundargarh-Raigarh Ckt – 3 & 400KV Sundargarh- Rourkela#1 D/C line near Sundergarh due to over crossing of dead LILO line of M/s Vedanta Ltd, Jharsuguda: Powergrid Odisha	3
2.2 Violation of IEGC due to sudden blocking of AGC: MPL.....	4
2.3 Provision of Hot Spare Bus reactor for 765 kV Sundargarh-Raipur#1&2 Lines at Sundargarh Substation: Powergrid Odisha	5
2.4 Update on Patna Islanding scheme: ERPC	6
2.5 Update on under-implementation Islanding schemes: ERPC	8
2.6 Status of ERS in Eastern Region: ERPC.....	8
2.7 Issues for follow up.....	9
2.8 Bus split operationalization at NTPC Kahalgaon: ERPC.....	15
2.9 Shutdown proposal of generating units for the month of July 2025: ERPC	16
2.10 Extension of COH of TTPS Unit#2 (210MW): TVNL	18
2.11 Impact on Power supply at Melli (Sikkim) & North Bengal: ERLDC.....	18
2.12 Update on replacement of SEM in ER, from Non-DLMS to DLMS platform and compliances to latest standards: Powergrid ER-II	20
2.13 Regarding construction of additional Transmission tower in front of newly constructed GIS building for transmission of Power generated from Teesta-V Power Station: NHPC .	22
2.14 Requirement of one 315MVA ICT on Loan basis from regional pool of spares: DVC 23	
2.15 Interim Modification/Heightening Work on 132kV D/C Patratu–PTPS(DVC) Line at Railway Siding Area of PVUNL:DVC.....	24
2.16 Near miss situation around Capital city of West Bengal & Odisha:	25
3. PART-C: ITEMS FOR UPDATE/FOLLOW-UP/INFORMATION	28
3.1. ER Grid performance during May 2025	28
3.2. Non-Submission of FRC data in stipulated timeframe: ERLDC.....	29
3.3. Regarding Non-Submission of Forecasting Data from States: ERLDC	31
3.4. Mock Black Start: ERLDC	32
4. PART-D: OPERATIONAL PLANNING.....	35
4.1. Anticipated power supply position for July-2025	35
4.2. Major Thermal Generating Units/Transmission Element outages/shutdown in ER Grid (as on 06-06-2025)	35
4.3. Commissioning of new units and transmission elements in Eastern Grid in the month of May-2025.....	40
4.4. UFR operation during the month of May 2025	44

EASTERN REGIONAL POWER COMMITTEE

MINUTES OF 228th OCC MEETING HELD ON 17.06.2025 (TUESDAY) AT 10:30 HRS

Member Secretary, ERPC chaired the **228th OCC** meeting. On welcoming all the participants, he outlined the performance of ER grid during **May-2025** and highlighted the following points:

- ❖ In **May-2025**, energy consumption of ER was **18.9 MU** which is **1% more** than **May-2024**.
- ❖ In **May-2025**, Peak demand met of ER was **31985 MW** which is **1.1% more** than **May-2024**.
- ❖ The nation-wide maximum demand met in the current financial year was **241 GW** on **09.06.2025** & regional Maximum demand crossed **33 GW** on **13.06.2025**.
- ❖ During **May-2025**, **73.3%** of time, the grid frequency was in IEGC Band (49.90Hz-50.05Hz).
- ❖ Thermal **PLF** of ER during **May-2025** was **82.6 %** against All India PLF of **68%**.
- ❖ Some thermal generating units were lauded for maintaining PLF more than **90%** during **May-2025** that are listed below:

Utility	Generating station	PLF (%)
WBPDC	BAKRESWAR TPS	93
	SANTALDIH TPS	96
	SAGARDIGHI TPS	95
NTPC	DARLIPALI STPS	92
IPP	HALDIA TPP	97

- ❖ **Coal stock position (As on 11.06.2025) is as follows:**

SL.	Name of States/Power Stns.	% of Actual Stock vis-à-vis Normative Stock
1.	Jharkhand (TVNL)	184%
2.	Odisha/IBTPS	69%
3.	WBPDC	75% (Min. KolaghatTPS -55 %, Max.Bandel TPS -108%)
4.	D.P.L. TPS	45%
5.	DVC	89%(Min. Mejia TPS-50%, Max Chandrapur (TPS `A-138%)
6.	NTPC	96% (Max. Farakka TPP -156% & Min. Talcher STPS - 85%)

He further highlighted the following:

- ❖ The COD of NKSTPP Unit#3 was achieved on 15th June, 2025.
- ❖ Further Barh Unit #3 has also completed the trial operation successfully on 5th June 2025. He emphasized that its CoD should be completed at the earliest to meet upcoming demand of Bihar.

- ❖ *Unallocated power of 250 MW from southern pool has been allocated to Bihar. They requested for additional 500 MW power.*
- ❖ *Powergrid has conducted a two-day ERS Field Training Program for all constituents of ER*
- ❖ *As TVNL coal stock is more than 180 % due to prolonged outage of unit#2, it was suggested that the excess coal stock may be shared with other generating companies.*
- ❖ *A database of large CPPs may be kept with regional entities like ERPC/ ERLDC to utilize them as alternate source in case of emergency.*
- ❖ *As per amended LPSC rules coming into effect from 01.07.2025, URS power shall be offered by Generators in the market which can be availed by DISCOMs to meet the shortfall in their demand.*

ED, ERLDC highlighted the following:

- ❖ *Due to pleasant weather this summer, demand in the region has not shoot much and has been successfully catered with present condition of grid without facing major challenges. However, Bihar's peak demand is yet to come.*
- ❖ *Although the CoD of NKSTPP unit#3 has been achieved, power is being evacuated by an arrangement of SPS with the support extended from ERLDC, owing to non- commissioning of the line.*
- ❖ *In case of PUVNL, Jharkhand, ERPC and ERLDC together reached to a consensus that until Jharkhand is in position to schedule the power of PUVNL unit #1, PUVNL may approach CERC to seek permission for ERLDC to carry out scheduling on its behalf.*
- ❖ *Over the last 3 Years, it has been observed that the Meramundali, Mendhasal, Lapanga lines have been tripping frequently, due to their location in cyclone prone area. However, owing to certain limitations in transmission system, whenever any lines, elements trips, alarm is generated and precautionary measures like SPS installation, may be planned to manage such contingencies.*
- ❖ *It was also highlighted that reliability of 765 kV New Ranchi – Medinipur- New Jeerat corridor is below satisfactory level due to many shortcomings, even during low demand season. The corresponding 400 KV New Jeerat-Jeerat, New Jeerat -Subhasgram lines are also been under frequent outage, resulting in constraints in meeting demand of Kolkata and adjoining area.*

1. PART-A: CONFIRMATION OF MINUTES

1.1. Confirmation of Minutes of 227th OCC Meeting held on 26th May,2025 physically at ERPC Kolkata.

The minutes of 227th Operation Coordination Sub-Committee meeting held on 26th May 2025 was circulated vide letter dated 30.05.2025.

Members may confirm the minutes of 227th OCC meeting.

Deliberation in meeting

Members confirmed the minutes of 227th OCC meeting.

2. PART-B: ITEMS FOR DISCUSSION

2.1 Endangering Grid connectivity, security & stability of 400 KV Sundargarh-Raigarh Ckt – 3 & 400KV Sundargarh- Rourkela#1 D/C line near Sundergarh due to over crossing of dead LILO line of M/s Vedanta Ltd, Jharsuguda: Powergrid Odisha

As per the agreement dated 22.12.2010 between M/s Vedanta Ltd. And Powergrid, the connectivity to Vedanta Ltd sub-station was carried out from LILO of 400 KV Sundargarh-Raigarh D/C line # 3 between Tower No – 834 (DD+0) & 835 (DD+0) and 400 KV Sundargarh-Raigarh D/C line # 4 between Tower No – 299 (DD+0) & new Vedanta Tower No-VL3 (DD+0) was done during the year 2011. This activity was taken up as per direction of CERC and instruction of ERLDC/WRLDC in order to charge the Vedanta switchyard at Jharsuguda for sending and receiving of power at Vedanta end with CTU transmission system.

(i) LILO-1 in 400KV Sundargarh-Raigarh Line #3 between existing tower No-834(DD+3) & 835(DD+0).

(ii) LILO-2 in 400KV Sundargarh-Raigarh#4 between tower No-299(DD+0) & tower no.298(DA+0) by inserting a Tower V1 (DD+0) in between Loc. 298 & 299 and over crossing POWERGRID 400KV Sundargarh-Raigarh#3 & 400KV Sundargarh-Raourkela#1 D/C line.

After direct connectivity of Vedanta 400 KV sub-station with 765/400 KV sub-station of Powergrid at Sundergarh, the tapping points of LILO portion of line # 3 & # 4 was disconnected by M/s Vedanta Pvt. Ltd. In the year 2014 & 2017 respectively and direct connectivity for Powergrid was completed in above-mentioned LILO lines in 2022 & 2023 respectively. However, removal of over crossing conductor of LILO-2 over D/C line 400KV Sundargarh-Raigarh#3 & 400KV Sundargarh- Rourkela#1 is still pending.

In this regard, the authority of M/s Vedanta has been informed many times to take necessary steps to de-string the over crossing line for keeping the tower in safe condition and to take urgent action for direct connectivity of both LILO points.

M/s Vedanta submitted through email that they will use the LILO for CTU connectivity with POWERGRID Sundargarh S/s. But till date no proper approval has been submitted by them.

Some of the Email correspondences with M/s Vedanta are attached herewith. In spite of these correspondences and discussions with M/s Vedanta Ltd., the over crossing lines have not been removed by them till date else which may cause severe danger to POWERGRID lines 400KV Sundargarh-Raigarh#3 & 400KV Sundargarh- Raourkela#1 D/C line and power flow will be affected.

POWERGRID submission: M/s Vedanta to remove the over crossing LILO line immediately so that there shall not be any damage to Powergrid system due to failure of over crossing conductors of dead LILO line.

Powergrid Odisha may update.

Deliberation in the meeting:

- i) *Powergrid informed that Vedanta has been communicated repeatedly to take necessary steps to de-string the LILO portion as it is crossing over the existing 400kV Sundargarh-Raigarh#3 & 400KV Sundargarh- Rourkela#1 D/C line of 400kV.*
- ii) *Vedanta intimated that they want to retain the LILO connectivity for reliability purpose.*

OCC Decision:

Matter may be placed before CMETS-ER for discussion.

2.2 Violation of IEGC due to sudden blocking of AGC: MPL

MPL has always ensured, and will continue to ensure, strict adherence to the Indian Electricity Grid Code (IEGC) to support secure and reliable grid operations. After a thorough internal review, we would like to respectfully clarify a few points that have been duly noted:

Event Details:

On 5th June 2025, the frequency profile was on the higher side (50.03 Hz and above), resulting in continuous under-injection. At 07:30 hrs, both units of MPL were running at full load with AGC at -0.161 MW and 3.192 MW respectively, and a DSM deviation of -19.37 MW to manage the rise in frequency. In the subsequent block, SG started to reduce (Ancillary Service was to reduce from 275.85 MW to 147.41 MW). In response to this change, desk engineers of both units provided a ULSP reduction from 525 MW to 450 MW, causing the AGC quantum to increase to +75 MW per unit (totalling 150 MW).

Shortly after, at 07:53 hrs, the MPL control room received a call from ERLDC control room regarding higher injection. While considering the beneficiary, Ancillary Services, and AGC schedule, we confirmed compliance, and this was communicated to ERLDC. At 07:56:49 hrs, AGC was blocked, and the 150 MW AGC quantum was abruptly reduced to zero, leading to an instantaneous 150 MW reduction in SG. Despite efforts to manage this sudden shortfall by ramping our units at greater than 1.2% ramp rate, we experienced positive deviations of 27 MW and 17 MW for blocks 33 and 34 respectively. The AGC remains blocked to this date. Supporting data for SG vs Export and deviations from blocks 31 to 36, along with AGC quantum trends, are provided. This data confirms that the over-injection at higher frequency was solely due to the sudden blocking of AGC quantum from +110 MW to zero, and there has been no violation on MPL's part.

Supporting data for SG vs Export and deviations from blocks 31 to 36, along with AGC quantum trends, are provided. This data confirms that **the over-injection at higher frequency was solely due to the sudden blocking of AGC quantum from +110 MW to zero, and there has been no violation on MPL's part.**

Owing to the instantaneous blocking of the AGC quantum, there was a sudden change in scheduled generation. This caused over-injection at high frequency, resulting in DSM losses during that and subsequent blocks.

MPL may explain. Members may discuss.


Deliberation in the meeting:

MPL informed that the matter has been separately discussed with ERLDC and resolved successfully.

OCC Decision: OCC noted.

2.3 Provision of Hot Spare Bus reactor for 765 kV Sundargarh-Raipur#1&2 Lines at Sundargarh Substation: Powergrid Odisha

- 765 kV Sundargarh-Raipur#1&2 along with their respective 240 MVR (3x80MVAR) switchable Line Reactors were commissioned on 29th & 30th March 2019
- The Reactors were supplied under the package :RT01 (under TBCB):- for (I) (a) 6x80MVAR, 765kV Shunt Reactor at Jharsuguda S/S , (b) 6x80MVAR, 765kV Shunt Reactor at Raipur Pooling S/S under Odisha Phase-II (DPR-2) and (II) 2x80MVAR, 400kV Shunt Reactor with 400 ohm NGR at Kishanganj GIS S/S under HEP's in Bhutan under POWERGRID works associated TBCB line under Common Transmission System for Phase-II Generation Projects in Odisha.
- Presently there is no provision for Hot Spare for Switchable Line Reactors of 765 kV Sundargarh-Raipur #1 & 2. However, Hot Spare of Line reactors is available at Raipur end for the same line.
- The existing 80 MVAR Hot Spare of 765 kV Bus Reactors and Line Reactors of all four 765 kV Angul Lines is connected to 765 kV Bus#2 and positioned 400m apart from Raipur LR's. Line Reactors of Raipur Lines are connected to 765 kV Bus#1. Being physically positioned apart, there is no possibility for electrical connectivity of Raipur Line Reactors with the existing Hot Spare Unit to meet any type of exigency condition.
- It is noteworthy to mention that there is repetitive switching of Line Reactors of Raipur Lines for Voltage Regulation and These Line reactors are being taken into service as Bus Reactors based on the System conditions as per the instruction of ERLDC.
- Being an oil filled equipment and exposed to higher switching surges in 765 kV system, requirement of hot spare is very much important for grid reliability. The availability of spare unit shall ensure quick restoration of these reactors in case of any major breakdown issue in any of the unit.
- Therefore, it is felt prudent to provide spare Reactor for these Line Reactors for smooth, reliable and flexible system operation with minimum outage to Line.

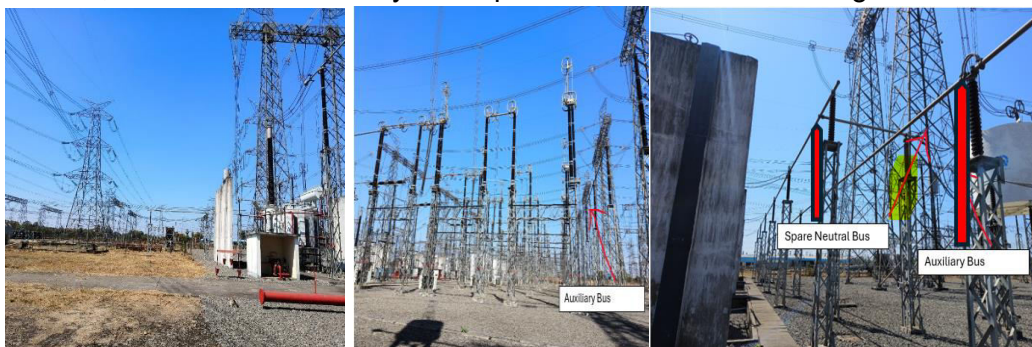

- As per the site condition there is availability of space in proximity to B-Ph unit of Raipur#1 Line Reactor.

- Auxiliary Bus and Neutral Bus for Spare rotation is already available at site as part of the above-mentioned Package considering future provision for accommodating spare unit.
- Based on the above, requirement of Hot spare for Line reactors of 765 kV Sundargarh-Raipur #1 & 2 may kindly be considered.

226 OCC Decision

- Power grid was advised to clarify on non-provisioning of the line reactor at Sundargarh end during the planning stage of TBCB project
- POWERGRID REPLY on 226 OCC Minutes
- Providing the 2x240 MVar switchable line reactor only at Jharsuguda end for Jharsuguda– Raipur Pool 765 kV D/c line was decided in the standing committee meeting on power system planning of Eastern Region held on 02.05.2014 at New Delhi & meeting minutes circulated by CEA on 11.07.2014 (copy of minutes attached). No such deliberations and decisions were taken regarding provisioning of hot spare in the said meeting.
- Considering availability and reliability of the said line, proposal for providing a hot/cold spare may kindly be considered.

Powergrid Odisha May explain.

Deliberation in the Meeting:

- i) *Powergrid Odisha apprised the forum regarding the importance of additional line reactor at Sundergarh end for 765kV Raipur – Sundargarh lines.*
- ii) *OCC inquired about the mechanism for tariff recovery in case of addition of new elements in existing TBCB projects.*

OCC Decision:

- i) *OCC observed that the proposed Reactor was not envisaged in the original scope of work during the planning stage. However, the same might be required at present scenario.*
- ii) *OCC advised that the matter may be referred to CMETS to establish its present requirement.*

2.4 Update on Patna Islanding scheme: ERPC

- The Patna islanding scheme would be formed with Units of NPGCL along with loads of Patna city.
- NTPC was entrusted for carrying out study of NPGC units and M/S Solvinia had submitted report on study of islanding scheme dated 08th May 2024. Thereafter based on comments received from ERLDC, replies were submitted by M/S Solvinia. NTPC had communicated the report to all concerned including SLDC Bihar.
- Some further tests needed could not be carried out due to non-receipt of relevant data from Bihar.
- The proposed Patna islanding scheme aims to isolate one running unit of NPGC (660 MW) with pre-identified load of Patna city and nearby areas. After isolation of selected loads and NPGC through the identified network, run the island in islanded mode to cater the city load and to extend start-up supply to generating stations in adjoining area to facilitate early restoration.

- Patna city and nearby loads will be islanded with one of the running units of NPGC (660 MW).

As per 53rd ERPC meeting:

ERPC agreed with the proposal of Patna Islanding Scheme and advised Bihar to go ahead with the implementation scheme in a **time bound manner**.

226 th OCC	227 th OCC
<i>SLDC Bihar submitted:</i> • <i>Bids have been submitted by vendors, but the element-wise cost breakup has been provided only by M/s Siemens. The final DPR, along with the cost breakup, will be submitted after receiving the element-wise cost breakup from the other vendors.</i> OCC Decision ✓ <i>OCC raised concern on the delay in finalization of DPR for Patna islanding scheme despite being accorded approval for approaching PSDF in 53rd ERPC meeting.</i> ✓ <i>The Patna islanding scheme will be discussed in the next NPC meeting. Therefore, OCC advised SLDC Bihar to expedite the submission of the final DPR for the Patna islanding scheme, along with the detailed cost breakup from the other vendors.</i>	<i>SLDC Bihar informed that cost estimate for purpose of DPR has been received only from one vendor i.e Siemens.</i> Decision: <i>OCC suggested SLDC Bihar to expedite the submission of final DPR in view of upcoming NPC meeting.</i>

SLDC Bihar may update.

Deliberation in the meeting:

Bihar SLDC has informed that complete proposal along with cost estimate has been prepared and submitted for administrative approval.

OCC Decision:

- OCC advised Bihar SLDC to expedite and submit the proposal for PSDF funding at the earliest.*
- OCC referred the matter to upcoming TCC.*

2.5 Update on under-implementation Islanding schemes: ERPC

IB valley TPS Islanding scheme has also been put on hold for long time. The status regarding the same has been sought on urgent basis by Ministry of Power (Govt of India).

As per 227th OCC meeting:

- i) SLDC Odisha on behalf of OPGC informed that currently their islanding scheme is being prepared for IB Valley TPS.
- ii) It was also informed that Islanding scheme for Bhubaneswar is under planning stage.

OCC Decision:

OCC advised SLDC Odisha to take up the matter with OPGC and ensure speedy implementation of the IB TPS islanding scheme.

OPGC/ SLDC Odisha may update. Members may discuss.

Deliberation in the Meeting:

OPTCL informed:

- a) *There was some difference of opinion with OPGC on earlier proposed islanding scheme.*
- b) *New scheme is being designed for islanding of IB TPS (2*210 MW) and the same shall be ready in a month's time.*

OCC Decision:

- i) *OCC expressed concern over the delay in finalization of IB TPS islanding scheme in view of strict follow up by MoP/CEA on the progress of such proposed schemes.*
- ii) *OCC advised OPGC/SLDC Odisha to mutually design the islanding scheme of IB TPS and present the scheme in next OCC.*

2.6 Status of ERS in Eastern Region: ERPC

Transmission lines are the arteries of the electricity grid and these are most prone to damage due to earthquakes, cyclones, floods etc. In case of damage to the transmission line, temporary arrangements for the restoration of power supply can be made with the help of ERS, which consists of a special type of lightweight modular structures, with lightweight polymer insulators and number of stays. In this regard CEA has issued guidelines for requisition of ERS and also an advisory has been issued by Ministry of Power to all state utilities.

As per Central Electricity Authority (grid standards) regulations, 2010 and "Disaster Management Plan for Power Sector" the following are mandated in case of the ERS:

- i. Each transmission licensee shall have an arrangement for the restoration of transmission lines of 400 kV and above and strategic 220 kV lines through the use of Emergency Restoration System in order to minimise the outage time of the transmission lines in case of tower failures.
- ii. Strategic locations should be decided for spares on centralized/ regional /zonal basis.

MOP guidelines attached at [Annex B.2.6](#)

ERPC may update.

Deliberation in the Meeting:

- i) *ERPC presented letter from MoP communications of 2014 and May 2025 regarding maintenance of ERS tower inventory by transmission utilities on the basis of total ckt km and no of sets of ERS towers.*

- ii) As per the letter dated 11.05.2025, it is mentioned that a set of ERS comprises of 15 towers comprising 9 tension & 6 suspension towers.
- iii) All transmission utilities submitted that they do not have any fixed standard or norms of maintaining nos. of towers as per set.
- iv) POWERGRID, INDIGRID and SPTL confirmed that they follow the standard of 15 ERS towers per set.
- v) It was also informed that ERS designed for higher voltage level could be used for lower voltage levels also.

OCC Decision:

OCC advised all transmission utilities including private transmission licensees and STUs to maintain required inventory of ERS as per the above communications of MoP.

2.7 Issues for follow up.

Issue	Reference	Last updated Status	Update
Update on Rajarhat GIS (POWERGRID) 400/220kV S/S: 2x500MVA	Vide 226th OCC dated 22.04.2024: The need to prioritize the installation of a 3rd 400/220KV,500MVA ICT at Rajarhat (PG) with the same urgency as Subhasgram (PG) to prevent a recurrence of similar critical situations in the future If the proposed 3rd ICT is not operational by the summer of 2026, severe congestion is likely to affect the ICTs at Rajarhat (PG).	As per 227th OCC: Powergrid informed the forum that Transformer has been transported from Hyderabad.	Deliberation in the meeting: i) Powergrid informed that GIS package bid opening is on 20.06.2025. ii) Transformer is on transit and will reach at site by end of July,2025.
Upgradation of 220kV Network in Kolkata Region.	- Vide 217th OCC dated 24.07.24 Due to persistent N-1 violation, Upgradation of these 220 KV feeders to be planned: ✓ 220kV Subhasgram (WB)-Lakshmikantpur D/C ✓ 220 kV Jeerat-Barasat D/C ✓ 220 kV Barasat-Kasba D/C	As per 227th OCC: WBSETCL has updated that TESC committee approved the proposal in the meeting held in April 2025. Decision: OCC advised to put up the proposal in the next PSDF meeting for approval of grant.	WBSETCL has updated that proposal has been submitted to CEA appraisal committee regarding PSDF funding. OCC advised WBSETCL to expedite completion of the above work keeping in view load growth and state election in next year.
Restoration status of	Vide 221st OCC dated 27.11.24	As per 227th OCC:	WBSETCL has informed that

220kV-Rajarhat (PG) - New Town IIC – II.	• The faulty b phase cable already is isolated at both ends. As, the repair of the b phase cable involves kits and spares (particularly for the jointing portion of two different sized cables) from abroad, which is time consuming, so to keep the other two phase UG cables healthy, it was extremely necessary to keep those in no load charging condition. • Repair of the faulty cable (B phase) is getting delayed due to non-availability of the imported cable jointing kit. • Neither charging the cable at low voltage nor charging from WBSETCL end was feasible • The said no load charging may please be allowed within shortest possible time to reduce any possibility of damage of R, Y phase cables in respect of Rajarhat (PG)- New Town AAIIC circuit II.	WBSETCL informed that cable Joint- Kit will arrive by 15th June, 2025 and overall work will be completed tentatively by end of June. Decision: OCC advised to update the status in next OCC meeting.	<i>cable joining Kit will reach at the site by 20.06.2025.</i> <i>OCC advised WBSETCL to complete the work by 1st week of July 2025.</i>
Update on Reconductoring of ISTS lines under Eastern Region Expansion Scheme-44	• Vide 226th OCC dated 22.04.2024 • Approved in 52nd TCC NCT (National Committee on Transmission) meeting dated 23.10.2024	• As per 227th OCC: • PGCIL has updated that notice inviting Tender (NIT) has been floated and bids submission date has been extended to 10.06.2025. • Decision: OCC advised to expedite the process.	<i>PGCIL updated that the bid is scheduled to be opened on 17.06.2025</i>

	Reconductoring of ISTS portion of 220 kV corridor viz. Alipurduar (POWERGRID) – Falakata (WBSETCL) – Birpara (POWERGRID) – Binaguri (POWERGRID) – Siliguri (POWERGRID) – Kishanganj (POWERGRID) – Dalkhola (POWERGRID) – Gazole (WBSETCL) – Malda (POWERGRID), may be taken up under ISTS		
Update on Restoration of 132kV Rangit-Kurseong & 132kV Siliguri-Melli-Rangpo lines	- Vide 226th OCC dated 22.04.2024 - Due to incessant rain and several landslides, towers at loc. 125-128 of 132 kV Rangit-Kurseong and 132 kV Siliguri-Melli got badly affected - Consequently, Kurseong and Melli (Kalimpong source) are fed through single source of Siliguri and Rangpo respectively - After necessary reconfiguration, 132 KV Siliguri-Kurseong-II (interim) arrangement charged on 9th October and 132kV-Rangit-Melli (interim) has been charged tentatively on 22nd October. POWERGRID intimated that it	As per 227th OCC: ✓ Powergrid updated that restoration work at location 127 is delayed due to torrential rain which is hampering transportation of materials over hilly areas. Further, Once the foundation work will be over tower erection work will be done within 15 days. Post the completion of work at location 127, work at location 126 will begin. Decision: OCC asked PGCIL to submit weekly progress report. - No further progress report received till date.	<i>Powergrid updated that:</i> <i>i) foundation work at Location 127 is done.</i> <i>ii) retaining wall work is ongoing.</i> <i>iii) erection work will begin from 23.06.2025.</i> <i>Further, Powergrid gave a presentation showing progress of work at site. The line will be charged after completion of tower at above location. Thereafter, work for erection of tower at loc126 will be taken up and job will be finished by Nov,2025.</i>

	would take 15-20 Days to restore the original configuration after rectifying damaged towers.		
MTDL of Intra-state generators (55%).	Vide 218th & 220th OCC dated 13.08.24 & 25.10.25: • WBPDCCL updated that all the thermal generating units including that of Kolaghat, are technically capable to operate at 55% MTDL But in absence of appropriate regulations of WBERC, generating units not operating at 55% MTL or below on sustained basis. • ED, ERLDC apprised that they have already highlighted the matter to WBERC & WBERC has assured to come up with appropriate regulation to incentivize generators.	As per 227th OCC: • OCC advised all Intra-state generators to abide by IEGC regulation and participate in TRAS down Market for compensation. • OCC highlighted the importance of operating thermal generating units upto MTDL considering the high RE capacity addition. • All intra-state generators were asked to approach their respective SERCs for necessary regulatory support. • iii) Generators were also advised explore participation TRAS Down market. • iv) Further, ERLDC has been asked to sensitize all states generators of ER region regarding participation in TRAS down Market. ✦ Meeting with IPPs was held by ERLDC on 29-05-25. ✦ Meeting with State Generators is scheduled on 12-06-25.	i) ERLDC informed that they have conducted Separate training sessions for TRAS down Market for IPPs on 29.05.2025 and for state Gencos on 12.06.2025. ii) Further, ERLDC informed that MPL has participated in the market since 01.06.2025. iii) All IPPs of ER have registered in TRAS down market. iv) WBPDCCL expressed willingness to participate in the TRAS Down market provided they receive the necessary support on scheduling modalities. OCC Decision: i) OCC advised all intra State Gencos to approach the respective SERCs for regulatory guidance on this issue. ii) OCC advised all intra State GENCOs and IPPs to participate in the TRAS Down market. iii) ERLDC was advised to conduct a meeting with SLDCs for addressing their concerns on

			scheduling aspects for participation in TRAS down market.
Provision of Reliable Power Evacuation from NKSTPP	Vide 227th OCC dated 26.05.25 - Presently, only the 400 KV D/C Chandwa line is available for power evacuation from NKSTPP, as the 400 KV NKSTPP–Gaya D/C line is still under construction. - As per the system study conducted by ERLDC for power evacuation, in the scenario where all three units at NKSTPP are operational, stable operation is possible only up to 1700 MW in the event of a trip or shutdown of one circuit of the 400 kV D/C Chandwa line. - The second evacuation corridor, i.e., the 400 kV NKSTPP–Gaya D/C line, is under construction and is being expedited by M/s NKTL.	As per 227th OCC: i) NTPC submitted that reliability of power evacuation from NKSTPP will be compromised due to availability of only one double ckt 400 KV NKSTPP Chandwa line. ii) It was proposed that an SPS may be designed and implemented for reliable evacuation of NKSTPP Power through existing double ckt line. OCC Decision: i) OCC advised NKTL to expedite the construction of 400 KV DC NKSTPP Gaya Transmission lines. ii) ERLDC was advised to design an SPS for reliable evacuation of power from NKSTPP through existing 400 KV NKSTPP Chandwa line. iii) NTPC was advised to implement the SPS within a week of the finalization of same. iv) OCC opined that Forest clearance and Land related issues come within purview of state govt. Joint meeting was held with all stakeholders on 27-05-25 and SPS quantum was finalized in this meeting.	Deliberation in the meeting: ERLDC informed that SPS has been implemented successfully. The detail of SPS for NKSTPP has been enclosed as Annexure B.2.7. ii) NTPC updated that erection work of double ckt 400 KV NKSTPP Gaya lines is going on in which 95 % & 75 % work has been completed in Bihar & Jharkhand respectively. NTPC further updated that foundation work of 197 out of 207 towers and stringing work in 10 KM out of 71 KM is finished in Jharkhand portion. OCC Decision: OCC approved the SPS scheme as implemented for reliable power evacuation from NkSTPP as an interim measure. Since, NKTL was not present, the timeline for completion of 400kV NkSTPP-Gaya lines could not be discussed and OCC referred the matter to TCC

Challenges in intra-state network of Odisha	Vide 227th OCC dated 26.05.25: - The load centre command area of Bhubaneswar, Puri & Cuttack city is fed from 400KV Mendhasal Grid Sub-Station, which draws power from Talcher, Sundargarh, and OPGC Plants of that geographical area. - In order to provide redundancy & share some of the load of this area a 400KV Pandiabil Sub-station is established. This Sub-station needs to draw power from Baripada CTU & upward network beyond Baripada. Unfortunately, it is observed that there is a limited flow from Baripada and Pandiabil continues to draw power from Mendhasal & New - Duburi (Odisha network) resulting into jeopardize of the evacuation of OPGC, Talcher, Kaniha Projects	As per 227th OCC: SLDC Odisha suggested to install a Phase Shifting Transformer (PST) at Baripada to divert power from Baripada to Pandiabil. OCC Decision: OCC advised SLDC Odisha and ERLDC to jointly carry a feasibility study to explore all alternative solutions and submit the report to ERPC. Preliminary discussion was done between ERLDC and Odisha. However, requisite data yet to be received from Odisha.	OCC decision: OCC advised Odisha SLDC to carry out comprehensive study. Thereafter, the matter may be discussed in consultation with CTU and ERLDC for the resolution of the challenges. ii)OCC further advised IBEUL (JSW-EUL) to complete the construction of DTL.
Relocating of existing 220/132kV Switchyard of TTPS for future capacity addition	Vide 227th OCC dated 26.05.25: Vide the letter reference: TTPP/OPTCL/11/01 did 09.11.2024, NTPC has stated that they are going to set up an additional 600MW / 800MW unit	As per 227th OCC: i) Representative of NTPC TTPS submitted that assistance of SLDC Odisha is required for purpose of shutdown required by OPTCL. ii) SLDC Odisha submitted that preliminary system study needs to be carried out prior to relocation of existing 220/132 KV Switchyard. OCC Decision:	<i>OPTCL has informed that the matter has already been placed before CMETS-ER for deliberation.</i> <i>OPTCL and SLDC Odisha</i>

	at Talcher after the commissioning of TTPS Stage-III. They have expressed their intention to utilize the land currently occupied by the existing 220/132kV TTPS switchyard for their expansion project.	i) OCC acknowledged the technical feasibility of the above proposal. ii) OCC advised SLDC Odisha to expedite by carrying out the studies and co-operate with NTPC TTPS. iii) OCC advised SLDC Odisha, OPTCL and NTPC TTPS to reach a consensus. iv) OCC also suggested that the matter may be placed before CMETS-ER.	<i>assured necessary assistance shall be extended in this regard.</i>
Implementation of AGC in Intra-state generating units.	218th OCC dated 13.08.24 With the increasing penetration of renewable energy, managing frequency is expected to become more challenging in the future. Therefore, it is crucial to enhance frequency control and stability through increased participation from intra-state AGC.	As per 227th OCC: i) ERLDC informed that GE has given a demonstration regarding AGC implementation. ii) WB SLDC has informed that AGC implementation will be completed by Feb, 2026. iii) NTPC Baruni informed that signal transmission from SLDC Bihar end needs to be checked. iv) DVC informed that the AGC implementation at Mejia, Koderma & DSTPS will be completed by June 2025. v) Odisha SLDC informed that SERC approval is necessary for its Implementation. Decision: i) OCC highlighted the importance of AGC implementation for grid stability and reliability. ii) All Intra-state generating stations may approach their respective SERCs for regulatory support. lii) OCC advised NTPC Baruni and SLDC Bihar to resolve the issue of signal testing bilaterally.	<i>SLDC Bihar informed that they have planned meeting with NTPC Baruni by the end of June 2025 regarding signal testing.</i> <i>OCC advised SLDC Bihar to pursue with NTPC Baruni without any further delay for implementation of AGC after completion of signal testing.</i>

All concerned may update. Members may discuss.

2.8 Bus split operationalization at NTPC Kahalgaon: ERPC

As decided in **219th OCC** Meeting, a committee comprising of members from ERPC and ERLDC visited NTPC Kahalgaon on 17-10-2024 to assess the status of Bus splitting at 400 kV level and way forward for operationalization of 400 KV Bus sectionalizer.

Following works need to be done to complete the installation of ICT 3 & 4:

1. Determination of underground cable conduit path for 400/132 kV ICT-3, 4 and 5 allocated for stage 2 supply.
2. Excavating the existing cable and relaying from Stage-1 132kV to New Stage-2 132 kV switchyard, where ICT 3 & 4 will be connected.
3. Laying of additional 22.8 ckt. km control cable for STs.
4. Jumpering of ICTs in 132kV & 400kV level.

5. Bay equipment testing.

- NTPC apprised that determination of underground power cables is one of the major challenges to proceed further with laying of cables between two 132kV switchyards.
- Meanwhile in view of increased fault level of NTPC Kahalgaon and to facilitate interim arrangement of standby ISTS connectivity to Godda Thermal Power project of M/s Adani Power (Jharkhand) Ltd. (APJL) with Indian grid, Bus splitting at 400KV Kahalgaon needs to be done on priority.

As per 227th OCC minutes

NTPC updated present status of bus -splitting of this line which will be finished by July 2025. OCC asked NTPC to expedite their bus-splitting operation work as per the submitted deadline so that ongoing project at Goda substation may not get hampered.

NTPC may update. Members may discuss.

Deliberation in the meeting:

NTPC updated that 132kV bay commissioning and testing activity shall be completed by June 2025. It was further updated that all testing activities of 400/132kV ICT 3 & 4 shall be completed by 1st week of July 2025.

NTPC informed that there was failure of 132 KV power cable at station transformer 3 on 22.05.2025 and proposed for extension of timeline for the completion of Bus -splitting to Dec,2025.

OCC Decision:

i) OCC raised serious concerns regarding repeated delay in completion of Bus-splitting work at Kahalgaon by NTPC in view of sustained operation in high fault level scenario.

ii) OCC referred the matter to TCC.

2.9 Shutdown proposal of generating units for the month of July 2025: ERPC

Maintenance Schedule of Thermal Generating Units of ER during 2025-26									
System	Station	Unit	Capacity (MW)	Proposed		No. of Days	CEA Approved		Reason
				From	To		From	To	
DPL (approved In 227 th OCC)	DPL	8	250	21-Jul-2025	16-Aug-2025	27	23/07/2025	31/08/2025	AOH
NTPC(approved In 227 th OCC)	TALCHER STPS	1	500	1-Jul-25	10-Aug-25	41	16/10/2025	30/11/2025	AOH
WBSLDC(approved In 227 th OCC)	BAKRESWAR TPS	4	210.00	1-Jul-25	04-Aug-25	35	16-June-25	30-Jul-2025	Boiler Lic Renewal

<i>NTPC (approved In 227th OCC)</i>	<i>Darlipalli STPS</i>	<i>2</i>	<i>800</i>	<i>01-04-2025</i>	<i>10-05-2025</i>	<i>45</i>	<i>01-07-2025</i>	<i>15-08-2025</i>	<i>AOH (Main Turbine Thrust bearing temperature is high (110 °C))</i>
NTPC	KhSTPS-I	1	210	01-Jul-2025	04-Aug-2025	35	01-Jul-2025	04-Aug-2025	Boiler +Boiler RLA + LPT
NTPC	BARH II	4	660.00	1-Jul-25	4-Aug-25	35	1-Jul-25	4-Aug-25	AOH: Boiler
WBPDC	BAKRES WAR TPS	5	210.00	20-Jul-25	30-Jul-25	11	20-Jul-25	30-Jul-25	Boiler Lic Renewal
WBPDC	SAGARDIGHI TPS	2	300.00	1-Jul-25	10-Jul-25	10	1-Jul-25	10-Jul-25	Boiler Lic Renewal
GMR	KAMALANGA TPS	1	350	06-07-2025	31-07-2025	26	06-07-2025	31-07-2025	AOH-R&M
MPL	MPL	1	525	16 July 2025	24-Aug-2025	40	Not Approved by CEA		COH

Members may discuss/update.

Deliberation in the meeting:

- WBPDC informed that shutdown of Bakrewsar U#5 & Sagardighi U#2 is not required now. Shutdown of Kolaghat TPS U#4 shall be availed for 25 days from 27/06/2025 to 21/07/2025.
- NTPC requested for shutdown of KhSTPS unit#2 instead of KhSTPS unit#1 for 35 days starting from 1/08/2025.
- NTPC further submitted that shutdown of Farakka unit#4 shall be availed from 1/08/2025 for 35 days.
- NTPC emphasized to approve the shutdown proposal of Barh II unit#5 as it is critical to run the plant without maintenance. However, SLDC Bihar objected to postpone the shutdown due to peak demand season of the year.
- M/S GMR has proposed for the shutdown of Kamalanga unit#2 in place of Kamalanga unit#1 in the same date.

OCC Decision:

- OCC advised NTPC to declare COD of Barh U#3 at the earliest.
- OCC opined that the proposed shutdown of Barh U#5 could be considered subject to COD of U#3 in view of the peak demand season of Bihar.
- OCC approved other shutdown proposals along with modifications as deliberated above.

2.10 Extension of COH of TTPS Unit#2 (210MW): TVNL

The unit #2 was under COH from 21-April-2025 to 30-May-2025 due to frequent rise in HPT front shaft vibration, resulting into various manual tripping. After dismantling of Turbine it was found that IP turbine has problem in its blades. Problem of IP turbine was tried to rectified at site by BHEL, but it was a failed attempt. Finally, they recommended to send turbine to BHEL, Bhopal unit. As per BHEL, it will take 60 days to repair. However, it was requested to M/S BHEL to complete in 45 days, thereafter reaching at its site it will take another 15 days to assemble. Thus unit#2 will remain under shutdown upto July 31,2025.

TVNL may update.

Deliberation in the meeting:

TVNL submitted that the complete work of turbine rectification at Bhopal and final assembly at the site shall be completed by 31st July 2025 and requested for extension of shutdown accordingly.

OCC Decision:

OCC noted the submission of TVNL and advised to complete the work and ensure the restoration of U#2 positively by 31st July 2025.

2.11 Impact on Power supply at Melli (Sikkim) & North Bengal: ERLDC

Subsequent to tower damage in 132 kV Rangit–Kurseong and 132 kV Siliguri–Melli, these lines were reconfigured as 132 kV Siliguri–Kurseong-II (interim – charged on 9th October '24) and 132 kV Rangit–Melli (interim – charged on 12th October'24). The original configuration is yet to be restored.

At 132 KV level of Rangpo SS there is Bus split arrangement, where 132 kV Rangit–Rangpo and Rangpo–Melli section is kept on one bus and Chuzachen, Gangtok and 220/132 KV ICTs are on another Bus.


Immediately after breakdown of lines, on 08.10.2024 an online meeting was organised with representatives from ERPC, ERLDC, West Bengal SLDC, Sikkim, POWERGRID and NHPC Rangit to discuss the way forward to maintain reliable power supply to Melli, Kalimpong and Kurseong.

In the meeting, it was decided to keep the 132KV Bus Coupler at Rangpo in open condition to avoid the possibility of high loading /even breakdown of 132 kV Rangit-Rammam in case 132 kV Rangpo-Melli trips.


Thereafter with multiple grid disturbances at Rangit HEP, Melli and keeping in view of lean hydro season, 132KV Bus Coupler at Rangpo was closed on 05.11.2024.

However, with increase in hydro generation in this complex, power has started to flow from Rangpo to Rangit, which ultimately has led to increased loading of 132 kV Rangit-Rammam and it might cross thermal limit and may lead to permanent damage in line.

- To avoid this, 132 kV Rangit–Rangpo and Rangpo–Melli sections are normally decoupled from the rest of Rangpo during high hydro conditions. In such a scenario, if the 132 kV Rangit–Rammam line trips, Rangit and Melli will be islanded, and 132kV-Siliguri-NBU-D/C will be also overloaded. In that case, any of these or both systems may collapse.

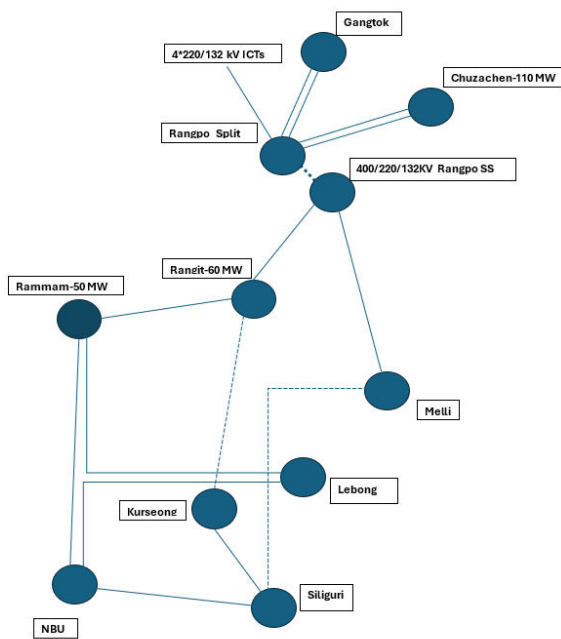

Network diagram of the area (before reconfiguration)

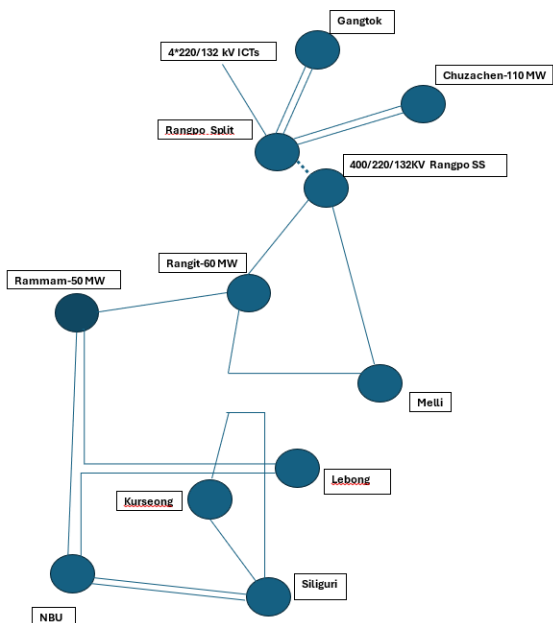

Network diagram of the area (current reconfiguration)

Hydro generation in the Sikkim complex has already picked up, and high loading is observed on the 132 kV Rangit–Rammam line and the 132kV-Siliguri-NBU-D/C network of WB due to low generation from TCF and TLDP. Situation will worsen with further increase of hydro generation during monsoon.

In 227th OCC meeting, PowerGrid ER-2 has confirmed that the original configuration will be restored by the end of June 2025. Until restoration of lines in original configuration, following may be noted:

1. 132KV Bus Coupler at Rangpo SS may be kept Open.
2. Melli (Sikkim) will be fed from Rangit only.

Members may discuss and POWERGRID may expedite the restoration of lines.

Deliberation in the meeting:

POWERGRID updated that damaged tower locations 126 and 127 huge ROW issue and at a time only one location would be allowed by the district administration so that minimal tea garden area is affected.

It was also added that foundation work at location 127 is completed and erection and stringing work would be completed by 10th July 2025. Thereafter, both the lines would be charged. However, the balance work of tower No. 126 will be taken up in the next winter.

ERLDC deliberated that with increase in hydro generation in the Sikkim complex and closed condition of 132KV Bus coupler at Rangpo, power has started to flow from Rangpo to Rangit,

which ultimately has led to increased loading of 132 kV Rangit-Rammam and it might cross thermal limit and may lead to permanent damage in line. On the other hand, if bus coupler is opened at Rangpo then in case of tripping of 132kV-Rangpo-Rammam, Rangit will be islanded with Melli and it may collapse due to mismatch of Load & Generation.

West Bengal SLDC submitted that loading of 132kV-NBU-Siliguri is already in higher side. In case of tripping of 132kV-Rangit-Ramman, support from Rangit will not be there, which will further increase the loading of NBU-Siliguri.

ERLDC supplemented that there is an SPS at Ramman HEP to take care of loading of Rammam-NBU and Rammam-Lebong ckts. ERLDC enquired whether loading of Rammam – Rangit may also be added in the existing SPS and modified accordingly.

OCC Decision:

OCC advised Powergrid to complete the tower erection and stringing work at Location 127 positively by 10th July 2025 and ensure restoration of 132 kV Rangit–Kurseong and 132 kV Siliguri–Melli lines.

OCC suggested West Bengal SLDC to study and convey possible modification in existing SPS at Rammam. It was further suggested that the status of Bus coupler at Rangpo may be decided after due consultation with West Bengal, Sikkim and Powergrid.

2.12 Update on replacement of SEM in ER, from Non-DLMS to DLMS platform and compliances to latest standards: Powergrid ER-II

- Considering the initial phase of metering (year 2012), all the Energy Meters procured were non DLMS type which are specially manufactured only to cater some specific requirements. The initial meters were procured from L&T OEM. Then gradually from 2016 onwards DLMS protocol Meters are introduced, and different OEM make Meters are procured.
- These Meters are capable of handling **15 min Load Survey** Block data. However, when the upcoming requirements and regulations are taken into consideration, some Meters do not have the technical functionality to cater the requirements. A brief analysis of Meter types connected with AMR system, is given below.

Time interval	L&T (Qty: 411)	Genus-01series (Qty: 763)	Genus-02 series (Qty: 325)	Secure (Qty: 18)
15 min Data Block	✓	✓	✓	✓
05 min Data Block	✗	✗	✓	✓
01 min instant	✗	✓	✓	✓

- ✓ The L&T make Meters are nearing 14 years of service on field and becoming susceptible to errors, frequent hang issues, and breakdowns. We have already received multiple complaints from different utilities regarding the same. It is imperative that all the L&T make meters (411 Qty) needs to be replaced with newly procured meters (GENUS/SECURE) to prevent any unwanted errors in settlement. In addition to that, a certain quantity of 01

series Genus make Meters are also needs to be replaced to ensure the technical capability of upcoming requirements.

- ✓ The approx. count of new Meters requirement will be 1021. At present newly supplied Secure make SEM are available in ER (ER-II- 250+ ER-I-210), i.e, 460 Nos.
- ✓ Going by phased manner replacement, immediately L&T make SEM's may be replaced, subsequently, procurement of new SEM by 600 quantity (Approx) also needs to be considered. However, phased manner can be considered for the same.

As per 223rd OCC Deliberation

Members discussed and apprised that in many areas the existing L&T meters are non-compatible with the new requirements of block-wise data

Powergrid ER-II informed:

- ✓ 411 no.s of L&T meters have already been in operation for more than 12 years, hence urgent replacement is required.
- ✓ As of now, there is a stock of 460 no.s of new meters,

However, ERLDC stated that replacement of 330 L&T meters is required.

OCC Decision

- OCC opined that 330 no.s of L&T meters should be replaced with existing stock of Secure make meters and the list of stations/Meters to be replaced shall be furnished by ERLDC. Powergrid was also advised to keep the remaining 130 meters (approx.) as buffer stock to take care of any urgent requirement.
- Members were of the view that procurement plan for new meters conforming to new TS shall be taken up for discussion once the roadmap of 05 min scheduling gets finalized and 5 min metering is put into practice.

As per latest update from Powergrid in special meeting on AMR system & IEM (5 min) in Eastern Region dated 07.04.2025, State wise breakup of 763 Genus 01 series meter is given as follows:

State	Main meter	Check meter	Standby meter	Total Meters
WestBengal	45	12	98	155
Sikkim	8	0	24	32
Odisha	62	12	93	167
Bihar	95	14	198	307
Jharkhand	36	3	63	102

Powergrid ER II may update. Members may discuss.

Deliberation in the meeting:

Powergrid ER-II informed that 30 nos. of new Genus meters have already been distributed for replacement of L&T meters and has assured that all existing L&T meters will be replaced with Genus Series 01 meters by the end of August 2025.

OCC decision:

OCC opined that significant mismatch in L&T make SEMs and SCADA has been observed due to severe time drift. This can have huge financial implications on utilities.

OCC advised Powergrid and ERLDC to get all the L&T make meters replaced by new Genus meters by the end of August 2025.

2.13 Regarding construction of additional Transmission tower in front of newly constructed GIS building for transmission of Power generated from Teesta-V Power Station: NHPC

A devastating flash flood occurred on the intervening night of 3rd and 4th October 2023. The said flood damaged many installations of Teesta-V Power Station. The Tower#1 of PGCIL was also washed away in the flood. Also, Pot head yard Gantry, Lightning Arresters, CVTs, Wave Traps, and GIS to Air Bushing etc. got damaged. The restoration work started after the occurrence of the flood.

Tower #1 has been re-erected by PGCIL, and the line was made available for power evacuation from Teesta-V Power Station.

Later on, a massive landslide occurred on 20th August 2024 at TRT area of the Power House resulting in the catastrophic collapse of the entire GIS building and the equipment housed within it. The majority of the GIS building was completely damaged, except for a small portion containing the DG sets, meter room, and 11kV switchgear. As complete impact of the landslide was faced by GIS building itself, therefore Tower #1 was remained protected.

Subsequent to damage of the GIS building, a New GIS building is being constructed near Main Access Tunnel, i.e. downstream side of TRT. Accordingly, PGCIL was requested to conduct survey and propose alternate solution for Power evacuation from Teesta-V Power Station.

PGCIL vide letter PG/ER-II/RPO/TL/01/25-25/271; Dated: 23.01.2025 proposed two solutions (letter and drawings are enclosed):

- a) Option-1: Provision of 03 no.s of gantry, two gantry of double tier and one gantry of single tier and required modification shall be done by PGCIL in existing tower no.01 (DD+ 09)
- b) Option-2: Provision of 01 no. additional tower (1A) with new pile foundation (DD+0) with auxiliary cross arm for dead end connection to newly constructed single gantry at GIS of Teesta-V Power Station.

Initially Option-1 was opted, but during detailed engineering it was opined by design & engineering division of NHPC that Option-2 is more suitable both technically & economically. In this context an online meeting was held between NHPC and PGCIL on 12/06/2025 to finalize one of the above options. Keeping in view the space availability and other constructional aspects, it has been decided to go for option-2, where an additional tower shall be erected. In this regard, PGCIL has been requested on 13/06/2025, to conduct a survey to finalize the exact location of the additional tower, considering the locations of existing bridges and its access road.

NHPC is going to recommission Teesta –V Power Station by the end of Dec 2025 this year.

NHPC proposal:

As PGCIL has expertise of designing, erecting, commissioning and maintaining of high voltage transmission lines/ towers, NHPC is of the view that 400 KV D/C Ringo –Teesta-V (Upto new GIS) Transmission line should be under the jurisdiction of Power Grid and Power grid should be the owner of entire transmission line including extension up to new GIS in view of maintenance of the line.

Powergrid may elaborate.

Deliberation in the meeting:

Powergrid updated that since NHPC has opted for Option II, site survey regarding additional tower and requisite modifications is required to be carried out.

OCC Decision:

OCC advised NHPC and Powergrid to jointly carry out the site survey as per the chosen option of erection of a new tower and submit the outcome in next OCC.

2.14 Requirement of one 315MVA ICT on Loan basis from regional pool of spares: DVC

One no. 400/220/33 KV,315MVA ICT got damaged at Koderma Thermal Power Station, DVC on 02.06.2025. Due to this outage, DVC is facing difficulties in managing power flow of that area.

In this context a special meeting under the chairmanship of MS, ERPC was conducted on 06.06.2025.

During the meeting, DVC informed that of the two nos. of 315 MVA ICTs at Koderma TPS one ICT caught fire and got damaged on the early morning of 02.06.2025. Importance of the Koderma switchyard was apprised as it is connected to both the PowerGrid network at 400 kV level and internal DVC grid at both 220 kV and 132 kV level and that it is supplying power to JVVNL and other industrial consumers. In view of the above, DVC is seeking for one 315 MVA ICT on loan basis urgently.

After detailed deliberation, the following decisions were arrived at during the meeting:

All ER utilities were advised to adhere to CEA guidelines for availability of spares and inventories as well as to ensure N-1 redundancy.

✓ DVC may inspect the 315 MVA spare ICT being made available by PowerGrid at 400 kV Durgapur S/S and upon satisfactory test results, the same may be deployed at Koderma TPS. As informed later, DVC has already carried out inspection of spare 315 MVA ICT. few photographs attached at [Annex-B.2.14](#)

Recently an inquiry committee has been formed by ERPC to analyse root causes that led to the burn out of the ICT.

DVC may update. Members may discuss.

Deliberation in the meeting

- i. *DVC informed that the spare 315 MVA ICT, previously made available from 400 kV Powergrid Durgapur Substation, has physical design mismatches. Hence, after discussion with Powergrid, spare ICT from Muzaffarpur S/s with matching design and specification has been agreed.*
- ii. *Powergrid submitted that the bushings of the proposed spare ICT are not available. DVC agreed to install the bushings and transport the ICT to Koderma after all necessary testing.*

OCC decision:

- i. *OCC agreed with the proposal of DVC for use of spare 315MVA 400/132/33kV Transformer from ER pool placed at PGCIL Muzaffarpur S/s at Koderma TPS of DVC.*
- ii. *OCC advised DVC to carry out necessary testing and healthiness check of the Transformer and arrange for its transportation to Koderma.*
- iii. *OCC advised Powergrid to extend all possible co-operation in this regard.*
- iv. *OCC referred the issue to TCC/ERPC for post facto approval.*

Additional Agenda

2.15 Interim Modification/Heightening Work on 132kV D/C Patratu–PTPS(DVC) Line at Railway Siding Area of PVUNL:DVC

A joint meeting between DVC, JUSNL, and PVUNL was held on 30th July 2024 at the PVUNL premises, where the need for immediate execution of heightening work on the 132kV DVC Patratu–PTPS line, passing through the railway siding area, was recognized. PVUNL emphasized the urgency of the work for progressing its siding construction, and DVC agreed to carry out the necessary modifications.

Technical Details:

- The existing configuration of the 132kV D/C Patratu–PTPS line includes two circuits: 5C and 6C.

Top X-arm: 5C(R) & 6C(R)

Middle X-arm: 5C(Y) & 6C(Y)

Bottom X-arm: 5C(B) & 6C(B)

- At present, only circuit 5C is under operation.
- Under the finalized scheme, to achieve statutory ground clearance at the railway crossing, a heightening was carried out. The revised configuration allows operation of only circuit 5C using the top and middle cross-arms.

Status Update:

- Shutdown clearance for this modification was obtained from ERLDC.
- Upon completion of the work, a charging clearance application was submitted to CEA's Regional Inspectorial Organisation (RIO), Eastern Region.

Observation by RIO-CEA:

In response, RIO-CEA has observed that while the execution of the heightening work was noted, such modifications should be taken up with knowledge and deliberation in the ERPC forum as per regulatory procedures. Consequently, RIO-CEA has advised that the agenda be placed before ERPC, and post ERPC deliberation, the final charging clearance may be issued.

Submission:

In light of the above, it is requested that the matter regarding interim modification and heightening work on the 132kV Patratu–PTPS line, undertaken by DVC in coordination with PVUNL and JUSNL. This will facilitate formal acknowledgment and record of the interim modification carried out.

Deliberation in the meeting:

DVC apprised that RIO (E), Kolkata office has asked for vetting of ERPC before issuing the charging clearance of 132kV D/C Patratu – PTPS line.


OCC Decision:

OCC agreed with the proposed modification of 132kV D/C Patratu – PTPS line and DVC was suggested to intimate CTU accordingly.

2.16 Near miss situation around Capital city of West Bengal & Odisha:

2.16.1 Kolkata:

Kolkata and surrounding suburban area are being fed from three main Substation Subhasgram(PG), Rajarhat(PG) and Jeerat(WBSETCL) substation. These substations receive power mainly from 765 kV New Jeerat(PG), Farakka(NTPC) and Sagardighi (WBPDC) other than internal generation of HEL and Budge Budge. During the peak demand period of 2023 there was significant transformation capacity shortage in Subhasgram S/S. Persistent effort of all stakeholders from ERPC forum ensured 500 MVA capacity addition at Subhasgram, 2X315 MVA capacity addition at Jeerat till date. Also commissioning of another 500 MVA ICT at Rajarhat and a spare of 500 MVA ICT at Subhasgram(PG) are under implementation stage and being actively monitored. This has ensured sufficient transformation capacity in steady state around Kolkata region. However, frequent and multiple transmission outages at 400KV and 765 kV corridors around Kolkata have resulted in near miss situations recently. From 28th May to 30th May 2025 outages of 400 kV New Jeerat-Jeerat -1 and New Jeerat-Subhasgram-D/C resulted in system operation without any reliability margin and system was one tripping away from voltage collapse or cascading tripping. Around 2330 MW load and 1300 MW generation could have been impacted with another one 400 kV line tripping.

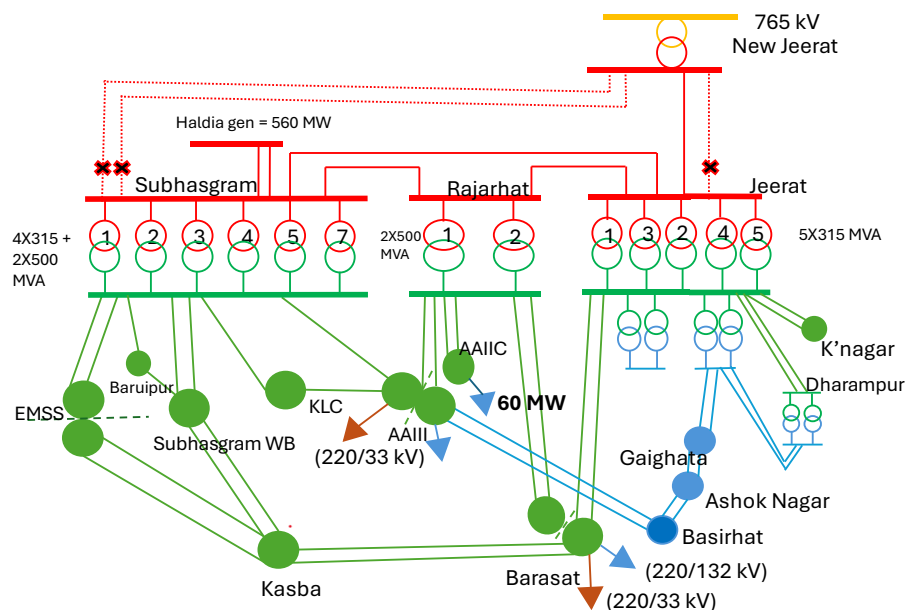

Repeated outages (Planned and forced) of 765 kV New Ranchi-Medinipur-New Jeerat and 400 kV New Jeerat- Subhasgram and Jeerat posing serious threat for reliability of Kolkata region. During the 28th May to 30th may WB demand was on the lower side, however during peak demand day extent of possible challenges and possible damage could have been more significantly higher.

Considering the rising demand and the critical nature of loads in key areas such as hospitals, metro railway, airports and the capital city of Kolkata, it is prudent to initiate a discussion on short-term mitigation strategies as well as long-term planning proposals.

Member May discuss.

OCC Deliberation:

- i. ERLDC highlighted that transformation capacity in Subhasgram (PG), Rajarhat (PG) and Jeerat (WBSETCL) around Kolkata is being augmented recently with persistent effort of POWERGRID, WBSETCL, CESC, ERPC & ERLDC. However, recently from 28th to 30th May 2025, due to prolonged & simultaneous forced outage of 400 kV New Jeerat-Jeerat one circuit and New Jeerat-Subhasgram D/C, a near miss scenario occurred, endangering approximately 2300 MW load and 1300 MW generation around Kolkata area.
- ii. ERLDC highlighted that during 28th to 30th May demand was on the lower side. If demand would have been on the higher side, then the situation would have become critical. ERLDC further highlighted that next year being election year such events of prolonged outage in this corridor needs to be avoided.
- iii. PMJTL/POWERGRID submitted that they have found certain problems in a batch of CLR insulators which resulted in such prolonged outage of the said lines. They are replacing all 4 strings of insulators in a location where any fault is taking place.
- iv. West Bengal supplemented that there were several instances of emergency S/D of one ckt of 765kV Ranchi-Medinipur-New Jeerat corridor taken by PMJTL. This poses a serious threat of voltage instability due to outage of entire corridor during high demand period. However, the healthiness of the 400 kV New Jeerat-Jeerat D/C and New Jeerat-Subhasgram D/C corridor is more important from overall reliability of Kolkata region.

OCC Decision:

- i) OCC advised PMJTL to perform a thorough checkup of the line and complete replacement of faulty insulator strings of entire stretch of all 400kV connecting lines from New Jeerat (including switchyard) and 765-New_Ranchi-Medinipur-New-Jeerat-D/C corridor. Replacement work should be started immediately after Festive season in the Sep-Oct-2025 and should be completed before Jan 2026. Insulator replacement work of 400 kV lines should be completed on priority basis.
- ii) Matter has been referred to TCC/ERPC meeting.

2.16.2 Bhubaneswar

400/220 kV Meramundali, Mendhasal, New Dubri & Pandiabilli are major substations which fed almost 40% of Odisha's load including capital city of Bhubaneswar. Demand in this area has increased significantly in last few years and expected to carry on the growth rate. As per the transformation capacity is concern, currently many of the S/stn ,400/220KV ICT's are not N-1 Compliant like Mendhasal, Meramundali and Lapanga SS. Further few important lines in these pockets are remaining above N-1 limit and approaching towards thermal limit even after exercising all the control measures :


1. 400 kV OPGC-Lapanga D/C
2. 400 kV Lapanga-Meramundali D/C
3. 400 kV Talcher-Meramundali D/C

Outage of any one pair leads to near miss situations and extreme low voltage issue in the region. Historically, the Odisha system is facing multiple tower collapses and transmission line outages in this region every year.

Name of the Line	From Date	To date	Remarks
400KV-MEERAMUNDALI-MENDHASAL-1	26-04-2025	14-05-2025	Tower collapse at loc no 110
400KV-MERAMUNDALI-LAPANGA	20-05-2024	17-07-2024	Tower collapse at location no 51
400KV-NEW DUBURI-MEERAMUNDALI	08-06-2023	19-06-2023	Tower collapse at loc no 135 (appx 31km from Meramundali)
400KV-MERAMUNDALI-LAPANGA	10-06-2023	19-06-2023	Tower collapse at loc no 08 (from Meramundali end)

During such long outage of transmission corridor system remains vulnerable and any further tripping could result in total system collapse.

Odisha Network

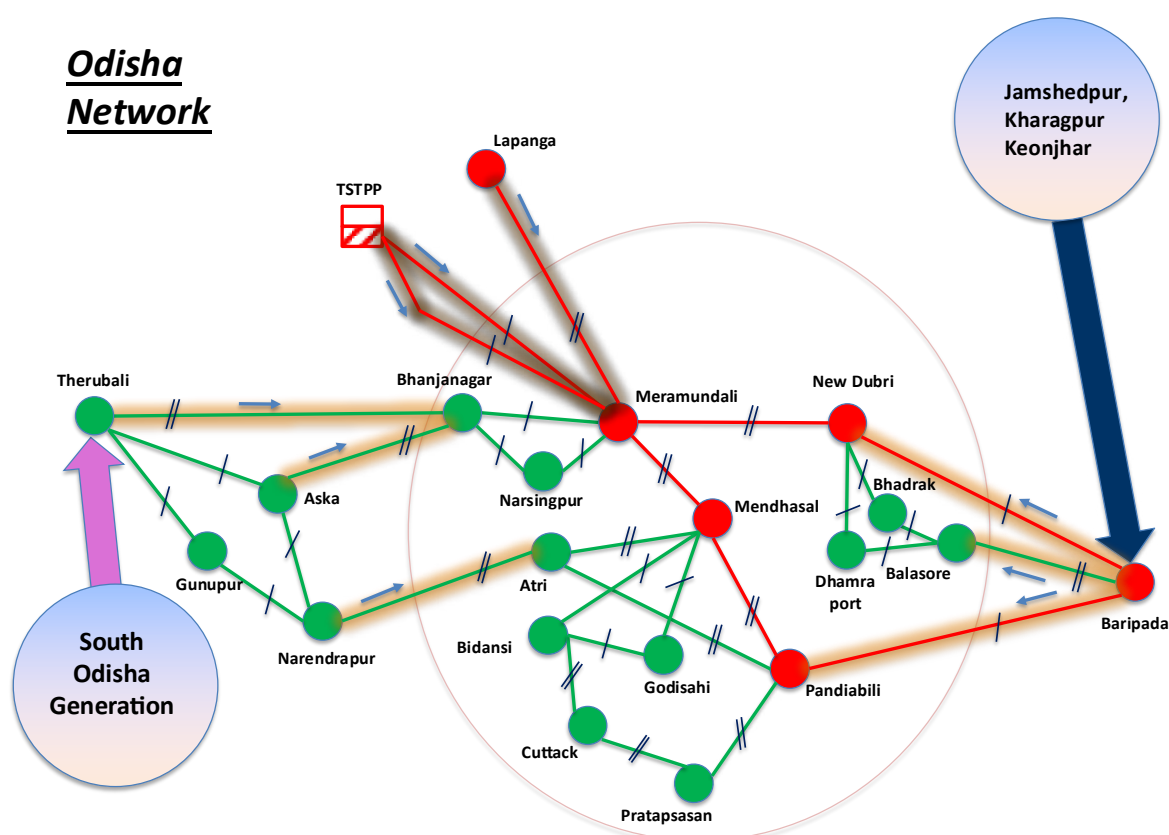

Considering the rising demand and the connected 40% load of Odisha's demand including capital city of BBSR, it is prudent to initiate a discussion on short-term mitigation strategies as well as long-term planning proposals.

Members may discuss.

Deliberation in the meeting:

- i) ERLDC explained that the major load center of Odisha including capital city (40% of state demand) is supplied from west side through 400 kV Talcher-Meramundali and Lapanga-Meramundali, from east side through 400 kV Baripada-New Dubri and Baripada-Pandiabili and from South side by 2-3 pairs of 220 kV lines. However, due to high availability, 80% of the power of this region is supplied from the west side via 400 kV Talcher-Meramundali and Lapanga-Meramundali. This is leading to severe congestion in the 400 kV OPGC-Lapanga-Meramundali and Talcher-Meramundali corridor. These lines are already N-1 violated and could reach thermal loading limit by next year itself.
- ii) ERLDC also highlighted that Odisha is having a history of tower collapse since 2023 in this corridor. Therefore, for ensuring reliability of capital city of Bhubaneswar and surrounding area in the coming summer, holistic planning may be initiated on urgent basis.
- iii) MS ERPC emphasised all possibility should be explored to ensure maximum generation (including CPP) in Bhubaneswar pocket as a reliability measure.

OCC Decision:

- i) OCC advised Odisha SLDC to carry out comprehensive study. Thereafter, the matter may be discussed in consultation with CTU and ERLDC for the resolution of the challenges.
- ii) OCC further advised IBEUL (JSW-EUL) to complete the construction of DTL.

3. PART-C: ITEMS FOR UPDATE/FOLLOW-UP/INFORMATION

3.1. ER Grid performance during May 2025

The average and maximum consumption of Eastern Region and Max/Min Demand (MW), Energy Export for the month April -2025 were as follows:

AVERAGE CONSUMPTION (MU)	MAXIMUM CONSUMPTION(MU)/ DATE	MAXIMUM DEMAND (MW)	MINIMUM DEMAND (MW)	SCHEDULE EXPORT	ACTUAL EXPORT
		DATE / TIME	DATE / TIME	(MU)	(MU)
609.7 MU	672 MU, 14.05.2025	31985 MW, 10.05.2025 at 23:41 Hrs.	18725 MW, 01.05.2025 at 17:44 Hrs.	2261	2357

**ERLDC/ERPC may highlight the performance of the ER grid.
Members may note.**

OCC Decision:

OCC noted ER grid performance during May 2025.

3.2. Non-Submission of FRC data in stipulated timeframe: ERLDC

Adhering to IEGC clauses **30.8** and **30.10.(a)** to **30.10.(q)**, generating stations within the Eastern region are required to submit essential data to ERLDC within two days of receiving a notification regarding a reportable frequency event. Additionally, according to clause 30.10.(n), all control areas within the eastern region must assess their frequency response characteristics and share the evaluation, along with high-resolution data, with the ERLDC. Therefore, timely submission of primary response data is crucial for compliance with the IEGC.

227th OCC Decision

- ✓ All generators were advised to regularly share high resolution data against each reportable frequency event with ERLDC on time to facilitate accurate assessment of FRP for respective control areas.
- ✓ All generating utilities were also urged to update the google sheet (link mentioned above) with email address where notifications of reportable events will be shared.

The latest data receipt status is given below: (as on 09.06.2025):

STATIONS	11-05-2025 16:51 HRS
FSTPP #STG 1 & 2	
FSTPP # STG 3	
KhSTPP #STG 1	
KhSTPP #STG 2	
TSTPP #STG 1	
Barh stage-1	
Barh stage-2	
BRBCL	
Darlipalli	
North Karanpura	
NPGC	
TEESTA V	
Dikchu	
IBEUL (JSW UTKAL)/INDBHARAT	
GMR	
MPL	
ADHUNIK	
JITPL	
TEESTA III	
Bihar	
Jharkhand	
DVC	
OPTCL	
WB	

 Received
 Not Received

[illegible]

- As per IEGC Reg. 34.3: A mock trial run of the procedure for different sub-systems including black-start of generating units along with grid forming capability of inverter-based

generating station and VSC-based HVDC black-start support at least once a year under intimation to the concerned SLDC and RLDC.

- Eastern region has 16 hydro power plants, which has capability to play a crucial role during restoration after any grid disturbance. Mock black start testing along with grid forming capability is being carried out on yearly basis, as mandated by IEGC reg 34.3, to ensure the capability & readiness of those generators for any contingency.
- Also, diesel generator sets and other standalone auxiliary supply source to be used for black start shall be tested on a weekly basis and the test reports are to be shared to the concerned SLDC, RLDC and NLDC on a quarterly basis.
- As per IEGC Reg. 34.4: Simulation studies are to be carried out by each user in coordination with RLDC for preparing, reviewing and updating the restoration procedures considering the following:
 - a) Black start capability of the generator;
 - b) Ability of black start generator to build cranking path and sustain island;
 - c) Impact of block load switching in or out;
 - d) Line/transformer charging;
 - e) Reduced fault levels;
 - f) Protection settings under restoration condition

So far, Balimela, Burla, U. Indravati, TLDP-IV, and Subarnarekha have completed their mock black start tests, while Jorethang and Tashiding have confirmed tentative dates for FY25. The remaining generators are yet to schedule their tests and are requested to confirm their mock drill dates. Status of mock black start is as follows:

Sl. No.	Name of Hydro Station	2024-25 Actual Date of Test	Tentative date for blackstart exercise for FY 2025-26
1	U. Kolab		
2	Balimela	15 th January 2025	
3	Rengali		
4	Burla	December-24	
5	U. Indravati	Sep-24	
6	Maithon	December-24	
7	TLDP-III		
8	TLDP-IV	December-24	
9	Subarnarekha	3 rd December 2024	
10	Teesta-V	N/A	
11	Chuzachen		
12	Teesta-III	N/A	
13	Jorethang		
14	Tashiding		
15	Dikchu	N/A	
16	Rongnichu		

227th OCC decision:

- OCC advised all black start capable hydro generating units of ER to update their schedule of mock black start to ERLDC at the earliest. This is in compliance to IEGC 2023 (CERC).
- OCC further opined that in case of non-receipt of further update by respective hydro generating units the proposed tentative schedule of mock black start may be considered as final. Thereafter all black start capable hydro units shall have to conduct mock black start at least once in a year as mandated in IEGC 2023.

All the generators are requested to confirm dates for black start of each generating unit. Also, the users are requested to share the data required simulation studies before the scheduled date of mock drill.

Members may note.

Deliberation in the meeting

OCC decision:

- ✓ *OCC advised all black start capable hydro generating units of ER to update their schedule of mock black start to ERLDC at the earliest. This is in compliance to IEGC 2023 (CERC)*

4. PART-D: OPERATIONAL PLANNING

4.1. Anticipated power supply position for July-2025

The abstract of peak demand (MW) vis-à-vis availability and energy requirement vis-à-vis availability (MU) for the month of July-2025 is prepared by ERPC Secretariat (**Annexure D.1**) on the basis of LGBR for 2025-26 and feedback of constituents, keeping in view that the units are available for generation and expected load growth etc.

Members may update.

Deliberation in the meeting

All states were requested to provide their anticipated power supply position for July-2025 within a week. Updated anticipated power supply position will be shared accordingly.

4.2. Major Thermal Generating Units/Transmission Element outages/shutdown in ER Grid (as on 06-06-2025)

a) **Thermal Generating Stations outage report:**

SL No	STATION	STATE	AGENCY	UNIT NO	CAPACITY (MW)	REASON(S)	OUTAGE DATE
1	TENUGHA T	JHARKHAND	TVNL	2	210	Due to high vibration in Turbine	20-Apr-2025
2	FSTPP	WEST BENGAL	NTPC	2	200	Boiler Tube Leakage	05-Jun-2025
3	BARH	BIHAR	NTPC	2	660	Abnormal sound in boiler.	03-Jun-2025
4	BARH	BIHAR	NTPC	1	660	Tripped on boiler tube leakage	01-Jun-2025
5	JSWEUL	ODISHA	JSWEUL	2	350	leakage in Turbine driven boiler feed pump	04-Jun-2025
6	NABINAGAR(NPGC)	BIHAR	NTPC	1	660	Tripped on boiler tube leakage	03-Jun-2025
7	NABINAGAR(NPGC)	BIHAR	NTPC	3	660	Tripped on boiler tube leakage	03-Jun-2025

8	KODERM A	DVC	DVC	1	500	Due to tripping of 11 KV board 1BA on account of flashover in the breaker of Booster Fan#1A	05-Jun-2025
9	CHANDRA PURA TPS	DVC	DVC	7	250	Loss of fuels	03-Jun-2025
10	MEJIA TPS	DVC	DVC	3	210	Tripped on boiler tube leakage	03-Jun-2025
11	Sterlite	ODISHA	SEL	2	600	APH A Gearbox Problem	31-May-2025
12	HEL HIRANMA YEE	WEST BENGAL	HEL	1	150	Turbine vibration high and rotor earth fault	26-Apr-2025

All Generating stations are requested to update expected restoration time and reason outage to ERLDC/ERPC on weekly basis in case of any change at their end.

b) Major Generating stations Out on Reserve Shutdown due to low system demand:

SL No	STATION	STATE	AGENCY	UNIT NO	CAPACITY (MW)	REASON(S)	OUTAGE DATE
1	SOUTHERN	WEST BENGAL	CESC	2	67.5	Low system demand	27-May-2025
2	SOUTHERN	WEST BENGAL	CESC	1	67.5	Initially tripped on Furnace Problem Later it was taken under Reserve shutdown due to low system demand	21-May-2025

c) Hydro Unit Outage Report:

S. NO	STATION	STATE	AGENCY	UNIT NO	CAPACITY (MW)	REASON(S)	OUTAGE DATE
1	TEESTA STG III Hep	SIKKIM	TUL	1	200	Sudden cloudburst at glacier fed LOHNAK Lake followed by huge inrush of water in Teesta River and damage of Teesta III Dam & downstream Powerhouses	04-Oct-2023
2	TEESTA STG III Hep	SIKKIM	TUL	2	200		
3	TEESTA STG III Hep	SIKKIM	TUL	3	200		
4	TEESTA STG III Hep	SIKKIM	TUL	4	200		
5	TEESTA STG III Hep	SIKKIM	TUL	5	200		
6	TEESTA STG III Hep	SIKKIM	TUL	6	200		

s7	TEESTA HPS	SIKKIM	NHPC	1	170	Sudden cloudburst at glacier fed LOHNAK Lake followed by huge inrush of water in Teesta River and damage of Teesta III Dam & downstream Powerhouses	04-Oct-2023
8	TEESTA HPS	SIKKIM	NHPC	2	170		
9	TEESTA HPS	SIKKIM	NHPC	3	170		
10	CHIPLIMA HPS / HIRAKUD II	ODISHA	OHPC	1	24	Capital Overhauling	15-Dec-2023
11	BALIMELA HPS	ODISHA	OHPC	5	60	Repair and maintenance work	16-Jan-2025
12	BALIMELA HPS	ODISHA	OHPC	6	60	Initially unit was out due to Severe water leakage from turbine, later unit was taken under Repair and maintenance work from 00:00 hrs of 16.01.25	06-Jan-2025

d)Long outage report of Transmission Element (MORE THAN 01 WEEK) (As on 06.06.2025):

Transmission Element / ICT	Outage From	Reasons for Outage
220/132 KV 100 MVA ICT II AT LALMATIA	22-01-2019	220/132KV, 100MVA Transformer (NTPC side) is charged on 07.02.2024 from HV side on no load. Now, it is in idle charged condition
220KV-FSTPP-LALMATIA-I	21-04-2021	"Two nos. of tower collapsed on 29.05.2024 near to Lalmatia GSS in the Loc. No. 246 & 247. Presently 220 kV Farakka-Lalmatia line is charged(from loc no 241 to loc 84) at 132 kV voltage level for anti-theft purpose by tapping at loc. No. 100-101."
220KV-WARIA-BIDHANNAGAR-1	08-06-2022	To control overloading of 220 kV Waria-DSTPS (Andal) D/C line
220KV-WARIA-BIDHANNAGAR-2	08-06-2022	To control overloading of 220 kV Waria-DSTPS (Andal) D/C line
" 132KV-BARHI-RAJGIR-1"	25-03-2023	" Dismantling of tower no. 227, 228, and 229 crossing the premises of Mahabodhi Cultural centre along with Destraining of conductor of both circuits and Earthwire between tension tower no. 218-237 in same line."

132KV-NALANDA-BARHI(DVC)-1	25-03-2023	" Dismantling of tower no. 227, 228, and 229 crossing the premises of Mahabodhi Cultural centre along with Destringing of conductor of both circuits and Earthwire between tension tower no. 218-237 in same line."
400KV-RANGPO-TEESTA-V-1	04-10-2023	Tower near gantry of Teesta V powerhouse collapsed due to sudden cloudburst at glacier fed LOHNAK Lake followed by huge inrush of water in TEESTA river and damage of Teesta III Dam & downstream Powerhouses
400KV-RANGPO-TEESTA-V-2	04-10-2023	Tower near gantry of Teesta V powerhouse collapsed due to sudden cloudburst at glacier fed LOHNAK Lake followed by huge inrush of water in TEESTA river and damage of Teesta III Dam & downstream Powerhouses
132KV-RANGPO-SAMARDONG-1	22-05-2024	Rangpo:Y_N fault with fault distance 0.157 KM ,14.562kA Samardong: NA
132KV-CHANDIL-MANIQUEI-1	05-06-2024	Power assistance withdrawn
220KV-RAJARHAT-NEW TOWN(AA-II)-2	10-07-2024	Initially line out due to rectification of gas leakage problem from B-Ph breaker pole. Line declared under breakdown after charging attempt after return of shutdown. After that fault found in b-phase cable.
400KV/220KV 315 MVA ICT 1 AT NORTH KARANPURA	12-09-2024	" Tripped on Differential protection"
132KV-MADHEPURA (BH)-SAHARSA(PMTL)-1	23-09-2024	To control loading on 132kV Madhepura-Saharsa line
132KV-MELLI-SILIGURI-1	05-10-2024	S/d for inspection of tower of Loc.127 found twisted due to heavy landslide & heavy continuous rainfall in Soom Tea Garden under Darjeeling section. Line charged as 132 KV Siliguri-Melli II (Interim arrangement) at 19:20 hrs on 09-10-2024. This interim arrangement is obtained by horizontal jumpering at Loc-129 after disconnecting main jumper for both Rangit & Melli side.
132KV-RANGIT-KURSEONG-1	05-10-2024	S/d for inspection of tower of Loc.127 found twisted due to heavy landslide & heavy continuous rainfall in Soom Tea Garden under Darjeeling section. Line charged as 132 KV Siliguri-Melli II (Interim arrangement) at 19:20 hrs on 09-10-2024. This interim arrangement is obtained by horizontal jumpering at Loc-129 after disconnecting main jumper for both Rangit & Melli side..

400KV/220KV 315 MVA ICT 1 AT TSTPP	01-11-2024	Tripped on PRD protection
132KV-PATRATU-PATRATU-1	16-11-2024	Diversion/Heightening of line due to inadequate clearance from under construction railway Line by PVUNL
132KV-PATRATU-PATRATU-2	16-11-2024	Diversion/Heightening of line due to inadequate clearance from under construction railway Line by PVUNL
400KV-ALIPURDUAR (PG)-PUNASANGCHUN-JIGMELING-2	02-12-2024	SD Aailed by Bhutan; For rectify/Replace the LA for 400kV Jigmeling _Puna_ALI-1.
400KV-ALIPURDUAR (PG)-PUNASANGCHUN-JIGMELING-1	10-12-2024	Jumper connection and interconnection removal at Kamichu
400KV/220KV 315 MVA ICT 2 AT MEJIA-B	20-01-2025	"Tripped during charging of ICT#1 bay with cable from 220 kv GIS side
132KV-CHUZACHEN-RANGPO-1	04-02-2025	Maintenance Activities
220KV-DALKHOLA (PG)-GAZOLE-2	06-02-2025	To reduce loading of malda gazole after dalkhola pg bus return
400KV-JHARSUGUDA-ROURKELA-2	01-03-2025	Reconductoring work
400KV-MEDINIPUR-KHARAGPUR-1	17-03-2025	Tripped on DP. Tower Collapsed
400KV-MEDINIPUR-KHARAGPUR-2	17-03-2025	Tripped on DP. Tower Collapsed
400KV/220KV 315 MVA ICT 1 AT LATEHAR(JUSNL)	30-03-2025	REF protection operated
220KV-BIDHANNAGAR-WARIA-2	17-04-2025	B-phase CT Blast at Bidhannagar end.
" 400KV-BUXAR-NAUBATPUR-2"	08-04-2025	Start up power shift to 220 kV
400KV/220KV 315 MVA ICT 1 AT LATEHAR	22-04-2025	R phase LA of 400/220/33 KV ICT - I got bursted
400KV/220KV 315 MVA ICT 2 AT LATEHAR	16-04-2025	Transformer REF protection operated
132KV-CHANDAUTI (PMTL)-Barachatti-2	01-05-2025	DC fail alarm
765KV-JHARSUGUDA-RAIPUR PS (DURG)-2	01-05-2025	Voltage Regulation
400KV-BINAGURI-TALA-1	15-05-2025	Hand-tripped at TALA end at 16:35hrs, Voltage Imbalance observed Vry=387kV Vyb=407kV Vbr=385kV

NEW ELEMENTS COMMISSIONED DURING May, 2025							
उत्पादन इकाइयाँ / GENERATING UNITS							
Sl. No	स्थान Location / Pooling Station	मालिक/यूनिट का नाम OWNER/U NIT NAME	यूनिट संख्या/ स्रोत Unit No/Sou rce	संकलित क्षमता (मेगावाट) Capacity added (MW)	कुल/स्थापित क्षमता (मेगावाट) Total/Ins talled Capacity (MW)	दिनांक DATE	टिप्पणी Remarks
NIL							
आई.सी.टी/जी.टी/एस.टी / ICTs/ GTs / STs							
क्र. Sl. No	एजेंसी/मालिक Agency/Ow ner	उप-केन्द्र SUB-STATION	आईसीटी संख्या ICT NO	वोल्टेज (केवी) Voltage Level (kV)	क्षमता (एमवीए) CAPACITY (MVA)	दिनांक DATE	टिप्पणी Remarks
1	WBSETCL	Jeerat	5	400	315	26-05-2025 18:51	
2	WBSETCL	SATGACHI A	1	400	500	11-05-2025 17:37	
3	WBSETCL	SATGACHI A	2	400	500	13-05-2025 20:22	
प्रेषण लाइन / TRANSMISSION LINES							

क्र. Sl. No	एजेंसी/मालिक Agency/Owner	लाइन का नाम LINE NAME	लंबाई (किमी) Length (KM)	कंडक्टर प्रकार Conductor Type	दिनांक DATE	टिप्पणी Remarks
1	Aditya Aluminium	400 kV Lapanga-Aditya Aluminium Ckt-1	5.37	AAAC MOOSE	23-05-2025 17:49	5.37
2	Aditya Aluminium	400 kV Lapanga-Aditya Aluminium Ckt-2	5.37	AAAC MOOSE	23-05-2025 18:12	5.37

लिलो / प्रेषण लाइन की पुनर्व्यवस्था / LILO/RE-ARRANGEMENT OF TRANSMISSION LINES

क्र. Sl. No	एजेंसी/मालिक Agency/Owner	लाइन का नाम / लिलो पर Line Name/LILO at	लंबाई (किमी) Length (KM)	कंडक्टर प्रकार Conductor Type	दिनांक DATE	टिप्पणी Remarks
1	WBSETCL	400KV-NEW CHANDITALA-SATGACHIA-2	88/ LILO Length - 2.5	ACSR MOOSE	09-05-2025 17:05	LILO of 400 kV Gokarna-New Chanditala D/C Line at 400 kV Satgachia GIS for FTC of the Substation's 400 kV System
2	WBSETCL	400KV-GOKARNA-SATGACHIA-2	98/LILO Length-3.4	ACSR MOOSE	09-05-2025 16:55	LILO of 400 kV Gokarna-New Chanditala D/C Line at 400 kV Satgachia GIS for FTC of the Substation's 400 kV System
3	WBSETCL	400KV-NEW CHANDITALA-SATGACHIA-1	88/LILO length-2.5	ACSR MOOSE	09-05-2025 15:42	LILO of 400 kV Gokarna-New

						Chanditala D/C Line at 400 kV Satgachia GIS for FTC of the Substation's 400 kV System
4	WBSETCL	400KV-GOKARNA- SATGACHIA-1	98/LILO Length-3.4	ACSR MOOSE	09-05-2025 15:21	LILO of 400 kV Gokarna- New Chanditala D/C Line at 400 kV Satgachia GIS for FTC of the Substation's 400 kV System
5	SPTL	400KV-DIKCHU- RANGPO-2	71.482	QUAD MOOSE	10-05-2025 18:38	FTC of 400 kV DIKCHU- RANGO TL bypassing Teesta 3

बस/लाइन रिएक्टर / BUS/LINE REACTOR

क्र. Sl. No	एजेंसी/मालि क Agency/Ow ner	एलेमेंट का नाम Element Name	उप-केन्द्र SUB- STATION	वोल्टेज (केवी) Voltage Level (kV)	दिनांक DATE	टिप्पणी Remarks
1	WBSETCL	125MVAR 400KV B/R-1 AT SATGACHIA	SATGAC HIA	400 KV 125 Mvar	11-05-2025 14:37	LILO of 400 kV Gokarna- New Chanditala D/C Line at 400 kV Satgachia GIS for FTC of the Substation's 400 kV System

बस / BUS

क्र. Sl. No	एजेंसी/मालि क Agency/Owner	एलेमेंट का नाम Element Name	उप-केन्द्र SUB-STATION	वोल्टेज (केवी) Voltage Level (kV)	दिनांक DATE	टिप्पणी Remarks
NIL						
एच.वी.डी.सी/ए.सी फिल्टर बैंक/फैक्ट्स डिवाइस संबद्ध प्रणाली / HVDC /AC Filter bank / FACTS DEVICE associated System						
क्र. Sl. No	एजेंसी/मालि क Agency/Owner	एलेमेंट का नाम Element Name	उप-केन्द्र SUB-STATION	वोल्टेज (केवी) Voltage Level (kV)	दिनांक DATE	टिप्पणी Remarks
NIL						
बे / BAYS						
क्र. Sl. No	एजेंसी/मालि क Agency/Owner	एलेमेंट का नाम Element Name	उप-केन्द्र SUB-STATION	वोल्टेज (केवी) Voltage Level (kV)	दिनांक DATE	टिप्पणी Remarks
1	OPTCL	400KV TIE BAY OF (ADITYA ALUMINIUM(AA)-2 AND FUTURE) AT LAPANGA	Lapanga	400	31-05-2025 12:15	
2	WBSETCL	400KV BUS COUPLER BAY AT JEERAT	Jeerat	400	26-05-2025 19:45	
3	OPTCL	400 kV Main Bay of Aditya Aluminium Ckt-1 at Lapanga	Lapanga	400	23-05-2025 17:49	
4	OPTCL	400 kV Main Bay of Aditya Aluminium Ckt-2 at Lapanga	Lapanga	400	23-05-2025 18:12	
5	WBSETCL	400KV MAIN BAY OF 315 MVA ICT 5 AT JEERAT	Jeerat	400	26-05-2025 18:51	
6	WBSETCL	400KV TIE BAY OF (NEW CHANDITALA -	Satgachia	400	13-05-2025 23:10	

		2 AND 500 MVA ICT 2) AT SATGACHIA				
7	WBSETCL	400KV TIE BAY OF (GOKARNA -2 AND 500 MVA ICT 1) AT SATGACHIA	Satgachia	400	11-05-2025 19:52	
8	WBSETCL	400KV Main Bay of 125MVAR B/R-1 AT SATGACHIA	Satgachia	400	11-05-2025 14:37	
9	WBSETCL	400KV Main Bay of 125MVAR Gokarna-1 AT SATGACHIA	Satgachia	400	09-05-2025 15:21	
10	WBSETCL	400KV Main Bay of 125MVAR Gokarna-2 AT SATGACHIA	Satgachia	400	09-05-2025 16:55	
11	WBSETCL	400KV Main Bay of New Chanditala-1 AT SATGACHIA	Satgachia	400	09-05-2025 15:42	
12	WBSETCL	400KV Main Bay of New Chanditala-2 AT SATGACHIA	Satgachia	400	09-05-2025 17:05	
13	WBSETCL	400KV Main Bay of ICT 1 AT SATGACHIA	Satgachia	400	11-05-2025 17:37	
14	WBSETCL	400KV Main Bay of ICT 2 AT SATGACHIA	Satgachia	400	13-05-2025 20:22	

Members may note.

Deliberation in the meeting

Members noted.

4.4. UFR operation during the month of May 2025

Frequency profile for the month as follows:

MONTH	MAX	MIN	% LESS IEGC BAND	% WITHIN IEGC BAND	% MORE IEGC BAND
	(DATE/TIME)	(DATE/TIME)			
May, 2025	50.49 Hz on 22-05-2025 at 07:58 Hrs	49.59 Hz on 22-05-2025 at 19:38 Hrs	3.60	73.30	23.10

Hence, no report of operation of UFR has been received from any of the constituents.

Members may note.

Deliberation in the meeting

Members noted.

Annexure B.2.14



Annexure D.1

Anticipated Peak Demand (in MW) of ER & its constituents for July 2025

1	BIHAR	Demand (MW)	Energy Requirement (MU)
	NET MAX DEMAND	8878	6062
	NET POWER AVAILABILITY- Own Sources	429	313
	Central Sector+Bi-Lateral	5122	3585
	SURPLUS(+)/DEFICIT(-)	-3327	-2165
2	JHARKHAND		
	NET MAXIMUM DEMAND	2212	1222
	NET POWER AVAILABILITY- Own Source	131	171
	Central Sector+Bi-Lateral+IPP	1031	783
	SURPLUS(+)/DEFICIT(-)	-685	-268
3	DVC		
	NET MAXIMUM DEMAND	3550	2555
	NET POWER AVAILABILITY- Own Source	5604	3467
	Central Sector+MPL	375	253
	Bi- lateral export by DVC	2356	1753
	SURPLUS(+)/DEFICIT(-) AFTER EXPORT	72	-588
4	ODISHA		
	NET MAXIMUM DEMAND (OWN)	6000	4400
	NET MAXIMUM DEMAND (In Case of CPP Drawal of 900 MW(peak) and average drawl of 700 MW)	6772	4028
	NET POWER AVAILABILITY- Own Source	3079	2614
	Central Sector	1696	1205
	SURPLUS(+)/DEFICIT(-) (OWN)	-1225	-581
	SURPLUS(+)/DEFICIT(-) (In Case of CPP Drawal of 900 MW(peak) and average drawl of 700 MW)	-1997	-209
5	WEST BENGAL		
	WBSEDCL		
5.1	NET MAXIMUM DEMAND	10133	6756
	NET MAXIMUM DEMAND (Incl. Sikkim)	10143	5987
	NET POWER AVAILABILITY- Own Source (Incl. DPL)	5347	2999
	Central Sector+Bi-lateral+IPP&CPP+TLDP	2170	1371
	EXPORT (To SIKKIM)	10	7
	SURPLUS(+)/DEFICIT(-) AFTER EXPORT	-2626	-1617
5.2	CESC		
	NET MAXIMUM DEMAND	2400	1235
	NET POWER AVAILABILITY- Own Source	830	591
	IMPORT FROM HEL	541	395

	TOTAL AVAILABILITY OF CESC	1371	986
	SURPLUS(+)/DEFICIT(-)	-1029	-249
		830	-249
	WEST BENGAL (WBSEDCL+CESC+IPCL)		
	(excluding DVC's supply to WBSEDCL's command area)		
	NET MAXIMUM DEMAND	12533	7991
	NET POWER AVAILABILITY- Own Source	6177	3590
	CS SHARE+BILATERAL+IPP/CPP+TLDP+HEL	2711	1766
	SURPLUS(+)/DEFICIT(-) BEFORE WBSEDCL'S EXPORT	-3645	-2635
	SURPLUS(+)/DEFICIT(-) AFTER WBSEDCL'S EXPORT	-3655	-2642
6	SIKKIM		
	NET MAXIMUM DEMAND	96	51
	NET POWER AVAILABILITY- Own Source	402	326
	Central Sector	77	52
	SURPLUS(+)/DEFICIT(-)	382	327
	EASTERN REGION		
	NET MAXIMUM DEMAND	33269	22281
	NET MAXIMUM DEMAND ((In Case of CPP Drawal of 900 MW(peak) and average drawl of 700 MW)	33374	21909
	BILATERAL EXPORT BY DVC (Incl. Bangladesh)	2356	1753
	EXPORT BY WBSEDCL TO SIKKIM	10	7
	EXPORT TO B'DESH & NEPAL OTHER THAN DVC	642	478
	NET TOTAL POWER AVAILABILITY OF ER	24478	16372
	(INCLUDING CS ALLOCATION +BILATERAL+IPP/CPP+HEL)		
	SURPLUS(+)/DEFICIT(-)	-8802	-5917
	SURPLUS(+)/DEFICIT(-) (In Case of CPP Drawal for Odisha)	-8906	-5545

प्रदीप कुमार सिन्हा
सचिव
भारत सरकार
PRADEEP K. SINHA
Secretary
Government of India



सत्यमेव जयते
Ministry of Power
Shram Shakti Bhawan
New Delhi - 110001

विद्युत मंत्रालय
श्रम शक्ति भवन
नई दिल्ली-110001
Tele : 23710271/23711316
Fax : 23721487
E-mail : secy-power@nic.in

D.O. No.20/6/2014-OM

05.12.2014

Dear *Shri Negi*,

As you are aware, India has one of the largest A.C. Synchronous Transmission Grids in the world with more than 3 lakhs circuit kms of 220kV and above lines which form the backbone of the Indian Power System.

2. However, this huge network needs to be operated in a sustained and secure manner, particularly, during the time of natural disasters. Failure to do so leads to severe constraints not only in meeting the power demand but also poses serious problems in maintaining safety and security of the Grid. Difficult situations came to light in the wake of recent natural disasters, such as, floods in J&K and Phailin as well as Hud-Hud cyclone in Odisha and Andhra Pradesh. These disasters caused extensive damage to transmission networks resulting in wide spread disruption of many important transmission links and substations affecting power supply for long periods due to the time taken in restoration.

3. You would appreciate that under such adverse situations, the availability of an effective mechanism for emergent restoration of transmission lines in the shortest possible time is of utmost importance. Immediate and temporary restoration of transmission networks is possible by deploying the "Emergency Restoration Systems (ERS)." Grid Standards notified by the Central Electricity Authority(CEA) stipulate that every Transmission Licensee shall have an arrangement for restoration of transmission lines of at least 220kV and above through the use of ERS. However, presently the States do not possess such ERS infrastructure. Consequently, POWERGRID becomes the last resort whose ERS infrastructure is also limited.

4. Therefore, deployment of adequate ERS infrastructure with the States is necessary. In this connection, CEA had recently convened a meeting of the representatives from State Utilities, CTUs and RPCs to deliberate and review their preparedness to effectively restore transmission networks in times of emergency. Based on the inputs received, an indicative requirement of ERS for States has been assessed which is at Annex-I. Further, CEA has also formulated guidelines for planning, deployment and procurement of such ERS infrastructure (Annex-II).

5. I would, therefore, request you to please issue necessary directives to Transmission Utilities/ Transmission licensees operating in your State to take stock, procure appropriate number of ERS infrastructure and place them at strategic locations. Action taken by the Utilities in this regard may be informed to the CEA and the Ministry of Power, at the earliest.

With regards,

Yours sincerely,

(Signature)
(Pradeep K. Sinha)

Encl : as above

Shri Ramesh Negi
Chief Secretary
Govt of Arunachal Pradesh
Itanagar



RIGHT TO
INFORMATION

Sist:- As per list attached.



एक कदम स्वच्छता की ओर

Availability and Proposed Plan for deployment of ERS

Sl. No.	Region	State Utilities / PGCIL	Availability of ERS sets	Additional ERS set to be procured	Remark
I	Northern Region				
	PGCIL	NR1	3	1	
		NR2	1		
	1	Haryana	-	1	
	2	HP	-	1	Hilly terrain
	3	J&K	-	1	-do-
	4	Punjab	-	2	
	5	Rajasthan	-	3	
	6	Uttar Pradesh	-	3	
	7	Uttarakhand	-	1	
	8	Chandigarh	-	-	
	9	Delhi	-	1	DTL is procuring 2 ERS sets
	10	POWERLINKS	2		1 set each is located in NR and ER; each setting having 14 towers of 400 kV
	Total		6	14	
II	Western Region				
	PGCIL	WR1	2	1	
		WR2	2		
	10	Gujarat	-	3	

	11	MP	1	2	
	12	Chhattisgarh	-		
	13	Maharashtra	2	2	
	14	Goa	-	1	
	15	D&NH	-	-	
	16	Daman & Diu	-	-	
	Total		7	9	
III	Southern Region				
	PGCIL	SR1	1	2	
		SR2	1		
	17	AP	-	3	(To be located at Vishakhapatnam, Vijawada, Nellore)
	18	Telengana	-	1	
	19	Karnataka	-	2	
	20	Kerala	-	1	
	21	Tamil Nadu	-	2	
	22	Lakshadweep	-	-	
	23	Puducherry	-	-	
	Total		2	11	
IV	Eastern Region	PGCIL			
	PGCIL	ER1	1	-	
		ER2	2		
	24	Bihar	2	2	
	25	Jharkhand	-	1	
	26	Orissa	3	2 (comprising of 12 nos. of 400kV towers which is in the process of procurement)	Existing ERS located at Bhubaneswar, Chatrapur and Budhipada (each with 14 ERS towers)
	27	West Bengal	-	2	
	28	DVC	-	1	

	29	A&N Island	-	-	
	30	Sikkim	-	-	
	Total		8	8	
V	North Eastern Region		-		
	PGCIL	NER	1		
	31	Assam	4	2	
	32	Manipur	-		
	33	Meghalaya	-		
	34	Nagaland	-		
	35	Tripura	-		
	36	Ar. Pradesh	-		
	37	Mizoram	-		
	Total		5	2	
	Total All India		28	44	

Note: POWERGRID has informed that they are procuring 6 additional sets of ERS for different regions.

Strategy adopted

- The primary criterion for deciding number of ERS to be arranged by a transmission utility has to be the length of transmission line (ckt-kms) at different voltage levels (e.g 220 kV, 400 kV, 765 kV and +/- 500kV HVDC). Other factors to be taken into account while deciding the number of ERS are
 - Importance of the line considering security of Grid
 - Areas prone to tower failure and failure pattern in different areas
 - Command area of the transmission utility and transportability across the command area
- For any transmission utility, one set of ERS has been planned to cater to failure of towers for transmission line lengths of up to 5000 Ckt. Kms.. Accordingly, two (2) sets of ERS have been planned for transmission line lengths of about 5000 to 10,000 Ckt. Kms. and three (3) sets for more than 10,000 Ckt. Kms and so on.
- The transmission Utility with line length less than 500 ckt kms (of 400kV lines) may be given option either to procure ERS or have agreement with other transmission utilities for providing ERS on mutually agreed terms, when need arises.

**GUIDELINES FOR PLANNING, PROCUREMENT AND DEPLOYMENT OF
EMERGENCY RESTORATION SYSTEM (ERS)**

1. One set of ERS should include all accessories [structures (Aluminum Alloy), polymer insulators & hardware, anchor assembly, guy wires, foundation plates, guy plate, other equipment & fittings, special Tools & Plants required for erection & stringing of ERS and trailer mounted detachable containers (without engine) for storage & transportation of ERS hardware / material etc.] and associated software.
2. One set of ERS shall be capable of restoring few numbers of suspension towers and tension towers of the transmission line corresponding to the highest transmission voltage in operation in the utility with required type of conductors. The same ERS can be used for lower voltage lines as well. The number of suspension, tension towers, insulators and associated hardware etc., to be included under one set of ERS, may be decided by the utilities at the time of procurement depending on their requirement.
3. Proper management of ERS and training of personnel for erection of towers on ERS and use of associated software is essential. A dedicated and specialized erection & commissioning gang, which is properly trained to execute such work, would be required.
4. ERS should be utilized only for emergency purposes and the line should be restored on normal towers as early as possible. It should not be a practice to run transmission line on ERS for a long time instead of shifting to normal towers. Moreover, ERS should not be used in new lines under construction. Otherwise, the very purpose of ERS will be defeated.
5. The deployment of ERS by any transmission utility / licensee should be reported to concerned RLDC and RPC.
6. The transmission utilities may approach Appropriate Commission for approval and initiate procurement process on urgent basis to comply with Grid Standards. Utilities may also approach State Disaster Management Authorities for funding.
7. The funding for procurement of ERS could be considered from PSDF for North Eastern States and a proposal be submitted by Member Secretary, NERPC.

List of Chief Secretaries of State and UTs

S. No.	State	Name and Address	Telephone/ Fax/Email
1.	Andhra Pradesh	Shri I.Y.R. Krishna Rao Chief Secretary Government of Andhra Pradesh, Secretariat, Hyderabad-500022	Tel: 040-23453620 040-23455340 Fax: 040-040-23453700, 23451133, 23451144
2.	Arunachal Pradesh	Shri Ramesh Negi Chief Secretary & Principal Secretary (Relief & Rehabilitation & Disaster Management) Arunachal Pradesh Civil Secretariat, Government of Arunachal Pradesh, Itanagar- 791 111	Tel: 0360-2212595 Fax: 0360-2212446, 2215719 M: 9436040035
3.	Assam	Shri Jitesh Khosla Chief Secretary Government of Assam, Assam Sachivalaya, Block C, 3 rd Floor, Dispur, Guwahati-781006	Tel: 0361-2261120, 2261403 Fax:-0361-2260900
4.	Bihar	Shri Anjani Kumar Singh Chief Secretary Government of Bihar Old Secretariat, Patna-800015	Tel: 0612-2215804 Fax: 0612-2217085
5.	Chattisgarh	Sh. Vivek Kumar Dhand Chief Secretary Government of Chattisgarh, DKS Bhawan, Mantralaya, Raipur-492001	Tel: 0771-2221207/8 Fax: 0771-2221206
6.	Goa	Shri R.K. Srivastava Chief Secretary Govt. of Goa Secretariat Porvorim	Tel: 0832-2419402 Fax: 0832-2415201
7.	Gujarat	Shri D.J. Pandian Chief Secretary Government of Gujarat New Sachivalaya Gandhinagar-382010	Tel: 079-23220372, 079-23250301-3 Fax: 079-23250305
8.	Haryana	Shri. P.K. Gupta Chief Secretary Government of Haryana, Room No.-4, 4 th floor, Haryana, Civil Secretariat, Sector-1, Chandigarh-160009	Tel: 0172-2740118 Fax: 0172-2740317
9.	Himachal Pradesh	Shri P. Mitra Chief Secretary Government of Himachal Pradesh Secretariat, Shimla- 171002	Tel: 0177-2621022 Fax: 0177-2621813

10.	Jammu & Kashmir	Sh. Mohammad Iqbal Khandey Chief Secretary Government of J & K Jammu Secretariat, Jammu	Tel: 0191-2546773, 2544338 (Jammu) Fax: 0191-2546188
11.	Jharkhand	Shri Sajal Chakrabarty Chief Secretary Government of Jharkhand Secretariat, Ranchi-834004	Tel: 0651-2400240, 2400250 Fax: 0651-2400255
12.	Karnataka	Shri Kaushik Mukherjee Chief Secretary Government of Karnataka 3rd Floor, R. No. 320, Vidhan Souda, Secretariat, Bangalore-560001	Tel: 080-22252442, 22092476 Fax: 080-22258913
13.	Kerala	Ms E K Bharat Bhushan Chief Secretary Government of Kerala Secretariat, Thiruvananthapuram-695001	Tel: 0471-2333147, 2327376 Fax: 0471-2327176
14.	Madhya Pradesh	Shri Anthony J C Desa Chief Secretary Government of Madhya Pradesh Mantralaya, Vallabh Bhawan, Bhopal-462004	Tel: 0755-2441370, 2441848 Fax: 0755-2441521
15.	Maharashtra dscsoffice @gmail.com	Shri Swadheen S Kshatriya Chief Secretary Government of Maharashtra Mantralaya, Mumbai-400032	Tel: 022-22852626 22025042, 22028762 22793762 Fax: 022-22028594
16.	Manipur	Shri P.C. Lawmkunga Chief Secretary Government of Manipur Manipur Secretariat, Imphal-790001	Tel: 0385-2451144, 2450064 Fax: 0385-2452629
17.	Meghalaya	Shri P B O Warjri Chief Secretary Government of Meghalaya, Meghalaya Civil Secretariat, Shillong-793001 Email: barkos.warjri@nic.in	Tel: (O)0364-2224801, 222250, Mob:-9774033922 (R)-0364-2534629 Fax: 0364-2225978
18.	Mizoram	Shri Lalmalsawma Chief Secretary Government of Mizoram, Block C, Civil Secretariat, Aizwal- 796001	Tel: 0389-2322411 Fax: 0389-2322745
19.	Nagaland	Shri M.T. Aier Chief Secretary Government of Nagaland Nagaland Civil Secretariat, Kohima-790001	Tel: 0370-2270082, 2270076 Fax: 0370-2270057
20.	Orissa	Shri Gokul Chandra Pati Chief Secretary Government of Orissa Secretariat, Bhubaneswar- 751001	Tel: 0674-2534300, 2536700 Fax: 0674-2536660
21.	Punjab	Shri Sarvesh Kaushal Chief Secretary Government of Punjab Punjab Secretariat, Chandigarh-160017	Tel: 0172-2740156, 2740860 Fax: 0172-2742488, 2740936

22.	Rajasthan	Shri C.S. Rajan Chief Secretary Government of Rajasthan Secretariat, Jaipur-302001	Tel: 0141-2227254 Fax: 0141-2227114
23.	Sikkim	Smt. Rinchen Ongmu Chief Secretary Government of Sikkim Secretariat, Gangtok- 737101	Tel: 03592-202315, 204323 (fax) Fax: 03592-222851 03592-204323
24.	Tamil Nadu	Shri. K. Gnanadesikan Chief Secretary Government of Tamil Nadu Secretariat, Chennai-600009	Tel: 044-25671555 Fax: 044-25672304
25.	Tripura	Shri G. Kameswara Rao Chief Secretary Government of Tripura Civil Secretariat, Agaratala-799001	Tel: 0381-2323200, 2324392 Fax: 0381-2324013
26.	Uttar Pradesh	Shri Alok Ranjan Chief Secretary Government of Uttar Pradesh Secretariat, Lucknow-226001	Tel: 0522-2621599 0522-2238212 0522-2238212 Fax: 0522-2239283
27.	Uttarakhand	Shri N. Ravi Shanker Chief Secretary Government of Uttarakhand 4, Subhash Road, Secretariat, Dehradun-248001	Tel: 0135-2712094 0135-2712100, 2712200 Fax: 0135-2712113 0135-2712500
28.	West Bengal	Shri Sanjay Mitra Government of West Bengal Secretariat, Writers Building Kolkata-700001	Tel: 033-22145858 Fax: 033-22144328
29.	Andaman & Nicobar	Sh. Anand Prakash Chief Secretary Secretariat & Administration, Government of Andaman & Nicobar Islands, Port Blair	Tel: 03192-233110, 234087 Fax: 03192-231100, 03192-232656
30.	Chandigarh	Shri K.K. Sharma Advisor to Administrator Union Territory of Chandigarh, Punjab Raj Bhawan, Sector – 6 Chandigarh-160017	Tel: 0172-2740154 Fax: 0172-2740317 0172-2740165
31.	Dadra & Nagar Haveli	Shri Ashish Kundra Administrator Government of Dadra & Nagar Haveli, Secretariat, Silvassa-396230	Tel: 0260-2230700 2642777 Fax: 0260- 2230775 0260-2642702
32.	Daman & Diu	Shri Ashish Kundra Administrator Secretariat Daman, Government of Daman & Diu, Daman & Diu	Tel: 0260-2230770, 2230700 Fax: 0260-2230775

33.	Delhi	Shri D.M. Spolia Chief Secretary Govt of NCT Delhi, Delhi Secretariat, I.P. Estate, New Delhi- 110002	Tel: 011-23392100 Fax: 011-23392102
34.	Lakshadweep	Shri H. Rajesh Prasad Administrator Union Territory of Lakshadweep, Kavaratti, Lakshadweep-682555	Tel: 04896-262255, 262279 Fax: 04896-262184
35.	Puducherry	Shri Chetan B Sanghi Chief Secretary Puducherry Administration, Chief Secretariat, 1 Beach Road, U.T. of Puducherry, Puducherry- 605001	Tel: 0413-2334145 0413-2335512 Fax: 0413-2337575

36. *Telangana* Dr. Rogiv Sharma,
Chief Secretary,
Govt of Telangana,
Hyderabad.

Utility	Voltage level	Length in CKM	Total number of ERS towers	Number of ERS towers available	Number of ERS towers in use/unavailable	Number of ERS towers required as per MoP norms	Location of ERS
OPTCL	400 kV	1196.87	29	27	2	1 set	Available: Mancheswar: 27 In use: 400 kV Mendhasal-Meramundali line: 2
	220 kV	6835.48	0	0	0	2 set	
	132 kV	8717.11	0	0	0	2 set	
PGCIL ER-I	765 kV	1075.17	24	24	0	1 set	Gaya
	400 kV	11569.95	16	16	0	3 set	Purnea
			16	16	0	1set	Jamshedpur
	220 kV	481.68	0	0	0	1 set	
	132 kV	94.09	0	0	0	1 set	
Adani transmission limited(ATL)	400 kV	959.32	3	3	0	1 set	Sami(Gujarat): 1, Koradi(Maharashtra): 1, Akola(Maharashtra): 1
PGCIL (Odisha)	765 kV	1845.00	9	9	0	1 set	Rengali (Suspension type: 6, Tension type: 3)
			15	15	0	set	Angul (Suspension type: 9, Tension type: 6)
	400 kV	3355.00	3	3	0	1 set	Rourkela (Suspension type: 2, Tension type: 1)
	220 kV	61.00			0	1 set	
PGCIL ER-II	400 kV	5840.00	10	10	0	2 set	Durgapur
			16	16	0	set	Siliguri
	220 kV	1041.00	0	0	0	1 set	
	132 kV	332.00	0	0	0	1 set	
	765 kV	639.00	0	0	0	1 set	
WBSCTCL	220kV	4051.22	6	6	0	1 set	Durgapur
			2	2	0	set	Jeerat
			1	1	0	set	New Town
			3	3	0	set	New Jalpaiguri
			4	4	0	set	Laxmikantapur
	400 kV	2492.51	0	0	0	1 set	
	132 kV	9670.58	0	0	0	2 set	
	66 kV	333.00	0	0	0	1 set	
Indigrid (ENICL, OGPTL & PKTCL)	400 kV	1556.70	1	1	0	1 set	Bhopal, IndiGrid, maintains a centrally located ERS set at Bhopal, which is deployed across all five regions on a need basis.
	765 kV	612.00	0	0	0	1 set	
JUSNL	220 KV	2599.51	3	3	0	1 set	Hatia
			2	2	0	set	Jamshedpur
			3	3	0	set	Dumka
	400 kV	360.94	0	0	0	1 set	
	132 kV	4067.80	0	0	0	1 set	
DVC	220 kV	2975.64	7	7	0	1 set	Maithon: Suspension /Running angle 0 to 20 deg S/C ERS Tower: 4 Tension / Dead End 0 to 60 deg S/C ERS Tower: 2
	400 kV	482.69				1 set	Tension / Dead End 0 to 90 deg S/C ERS Tower: 1

	132 kV	4005.21	0	0	0	1 set	
BSPTCL	132kV	12194.38	42	13	29	3 set	Available: Fathua: 2, Purnea: 2, Muzaffarpur: 4, Gaya: 5 In use: 132kV Supal-Kathiya:4 132kV Chandauti-new Chandauti: 8 132kV Auraiya: 1 33kV supply near Masan River: 6 132kV Majhau-Balia: 4 132kV Dehri-Kochas 3 Under maintenance: Fathua: 1, Purnea: 1, Muzaffarpur: 1
	220 kV	5476.29	0	0	0	1 set	
	400 kV	600.00	0	0	0	1 set	
TOTAL		95521.14	215	184	31		

No. 34/7/2025-TRANSMISSION(MoP)
Government of India
Ministry of Power
Shram Shakti Bhawan, Rafi Marg, New Delhi- 110001

Dated the 11th May, 2025

To,

CMD,
POWERGRID
Gurugram

Subject: Disaster Preparedness of Transmission Infrastructure – reg.

Sir,

I am directed to refer to the meeting chaired by Secretary (Power) held on 10.05.2025, to review the disaster preparedness of Grid Operations and Transmission Infrastructure in view of prevailing security situation. Based on the decisions taken in the meeting, the following actions may be taken:

- (i) To immediately **place orders for 20 sets (300 towers) ERS**, under Make In India, to meet potential requirement in the states through emergency procurement process.
 - (ii) To organise a **Training Programe** in Meerut on 14-5-2024, in consultation with CEA, on the use and deployment of Emergency Restoration Systems for officials from State Transmission Utilities (STUs) of J&K, Ladakh, Punjab, Rajasthan, Gujarat, Delhi and Haryana.
 - (iii) To plan construction of bunkers at critical transmission substations (400 kV and above, HVDC, etc.) in close proximity to the border, in consultation with the Local Military Authority.
3. This issues with the approval of Competent Authority.

Yours faithfully,



(Naorem Indrakumar Singh)

Under Secretary (Trans)

Tele Fax: 011-23325242

E-mail: transdesk-mop@nic.in

Copy to:


1. Chairperson, CEA
2. Chief Engineer (NPC), CEA – with request to communicate with all STUs of the Northern and Western Regions, either directly or through the Member Secretaries of the respective Regional Power Committees, to ensure the nomination of at least four officials (preferably with relevant seniority and practical experience) for the training.
3. State Transmission Utilities of J&K, Ladakh, Punjab, Rajasthan, Gujarat, Delhi and Haryana
4. Sr. PPs/ PPS/PS to Secretary (Power)/ AS (Trans)/ JS (Trans)/ Director (Trans)/ Director (PG), Ministry of Power

Indira
11/5/25


North Karanpura SPS


Switchyard Logic:





LINE-1 Status (In BCU)

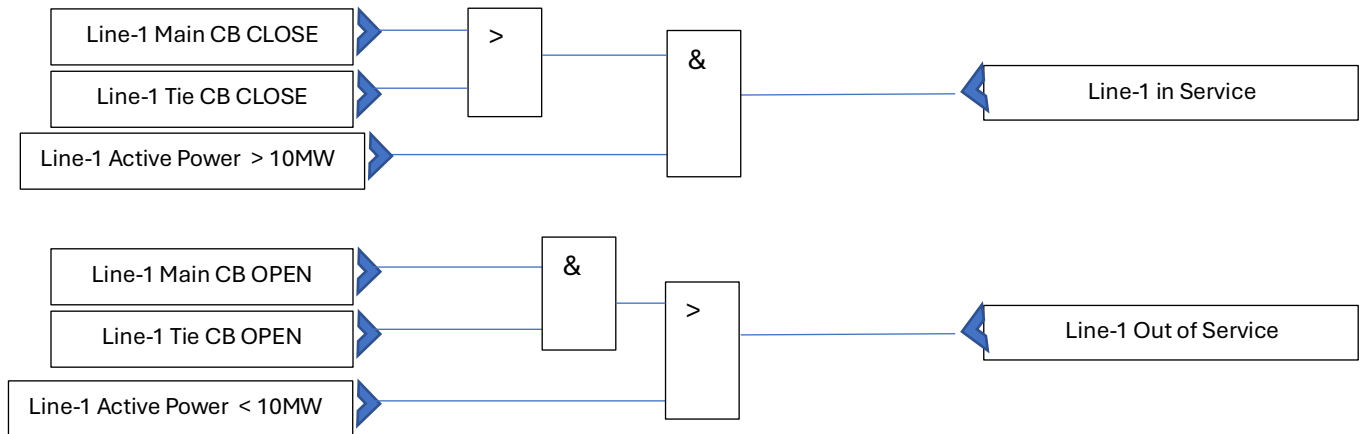

LINE-2 Status (In BCU)

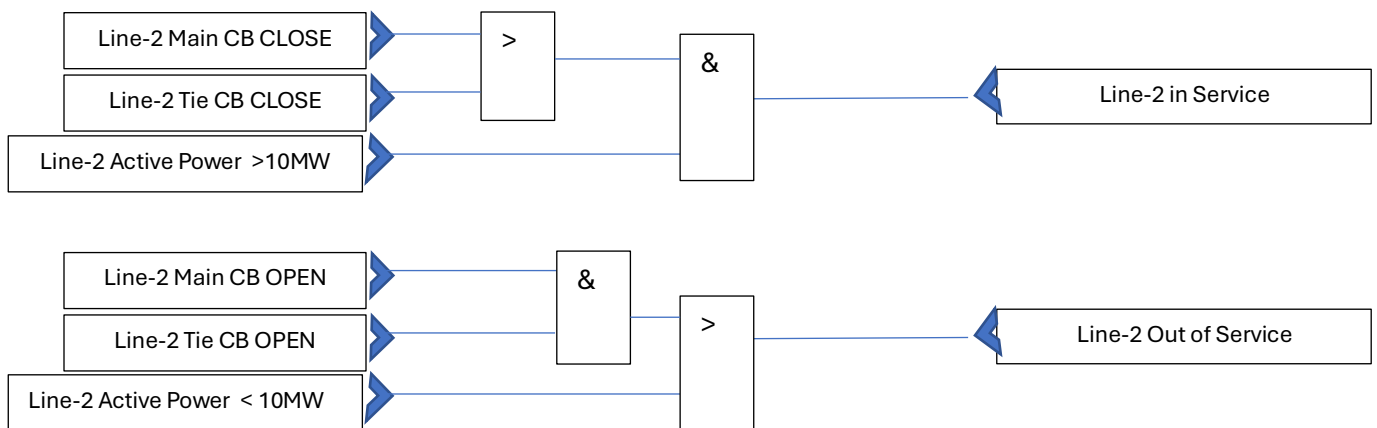

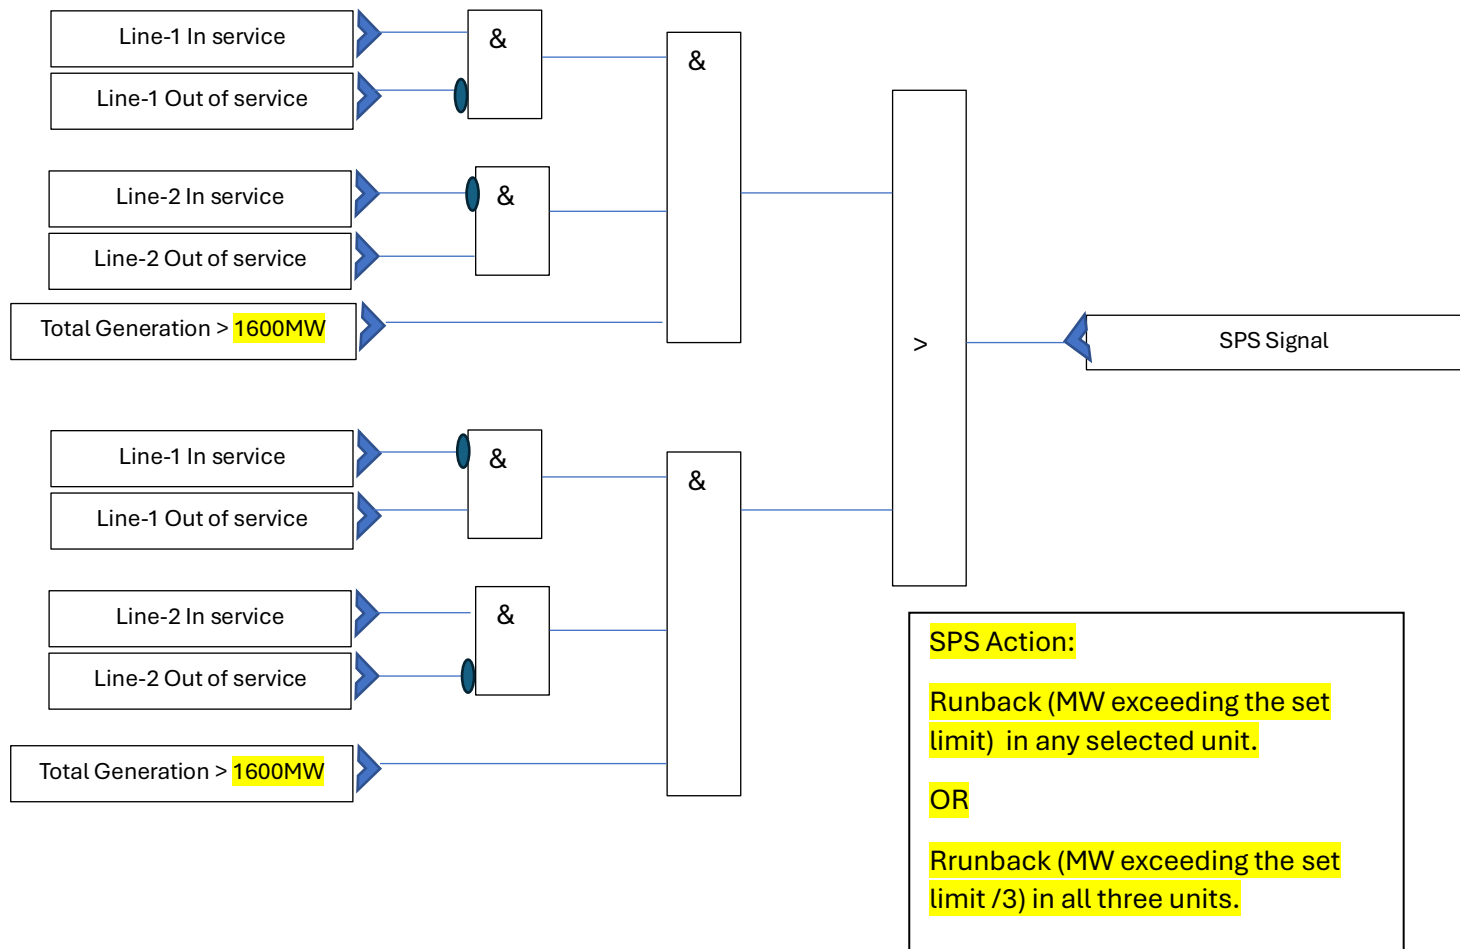IN DDCIMS:

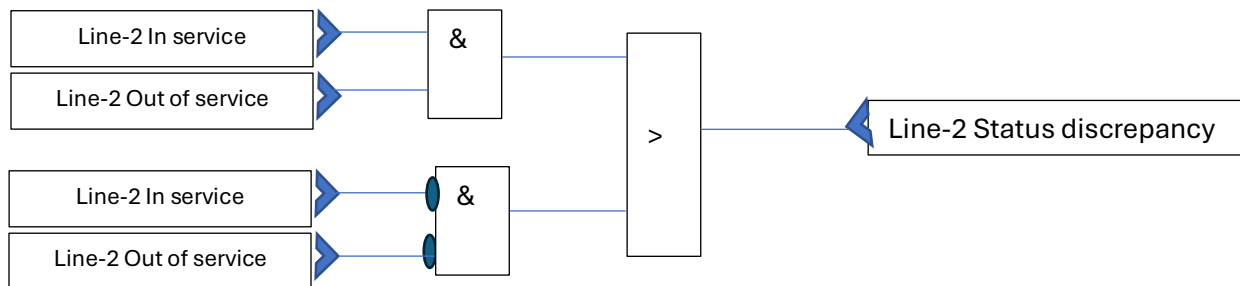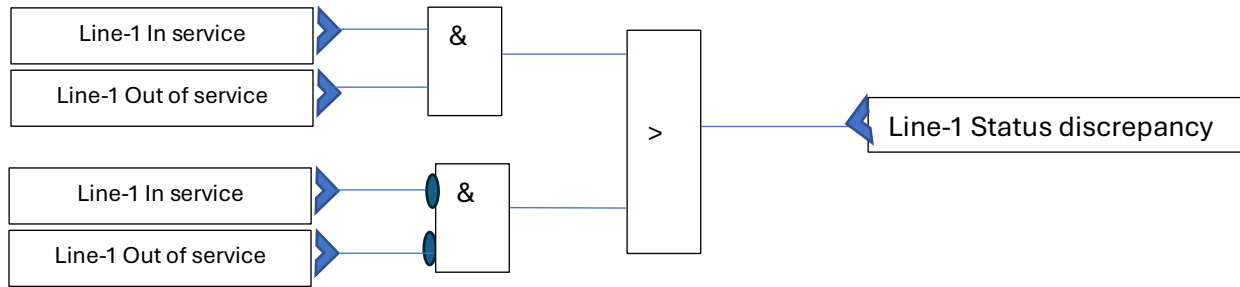Alarms

Note:-

If load reduction is planned in all three units:

1. During TO of Unit-3, SPS command shall extend to Unit-1 and Unit-2 only. Load reduction shall be equal to **MW exceeding the set limit**/2.
 - a. SPS command magnitude if exceeds **100MW**, Unit operators shall trip the top mill manually.
 - b. As far as possible Units shall be run in CMC mode.
2. After successful demonstration of TO of Unit-3, SPS command shall be extend to all three units. Load reduction shall be equal to **MW exceeding the set limit**/3.
